



Santa Monica Community College District
Citizens' Bond Oversight Committee
MEETING – APRIL 26, 2017
AGENDA

A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee will be held on Wednesday, **April 26, 2017 at 8 a.m.** The meeting will be held in Drescher 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

#### **Public Comments**

Individuals may address the Citizens' Bond Oversight Committee concerning any subject that lies within the jurisdiction of the Citizens' Bond Oversight Committee by submitting an information card with name and topic on which comment is to be made. The Chair reserves the right to limit the time for each speaker.

#### 1. CALL TO ORDER

#### 2. ROLL CALL

Sonya Sultan - Chair Katherine Reuter - Co-Chair Sharon Barovsky Michael Dubin Jeffrey Graham Sion Roy Negron Zavanna

#### 3. APPROVAL OF MINUTES

Citizens' Bond Oversight Committee meeting of January 18, 2017 (enclosed)

#### 4. REPORTS and DISCUSSION (reports enclosed)

- SMC Bond Capital Construction Budget Summary as of March 31,2017
- Bond Budgets

Measure U

Measure S

Measure AA

Measure U Reports

**Project Schedule** 

Expenditures

Measure S Reports

**Project Schedule** 

Expenditures

• Measure AA Reports

**Project Schedule** 

Expenditures

- Bond Sales/Expenses Report
- SMC Bond Program Contractor List

#### 5. INFORMATION – EXPIRING TERMS OF MEMBERS OF THE CITIZENS' BOND OVERSIGHT COMMITTEE

The term of the following member(s) of the Citizens' Bond Oversight Committee is expiring effective **June 30, 2017** and is eligible for reappointment:

- Sharon Barovsky, Local Community/Malibu
- Michael Dubin, Business Community / Taxpayers' Organization
- Sonya Sultan, Local/Business Community
- Sion Roy, Business Community/Taxpayers' Organization
- Negron Zavanna, SMC Student

The term of the following member(s) of the Citizens' Bond Oversight Committee is expiring effective **June 30, 2018** and is eligible for reappointment:

- Jeffrey Graham, Local Business
- Katharine Reuter, Senior Citizens' Organization

The Board of Trustees will follow a recruitment and application process to appoint/reappoint members to fill the vacancies.

#### 6. TOUR OF THE CORE PERFORMANCE CENTER

Please allow 30 minutes to tour the New Core Performance Center

#### 7. PUBLIC COMMENTS

#### 8. SCHEDULE OF MEETINGS, 2017-2018

Wednesday at 8 a.m. July 19, 2017

#### 9. ADJOURNMENT

a. The next meeting of the Citizens' Bond Oversight Committee will be held on Wednesday, July 19, 2017 at 8 a.m. in Drescher Hall Room 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.



Santa Monica Community College District
Citizens' Bond Oversight Committee
MEETING – JANUARY 18, 2017
MINUTES

A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee was held on Wednesday, **January 18, 2017 at 8 a.m.** in Drescher 300---E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

#### 1. **CALL TO ORDER:** 8:05 a.m.

#### 2. ROLL CALL --- Members

- Sonya Sultan, Chair --- Present
- Katherine Reuter, Vice---Chair --- Present
- Jeffrey Graham Present
- Sion Roy --- Present
- Sharon Barovsky --- Present
- Michael Dubin --- Present
- Zavanna Negron –

#### Absent Others Present:

- Mr. Bill Rauch Partner, Varinek, Trine, Day & Company (VTD)– CPA
- Dr. Kathryn E. Jeffery, Superintendent/President
- Don Girard, Senior Director, Government Relations/Institutional Communications
- Greg Brown, Director Facilities
- Chris Bonvenuto, Chief Director, Business Services
- Ramin Nematollahi, Citizens' Bond Oversight Committee Coordinator
- Charlie Yen, Director --- Contracts
- Emil Zordilla, Assistant Director, Facilities Planning

#### 3. APPROVAL OF MINUTES

The minutes of the Citizens' Bond Oversight Committee meeting of October 19, 2016 were approved as is. *Motion was made by Katherine Reuter and seconded by Jeffrey Graham and unanimously approved by the committee.* 

#### 4. CONFLICT OF INTEREST FORM

Members completed and endorsed forms. The forms are on file.

#### 5. REPORTS and DISCUSSION

Chris Bonvenuto discussed Santa Monica College's previous audit firm (Vicenti, Lloyd & Stuzman, CPAs), which had served as SMC's auditor for 15 years and had given SMC "Unmodified Opinions". Varinek, Trine, Day & Company was selected after a formal bidding process and received a 3 year contract with an option of 2 years. Dr. Jeffery commented on the common and good practice of changing auditors.

#### A. Santa Monica Community College District

Measure U, Measure S, Measure AA General Obligation Bonds Financial and Performance Audit, June 30, 2016

Mr. Bill Rauch, presented the 2015---2016 Financial and Performance Audit Reports and reviewed the findings with the committee. He reviewed the Opinion of the findings which state:

"In our opinion, the financial statements referred to above present fairly, in all material respects, the financial position of Measure U, Measure S, Measure AA General Obligation Bond Funds (Measure U, Measure S, and Measure AA) of the District as of June 30, 2016, and the respective changes in financial position for the year then ended in accordance with accounting principles generally accepted in the Unites State of America." (Page 3, of the SMCCD, Measure U, Measure S & Measure AA General Obligation Bonds Financial And Performance Audits – June 30, 2016 – Varinek, Trine, Day & Co. LLP)

He reiterated the "unmodified opinion", which is the highest mark that can be received for a financial and performance audit. He further reviewed, **The Statement of Revenues, Expenditures, and Changes in Fund Balance** on page 5. He also discussed the "**None Reported**" findings on Financial Statement Findings on page 17.

### B. Santa Monica Community College District

Measure U, Measure S, Measure AA General Obligation Bonds Performance Audit June 30, 2016

Mr. Rauch discussed the procedures performed for the performance audit. A sample of expenditures was selected starting July 1, 2015 and ending June 30, 2016, and supporting documentation was reviewed to ensure that funds were properly expended on specific project list. The sample included transactions totaling \$49,446,725, which represent 71 percent of the total expenditures of \$69,373,518.

Based on this testing, Varinek, Trine, Day & Co. LLP, verified that funds from Measures U, Measures S, and Measures AA general Obligation Bond Funds (Measure U, Measure S, Measure AA) were expended for the construction, renovation, funding and equipment of District facilities constituting authorized bond projects.

#### Conclusion:

"The results of our test indicated that, in all significant respect, the Santa Monica Community College District has properly accounted for the expenditures held in the Measure, U, Measure S, and Measure AA general Obligation Bond Funds (Measure U, Measure S, Measure AA) and such expenditures were made for authorized bond projects. There were no salaries of administrative charged to the Measure U, Measure S, and Measure AA General Obligation Bond Funds for District general administration or operations." (Page 4, of the SMCCD, Measure U, Measure S & Measure AA General Obligation Bonds Performance Audits – June 30, 2016 – Varinek, Trine, Day & Co. LLP).

Mr. Rauch also discussed the "none reported" comment regarding the Schedule of Findings and Questioned Costs – Page 5, (June 30, 2016) and reiterated that "There were no audit findings reported in the prior year's Schedule of Findings and Questioned Costs."

Motion was made by Sharon Barovsky to accept the report as is and seconded by Katharine Reuter and unanimously approved by the committee.

c. SMC Bond Capital Construction Budget Summary as of December 31, 2016.

Emil Zordilla, Assistant Director, Facilities planning, gave a visual presentation of the bond construction project:

- Center for Media and Design: The project is progressing as planned. Date of Completion is first quarter of 2017 with a move in date of fall 2017.
- East Wing Performing Arts Center: The PAC is scheduled to open for spring 2017 semester.
- **Core Performance Center**: Formerly known as the Fitness Center is going to be completed in January and will be occupied spring 2017 semester.
- Student Services Building: Large structure beams will be placed in the coming weeks. The student services building is schedule to open last quarter of 2018 and occupied by early 2019.
- Malibu Campus: Currently awaiting the finalization of lease from Los Angeles County. Bidding for the project will take place in the summer of 2017 with construction to begin in fall of 2017. Completion date is last quarter of 2019.
- Early Childhood Education Center: Awaiting coastal commission approval. Bidding
  for the project is expected in the summer of 2017 with construction to commence
  fall 2017. The project is schedule to be completed fall of 2018.
- D. Measure U, S and AA and Bond Sales Expense Reports

The SMC Bond Capital Construction Budget Summary as of December 31, 2016 reports the following:

Measure U Budget: \$160,000,000 Measure S Budget: \$143,500,000 Measure AA Budget: \$295,000,000 Other Funding Received: \$ 26,195,758 Other Funding Pending: \$ 52,594,548 **Total Budget:** \$698,766,706 Estimate at Completion: \$698,590,482 **Bond Funds Remaining:** \$158,468,301

 Measure U: Total Measure U Expenditures last period were \$3,144,064; total remaining funds are

**\$8,848,412**; no budget variance.

- Measure S: Total Measure S Expenditures last period were \$180,983; total remaining funds are \$55,560,851; no budget variance.
- Measure AA: Total Measure AA Expenditures last period were \$17,720,703; total remaining funds are \$94,059,038; no budget variance.
- The Bond Sales/Expense Report indicates total bond amounts, bond issue dates/amounts unsold bond amount and total available as of December 31, 2016.

 Total Bond:
 \$598,500,000

 Total Available:
 \$528,492,559

 Total Expenses:
 \$440,031,699

 Total Available Remaining:
 \$ 88,460,860

**Total Unsold Bond:** \$ 70,007,441

• The SMC Bond Construction Program Contractor List as of December 31, 2016 was included in the packet.

 Current information on all bond construction projects is available at: <a href="http://smcbondprogram.com">http://smcbondprogram.com</a> and at <a href="http://www.smc.edu/CBOC">http://www.smc.edu/CBOC</a>

#### 7. **SCHEDULE OF MEETINGS, 2016---2017**

Wednesday, April 19, 2017 at 8 a.m.

#### **8. ADJOURNMENT:** 9:10 am

The next meeting of the Citizens' Bond Oversight Committee will be held on Wednesday, April 19, 2017 at 8 a.m. in Drescher Hall Room 300---E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

Project Number	Project Name	Measure U Budget	Measure S Budget	Measure AA Budget	Measure V Budget	Interest	Other Funding Received *	Other Funding Pending **	Total Budget	Estimate at Completion	Status	Bond Funds Remaining
U-A	Purchase of BAE Airport Site	\$30,280,878	Buuget	Buaget	Buuget		Received	renaing	\$30,280,878	\$30,280,878	Completed	Remaining
U-B	Emeritus College Facility	\$8,909,940					\$693,842		\$9,603,782	\$9,603,782	Completed	
U-C	Purchase of 1738 Pearl Street	\$749,208					7 00 0,0 12		\$749,208	\$749,208	Completed	
U-D	PE Temp. Bldg. Replacement	\$2,797,033							\$2,797,033	\$2,797,033	Completed	
U-E	Remodel Library Village for Math	\$1,458,690							\$1,458,690	\$1,458,690	Completed	
U-F	SM Airport Campus Site Improvements	\$4,170,264							\$4,170,264	\$4,170,264	Completed	
U-G	SM Airport Campus West Building	\$19,709,741							\$19,709,741	\$19,709,741	Completed	
U-H	Theater Arts Renovation	\$19,544,314							\$19,544,314	\$19,544,314	Completed	
U-I	Earthquake Rpl. Liberal Arts North	\$6,505,400					\$6,002,325		\$12,507,725	\$12,507,725	Completed	
U-K	Earthquake Rpl. Liberal Arts South	\$6,108,150					\$10,625,070		\$16,733,220	\$16,733,220	Completed	
U-L	Shuttle Replacement Parking	\$18,969,509					ψ10,0 <b>1</b> 0,01		\$18,969,509	\$18,969,509	Completed	
U-M	North Quad Plaza	\$11,388,463							\$11,388,463	\$11,388,463	Completed	
U-Q	Infrastructure & Safety	\$4,003,084							\$4,003,084	\$4,003,084	Completed	
U-R	Restroom Improvements	\$17,501							\$17,501	\$17,501	Completed	
S-1	Athletic Fields Phase I, Corsair Field	717,501	\$4,372,535				\$67,530		\$4,440,065	\$4,440,065	Completed	
S-1A	Athletic Fields Phase I, John Adams		\$2,969,807				Ş07,530		\$2,969,807	\$2,969,807	Completed	
S-1A	Pico Promenade Improvements, Phase I		\$1,018,009						\$1,018,009	\$1,018,009	Completed	
S-10	Adv. Architecture Related Exp for AA		\$1,018,009						\$1,018,009	\$1,018,009	Completed	
AA-114	Community Classroom & Facility Projects		ŞU	\$3,162,183					\$3,162,183	\$3,162,183	Completed	
U-T	14th and Pico Project	\$319,242		\$3,102,163					\$3,102,183	\$3,102,163	Completed	
U-N	Letters & Sci Demo/Restore	\$519,242							\$319,242	\$319,242	Completed	
		\$0	¢45 507	\$24,902,902					\$24,948,499			<u> </u>
S-14, AA-115	Real Property Acquisition		\$45,597							\$24,948,499	Completed	\$5,050,0
AA-108	Renovation of Corsair Stadium		¢27.607.625	\$35,299			62.002.576		\$35,299	\$35,299	Completed	
S-2	Performing Arts Complex	62.044.074	\$37,697,625				\$2,992,576		\$40,690,201	\$40,690,201	Completed	
U-J	Music Complex	\$2,011,371		60			\$2,618,113		\$4,629,484	\$4,629,484	Completed	
S-3, AA-109	Career Opportunity Center			\$0					\$0	\$0	Completed	
AA-118	Infrastructure & Technology - Utility			\$27,753					\$27,753	\$27,753	Completed	
AA-111	Business & Facilities Infrastructure			\$1,968,124					\$1,968,124	\$1,968,124	Completed	
AA-117	Infrastructure & Technology - Technology			\$2,434,417					\$2,434,417	\$2,434,417	Completed	
S-7, AA-113	Energy Efficiency Projects		\$293,361	\$3,016,773			\$708,637		\$4,018,771	\$4,018,771	Completed	
S-15	Signage Safety/Information		\$706,223						\$706,223	\$706,223	Completed	\$8
AA-102	Infrastructure & Technology - Information Technology Relocation			\$24,399,627					\$24,399,627	\$24,399,627	Completed	\$1,254,0
S-8, AA-116	Satellite Campus Parking Facilities and Roadway		\$3,891,747						\$7,022,417	\$7,022,417	Deferred	\$1,000,0
-	Replacement Math and Science Extension Building	\$308,336			\$50,000,000			\$40,088,000	\$90,401,286	\$90,401,286	+	\$50,000,0
AA-105	Drescher - Academic Modernization, Bookstore, Pico Promenade II				\$13,000,000				\$13,005,082	\$13,005,082	Deferred	\$13,000,0
AA-103	Media and Technology Complex - Academy Site			\$103,219,665			\$990,441	\$5,844,950	\$110,055,056		In Construction	\$20,428,7
AA-107	Madison East Wing Seismic Upgrade			\$27,608,816					\$27,608,816		In Construction	\$2,890,4
S-4, AA-104	Replacement Health/PE/Fitness Central Plant Building		\$11,603,383				\$190,847		\$58,272,030		In Construction	\$11,116,0
AA-119	Emergency Lighting, Fire Alarm, and Security System			\$11,520,794					\$11,520,794		In Construction	\$2,004,7
AA-101	Environmental Performance - Central Plant Connections			\$11,206,164					\$11,206,164		In Construction	\$2,312,9
	Student Services Building	\$20,638,446			\$15,095,896		\$1,321,000		\$130,224,164		In Construction	\$76,313,5
S-5	Early Childhood Development/Childcare		\$7,000,000			\$1,858,578		\$6,661,598	\$15,520,176	\$15,520,176	In Design	\$5,904,0
S-6, AA-110	Malibu Site Acquisition and Facility		\$25,000,000						\$25,000,000	\$25,000,000	In Design	\$17,438,9
, S-11, AA-112	Master Planning	\$2,110,430	\$716,428	\$750,000					\$3,576,858	\$3,576,858	In Design	\$503,0
S-12	Other Bond Related Expenses		\$609,282						\$609,282	\$609,282	In Planning	\$228,
	TBD		•		\$237,104,104				\$237,104,104	\$237,104,104	In Planning	\$237,104,
-16, AA-212	Cost of Issuance		\$100,000	\$500,000					\$1,400,000	\$1,400,000	In Planning	\$1,115,
	Management Reserve				\$28,000,000				\$33,553,984	\$33,553,984	In Planning	\$28,190,
	Project Totals	\$160,000,000	¢142 E00 000	\$295,000,000			\$26,210,381	¢E2 E04 E49	\$1,043,781,329		J	\$475,855

<sup>\*</sup> City of SM: \$10,206,823; FEMA: \$1,962,572; State: \$5,779,000; Prop T: 2,618,113; DWP: \$86,245; SCE: \$824,486; Gas Co.: \$88,262; Madison Foundation: \$2,992,576; KCRW: \$958,462; Emeritus College Foundation: \$693,842; Bond Interest and Cost of Issuance Refund: \$21,476,400

4/6/1

<sup>\*\*</sup> City of SM: 6,661,598; KCRW: \$5,844,950; State: \$40,088,000


#### SANTA MONICA COMMUNITY COLLEGE DISTRICT Bond Sales / Expenses Report As of March 31, 2017

Measure U Bond \$160,000,000	
Bond Issue Date	Amount
2002	\$25,000,000
2004	\$21,999,971
2005	\$89,999,923
2007	\$11,999,987
2010	\$10,998,992
Total Available	\$159,998,873
Expenses as of 3-31-17	\$157,955,335
Total Available Remaining	\$2,043,538
Unsold Bond Amount	\$1,127
Total Available as of 4-1-17	\$2,044,665

Measure S Bond \$143,500,000 (1)		
Bond Issue Date		Amount
	2005	\$58,000,000
	2007	\$8,500,000
	2009	\$56,997,857
Total Available		\$123,497,857
Expenses as of 3-31-17		\$92,093,108
Total Available Remaining		\$31,404,749
Unsold Bond Amount		\$20,002,143
Total Available as of 4-1-17	•	\$51,406,892

Measure AA Bond \$295,000,000	
Bond Issue Date	Amount
2010	\$100,000,000
2014	\$144,995,829
Total Available	\$244,995,829
Expenses as of 3-31-17	\$217,596,103
Total Available Remaining	\$27,399,726
Unsold Bond Amount	\$50,004,171
Total Available as of 4-1-17	\$77,403,897

Total Bond	\$598,500,000
Total Available	\$528,492,559
Total Expenses as of 3-31-17	\$467,644,546
Total Available Remaining	\$60,848,013
Total Unsold Bond	\$70,007,441

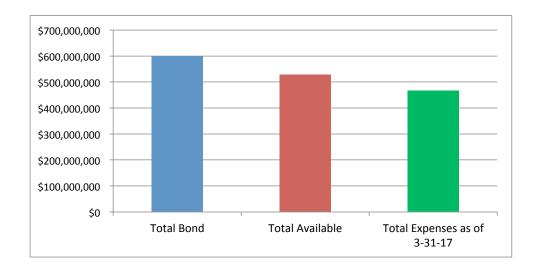

Interest	Measure U	Measure S	Measure AA
As of 6-30-16	\$6,843,003	\$10,172,764	\$4,824,407
Arbitrage Payment as of 6-30-16	\$0	\$420,037	\$0
Available Interest as of 6-30-16	\$6,843,003	\$9,752,727	\$4,824,407

Cost of Issuance Refund	Measure U	Measure S
As of 6-30-16	\$20,688	\$35,575


<sup>(1)</sup> Original Bond \$135,000,000.00, refunding on 2-15-07 received additional \$8,500,000.00

#### SANTA MONICA COMMUNITY COLLEGE DISTRICT

#### Measure U Bond Budget

As of March 31, 2017

	Project Name	Completion	Project Budget	Measure U Allocation	Other Funding	Measure U Expenditures as of 3/31/17	Measure U Expenditures as of 12/31/16	Measure U Expenditures Last Period	Total Measure U Remaining
Α	Purchase of BAE Airport Site	Completed	\$30,280,878	\$30,280,878	\$0	\$30,280,878	\$30,280,878	\$0	\$0
В	Emeritus College Facility	Completed	\$9,603,782	\$8,909,940	\$693,842	\$8,909,940	\$8,909,940	\$0	\$0
С	Purchase of 1738 Pearl Street	Completed	\$749,208	\$749,208	\$0	\$749,208	\$749,208	\$0	\$0
D	PE Temp. Bldg. Replacement	Completed	\$2,797,033	\$2,797,033	\$0	\$2,797,033	\$2,797,033	\$0	\$0
E	Remodel Library Village for Math	Completed	\$1,458,690	\$1,458,690	\$0	\$1,458,690	\$1,458,690	\$0	\$0
F	SM Airport Campus Site Improvements	Completed	\$4,170,264	\$4,170,264	\$0	\$4,170,264	\$4,170,264	\$0	\$0
G	SM Airport Campus West Building	Completed	\$19,709,741	\$19,709,741	\$0	\$19,709,741	\$19,709,741	\$0	\$0
Н	Theater Arts Renovation	Completed	\$19,544,314	\$19,544,314	\$0	\$19,544,314	\$19,544,314	\$0	\$0
- 1	Earthquake Rpl. Liberal Arts North	Completed	\$12,507,725	\$6,505,400	\$6,002,325	\$6,505,400	\$6,505,400	\$0	\$0
J	Music Complex	Completed	\$4,629,484	\$2,011,371	\$2,618,113	\$2,011,371	\$2,011,371	\$0	\$0
K	Earthquake Rpl. Liberal Arts South	Completed	\$16,733,220	\$6,108,150	\$10,625,070	\$6,108,150	\$6,108,150	\$0	\$0
L	Shuttle Replacement Parking	Completed	\$18,969,509	\$18,969,509	\$0	\$18,969,509	\$18,969,509	\$0	\$0
М	North Quad Plaza	Completed	\$11,388,463	\$11,388,463	\$0	\$11,388,463	\$11,388,463	\$0	\$0
N	Letters & Sci Demo/Restore	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0	Student Services Building	January 2019	\$130,224,164	\$20,638,446	\$109,585,718	\$18,593,781	\$11,790,034	\$6,803,747	\$2,044,665
Р	Science Complex Addition	Completed	\$90,401,286	\$308,336	\$90,092,950	\$308,336	\$308,336	\$0	\$0
Q	Infrastructure & Safety	Completed	\$4,003,084	\$4,003,084	\$0	\$4,003,084	\$4,003,084	\$0	\$0
R	Restroom Improvements	Completed	\$17,501	\$17,501	\$0	\$17,501	\$17,501	\$0	\$0
S	Master Planning	Completed	\$2,110,430	\$2,110,430	\$0	\$2,110,430	\$2,110,430	\$0	\$0
Т	14th and Pico Project	Completed	\$319,242	\$319,242	\$0	\$319,242	\$319,242		\$0
	Project Totals		\$379,618,018	\$160,000,000	\$219,618,018	\$157,955,335	\$151,151,588	\$6,803,747	\$2,044,665

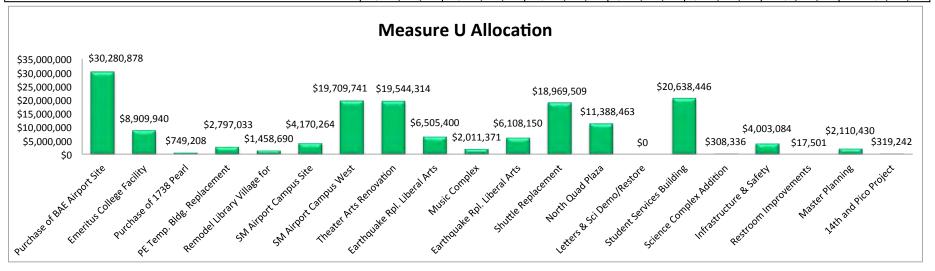

## SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure U Bond Budget History

as of March 31, 2017


	Project Name	Completion	Preliminary Measure U Budget	Measure U Budget as of 12/31/16	Measure U Budget as of 3/31/17	Variance	Measure U Remaining as of 3/31/17
Α	Purchase of BAE Airport Site	Completed	\$30,000,000	\$30,280,878	\$30,280,878	\$0	\$0
В	Emeritus College Facility	Completed	\$8,883,381	\$8,909,940	\$8,909,940	\$0	\$0
С	Purchase of 1738 Pearl Street	Completed	\$749,208	\$749,208	\$749,208	\$0	\$0
D	PE Temp. Bldg. Replacement	Completed	\$2,673,247	\$2,797,033	\$2,797,033	\$0	\$0
Е	Remodel Library Village for Math	Completed	\$1,425,565	\$1,458,690	\$1,458,690	\$0	\$0
F	SM Airport Campus Site Improvements	Completed	\$6,200,000	\$4,170,264	\$4,170,264	\$0	\$0
G	SM Airport Campus West Building	Completed	\$20,071,124	\$19,709,741	\$19,709,741	\$0	\$0
Н	Theater Arts Renovation	Completed	\$16,992,296	\$19,544,314	\$19,544,314	\$0	\$0
- 1	Earthquake Rpl. Liberal Arts North	Completed	\$5,352,752	\$6,505,400	\$6,505,400	\$0	\$0
J	Music Complex	Completed	\$4,802,537	\$2,011,371	\$2,011,371	\$0	\$0
K	Earthquake Rpl. Liberal Arts South	Completed	\$2,863,566	\$6,108,150	\$6,108,150	\$0	\$0
L	Shuttle Replacement Parking	Completed	\$17,256,000	\$18,969,509	\$18,969,509	\$0	\$0
М	North Quad Plaza	Completed	\$3,939,759	\$11,388,463	\$11,388,463	\$0	\$0
N	Letters & Sci Demo/Restore	Completed	\$1,192,250	\$0	\$0	\$0	\$0
0	Student Services Building	January 2019	\$23,952,004	\$20,638,446	\$20,638,446	\$0	\$2,044,665
Р	Science Complex Addition	Completed	\$10,613,910	\$308,336	\$308,336	\$0	\$0
Q	Infrastructure & Safety	Completed	\$5,000,000	\$4,003,084	\$4,003,084	\$0	\$0
R	Restroom Improvements	Completed	\$400,000	\$17,501	\$17,501	\$0	\$0
S	Master Planning	Completed	\$500,000	\$2,110,430	\$2,110,430	\$0	\$0
Т	14th and Pico Project	Completed	\$14,662,000	\$319,242	\$319,242	\$0	\$0
	Project Totals		\$177,529,599	\$160,000,000	\$160,000,000	\$0	\$2,044,665

#### SANTA MONICA COMMUNITY COLLEGE DISTRICT

#### **Measure S Bond Budget**

As of March 31, 2017

	Project Name	Completion	Project Budget	Measure S Allocation	Other Funding	Measure S Expenditures as of 3/31/17	Measure S Expenditures as of 12/31/16	Measure S Expenditures Last Period	Total Measure S Remaining
1	Athletic Fields Phase I, Corsair Field	Completed	\$4,440,065	\$4,372,535	\$67,530	\$4,372,535	\$4,372,535	\$0	\$0
1A	Athletic Fields Phase I, John Adams	Completed	\$2,969,807	\$2,969,807	\$0	\$2,969,807	\$2,969,807	\$0	\$0
2	Performing Arts Complex	Completed	\$40,690,201	\$37,697,625	\$2,992,576	\$37,697,625	\$37,697,625	\$0	\$0
3	Career Opportunity Center	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	June 2017	\$58,272,030	\$11,603,383	\$46,668,647	\$11,603,383	\$11,603,383	\$0	\$0
5	Early Childhood Development/Childcare	September 2019	\$15,520,176	\$7,000,000	\$8,520,176	\$1,095,906	\$1,065,703	\$30,203	\$5,904,094
6	Malibu Site Acquisition and Facility	March 2019	\$25,000,000	\$25,000,000	\$0	\$7,561,052	\$7,387,886	\$173,166	\$17,438,948
7	Energy Efficiency Projects	Completed	\$510,683	\$293,361	\$217,322	\$293,361	\$293,361	\$0	\$0
8	Satellite Campus Parking Facilities and Roadway Improvements	Deferred	\$7,022,417	\$3,891,747	\$3,130,670	\$3,891,747	\$3,891,747	\$0	\$0
9	Parking Garage, Grounds and Equipment - Student Services	January 2019	\$130,224,164	\$47,476,003	\$82,748,161	\$19,741,170	\$15,797,597	\$3,943,573	\$27,734,833
10	Pico Promenade Improvements	Completed	\$1,018,009	\$1,018,009	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	Completed	\$716,428	\$716,428	\$0	\$716,428	\$716,428	\$0	\$0
12	Other Bond Related Expenses	On-Going	\$609,282	\$609,282	\$0	\$381,080	\$377,211	\$3,869	\$228,202
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	Completed	\$45,597	\$45,597	\$0	\$45,597	\$45,597	\$0	\$0
15	Signage Safety/Information	Completed	\$706,223	\$706,223	\$0	\$705,408	\$702,260	\$3,148	\$815
16	Cost of Issuance	On-Going	\$100,000	\$100,000	\$0	\$0	\$0	\$0	\$100,000
	Project Totals		\$287,845,082	\$143,500,000	\$144,345,082	\$92,093,108	\$87,939,149	\$4,153,959	\$51,406,892

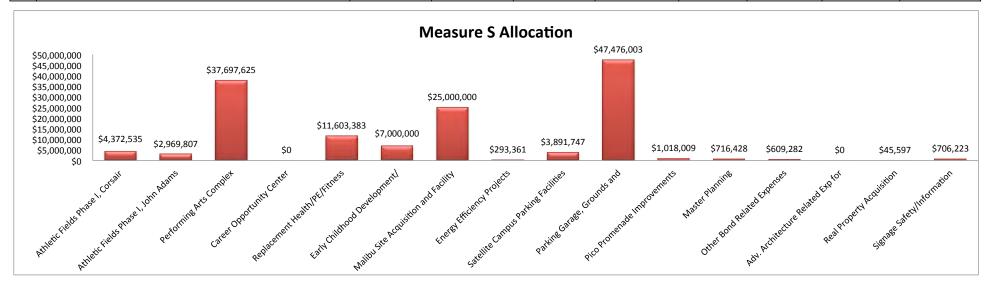


## SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure S Bond Budget History

as of March 31, 2017

	Project Name	Completion	Preliminary Measure S Budget	Measure S Budget as of 12/31/16	Measure S Budget as of 3/31/17	Variance	Measure S Remaining as of 3/31/17
1	Athletic Fields Phase I, Corsair Field	Completed	\$1,800,000	\$4,372,535	\$4,372,535	\$0	\$0
1A	Athletic Fields Phase I, John Adams	Completed	\$35,200,000	\$2,969,807	\$2,969,807	\$0	\$0
2	Performing Arts Complex	Completed	\$24,000,000	\$37,697,625	\$37,697,625	\$0	\$0
3	Career Opportunity Center	Completed	\$20,000,000	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	June 2017	\$20,000,000	\$11,603,383	\$11,603,383	\$0	\$0
5	Early Childhood Development/Childcare	September 2019	\$7,000,000	\$7,000,000	\$7,000,000	\$0	\$5,904,094
6	Malibu Site Acquisition and Facility	March 2019	\$25,000,000	\$25,000,000	\$25,000,000	\$0	\$17,438,948
7	Energy Efficiency Projects	Completed	\$2,000,000	\$293,361	\$293,361	\$0	\$0
8	Satellite Campus Parking Facilities and Roadway Improvements	Deferred	\$0	\$3,891,747	\$3,891,747	\$0	\$0
9	Parking Garage, Grounds and Equipment - Student Services	November 2018	\$0	\$47,476,003	\$47,476,003	\$0	\$27,734,833
10	Pico Promenade Improvements, Phase I	Completed	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	Completed	\$0	\$716,428	\$716,428	\$0	\$0
12	Other Bond Related Expenses	On-Going	\$0	\$609,282	\$609,282	\$0	\$228,202
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	Completed	\$0	\$45,597	\$45,597	\$0	\$0
15	Signage Safety/Information	Completed	\$0	\$706,223	\$706,223	\$0	\$815
16	Cost of Issuance	On-Going	\$0	\$100,000	\$100,000	\$0	\$100,000
	Project Totals		\$135,000,000	\$143,500,000	\$143,500,000	\$0	\$51,406,892

#### SANTA MONICA COMMUNITY COLLEGE DISTRICT **Measure AA Bond Budget** As of March 31, 2017

	Project Name	Completion	Project Budget	Measure AA Allocation	Other Funding	Measure AA Expenditures as of 3/31/17	Measure AA Expenditures as of 12/31/16	Measure AA Expenditures Last Period	Total Measure AA Remaining
101	Environmental Performance - Central Plant Connections	August 2017	\$11,206,164	\$11,206,164	\$0	\$8,893,242	\$7,192,175	\$1,701,067	\$2,312,922
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$24,399,627	\$24,399,627	\$0	\$23,145,587	\$23,037,403	\$108,184	\$1,254,040
103	Media and Technology Complex - Academy Site	July 2017	\$110,055,056	\$103,219,665	\$6,835,391	\$82,790,943	\$79,821,257	\$2,969,686	\$20,428,722
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	July 2017	\$58,272,030	\$46,477,800	\$11,794,230	\$35,361,758	\$30,862,131	\$4,499,627	\$11,116,042
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	Deferred	\$13,005,082	\$5,082	\$13,000,000	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	Deferred	\$90,401,286	\$4,950	\$90,396,336	\$4,950	\$4,950	\$0	\$0
107	Madison East Wing Seismic Upgrade	Completed	\$27,608,816	\$27,608,816	\$0	\$24,718,409	\$23,327,685	\$1,390,724	\$2,890,407
108	Renovation of Corsair Stadium	Completed	\$35,299	\$35,299	\$0	\$35,299	\$35,299	\$0	\$0
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
110	Malibu Center	March 2019	\$25,000,000	\$0	\$25,000,000	\$0	\$0	\$0	\$0
111	Business & Facilities Infrastructure	Completed	\$1,968,124	\$1,968,124	\$0	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	On-Going	\$750,000	\$750,000	\$0	\$246,945	\$241,926	\$5,019	\$503,055
113	Energy Efficiency Projects	Completed	\$3,508,088	\$3,016,773	\$491,315	\$3,016,773	\$3,016,773	\$0	\$0
114	Community Classroom & Facility Projects	Completed	\$3,162,183	\$3,162,183	\$0	\$3,162,183	\$3,162,183	\$0	\$0
115	Real Property Acquisition	Completed	\$24,902,902	\$24,902,902	\$0	\$19,852,902	\$14,802,902	\$5,050,000	\$5,050,000
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Deferred	\$7,022,417	\$2,130,670	\$4,891,747	\$2,130,670	\$2,130,670	\$0	\$0
117	Infrastructure & Technology - Technology	Completed	\$2,434,417	\$2,434,417	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	Completed	\$27,753	\$27,753	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	On-Going	\$11,520,794	\$11,520,794	\$0	\$9,516,066	\$8,585,232	\$930,834	\$2,004,728
120	Student Services	January 2019	\$130,224,164	\$31,438,134	\$98,786,030	\$0	\$0	\$0	\$31,438,134
121	Cost of Issuance	On-Going	\$500,000	\$500,000	\$0	\$285,000	\$285,000	\$0	\$215,000
	Management Reserve	On-Going	\$176,224	\$190,847	\$0	\$0	\$0	\$0	\$190,847
	Project Totals		\$546,004,202	\$295,000,000	\$251,195,049	\$217,596,103	\$200,940,962	\$16,655,141	\$77,403,897



# SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget History as of March 31, 2017

	Project Name	Completion	Preliminary Measure AA Budget	Measure AA Budget as of 12/31/16	Measure AA Budget as of 3/31/17	Variance	Measure AA Remaining as of 3/31/17
101	Environmental Performance - Central Plant Connections	August 2017	\$12,034,042	\$11,206,164	\$11,206,164	\$0	\$2,312,922
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$13,287,218	\$24,399,627	\$24,399,627	\$0	\$1,254,040
103	Media and Technology Complex - Academy Site	July 2017	\$57,480,824	\$103,219,665	\$103,219,665	\$0	\$20,428,722
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	July 2017	\$29,232,317	\$46,492,423	\$46,477,800	-\$14,623	\$11,116,042
105	Drescher - Academic Modernization, Bookstore, Pico Promenade II	Deferred	\$34,026,480	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	Deferred	\$68,259,000	\$4,950	\$4,950	\$0	\$0
107	Madison East Wing Seismic Upgrade	Completed	\$6,146,000	\$27,608,816	\$27,608,816	\$0	\$2,890,407
108	Renovation of Corsair Stadium	Completed	\$11,203,000	\$35,299	\$35,299	\$0	\$0
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$32,384,000	\$0	\$0	\$0	\$0
110	Malibu Center	March 2019	\$6,069,031	\$0	\$0	\$0	\$0
111	Business & Facilities Infrastructure	Completed	\$17,506,952	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	On-Going	\$2,000,000	\$750,000	\$750,000	\$0	\$503,055
113	Energy Efficiency Projects	Completed	\$5,371,136	\$3,016,773	\$3,016,773	\$0	\$0
114	Community Classroom & Facility Projects	Completed	\$0	\$3,162,183	\$3,162,183	\$0	\$0
115	Real Property Acquisition	Completed	\$0	\$14,802,902	\$24,902,902	\$10,100,000	\$5,050,000
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Deferred	\$0	\$2,130,670	\$2,130,670	\$0	\$0
117	Infrastructure & Technology - Technology	Completed	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	Completed	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	On-Going	\$0	\$10,320,794	\$11,520,794	\$1,200,000	\$2,004,728
120	Student Services	January 2017	\$0	\$42,738,134	\$31,438,134	-\$11,300,000	\$31,438,134
121	Cost of Issuance	On-Going	\$0	\$500,000	\$500,000	\$0	\$215,000
	Management Reserve	On-Going	\$0	\$176,224	\$190,847	\$14,623	\$190,847
	Project Totals		\$295,000,000	\$295,000,000	\$295,000,000	\$0	\$77,403,897

## SANTA MONICA COMMUNITY COLLEGE DISTRICT

## Measure U Project Schedule As of March 31, 2017

	Project Name	Completion		20	14		20	)15		2	016		201	7		20	18	2	019	
Α	Purchase of BAE Airport Site	Completed																		
В	Emeritus College Facility	Completed																		
С	Purchase of 1738 Pearl Street	Completed																		
D	PE Temp. Bldg. Replacement	Completed																		
Е	Remodel Library Village for Math	Completed																		
F	SM Airport Campus Site Improvements	Completed																		
G	SM Airport Campus West Building	Completed																		
Н	Theater Arts Renovation	Completed																		
T	Earthquake Rpl. Liberal Arts North	Completed																		
J	Music Complex	Completed																		
K	Earthquake Rpl. Liberal Arts South	Completed																		
L	Shuttle Replacement Parking	Completed																		
М	North Quad Plaza	Completed																		
N	Letters & Sci Demo/Restore	Completed																		
0	Student Services Building	January 2019																		
Р	Science Complex Addition	Completed																		
Q	Infrastructure & Safety	Completed																		
R	Restroom Improvements	Completed				$\Box$														
S	Master Planning	Completed				ヿ														
Т	14th and Pico Project	Completed				コ														
	* SM Airport Campus also known as Bundy	Site	-		In (		nstruc	tion	_				-	+	+	-	-	+	-	

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
Lumi and co																	
U7100010																	
Purchase of BAE Airport Site (A)					****												200 000 000
Site Acquisition		\$0			\$30,280,878	\$0											
Total		\$0	\$0	\$0	\$30,280,878	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$30,280,878
Project Budget	\$30,280,878																
Less Other Funding	\$0																
Net	\$30,280,878																
Actual Measure U Expenditures	\$30,280,878																
Running Balance	\$0																
U7100028			ı				1							1			
Emeritus College Facility (B)														1			
Site Acquisition		\$8,658,675	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$8,658,675
		\$14.649	\$3.009	\$20.421	\$0												
Legal Architect		\$93.735	\$27,831	\$161	\$0												
		\$18,400	\$27,631	\$101	\$0 \$0	\$0											
Engineering		\$10,400	\$4,461	\$0	\$0 \$0	\$C											
Supply			\$17,496		\$4,000	\$C											
Building & Additions		\$0		\$0				\$0									
Cap Equipment		\$0	\$49,406	\$0	\$0							\$0					
Non-Cap Equipment		\$0	-\$2,197	\$0	-\$108	\$0		\$0			\$0						
Total		\$8,785,459	\$100,007	\$20,582	\$3,892	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$8,909,940
Project Budget	\$9,603,782	Received															
Less Other Funding*	\$693,842	\$693,842		* Other Funding													
Net	\$8,909,940			Emeritus Colle	ge Foundation	\$693,842 rece	ived										
Actual Measure U Expenditures	\$8,909,940																
Running Balance	\$0																
U7100006							_							1			
1738 Pearl Street (C)				-			+							-			
Site Acquisition		\$0	\$704,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$704,534
Site Acquisition Site Improvement		\$0 \$0	\$704,534	\$0 \$0	\$0 \$0			\$0 \$0									
Building & Additions		\$0 \$0	\$3,250 \$41,424		\$0	\$0											
				\$0 <b>\$0</b>	\$0 <b>\$0</b>	\$0		\$0 <b>\$0</b>	\$0 \$0	\$0 \$0	\$0 \$0	\$0 <b>\$0</b>	\$0		\$0		
Total Project Project	6740.000	\$0	\$749,208	\$0	\$0	\$0	ן \$0	\$0	\$0	\$0	1 \$0	\$0	\$0	\$0	\$0	\$0	\$749,208
Project Budget	\$749,208																
Less Other Funding	\$0																
Net	\$749,208																
Actual Measure U Expenditures	\$749,208																
Running Balance	\$0																

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Einal	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/1/ Final	14/15 Final	15/16 Final	16/17	Combined Totals
Fiojects	Duuget	02/03 i iiiai	03/04 1 11181	04/03 1 11181	03/00 i illai	00/07 1 11101	07/00 T IIIai	00/03 1 11181	03/10 1 11141	10/11 I IIIai	11/12/11/01	12/13 1 11101	13/14 1 11101	14/13 1 11101	13/10 1 11141	10/17	Combined Totals
U7100026																	
PE Temporary Building Replacement (D)																	
Architect		\$148,055	\$42,372	\$6,220	\$485	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$197,133
Building & Additions		\$43,866	\$1,922,493	\$415,932	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,382,291
Inspection & Testing		\$6,455	\$136,510	\$716	\$0	\$0	\$0		\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$143,681
Project Management		\$4,800	\$56,247	\$5,225	\$0		\$0					\$0	\$0	\$0	\$0	\$0	
Advertising and Moving Expenses		\$763	\$0	\$6,893	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$7,656
Total		\$203,939	\$2,157,622	\$434,987	\$485	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,797,033
Project Budget	\$2,797,033																
Less Other Funding	\$0																
Net	\$2,797,033																
Actual Measure U Expenditures	\$2,797,033																
Running Balance	\$0																
•																	
U7100310																	
Remodel Library Village for Math (E)																	
Moving Exp.		\$0	\$38,625	\$0	\$0		\$0					\$0		\$0		\$0	
Building & Additions		\$0		\$115,653	\$0	\$0	\$0	\$0	\$0			\$0		\$0		\$0	
Architect		\$104,992	\$27,141	\$1,340	\$486	\$0	\$0	\$0 \$0	\$0			\$0	\$0	\$0		\$0	
Engineering		\$0	\$2,658	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0		\$0	
Inspection & Testing		\$0	\$27,083	\$25,175	\$0	\$0	\$0			\$0		\$0	\$0	\$0		\$0	\$52,258
Project Management		\$0	\$51,679	\$4,400	\$0		\$0			\$0		\$0	\$0	\$0		\$0	\$56,079
Advertising and Moving Expenses		\$207	\$10,137	\$12,623	\$0		\$0			\$0		\$0	\$0	\$0		\$0	
Total		\$105,199	\$1,193,813	\$159,191	\$486	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,458,690
Project Budget	\$1,458,690																
Less Other Funding	\$0																
Net	\$1,458,690																
Actual Measure U Expenditures	\$1,458,690	I															

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
U7100027	1																
SM Airport Campus Site Improvements (F)																	
Supplies		\$0	\$26,234	\$975	\$5.873	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$33.082
Misc Fees		\$0 \$0	\$26,234	\$975	\$5,673 \$0	\$34.274	\$0	\$0 \$0		\$0 \$0		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	
Other Contract Services		\$3.860	\$25 \$11.508	\$8,434	\$1.501	\$34,274 \$0	\$0	\$0 \$0		\$0			\$0 \$0		\$0 \$0		
			\$11,508	\$8,434 \$15.182	\$1,501	\$7,237		\$0 \$0							\$0 \$0		
Site Improvement Building & Additions		\$0 \$0	\$1,495,697	\$1,670,788	\$4,824	\$1,231	\$0 \$0	\$0 \$0		\$0 \$0			\$0 \$0		\$0 \$0		
Architect		\$104,934	\$500	\$0	\$43,570	\$0	\$0	\$0		\$0	\$0	\$0		\$0	\$0	\$0	
Engineering		\$35,000	\$148,304	\$950	\$10,040	\$0	\$0	\$0							\$0		
Inspection & Testing		\$5,032	\$118,662	\$191,271	\$0	\$0	\$0	\$0		\$0					\$0		
Project Management		\$750	\$155,798	\$38,425	\$1,365	\$220	\$0	\$0							\$0		
City Fees, Advertising and Security System		\$16,587	\$1,802	\$327	\$150	\$4,375	\$0	\$0		\$0		\$0	\$0		\$0		
Total		\$166,163	\$1,958,530	\$1,926,352	\$73,113	\$46,106	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,170,264
Project Budget	\$4,170,264																
Less Other Funding	\$0																
Net	\$4,170,264																
Actual Measure U Expenditures	\$4,170,264																
Running Balance	\$0																
U7110027																	
SM Airport Campus West Building (G)																	
Supply		\$0	\$0	\$17,650	\$28,017	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$45,667
Other Contract Services		\$0	\$0	\$0	\$3,576	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,576
Moving Expenses		\$0	\$0	\$180	\$15,824	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$16,004
Building & Additions		\$0	\$0	\$15,037,532	\$1,256,065	\$46,946	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$16,340,543
Architect		\$0	\$971,954	\$1,043,950	\$49,779	\$1,147	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,066,830
Engineering		\$0	\$2,920	\$9.800	\$5,010	\$963	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$18,693
Inspection & Testing		\$0	\$21,173	\$126,510	\$9,856	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$157,539
Project Management		\$0	\$14,450	\$313,715	\$13,956	\$0	\$0	\$0		\$0	\$0				\$0		
Cap Equipment		\$0	\$49,795	\$326,382	\$4,792	\$0	\$0	\$0							\$0		
Non-Cap Equipment		\$0	\$0	\$280,558	\$57,240	\$0	\$0	\$0					\$0		\$0		
Total		\$0			\$1,444,115	\$49.056	\$0					\$0			\$0		
Project Budget	\$19,709,741	7.	. ,	. ,,	. ,,	,,	**				1 7-1	**			7-1	**	,,,
Less Other Funding	\$0																
Net	\$19,709,741																
Actual Measure U Expenditures	\$19,709,741																
Running Balance	\$0																
ranning Dalanco	ΨΟ																

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
7																	
U7100025																	
Theatre Arts Renovation (H)																	
Supplies		\$0	\$8,904	-\$14	\$12,858	\$16,619	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$38,367
Legal		\$0	\$0	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$0	\$0	\$14,061	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$14,061
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$5,245	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,245
Rental / Lease		\$0	\$1,446	\$2,200	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,646
Building & Additions		\$528	\$1,326,630	\$4,540,487	\$10,897,603	\$56,122	\$25,220	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$16,846,590
Architect		\$289,913	\$369,213	\$423,416	\$82,639	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$1,212,545
Engineering		\$6,174	\$2,981	\$16,606	\$2,375	\$1,250	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$29,386
Inspection & Testing		\$150	\$14,785	\$353,890	\$297.675	\$1,116	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$667,616
Project Management		\$150	\$45,698	\$184,219	\$193,898			\$0				\$0		\$0		\$0	\$439,013
Cleaning, Storage and Installation		\$0	\$812	\$0			7 \$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,627
Cap Equipment		\$0	\$31,638	\$0	\$6,458				\$0			\$0	\$0	\$0	\$0	\$0	\$97,785
Non-Cap Equipment		\$0	\$2,388	\$0	\$36,749	\$145,294	\$0	\$0			\$0	\$0	\$0	\$0		\$0	\$184,432
Total		\$296.915	\$1,804,496	\$5,520,804								\$0		\$0		\$0	\$19,544,314
Project Budget	\$19,544,314		, , ,	, , ,	, , , , , , , , , , , , , , , , , , , ,								, , ,				, .,. ,.
Less Other Funding	\$0																
Net	\$19.544.314																
Actual Measure U Expenditures	\$19,544,314																
Running Balance	\$0																
· · · · · · · · · · · · · · · · · · ·	7.																
U7100110																	
Earthquake Rpl. Liberal Arts North (I)																	
Supplies		\$0	\$0	\$0	\$0	\$1,408	3 \$0	\$75	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,483
Legal		\$0	\$0	\$0								\$0				\$0	\$887
Other Contract Services		\$0	\$0	\$0								\$0				\$0	\$75
Building & Additions		\$265	\$0	\$1,043,660								-\$1,127,809	\$0			\$0	\$4,360,876
Architect		\$0	\$611.732	\$102.824	\$209,490			\$3,465				\$0				\$0	\$1,165,289
Engineering	1	\$3,248	\$4,295	\$0	\$250			\$0				\$0		\$0		\$0	\$8.043
Inspection & Testing		\$0	\$0	\$28,312	\$326,203							\$0		\$0		\$0	\$432,458
Project Management		\$0	\$26.072	\$33,549	\$128,937							\$0				\$0	\$314,475
Advertising and Fees		\$0	-\$4	\$7.334	\$0							\$0				\$0	\$7,330
Cap-Equipment		\$0	\$0	\$0	\$0							\$0				\$0	\$37,935
Non-Cap Equipment		\$0	\$0	\$0	\$2.033			\$0				\$0	\$0			\$0	\$176.550
Total		\$3.513	\$642,095									-\$1,127,809	\$0			\$0	\$6,505,400
Project Budget	\$12,507,725	Received	₩07£,333	₩1,210,013	ψυ,000,134	-4000,120	ψυσυ,/σ/	ψ15,53 <u>2</u>	<b>\$200</b>	- 400-1,704	1 40	₩1,121,303	40		1 90	40	ψ0,000, <del>4</del> 00
Less Other Funding*	\$6,002,325	\$6,002,325		* Other Fundin	a Source:												
Net	\$6,505,400	ψυ,υυ2,323			g 3001ce. //onica \$4,039,7	753 received											
Actual Measure U Expenditures	\$6,505,400				572 commited,		havia										
Running Balance	\$0,505,400			1 LIVIA \$1,802,	orz committeu,	ψ1,302,372 TeU	civeu										
Rullilly Dalatice	1 20																

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
U7100013, U7100047																	
Music Complex (J)				2100													2100
Advertising		\$0		\$436	\$0		\$0	\$0				\$0					
Supplies		\$0	\$0	\$0	\$0	\$194	\$19,094	\$0	\$0	\$0		\$0		\$0			
Consultants		\$0			\$0	\$0	\$36,000	\$0		\$0		\$0	\$0				
Other Contract Services		\$0			\$0			\$0				\$0					
Moving Services		\$0		\$0	\$0		\$6,330	\$0		\$0		\$0		\$0			
Building & Additions		\$0			\$1,293,726		\$273,531	\$0		\$0		\$0		\$0			
Architect		\$0		\$22,500	\$37,227		\$4,052	\$14,356	\$0	\$681		\$3,992	\$2,038	\$0			
Engineering		\$0		\$0	\$0		\$0	\$21,370	\$0			\$0					
Inspection & Testing		\$0			\$19,265		\$35,880	\$0	\$0	\$0		\$0					
Project Management		\$0		\$36,739	\$36,351		\$16,200	\$1,288				\$0					
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$62,600	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$62,600
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$29,852	\$78,582	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$108,434
Total		\$0	\$188,092	\$445,879	\$1,386,568	-\$585,566	\$532,447	\$37,014	\$0	\$681	\$225	\$3,992	\$2,038	\$0	\$0	\$0	\$2,011,371
Project Budget	\$4,629,484	Received															
Less Other Funding*	\$2,618,113	\$2,618,113	1	* Other Funding	Source:												
Net	\$2,011,371	, , , , , , ,	•	Prop T Refinan	ce \$2.618.113	received											
Actual Measure U Expenditures	\$2,011,371	1															
Running Balance	\$0	†															
U7100111																	1
Earthquake Rpl. Liberal Arts South (K)																	
Supply		\$0	\$0	\$855	\$2,497	\$379	\$23,811	\$75	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$27,618
Legal		\$0	\$0	\$0	\$0	\$0	\$2,203	\$50	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,253
Moving Services		\$0			\$0	\$0	\$4,063	\$0	\$0	\$0		\$0		\$0	\$0	\$0	
Consultants		\$0			\$17,265	\$41,435	\$0	\$0		\$0		\$0			\$0	\$0	
Other Contract Services		\$0	\$0	\$6,154	\$202	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,356
Building & Additions		\$0			\$3,091,306	\$5,706,802	-\$4.642.459	\$0		\$0		\$0					
Architect		\$0			-\$503,297		\$183,877	\$39,984	\$2,549	\$0		\$0					
Engineering		\$0			\$150		\$500	\$0		\$0		\$0					
Inspection & Testing		\$0			\$179,798		\$68,273	\$0		\$0		\$0					
Project Management		\$0		\$0	\$43,989		\$52,690	\$1,722		\$0		\$0					
Cap-Equipment		\$0			\$0		\$0	\$0	\$0	\$0		\$0		\$0			
Non-Cap Equipment		\$0		\$0	\$0		\$45.388	-\$7.074	\$0	\$0		\$0		\$0			
Total		\$0			\$2,831,909			\$34,757	\$95,342	\$0		\$0					
Project Budget	\$16.733.220		40	Ç012,001	<b>+=,501,000</b>	+5,504,000	Ţ.,=01,000	Ç34,101	<b>430,042</b>		1 40	- 40					\$0,100,100
Less Other Funding*		\$10,625,070	†	* Other Funding	Source:												
Net	\$6,108,150	ψ10,023,070		City of Santa M		170 received											
Actual Measure U Expenditures	\$6,108,150	1		State of Californ													
Running Balance	\$6,106,150	1		State of Callion	ilia φ4,456,000	received											
Running baldifice	1 \$0	1															

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
U7100221																	
Shuttle Replacement Parking (L)																	
Supplies		\$0	\$0	\$0	\$0	\$0	\$1,347	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,347
Legal		\$0	\$0	\$0	\$8,462	\$35,103	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$43,565
Site Acquisition		\$0	\$0	\$0	\$0	\$16,903,087	\$0	\$0	\$0			\$0	\$0	\$0		\$0	
Site Improvement		\$0	\$0	\$0	\$0	\$3,027	\$0	\$0				\$0	\$0	\$0		\$0	
Building & Additions		\$0	\$0	\$0	\$0	\$484,000	\$1,252,224	\$2,353	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,738,577
Architect		\$0	\$0	\$0	\$0	\$51,569	\$7,208	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$58,777
Inspection & Testing		\$0	\$0	\$0	\$0	\$139,822	\$41,250	\$0		\$0		\$0	\$0	\$0		\$0	
Project Management		\$0	\$0	\$0	\$0	\$7,631	\$32,425	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$40,056
Total		\$0	\$0	\$0	\$8,462	\$17,624,240	\$1,334,455	\$2,353	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$18,969,509
Project Budget	\$18,969,509																
Less Other Funding	\$0																
Net	\$18,969,509																
Actual Measure U Expenditures	\$18,969,509																
Running Balance	\$0																
U7100321																	
North Quad Plaza (M)																	
Legal		\$0	\$0	\$0	\$0	\$0	\$3,825	\$5,604	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$9,429
Building & Additions		\$0	\$0	\$0	\$0	-\$443	\$6,130,081	\$3,634,487	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$9,764,125
Architect		\$0	\$231,055	\$8,444	\$140,048	\$435,618	\$171,225	\$68,633	\$2,901	\$10,483		\$0	\$0	\$0		\$0	\$1,068,407
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$186,220	\$107,477		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$294,025
Project Management		\$0	\$0	\$760	\$210	\$2,200	\$135,601	\$55,782	\$606	\$0		\$0	\$0	\$0		\$0	
Printing		\$0	\$1,900	\$0	\$0	\$0	\$0	\$0	\$0			\$0	\$0			\$0	
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$55,420		\$0		\$0	\$0	\$0		\$0	
Total		\$0	\$232,955	\$9,204	\$140,258	\$437,375	\$6,626,952	\$3,927,402	\$3,834	\$10,483	\$0	\$0	\$0	\$0	\$0	\$0	\$11,388,463
Project Budget	\$11,388,463				•												
Less Other Funding	\$0																
Net	\$11,388,463																
Actual Measure U Expenditures	\$11,388,463																
Running Balance	\$0	Ī															

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
U7100500, U7126450, U7100334, U7100142																	
Student Services Building (O)																	
Supplies		\$2,014	\$0	\$0	\$0	\$0	\$0	\$718	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,732
PC Upgrades		\$0	\$765	\$0	\$0		\$0	\$0		\$0	\$0	\$0		\$0	\$0	\$0	\$765
Consultants		\$0	90	\$0	\$0	\$9,334	\$55,693	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$65,027
Legal		\$0	\$0	\$0	\$0	\$38	\$2,775	\$31,776			<b>Ψ</b> 0	\$0	\$0	\$0	\$0	\$0	\$34,588
Other Contract Services		\$210	\$0	\$0	\$0	\$0	\$17,561	\$17,495	\$18,817	-\$70	\$0	\$0	\$0	\$0	\$0	\$0	\$54,014
Moving		\$7,571	\$0	\$0	\$0	\$0	\$0	\$616	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$8,187
Building & Additions		\$359,141	\$2,441	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$776	\$560	\$1,717,465	\$9,584,254	\$11,664,637
Architect		\$31,782	\$0	\$235,230	\$0	\$43,992	\$0	\$690,099	\$208,521	\$38,643	\$48,442	\$388,611	\$973,427	\$2,502,652	\$567,231	\$296,773	\$6,025,403
Engineering		\$1,838	\$0	\$0	\$0	\$0	\$0	\$6,205	\$27,363	\$3,171	\$0	\$0	\$0	\$55,680	\$73,757	\$2,705	\$170,718
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$25,670	\$34,687	\$0	\$0	\$0	\$0	\$2,478	\$0	\$69,480	\$69,396	\$201,711
Project Management		\$4,650	\$0	\$2,470	\$0	\$1,100	\$0	\$124,148		\$0	\$0	\$6,675	\$15,650	\$11,616	\$120,550	\$3,275	\$290,134
Cap Equipment		\$59,063	\$0	\$0	\$0		\$8,745	\$8,056	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$75,864
Total		\$466,268	\$3,207	\$237,700	\$0	\$54,464	\$110,445	\$913,802	\$254,701	\$41,744	\$48,442	\$395,286	\$992,330	\$2,570,508	\$2,548,483	\$9,956,402	\$18,593,781
Project Budget	\$130,224,164	Received		Other Funding	g Source:												
Less Other Funding*	\$109,585,718	\$1,321,000		State of Californ	nia \$1,321,000	received											
Net	\$20,638,446			Measure S \$47	,476,003, Mea	sure AA \$31,438	,134, Measure	V \$15,095,89	6 allocated								
Actual Measure U Expenditures	\$18,593,781			Measure U, S &	AA Interests \$	18,050,581 allo	cated										
Running Balance	\$2,044,665																

#### **Student Services Building**

#### Project Discription:

Consolidates various student services departments and college administration in a single complex at the front of the campus

Facility Size: 110,000 sq/ft & 500 cars underground parking structure

#### Status:


In construction

#### Architect:

Steinberg Architects, Morris Architects

#### Contractor:

Minaco, Bernards



Projects	Budaet	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
U7100090																	
Science Complex Additional (P)																	
Architect		\$0	\$0	\$0	\$0	\$246,425	\$61.911	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$308.336
Total		\$0	\$0	\$0	\$0	\$246,425	\$61,911		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$308.336
Project Budget	\$90,401,286	7-1		* Other Funding		7=,,	77.,,	***							***		, , , , , , , , , , , , , , , , , , , ,
Less Other Funding	\$90,092,950				nia \$40,088,000	pendina											
Net	\$308,336				,950, Measure \		llocated										
Actual Measure U Expenditures	\$308,336																
Running Balance	\$0																
U6780000, U7100022, U7100331, U7100550,																	
U7100005, U7100030, U7100031, U7100029.																	
U7100003, U7100008, U7100332, U7100072.																	
U7100042, U7100056, U7100039																	
Infrastructure & Safety (Q)																	
Supplies		\$0	\$0	\$254	\$0	\$0	\$0	\$1,700	\$1,393	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,347
Consultants		\$0	\$0	\$0	\$0	\$0	\$0		\$0		\$0	\$0	\$0			\$0	
Maintenance Agreement		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$14.673	\$12,979	\$12,979	\$0	\$0	\$0	\$0	\$40,632
Legal		\$0	\$0	\$0	\$0	\$0	\$3,527	\$3,294	\$0	\$0		\$0	\$0			\$0	
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$7,825	\$81,445	\$203,383	\$3,320	\$0	\$0	\$0	\$0	\$0	\$0	\$295,973
Building & Additions		\$681,900	\$195,175	\$20,600	\$0	\$200,620	\$733	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,099,028
Architect		\$69,081	\$42,108	\$0	\$155,321	\$448,507	\$91,127	\$4,227	\$0	\$0	\$0	-\$1,365	\$0	\$0	\$0	\$0	\$809,005
Engineering		\$8,050	\$0	\$0	\$6,750	\$12,000	\$18,429	\$2,360	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Inspection & Testing		\$2,241	\$4,250	\$0	\$0	\$0	\$5,807	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,298
Project Management		\$0	\$2,805	\$0	\$0	\$3,520	\$1,840	\$38	\$196	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$8,399
Cap Equipment		\$0	\$0	\$343,861	\$0	\$0	\$0	\$895,171	\$349,531	\$40,002	\$0	\$0	\$0	\$0	\$0	\$0	\$1,628,565
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,216	\$0	\$29,694	\$0	\$0		\$0	\$0	
Advertising		\$0	\$785	\$0	\$0	\$0	\$0		\$0	\$0		\$0	\$0			\$0	
Total	· ·	\$761,272	\$245,122	\$364,715	\$162,071	\$664,647	\$129,287	\$1,004,968	\$558,718	\$57,995	\$42,673	\$11,614	\$0	\$0	\$0	\$0	\$4,003,084
Project Budget	\$4,003,084				-	,											
Less Other Funding	\$0																
Net	\$4,003,084																
Actual Measure U Expenditures	\$4,003,084																
Running Balance	\$0																

Pasterior improvement (R)   Supplies   Sup	Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
Restroom Improvement (R)	117100007			1		1					I	I						T
Supplies   50   \$564   \$50   \$1,076   \$0   \$0   \$0   \$0   \$0   \$0   \$0   \$																		
Other Contract Services			\$0	\$564	\$0	\$1.075	90	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,63
Sulding Additions   SO   S1 305   SO   SO   SO   SO   SO   SO   SO   S																		
Imagesing   So   SC   SC   SC   SC   SC   SC   SC																		
Total																		
Project Budget	Total																	
Liess Other Funding		\$17.501	40	Ψ0,512	ΨΟ	ψ10,000	Ψ	Ψ	Ψ0	- 40			ΨŪ	ΨŪ	ų,	40		Ų11,0C
Net Actual Measure U Expenditures   \$17,501   Rounting Balance   \$0    V7100004, U7110020			+															
Actual Measure U Expenditures			+															
U17100004 U17110020			+															
			+															
Master   Planning (S)	Running Balance	\$0																
Consultants   S9,000   \$26,516   \$158,449   \$374,329   \$125,404   \$17,998   \$363,342   \$0   \$0   \$0   \$0   \$0   \$0   \$0   \$	U7100004, U7110020																	
Architect	Master Planning (S)																	
Architect	Consultants		\$9.000	\$26.516	\$158,449	\$374.329	\$125,404	\$17.998	\$363,342	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,075,03
Rental / Lease	Architect		\$0				\$126,701								\$0			
Postage   S0   \$0   \$30,000   \$0   \$0   \$0   \$0   \$0   \$0   \$0	Rental / Lease		\$0	\$0	\$6,453	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,45
Reimbursement to SMC   \$0   \$0   \$0   \$180   \$0   \$0   \$0   \$0   \$0   \$0   \$0															\$0			
Project Management \$ \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$																		
Total   Sp. 000   \$44,133   \$321,335   \$478,593   \$252,105   \$364,825   \$640,439   \$0   \$0   \$0   \$0   \$0   \$0   \$0   \$	Project Management		\$0	\$0	\$0	\$0	\$0						\$0	\$0	\$0	\$0	\$0	
Project Budget \$2,110,430   Less Other Funding \$0   Net \$2,110,430   Actual Measure U Expenditures \$2,110,430   Running Balance \$0    U7100024			\$9.000	\$44.133			\$252,105											
Consultants		\$2 110 430	<b>\$0,000</b>	<b>V.1,100</b>	<b>402</b> .,000	¥ 1.7 0,000	<b>V</b> 202, . 00	<b>\$00.,020</b>	<b>\$0.10,100</b>	***	, ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,		***	<b>4</b> 0	***	+	•	<b>V</b> 2,,
Net			†															
Actual Measure U Expenditures \$2,110,430 Running Balance \$2,110,430 Running Balance \$30 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0			†															
U7100024			†															
14th and Pico Project (T)			†															
14th and Pico Project (T)	Ituling Balance	ψ0																
Consultants																		
Architect \$258,601 \$47,343 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	14th and Pico Project (T)																	
Inspection & Testing   \$12,070   \$0   \$0   \$0   \$0   \$0   \$0   \$0	Consultants														\$0	\$0		
Project Management \$0 \$340 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	Architect		\$258,601	\$47,343	\$0	\$0	\$0	\$0	\$0			\$0			\$0	\$0	\$0	\$305,94
Total   \$270,671   \$48,571   \$0   \$0   \$0   \$0   \$0   \$0   \$0   \$	Inspection & Testing		\$12,070		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,07
Project Budget         \$319,242           Less Other Funding         \$0           Net         \$319,242           Actual Measure U Expenditures         \$319,242	Project Management		\$0	\$340	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$34
Less Other Funding         \$0           Net         \$319,242           Actual Measure U Expenditures         \$319,242	Total		\$270,671	\$48,571	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$319,24
Less Other Funding         \$0           Net         \$319,242           Actual Measure U Expenditures         \$319,242	Project Budget	\$319,242																
Net \$319,242 Actual Measure U Expenditures \$319,242			1															
Actual Measure U Expenditures \$319,242			1															
			†															
Running Relance   SO	Running Balance	\$319,242	†															
running bulunce 90	raming balance	J \$0	<u> </u>															
Grand Total   \$11,068,400   \$10,432,055   \$28,685,697   \$54,940,416   \$25,278,771   \$5,283,853   \$6,585,573   \$912,880   \$91,341   \$716,916   \$1,041,732   \$2,570,508   \$2,548,483   \$9,956,402	Grand Total		\$11.068.400	\$10.432.055	\$28 685 697	\$54 940 416	\$25 278 774	\$5 283 853	\$6 585 572	\$912 880	-\$723 860	\$91 2/1	-\$716 016	\$1 041 722	\$2 570 509	\$2 548 492	\$9.956.403	\$157,955,33

Note: Project N had no expenses

## SANTA MONICA COMMUNITY COLLEGE DISTRICT

## Measure S Project Schedule As of March 31, 2017

	Project Name	Completion	2015	5		2016	2	017		20	)18	201	9
1	Athletic Fields Phase I, Corsair Field	Completed											
1A	Athletic Fields Phase I, John Adams	Completed											
2	Performing Arts Center	Completed											
3	Career Opportunity Center	Completed											
4	Replacement Health/PE/Fitness Building	June 2017											
5	Early Childhood Development/Childcare	September 2019											
6	Malibu Site Acquisition and Facility	March 2019											
7	Energy Efficiency Projects	Completed											
8	Satellite Campus Parking Facilities and Roadway Improvements	Deferred											
9	Parking Garage, Grounds and Equipment - Student Services	January 2019											
10	Pico Promenade Improvements	Completed											
11	Master Planning	Completed											
12	Other Bond Related Expenses	On-Going											
13	Adv. Architecture Related Exp for AA	Completed											
14	Real Property Acquisition	Completed											
15	Signage Safety/Information	Completed											
16	Cost of Issuance	On-Going											
			In Pla	annii	ng		In	Con	nstru	ction	1		

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
S7100019															
Athletic Field Phase I, Corsair Field (1)															
Legal		\$0	\$0	\$0	\$301	\$175	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$476
Building & Additions		\$0	\$0	\$0	\$300,380	\$2,579,095	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,879,475
Architect		\$27,332	\$43,815	\$197,557	\$252,736	\$279,173	\$26,563	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$827,176
Inspection & Testing		\$0	\$0	\$0	\$23,411	\$57,585	\$640	\$296	\$0	\$0	\$0	\$0	\$0	\$0	\$81,932
Project Management		\$0	\$0	\$0	\$9,871	\$42,374	\$565	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$52,810
Cap Equipment		\$0	\$0	\$0	\$0	\$483,017	\$35,271	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$518,288
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$2,066	\$10,312	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,378
Total		\$27,332	\$43,815	\$197,557	\$586,699	\$3,443,485	\$73,350	\$296	\$0	\$0	\$0	\$0	\$0	\$0	\$4,372,535
Project Budget	\$4,440,065	Received							-				-	-	
Less Other Funding*	\$67,530	\$67,530		* Other Funding											
Net	\$4,372,535			Metropolitan W	ater District \$6	7,530 received									
Actual Measure S Expenditures	\$4,372,535														
Running Balance	\$0														

#### Athletic Field Phase I, Corsair Field

Project Description:
Renovation of the Corsair Field, stadium lighting and sound system


Status:

Completed, 2009

Architect: CO Architects

Contractor:

Byrom Davey, Inc.



Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
													•		
S7100038															
Athletic Field Phase I, John Adams (1A)															
Legal		\$0	\$0	\$0	\$75	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$75
Building & Additions		\$0	\$0	\$0	\$16,556	\$1,395,261	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,411,817
Architect		\$0	\$5,807	\$93,941	\$12,150	\$31,818	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$143,715
Inspection & Testing		\$0	\$2,874	\$3,207	\$0	\$49,984	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$56,066
Project Management		\$0	\$0	\$0	\$10,921	\$45,170	\$38	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$56,128
Cap Equipment		\$0	\$0	\$0	\$0	\$1,290,672	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,290,672
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$11,334	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$11,334
Total		\$0	\$8,681	\$97,148	\$39,701	\$2,824,239	\$38	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,969,807
Project Budget	\$2,969,807							_	-				-	-	
Less Other Funding	\$0														
Net	\$2,969,807														
Actual Measure S Expenditures	\$2,969,807														
Running Balance	\$0														

#### Athletic Field Phase I, John Adams


Project Description: Renovation of John Adams Field and lighting

Status:

Completed, 2008


Architect: Caldwell Architects

Contractor: Byrom Davey, Inc.



Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
S7100012															
Performing Arts Center (2)															
Consultants		\$0	\$0	\$0	\$121,790	\$76,639	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$198,429
Other Contract Services		\$0	\$0	\$4,269	\$0	\$22,729	\$22	\$68	\$0	\$0	\$0	\$0	\$0	\$0	\$27,088
Supplies		\$0	\$0	\$0	\$14,565	\$5,810	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$20,375
Legal		\$0	\$0	\$34,329	\$275,667	\$492,731	\$15,629	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$818,356
Advertising		\$0	\$0	\$0	\$320	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$320
Building & Additions		\$7,784,151	\$10,292,986	\$8,930,813	\$2,991,903	\$1,629,990	\$50,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$31,679,843
Architect		\$0	\$811,312	\$182,457	\$412,309	\$121,588	\$108	\$1,962	\$0	\$0	\$87,054	\$0	\$0	\$0	\$1,616,790
Engineering		\$0	\$3,600	\$5,250	\$1,500	\$9,650	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$20,000
Inspection & Testing		\$104,308	\$722,685	\$411,193	\$210,381	\$22,256	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,470,823
Project Management		\$31,984	\$155,732	\$248,876	\$263,690	\$47,915	\$3,244	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$751,441
Cap Equipment		\$0	\$0	\$130,218	\$292,565	\$342,693	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$765,476
Non-Cap Equipment		\$0	\$0	\$15,124	\$93,106	\$220,455	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$328,685
Total		\$7,920,443	\$11,986,315	\$9,962,528	\$4,677,797	\$2,992,455	\$69,003	\$2,030	\$0	\$0	\$87,054	\$0	\$0	\$0	\$37,697,625
Project Budget	\$40,690,201	Received			•					-					
Less Other Funding*	\$2,992,576	\$2,992,576		* Other Funding	g Source:										
Net	\$37,697,625		•	Madison Project	ct Foundation \$	2,992,576 rece	eived								
Actual Measure S Expenditures	\$37,697,625			•											
Running Balance	\$0														

# Performing Arts Center Project Description: Construction of a state-of-the-art 499 seat performing arts theater Status: Completed, 2008 Architect: Renzo Zecchetto Contractor: FTR International



Architect         \$0	\$0 \$( \$0 \$( \$0 \$) \$0 \$( \$0 \$) \$0 \$( \$4,775,714 \$)	0 \$1,488 0 \$27,985
Replacement Health/PE/Fitness Building (4)	\$0 \$6 \$0 \$6 \$0 \$6 \$0 \$6 \$4,775,714 \$6	0 \$1,488 0 \$27,985
Supplies         \$4,809         \$288         \$0         \$0         \$163         \$0         \$0         \$0         \$0           Legal         \$0         \$0         \$0         \$0         \$1,413         \$75         \$0	\$0 \$6 \$0 \$6 \$0 \$6 \$0 \$6 \$4,775,714 \$6	0 \$1,488 0 \$27,985
Legal         \$0         \$0         \$0         \$0         \$1,413         \$75         \$0         \$0         \$0         \$0           Other Contract Services         \$1,634         \$25,934         \$0         \$0         \$253         \$165         \$0	\$0 \$6 \$0 \$6 \$0 \$6 \$0 \$6 \$4,775,714 \$6	0 \$1,488 0 \$27,985
Other Contract Services         \$1,634         \$25,934         \$0         \$0         \$253         \$165         \$0         \$0         \$0         \$0           Repair Facility         \$0         \$4,861         \$0	\$0 \$0 \$0 \$0 \$4,775,714 \$0	0 \$27,985
Repair Facility	\$0 \$0 \$4,775,714 \$0	
Building & Additions         \$0         \$0         \$0         \$0         \$112,410         \$526,552         \$0         \$0         \$0         \$6,037,080         \$           Architect         \$0         \$0         \$0         \$0         \$41,044         \$0         \$0         \$0         \$0           Inspection & Testing         \$0         \$0         \$0         \$0         \$14,363         \$0         \$0         \$0         \$0           Project Management         \$0         \$0         \$0         \$9,070         \$23,425         \$0         \$0         \$0         \$0           Cap Equipment         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0	\$4,775,714 \$0	0 \$4.861
Architect         \$0		
Inspection & Testing         \$0 <td></td> <td></td>		
Project Management         \$0         \$0         \$0         \$9,070         \$23,425         \$0         \$0         \$0         \$0           Cap Equipment         \$0         \$0         \$0         \$0         \$17,613         \$0         \$0         \$0	\$0 \$0	
Cap Equipment         \$0         \$0         \$0         \$0         \$17,613         \$0         \$0         \$0	\$0 \$0	
	\$0 \$0	
	\$0 \$0	
	\$4,775,714 \$0	0 \$11,603,383
Project Budget \$58,272,030		
Less Other Funding* \$46,668,647 * Other Funding Source:		
Net \$11,603,383 Measure AA \$46,477,800 allocated		
Actual Measure S Expenditures \$11,603,383 SCE \$190,847.28 received		
Running Balance \$0		
S7100045		
S7 I 100045 Early Childhood Development/Childcare (5)		+
Early Childhood Development/Childcare (3)  So S	\$1,388 \$0	0 \$42,395
Consolidation	\$1,690 \$6,90	
Legal 50 50 50 50 50 50 50 50 50 50 50 50 50	\$1,090 \$6,903	
	\$476,827 \$54,450	
Addition   A   Su	\$2,323	
Special Arrangement   Special Specia	\$3.118	
Total	\$485.344 \$61.597	
10tal 30 30 30 30 30 30 30 30 31 31,240 32,340 312,333 3130,330 3130,370 Project Budget \$15,520,176 Received	\$400,344 \$01,35	1 \$1,095,900
15,22,170   160,680   17,080   17,080   180		
ST.000.000   City of Santa Monica \$6.661.598 committed		
Actual Measure S Expenditures \$1,005,006 Measure S interest \$1,558,578 allocated		
Running Balance \$5,994,994		
rummy balance \$5,504,004		
\$7100077, \$7100015		
Malibu Site Acquisition and Facilities (6)		
Consultants \$0 \$0 \$0 \$0 \$30,000 \$0 \$72,157 \$68,109 \$30,342 \$66,277	\$60,262 \$3,406	6 \$330,553
Legal \$0 \$27,722 \$16,787 \$6,159 \$504 \$0 \$0 \$0 \$0 \$1,360 \$78,851	\$40,114 \$5,14	1 \$176,637
Other Contract Services \$0 \$0 \$0 \$0 \$0 \$2,092 \$0 \$0 \$1,820	\$0 \$0	0 \$3,912
Building & Additions \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0	0 \$536
Architect \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$966 \$257,584 \$732,891 \$173,610	\$34,753 \$151,772	2 \$1,351,578
Engineering \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$785 \$562 \$0	\$0 \$0	0 \$1,346
Inspection & Testing \$4,388 \$3,750 \$141,462 \$0 \$0 \$0 \$0 \$98,022 \$15,575 \$22,939 \$10,960	\$0 \$0	
Project Management \$0 \$0 \$220 \$0 \$0 \$0 \$2,886 \$55,064 \$53,185 \$47,778 \$118,144	\$97,856 \$24,263	3 \$399,394
Storm/Waste Water Treatment Center \$0 \$2,500,000 \$0 \$0 \$0,500,000 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0	0 \$5,000,000
Total \$4,388 \$2,531,472 \$158,468 \$6,159 \$2,530,504 \$0 \$2,886 \$228,301 \$395,237 \$836,407 \$449,662	\$232,985 \$184,581	1 \$7,561,052
Project Budget \$25,000,000		
Less Other Funding* \$0		
Net \$25,000,000		
Actual Measure S Expenditures \$7,561,052		
Running Balance \$17,438,948		

					5.700 i iiiai	00/03 i iliai	03/10 1 11141	10/11 I IIIai	11/12 I IIIai	12/13 Final	13/14 Final	14/15 Fillal	15/16 Final	16/17	Combined Totals
S7100043, S7100066															
Energy Efficiency Projects (7)		- 00	00	- 00		0000	0.0	00		00				00	0000
Legal		\$0	\$0	\$0	\$0	\$988	\$0	\$0			\$0	\$0	\$0	\$0	\$988
Building & Additions		\$0	\$0	\$0	\$0	\$106,921	\$355,294	-\$180,342			\$0	\$0	\$0	\$0	\$281,873
Engineering		\$0	\$0	\$0	\$10,500	\$0		\$0	\$0		\$0	\$0	\$0	\$0	\$10,500
Inspection & Testing		\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0	\$0	\$10,500	\$107,910	\$355,294	-\$180,342	\$0	\$0	\$0	\$0	\$0	\$0	\$293,361
	\$510,683	Received													
	\$217,322	\$217,322		Other Funding											
	\$293,361		;	SCE & The Gas	Co. \$217,322	received									
	\$293,361														
Running Balance	\$0														
•															
S7100091, S7100092, S7100147															
Satellite Campus Parking Facilities and Roadway Improve	ovements (8	)													
Legal		\$0	\$0	\$0	\$300	\$175		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$475
Other Contract Services		\$0	\$0	\$0	\$300	\$0		\$0	\$0		\$0	\$0	\$0	\$0	\$300
Advertising		\$0	\$0	\$0	\$0	\$0		\$0			\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$278,178	\$1,860,152	\$449,543	\$37,777	\$0	\$0	\$0	\$64	\$0	\$0	\$2,625,714
Architect		\$0	\$0	\$324,919	\$324,864	\$136,911	\$34,490	\$1,397	\$2,289	\$0	\$0	\$0	\$0	\$0	\$824,871
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$30,896	\$5,470	\$12,165	\$0	\$48,531
Inspection & Testing		\$0	\$0	\$0	\$31,100	\$185,947	\$28,218	\$360	\$0	\$0	\$0	\$0	\$0	\$0	\$245,626
Project Management		\$0	\$0	\$0	\$18,288	\$64,880	\$31,137	\$8,659	\$0	\$2,569	\$10,730	\$6,046	\$535	\$0	\$142,844
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$3,387	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,387
Total		\$0	\$0	\$324,919	\$653,031	\$2,248,065	\$546,775	\$48,194	\$2,289	\$2,569	\$41,626	\$11,580	\$12,700	\$0	\$3,891,747
Project Budget \$	\$7,022,417											,			, ,
Less Other Funding \$	33,130,670			Other Funding	Source:										
	3,891,747			Measure AA \$2		sure V \$1,000,	000 allocated								
	3,891,747														
Running Balance	\$0														

Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
	\$0	\$0	\$0	\$0	\$1,745	\$0	\$0	\$648	\$0	\$0	\$813	\$0	\$0	\$3,206
	\$0	\$0	\$0	\$0	\$20,700	\$0	\$0	\$0	\$0	\$0	\$0	\$1,740	\$0	\$22,440
	\$0	\$0	\$0	\$0	\$2,154	\$17,486	\$4,800	\$2,257	\$17,221	\$0	\$3,570	\$0	\$0	\$47,488
	\$0	\$0	\$0	\$0	\$1,508	\$10,952	\$1,986	\$46	\$0	\$12,083	\$5,034	\$0	\$0	\$31,608
	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,086	\$0	\$1,308	\$0	\$0	\$2,394
	\$0	\$0	\$0	\$0	\$2,555,940	\$5,925,152	\$78,717	\$77,320	\$5,509	\$715	\$0	\$3,721	\$3,781,155	\$12,428,228
	\$0	\$0	\$0	\$2,266,766	\$2,674,054	\$0	\$37,111	\$75,163	\$0	\$0	\$0	\$0	\$0	\$5,053,094
	\$0	\$0	\$0	\$0	\$4,813	\$38,330	\$42,968	\$50,952	\$9,735	\$0	\$0	\$0	\$0	\$146,797
	\$0	\$0	\$0	\$0	\$131,009	\$161,847	\$54,069	\$32,306	\$30,909	\$4,123	\$22,296	\$38,186	\$155,684	\$630,429
	\$0	\$0	\$0	\$0	\$158,766	\$373,559	\$184,088	\$92,118	\$224,994	\$59,525	\$29,714	\$50,380	\$176,567	\$1,349,710
	Budget	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0	\$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$1,745 \$0 \$0 \$0 \$0 \$0 \$20,700 \$0 \$0 \$0 \$0 \$2,750 \$0 \$0 \$0 \$0 \$2,1558 \$0 \$0 \$0 \$0 \$0 \$0 \$1,508 \$0	\$0 \$0 \$0 \$0 \$0 \$1,745 \$0 \$0 \$0 \$0 \$0 \$20,700 \$0 \$0 \$0 \$0 \$0 \$2,20700 \$0 \$0 \$0 \$0 \$0 \$2,255 \$1,746 \$0 \$0 \$0 \$0 \$0 \$2,255 \$1,508 \$10,952 \$0 \$2,255,940 \$5,925,152 \$0 \$0 \$0 \$0 \$0 \$2,266,766 \$2,674,054 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$4,813 \$38,330 \$0 \$0 \$0 \$0 \$0 \$0 \$1,009 \$131,009 \$161,847	\$0 \$0 \$0 \$0 \$0 \$1,745 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$1,745 \$0 \$0 \$648 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$1,745 \$0 \$0 \$0 \$648 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$1,745 \$0 \$0 \$0 \$648 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$20,700 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0. \$1,745 \$0 \$0 \$0 \$648 \$0 \$0 \$0 \$813 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$1,745 \$0 \$0 \$0 \$648 \$0 \$0 \$0 \$813 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0

\$0 \$0 \$0 \$2,266,766 \$5,550,689 \$6,541,719 Other Funding Source:

\$0

\$0 \$0

\$0

\$130,224,164

\$82,748,161

\$47,476,003

\$19,741,170

State of California \$1,321,000 received Mease U \$20,638,446, Measure AA \$31,438,134, Measure V \$15,095,896 allocated

\$0

Measure U, S & AA interests \$18,050,581 allocated

#### Parking Garage and Grounds - Student Services

#### Project Description:

Actual Measure S Expenditures

Consolidates various student services departments and college administration in a single complex at the front of the campus

Cap Equipment Non-Cap Equipment

Project Budget Less Other Funding\*

Running Balance

Total


Facility Size: 110,000 sq/ft & 500 cars underground parking structure

Phase 1 completed Phase 2 In construction

Steinberg Architects, Morris Architects

#### Contractor:

Minaco, Bernards

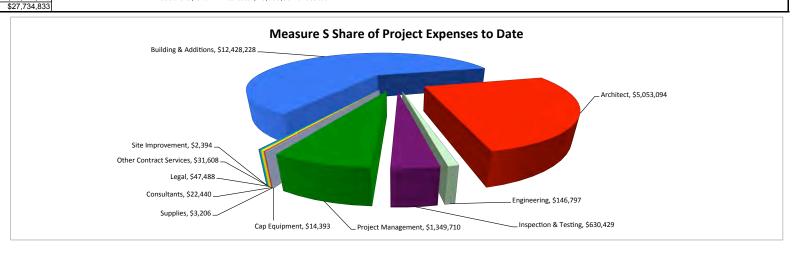

\$0 \$0

\$403,737

\$0 \$11.381

\$342,192

\$0 \$0

\$289,454

\$0

\$62,735

\$76,445

\$0

\$94,027 \$4,113,406

\$14,393 \$11,381

\$19,741,170

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/1/ Final	14/15 Final	15/16 Final	16/17	Combined Totals
Trojects	Duaget	04/03 i iliai	03/00 1 11141	00/07 Tillal	07700 1 11101	00/03 1 11141	03/10 1 11141	10/11 Tillai	11/12 1 11101	12/13 1 11101	13/14 1 11101	14/13 1 11141	13/10 1 11141	10/17	Combined Totals
S7100044															
Pico Promenade Improvements (10)															
Building & Additions		\$0	\$0	\$0	\$690	\$883,401	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$884,091
Architect		\$0	\$0		\$69,190	\$28,540		\$0			\$0			\$0	\$98,595
Inspection & Testing		\$0				\$7,591	\$0	\$0			\$0			\$0	\$7,591
Project Management		\$0				\$25,548		\$0			\$0			\$0	\$27,733
Total		\$0	\$0			\$945,080		\$0			\$0			\$0	\$1,018,009
Project Budget	\$1.018.009	,													
Less Other Funding	\$0														
Net	\$1,018,009														
Actual Measure S Expenditures	\$1,018,009														
Running Balance	\$0														
S7100004															
Master Planning (11)															
Consultants		\$0	\$0	\$0	\$0	\$0		\$13,320	\$0		\$0			\$0	\$454,869
Printing		\$0	\$0		\$0	\$0		\$0	\$0		\$0			\$0	\$4,157
Advertising		\$0				\$0		\$0			\$0			\$0	\$3,000
Other Contract Services		\$0				\$0		\$200	\$0		\$0			\$0	\$642
Architect		\$0	\$0	\$0		\$0		\$24,736	\$0		\$0			\$0	\$217,094
Project Management		\$0	\$0	\$0	\$0	\$0		\$9,341	\$0		\$7,845			\$0	\$33,824
Filling Fees		\$0	\$0			\$0		\$2,842	\$0		\$0			\$0	\$2,842
Total		\$0	\$0	\$0	\$0	\$0	\$658,143	\$50,439	\$0	\$0	\$7,845	\$0	\$0	\$0	\$716,428
Project Budget	\$716,428														
Less Other Funding	\$0														
Net	\$716,428														
Actual Measure S Expenditures	\$716,428														
Running Balance	\$0														
S7100048															
Other Bond Related Expenses (12)															
Consultants		\$0	\$0	\$0	\$0	\$0		\$0	\$0		\$2,524			\$0	\$13,089
Lease/Rental		\$0	\$0	\$0	\$0	\$0		\$0			\$15,285	\$14,809		\$9,337	\$79,090
Supplies		\$0	\$0	\$0	\$0	\$0		\$0	\$0		\$0			\$0	\$3,638
Legal	-	\$0	\$0	\$0	\$0	\$0		\$15,649	\$13,401		\$503	\$38,130		\$0	\$86,236
Software License		\$0 \$0				\$0 ©0		\$1,997	\$0		\$0			\$0 \$864	\$9,762 \$3.142
Advertising		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0		\$0	\$0		\$0				
Other Contract Services		\$0 \$0	\$0 \$0		\$0 ©0	\$1,800	\$17,206	\$23,558	\$19,208		\$13,627	\$13,952		\$11,760	\$129,889
Moving Services	1	\$0 \$0	\$0 \$0		\$0 ©0	\$0		\$0	\$0		\$0 \$0			\$0 \$0	\$400
Project Management	<del>                                     </del>	\$0 \$0	\$0 \$0		\$0	\$0 \$0		\$13,179 \$10,086	\$11,963		\$0 \$0				\$42,888 \$10,086
Cap Equipment	1	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		\$10,086	\$0 \$0		\$0 \$0			\$0 \$0	\$10,086 \$2,860
Non-Cap Equipment		\$0 <b>\$0</b>				\$0 \$1.800		\$2,860 <b>\$67,328</b>	\$55,713		\$0 \$31.939			\$21.961	\$2,860 <b>\$381,080</b>
Total Project Budget	\$609.282	\$0	\$0	\$0	\$0	\$1,800	\$5U,185	<b>⊅07,328</b>	<b>\$55,/13</b>	<b>↓ \$37,901</b>	\$31,93 <u>9</u>	\$11,33U	<b>\$30,921</b>	<b>\$∠1,961</b>	<b>\$351,080</b>
Project Budget Less Other Funding	\$609,282														
Net	\$609,282														
Actual Measure S Expenditures	\$381,080														
Running Balance	\$381,080														
running balance	<b>ΦΖΖΟ,ΖUZ</b>														

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
r-															
S7100049															
Adv Architecture Related Exp for AA (13)															
Legal		\$0				\$0		\$0	\$0	\$0				\$0	
Other Contract Services		\$0	\$0			\$0		\$0		\$0				\$0	\$
Architect		\$0	\$0	\$0		\$0		\$0			\$0		\$0	\$0	5
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	Ş
Inspection & Testing		\$0	\$0	\$0	\$0	\$45,734	-\$45,734	\$0	\$0	\$0	\$0	\$0	\$0	\$0	(
Project Management		\$0				\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	
Total		\$0				\$45,734	-\$45.734	\$0						\$0	
Project Budget	\$0		7-1	***	7-1	¥,. v .	¥,	**	7-1	**		**	7-1	7-1	
Less Other Funding	\$0														
Net	\$0														
Actual Measure S Expenditures	\$0														
Running Balance	\$0														
Rulling Balance	φυ														
S7100057											г		г г		
	+														
Real Property Acquisition (14)	+						040.701			**					0:0=
Other Contract Services		\$0		\$0		\$0		\$0						\$0	\$18,72
Architect		\$0	\$0			\$0		\$0						\$0	
Engineering		\$0	\$0			\$0		\$0	\$0	\$0				\$0	
Inspection & Testing		\$0				\$0		\$0						\$0	\$6,33
Project Management		\$0	\$0			\$0		\$0		\$0				\$0	\$20,54
Total		\$0	\$0	\$0	\$0	\$0	\$45,597	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$45,59
Project Budget	\$45,597								-					-	
Less Other Funding	\$0	1													
Net	\$45.597	1													
Actual Measure S Expenditures	\$45,597	1													
Running Balance	\$0														
rtanning Balanco	1 40														
S7100072															
Campus Signage (15)															
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$303	\$0	\$0	\$0	\$0	\$0	\$0	\$30
		\$0	\$0 \$0			\$0		\$23,725		\$0 \$0				\$0 \$0	\$55.95
Consultants			\$0 \$0						\$0	\$836					
Other Contract Services		\$0				\$0		\$187	\$0					\$0	\$1,02
Architect		\$0	\$0			\$0		\$0	\$0	\$0				\$0	
Building & Additions		\$0				\$0		\$638	\$0					\$0	\$420,33
Inspection & Testing		\$0	\$0			\$0		\$0	\$0					\$0	
Project Management		\$0	\$0			\$0		\$22,953	\$0	\$0				\$165	\$68,38
Cap Equipment		\$0	\$0			\$0		\$156,258	\$0	\$0				\$0	\$156,2
Non-Cap Equipment		\$0	\$0			\$0		\$0	\$0	\$0				\$3,147	\$3,14
Total		\$0	\$0	\$0	\$0	\$0	\$32,225	\$204,064	\$0	\$836	\$9,700	\$9,712	\$445,559	\$3,312	\$705,40
Project Budget	\$706,223														
Less Other Funding	\$0	1													
Net	\$706,223														
Actual Measure S Expenditures	\$705,408														
Running Balance	\$815														
Italiang Balance	1 4013	l													
Owner d Total		AT 050 555	044 004 000	A40 740 CC :	40.004.615	****	40.000.01=1	0047 100	0054 444	6070.000	64 007 007	00.044.777	#0.000.0=: <sup>1</sup>	04.004.5=5	****
Grand Total	1	\$7,958,606	\$14,601,366	\$10,740,621	\$8,321,918	\$20,819,624	\$8,933,245	\$617,492	\$651,441	\$878,632	\$1,287,285	\$6,814,769	\$6,083,251	\$4,384,858	\$92,093,1

## SANTA MONICA COMMUNITY COLLEGE DISTRICT

## Measure AA Project Schedule As of March 31, 2017

	Project Name	Completion	201	5		201	6	2	017			2018	3	201	9	1	2020	
101	Environmental Performance - Central Plant Connections	August 2017																
102	Infrastructure & Technology - Information Technology Relocation	Completed																
103	Media and Technology Complex - Academy Site	July 2017																
104	Replacement Health/PE/Fitness/Dance Building with Central Plant	July 2017																
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	Deferred																
106	Replacement Math and Science Extension Building	Deferred																
107	Madison East Wing Seismic Upgrade	Completed																
108	Renovation of Corsair Stadium	Completed																
109	Career Opportunity and Advancement Center (Bundy)	Completed																
110	Malibu Center	March 2019	,													П		
111	Business & Facilities Infrastructure	Completed																
112	Master Planning, Program Management, Overhead	On-Going																
113	Energy Efficiency Projects	Completed														П		
114	Community Classroom & Facility Projects	Completed														П		
115	Real Property Acquisition	Completed																
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Deferred														П		
117	Infrastructure & Technology - Technology	Completed																
118	Infrastructure & Technology - Utility	Completed																
119	Emergency Lighting, Fire Alarm, and Security System	On-Going														П		П
120	Student Services	January 2019														П		П
121	Cost of Issuance	On-Going														$\prod$		П
				In	Pla	nnin	g	Ir	n Co	nstr	ucti	on						

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
·										
AA 7100062										
Environmental Performance - Central Plant Connections (101)										
Legal		\$0	\$0	\$0	\$125	\$0	\$0	\$0	\$0	\$125
Other Contract Services		\$0	\$0	\$49,837	\$16,239	\$0	\$0	\$0	\$0	\$66,076
Consultants		\$0	\$0	\$0	\$0	\$28	\$0	\$0	\$0	\$28
Building & Additions		\$0	\$0	\$0	\$361	\$729	\$640	\$1,328,592	\$5,953,104	\$7,283,427
Architect		\$0	\$385	\$148,311	\$176,897	\$36,256	\$0	\$0	\$0	\$361,849
Engineering		\$48,500	\$0	\$4,000	\$0	\$152,010	\$39,638	\$66,918	\$65,516	\$376,582
Inspection & Testing		\$0	\$0	\$7,688	\$0	\$0	\$0	\$7,310	\$107,132	\$122,130
Project Management		\$0	\$17,263	\$55,116	\$48,685	\$61,908	\$19,313	\$104,575	\$376,166	\$683,025
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$48,500	\$17,648	\$264,951	\$242,307	\$250,931	\$59,591	\$1,507,396	\$6,501,919	\$8,893,242
Project Budget	\$11,206,164	-	-			-		-		
Less Other Funding	\$0									
Net	\$11,206,164									
Actual Measure AA Expenditures	\$8,893,242									
Running Balance	\$2,312,922									

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
AA 7100063										
Infrastructure & Technology - IT Relocation (102)										
Supplies		\$0	\$0	\$965	\$8,442	\$3,137	\$2,600	\$0	\$0	\$15,144
Consultants		\$0	\$0	\$0	\$0	\$408	\$0	\$7,800	\$0	\$8,208
Maintenance Contract		\$0	\$0	\$0	\$0	\$107,390	\$0	\$77,074	\$79	\$184,543
Legal		\$0	\$0	\$0	\$1,363	\$50	\$0	\$0	\$0	\$1,413
Printing		\$0	\$0	\$0	\$0	\$1,624	\$0	\$0	\$0	\$1,624
Postage		\$0	\$0	\$0	\$0	\$1,567	\$0	\$0	\$0	\$1,567
Other Contract Services		\$0	\$0	\$2,163	\$15,259	\$23,356	\$0	\$19,050	\$2,250	\$62,078
Moving		\$0	\$0	\$0	\$577	\$266	\$27,655	\$22,618	\$0	\$51,116
Site Improvement		\$0	\$0	\$0	\$24	\$0	\$0	\$0	\$0	\$24
Building & Additions		\$0	\$0	\$0	\$1,767,083	\$9,667,362	\$4,288,987	\$1,203,916	\$152,498	\$17,079,846
Architect		\$105,049	\$482,261	\$505,580	\$183,181	\$287,201	\$236,860	\$120,091	\$0	\$1,920,223
Engineering		\$0	\$0	\$10,037	\$11,065	\$17,147	\$19,512	\$25,994	\$1,956	\$85,712
Inspection & Testing		\$10,291	\$8,793	\$21,449	\$137,523	\$499,982	\$200,262	\$568	\$0	\$878,868
Project Management		\$33,460	\$76,290	\$84,991	\$331,754	\$431,730	\$297,951	\$22,978	\$1,500	\$1,280,653
Cap Equipment		\$0	\$0	\$0	\$29,422	\$645,830	-\$29,090	\$589,604	\$9,811	\$1,245,576
Non-Cap Equipment		\$0	\$0	\$0	\$18,344	\$10,852	\$277,219	\$1,891	\$20,689	\$328,994
Total		\$148,800	\$567,344	\$625,185	\$2,504,035	\$11,697,901	\$5,321,956	\$2,091,584	\$188,782	\$23,145,587
Project Budget	\$24,399,627							•		
Less Other Funding	\$0									
Net	\$24,399,627									
Actual Measure AA Expenditures	\$23,145,587									
Running Balance	\$1,254,040									

# Infrastructure & Technology - IT Relocation

### **Project Description:**

Relocation of IT/Telecom Departments, and renovation of Media Center

### Facility Size:

9,230 sq/ft

### Status:


Completed

### Architect:

Morris Architects

### Contractor:

Minco, Bernards Brothers

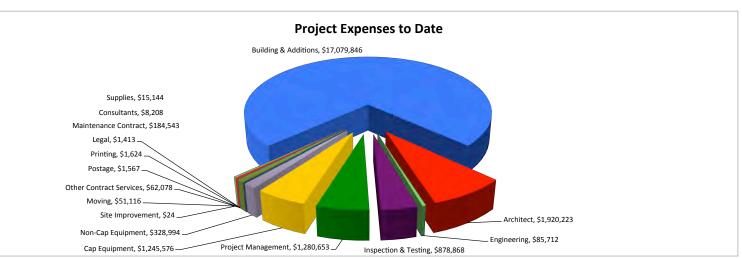

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
AA 7100061										
Media and Technology Complex - Academy Site (103)										
Consultants		\$0	\$0	\$20,675	\$12,576	\$9,488	\$7,789	\$2,102	\$0	\$52,629
Supplies		\$0	\$0	\$0	\$19,481	\$1,048	\$289	\$0	\$0	\$20,818
Legal		\$16,903	\$0	\$7,958	\$43,363	\$5,066	\$26,186	\$49,155	\$12,834	\$161,463
Service Fee		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$17,000	\$17,000
Other Contract Services		\$3,993	\$5,763	\$13,456	\$39,188	\$0	\$0	\$5,853	\$22,622	\$90,875
Moving Expenses		\$0	\$0	\$0	\$38,756	\$0	\$0	\$0	\$0	\$38,756
Software Support		\$0	\$0	\$0	\$1,982	\$0	\$0	\$0	\$0	\$1,982
Site Improvement		\$0	\$0	\$0	\$100,505	\$664	\$606	\$476	\$622	\$102,873
Building & Additions		\$0	\$538	\$1,498,660	\$3,543,657	\$11,820,615	\$17,734,534	\$23,465,347	\$7,436,347	\$65,499,698
Architect		\$2,097,553	\$2,508,588	\$295,753	\$265,481	\$778,015	\$517,794	\$1,048,935	\$505,880	\$8,017,998
Engineering		\$16,459	\$29,293	\$9,102	\$29,223	\$8,203	\$72,993	\$118,368	\$65,874	\$349,514
Inspection & Testing		\$64,905	\$27,527	\$123,842	\$235,287	\$563,746	\$1,381,801	\$641,972	\$338,551	\$3,377,630
Project Management		\$121,786	\$233,826	\$269,249	\$506,917	\$800,315	\$930,115	\$1,207,850	\$792,566	\$4,862,623
Cap Equipment		\$0	\$0	\$0	\$186,301	\$0	\$0	\$0	\$0	\$186,301
Non-Cap Equipment		\$0	\$0	\$0	\$10,782	\$0	\$0	\$0	\$0	\$10,782
Total		\$2,321,599	\$2,805,534	\$2,238,694	\$5,033,499	\$13,987,159	\$20,672,105	\$26,540,059	\$9,192,295	\$82,790,943
Project Budget	\$110,055,056	Received								
Less Other Funding*	\$6,835,391	\$990,441	* Other Funding So	urce:						
Net	\$103,219,665		KCRW Foundation	\$6,803,412 comm	ited, \$958,462 red	ceived				
Actual Measure AA Expenditures	\$82,790,943		Edison \$31,979.48	received						
Running Balance	\$20,428,722									

### Media and Technology Complex - Academy Site

### Project Description:

Renovation and new extension to the existing building, new building for KCRW, and a new parking structure

### Facility Size:

Building - 116,000 sq/ft Parking Structure - 450 spaces

### Status:

In construction

### Architect:

Clive Wilkinson Architects

### Contractor:

H.B. Parkco Construction Fast Track Construction CW Driver

**Project Expenses to Date** Building & Additions; \$65,499,698 Site Improvement; \$102,873 Consultants; \$52,629. Moving Expenses; \$38,756. Other Contract Services; \$90,875 Software Support; \$1,982. Service Fee; \$17,000 Legal; \$161,463. Supplies; \$20,818 Cap Equipment; \$186,301 Non-Cap Equipment; \$10,782 \_ \_ Architect; \$8,017,998 Inspection & Testing; \$3,377,630 Engineering; \$349,514 Project Management; \$4,862,623 \_

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
AA 7100060										
Repl. Health/PE/Fitness/Dance Building with Central Plant (104)										
Consultants		\$0	\$0	\$0	\$14	\$62	\$2,304	\$184	\$0	\$2,564
Supplies		\$0	\$0	\$0	\$0	\$7,089	\$195	\$484	\$8,512	\$16,280
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$663	\$80	\$742
Software Support		\$0	\$0	\$0	\$0		\$0	\$0	\$1,209	\$1,209
Site Improvement		\$0	\$0	\$0	\$0	\$0	\$559	\$440	\$0	\$999
Off Campus Printing		\$0	\$0	\$0	\$0	\$0	\$2,165	\$0	\$0	\$2,165
Postage		\$0	\$0	\$0	\$0	\$0	\$1,505	\$0	\$0	\$1,505
Other Contract Services		\$120	\$38	\$112	\$32,634	\$0	\$1,019	\$581	\$0	\$34,504
Building & Additions		\$0	\$0	\$0	\$817	\$4,188	\$1,623	\$13,783,023	\$12,322,213	\$26,111,863
Architect		\$256,076	\$1,568,564	\$1,790,207	\$518,973	\$177,583	\$364,853	\$585,900	\$289,917	\$5,552,073
Engineering		\$0	\$8,507	\$31,650	\$7,871	\$6,529	\$9,276	\$76,712	\$22,621	\$163,166
Inspection & Testing		\$36,892	\$490	\$21,150	\$1,285	\$360	\$133,756	\$846,765	\$275,706	\$1,316,404
Project Management		\$34,968	\$113,379	\$118,783	\$94,768	\$108,528	\$463,418	\$564,240	\$354,773	\$1,852,856
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$121,727	\$121,727
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$9,015	\$0	\$174,687	\$183,702
Total		\$328,056	\$1,690,978	\$1,961,901	\$656,362	\$304,338	\$989,689	\$15,858,991	\$13,571,442	\$35,361,758
Project Budget	\$58,272,030									
Less Other Funding*	\$11,794,230		* Other Funding So	urce:						
Net	\$46,477,800		Measure S \$11,603	3,383 allocated						
Actual Measure AA Expenditures	\$35,361,758		SCE \$190,847.28 r	eceived						
Running Balance	\$11,116,042									



### **Project Description:**

Replacement of locker rooms, fitness center, dance studios, and new central plant

# Facility Size: 62,000 sq/ft


Status:

# In construction Architect:

Gensler Architects

### Contractor:

Bernards Brothers

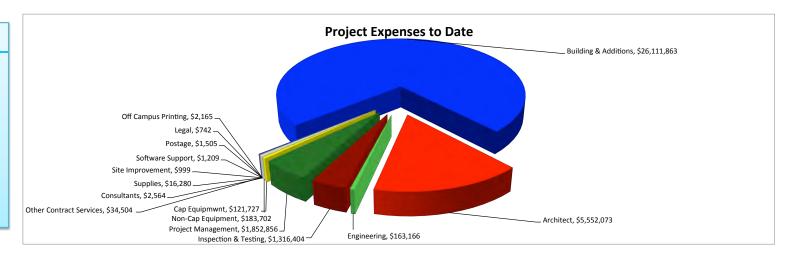

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
AA 7100065										
Drescher - Academic Modernization, Bookstore, Pico Promenade (105)										
Legal		\$0	\$0	\$0	\$0			\$0	\$0	
Other Contract Services		\$0	\$0	\$0	\$0	\$0		\$0	\$0	
Site Acquisition		\$0	\$0	\$0	\$0	\$0		\$0	\$0	
Inspection & Testing		\$0	\$0	\$0	\$0	\$0		\$0	\$0	
Project Management		\$0	\$0	\$5,082	\$0			\$0	\$0	
Total		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$0	\$5,082
Project Budget	\$13,005,082									
Less Other Funding	\$13,000,000		<ul> <li>Other Funding S</li> </ul>							
Net	\$5,082		Measure V 13,000	0,000 allocated						
Actual Measure AA Expenditures	\$5,082									
Running Balance	\$0									
AA 7100090										
Replacement Math and Science Extension Building (106)										
Legal		\$0	\$0	\$0	\$0			\$0	\$0	
Other Contract Services		\$0	\$0	\$0	\$0	\$0		\$0	\$0	
Site Acquisition		\$0	\$0	\$0	\$0			\$0	\$0	
Inspection & Testing		\$0	\$0	\$0	\$0			\$0	\$0	
Project Management		\$0	\$0	\$0	\$0	\$4,950		\$0	\$0	
Total		\$0	\$0	\$0	\$0	\$4,950	\$0	\$0	\$0	\$4,950
Project Budget	\$90,401,286									
Less Other Funding	\$90,396,336		* Other Funding S							
Net	\$4,950			36, Measure V \$5		d				
Actual Measure AA Expenditures	\$4,950		State of California	\$40,088,000 pend	ing					
Running Balance	\$0									

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
				'			<u>'</u>			
AA 7100047										
Madison East Wing Seismic Upgrade (107)										
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,970	\$4,970
Consultants		\$0	\$0	\$0	\$0	\$135	\$28	\$0	\$0	\$163
Off Campus Printing		\$0	\$0	\$0	\$0		\$285	\$0	\$0	\$285
Maintenance Contract		\$0	\$0	\$0	\$0		\$0	\$0	\$357	\$357
Legal		\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0
Software Support		\$0	\$0	\$0	\$0		\$0	\$0	\$806	\$806
Other Contract Services		\$0	\$364	\$997	\$0	\$0	\$1,328	\$711	\$0	\$3,400
Building & Additions		\$0	\$656	\$312,643	\$0	7 .,	\$6,030,371	\$8,829,626	\$4,280,407	\$19,457,951
Architect		\$76,073	\$398,050	\$550,589	\$65,444		\$199,100	\$404,764	\$85,623	\$1,837,124
Engineering		\$0	\$0	\$10,707	\$778		\$13,792	\$33,184	\$32,974	\$91,436
Inspection & Testing		\$0	\$19,848	\$16,752	\$3,036	\$5,851	\$676,323	\$405,443	\$101,004	\$1,228,258
Project Management		\$5,557	\$128,878	\$112,573	\$67,447	\$118,242	\$494,874	\$481,165	\$287,102	\$1,695,836
Cap Equipment		\$0	\$0	\$30,603	\$0		\$0	\$0	\$184,468	\$215,071
Non-Cap Equipment		\$0	\$0	\$71,827	\$9,788		\$0	\$0	\$101,138	\$182,752
Total		\$81,630	\$547,796	\$1,106,691	\$146,492	\$185,956	\$7,416,101	\$10,154,894	\$5,078,849	\$24,718,409
Project Budget	\$27,608,816									
Less Other Funding	\$0									
Net	\$27,608,816									
Actual Measure AA Expenditures	\$24,718,409									
Running Balance	\$2,890,407									

### Madison East Wing Seismic Upgrade

Project Description: Replacement of east wing with a new multipurpose room and additional classrooms

### Facility Size:

20,838 sq/ft


### Status:

In construction

Architect: DLR Group WWCOT

## Contractor:

Bernards Brothers



Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
Trojects	Duaget	03/10 1 11141	10/11 Tillal	11/12 1 11101	12/10/11/10	13/14111101	14/10111101	13/10 1 11141	10/17	Odinbined Totals
AA 7100068										
Renovation to Corsair Stadium (108)										
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0 \$0	\$0 \$0		\$0 \$0	\$0 \$0		\$0	
Architect		\$0	\$30,759	\$0 \$0		\$0 \$0	\$0 \$0		\$0	
Engineering		\$0	\$0,733	\$0		\$0	\$0		\$0	
Inspection & Testing		\$0	\$0	\$0		\$0	\$0		\$0	
Project Management		\$0	\$4,540	\$0		\$0	\$0		\$0	
Total		\$0	\$35,299	\$0	\$0				\$0	
Project Budget	\$35,299	401	ψου,200		ΨΟ	Ψ0		Ψ0	Ψ.	<b>400,20</b>
Less Other Funding	\$0									
Net	\$35,299									
Actual Measure AA Expenditures	\$35,299									
Running Balance	\$0									
. canning Datanoo	Ι ΨΟ									
AA 7100067, 7100152, 7100155, 7100157					I					
Business & Facilities Infrastructure (111)										1
Supplies		\$0	\$0	\$0	\$1,493	\$4,840	\$0	\$0	\$0	\$6,33
Service Fee		\$0 \$0	\$0 \$0	\$0 \$0		\$4,640 \$0	\$0		\$0	
Consultants		\$0	\$0 \$0	\$0 \$0		\$14	\$8		\$0	
Maintenance Contract		\$0	\$0 \$0	\$0 \$0		\$1,366	\$0		\$0	
Legal		\$0	\$0 \$0	\$75		\$1,300	\$0		\$0	
Software License		\$0	\$0 \$0	\$75 \$0	\$0 \$0	\$375	\$0		\$0	
Other Contract Services		\$0 \$0	\$6,289	\$6,988	\$750	\$375 \$0	\$2,209		\$0	
Moving Services		\$0	\$0,289	\$0,966 \$0	\$395	\$0 \$0	\$2,209		\$0	
Building & Additions		\$0	\$34,672	\$198,667	\$200,585	\$284,668	\$0		\$0	
Architect		\$0	\$34,672	\$80,626	\$170,132	\$37,906	\$0		\$0	
Engineering		\$0	\$0 \$0	\$00,020	\$3,705	\$9.735	\$6.840		\$0	
Inspection & Testing		\$0	\$0 \$0	\$8,142	\$10,938	\$10,500	\$0,640		\$0	
Project Management		\$0	\$3,073	\$154.904	\$87,291	\$139,821	\$3,571		\$0	
Cap Equipment		\$0	\$3,073	\$154,904	\$35,892	\$80,090	\$3,371		\$0	
Non-Cap Equipment		\$0	\$89,204	\$0 \$0		\$193,782	\$0		\$0	
Total		\$0	\$133,238	\$449,401		\$763,095	\$12,628		\$0	
Project Budget	\$1,968,124	<b>\$</b> 0	\$133,230	\$449,401	\$600,000	\$763,095	\$12,626	\$1,105	ψU	\$1,900,12
Less Other Funding	\$1,908,124									
Net	\$1,968,124									
Actual Measure AA Expenditures	\$1,968,124									
Running Balance	\$1,900,124									
Itulining Dalance	Ι Φ0									
A A 7400004										
AA 7100004										+
Master Planning, Program Management, Overhead (112)		<b>#</b> O	60	\$0	60	<b>60</b>	60	<b>#</b> 0	<b>ው</b> ብ	\$(
Supplies		\$0 ©0	\$0 ©0	\$0 \$0		\$0 \$0	\$0		\$0	
Architect		\$0 ©0	\$0 \$0	\$0 \$0			\$0 \$150		\$31,477	
Project Management		\$0 ©0				\$76,015	\$150		\$0	
Cap Equipment		\$0 ©0	\$0 60	\$0 ©0		\$0 \$0	\$0		\$0	
Non-Cap Equipment		\$0 \$0	\$0	\$0		\$0 \$76.045	\$0		\$0	
Total	0750 000	\$0	\$0	\$0	\$0	\$76,015	\$150	\$139,302	\$31,477	\$246,94
Project Budget	\$750,000									
Less Other Funding	\$0									
Net	\$750,000									
Actual Measure AA Expenditures	\$246,945									
Running Balance	\$503,055									

Districts	D. dest	00/40 51	40/44 Fire I	44/40 51	12/13 Final	40/44 Fin al	4445 51	45/40 Fire -1	40/47	0 bi d T d l
Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Finai	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
AA 7100154										
Energy Efficiency Projects (113)		0.0		20			20		20	20
Legal		\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0		\$0 -\$97,621	\$0	\$0	\$0
Building & Additions		\$0	\$0 \$0	\$189 \$0	\$2,108,853 \$0	\$990,389 \$0	-\$97,621 \$0	\$0 \$0	\$0 \$0	\$3,001,810
Architect		\$0					\$0 \$0			\$0 \$0
Engineering		\$0	\$0 \$0	\$0	\$0 \$4,020		\$0 \$10.118	\$0	\$0	
Inspection & Testing		\$0	\$0 \$0	\$0				\$0	\$0	\$14,138
Project Management		\$0		\$0	\$0		\$825	\$0	\$0	\$825
Non-Cap Equipment		\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0
Total	<b>60 500 000</b>	\$0	\$0	\$189	\$2,112,873	\$990,389	-\$86,678	\$0	\$0	\$3,016,773
Project Budget	\$3,508,088		+ O45 F 15 O							
Less Other Funding	\$491,315		* Other Funding S							
Net	\$3,016,773		DWP \$18,715.00 r							
Actual Measure AA Expenditures	\$3,016,773		SCE \$446,519.77							
Running Balance	\$0		Gas Co. \$26,080 r	eceivea						
A A 7400004			1					,		
AA 7100064										
Community Classroom & Facility Projects (114)										
Supplies		\$0	\$0	\$0	\$124		\$0	\$0	\$0	\$124
Legal		\$0	\$0	\$1,867	\$1,418	\$0	\$0	\$0	\$0	\$3,285
Other Contract Services		\$0	\$3,720	\$1,869	\$0		\$0	\$0	\$0	\$5,588
Building & Additions		\$0	\$434,578	\$1,369,441	\$408,696		\$0	\$0	\$0	\$2,211,712
Architect		\$0	\$263,833	\$48,120	\$1,318		\$0	\$0	\$0	\$313,272
Engineering		\$0	\$3,220	\$3,143	\$0		\$0	\$0	\$0	\$6,363
Inspection & Testing		\$0	\$41,002	\$80,885	\$1,495		\$0	\$0	\$0	\$123,382
Project Management		\$135	\$117,247	\$143,780	\$27,570		\$0	\$0	\$0	\$288,732
Non-Cap Equipment		\$0	\$0	\$209,726	\$0		\$0	\$0	\$0	\$209,726
Total		\$135	\$863,599	\$1,858,831	\$440,621	-\$1,003	\$0	\$0	\$0	\$3,162,183
Project Budget	\$3,162,183									
Less Other Funding	\$0									
Net	\$3,162,183									
Actual Measure AA Expenditures	\$3,162,183									
Running Balance	\$0									
AA 7100057										
Real Property Acquisition (115)										
Legal		\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$39	\$7,000	\$0		\$0	\$0	\$5,050,000	\$5,072,839
Site Acquisition		\$1,739,979	\$4,001,204	\$9,022,207	\$0		\$0	\$0	\$0	\$14,763,389
Inspection & Testing		\$8,689	\$7,986	\$0	\$0		\$0	\$0	\$0	\$16,674
Project Management		\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0
Total		\$1,748,667	\$4,009,228	\$9,029,207	\$0	\$15,800	\$0	\$0	\$5,050,000	\$19,852,902
Project Budget	\$24,902,902									
Less Other Funding	\$0									
Net	\$24,902,902									
Actual Measure AA Expenditures	\$19,852,902									
Running Balance	\$5,050,000									

AA 7100069 Infrastructure & Technology - Technology (117)	Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
Readways, Graunds, Parking Lots, and Garages (116)	·					·					
Surgiles											
Second   S											
Section   Sect				\$0							
S216   \$770   \$122   \$27,249   \$50											
Sulding A Actionne   \$185,345   \$9,731   \$113,794   \$321,603   \$975,401   \$0   \$0   \$0   \$1,502,247											
Signature   Sign											
Sol											
Inspection   Sesting   S13,880   \$7.685   \$13,553   \$20,126   \$42,866   \$0   \$0   \$0   \$97.785     Project Management   \$13,880   \$7.685   \$13,553   \$20,126   \$42,866   \$10,963   \$11,11   \$1   \$0   \$0   \$21,235     Total											
S24 404   S12,33   S21,945   S54,095   S104,945   S1,411   S0   S0   S219,337   S761   S1   S22,334   S27,945   S14,9403   S27,951   S1,155,512   S2,652   S0   S0   S2,130,677   S1,000   S1,00											
Section   Sect											
Project Budget											
Less Other Funding   \$4,891,747   Measure V \$1,000,000 allocated   \$2,100,000				\$27,804	\$149,403	\$573,951	\$1,153,512	\$2,652	\$0	\$0	\$2,130,670
Net Actual Measure A Expenditures											
Actual Measure AA Expenditures	Less Other Funding										
AA 7100069				Measure S \$3,891	,747, Measure V \$	1,000,000 allocate	d				
AA 7100069   Infrastructure & Technology - Technology (117)   S0   S0   S0   S0   S0   S0   S0   S	Actual Measure AA Expenditures										
Infrastructure & Technology (117)	Running Balance	\$0									
Infrastructure & Technology (117)	AA 74000CO										
Software											
Supplies		_	60	60	60	60	60	£210	60	60	¢210
Maintenance Contract   S0   \$9,472   \$46,300   \$210,581   \$18,944   \$42,415   \$9,472   \$0   \$337,186   \$10											
Solid   Soli											
Building Additions    \$0											
Project Management											
Sequence											
Non-Cap Equipment   S0   S0   S42,827   S500   S0   S3,447   S0   S0   S46,775   S46											
\$0   \$216,896   \$135,838   \$794,963   \$18,944   \$1,258,304   \$9,472   \$0   \$2,434,417     Less Other Funding											
Project Budget \$2,434,417   Less Other Funding \$5,2434,417   Actual Measure AA Expenditures \$2,434,417   Actual Measure AA Expenditures \$2,434,417   Actual Measure AA Expenditures \$3,434,417   Actual Measure AA Expenditures \$3,2434,417   Actual Measure AA Expenditures \$3,244,417   Actual Measure AA Expenditures \$4,244,417   Actual Measure AA Expenditures \$4,244,4											
Less Other Funding Net		20 404 447	\$0	\$216,896	\$135,838	\$794,963	\$18,944	\$1,258,304	\$9,472	\$0	\$2,434,417
Net											
Actual Measure AA Expenditures   \$2,434,417   Running Balance   \$0											
Running Balance											
AA 7100150   Infrastructure & Technology - Utility (118)											
Infrastructure & Technology - Utility (118)   Sofeware License   \$0 \$12,000 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	Running Balance	\$0									
Infrastructure & Technology - Utility (118)   Sofeware License   \$0 \$12,000 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	AA 7100150	1	1				1				
Sofeware License											
Legal     \$0			\$0	\$12,000	\$0	\$0	\$0	\$0	\$0	\$0	\$12,000
Building & Additions   \$0											
Architect \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0											
Inspection & Testing											
Project Management \$0 \$3,240 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$3,240 \$0 \$0 \$0 \$0 \$0 \$3,240 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0											
Cap Equipment         \$0         \$0         \$7,534         \$0         \$0         \$0         \$7,534         \$0         \$0         \$0         \$7,534         \$0         \$0         \$0         \$0         \$7,534         \$0											
Non-Cap Equipment \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0											
Total         \$0         \$20,219         \$7,534         \$0         \$0         \$0         \$0         \$27,753           Project Budget         \$27,753         \$0											
Project Budget         \$27,753           Less Other Funding         \$0           Net         \$27,753           Actual Measure AA Expenditures         \$27,753											
Less Other Funding         \$0           Net         \$27,753           Actual Measure AA Expenditures         \$27,753		\$27 753		Ψ <b>2</b> 0, <b>2</b> 13	Ψ1,334	401	φυ	Ψυ	<b>40</b>	φυ	Ψ21,133
Net         \$27,753           Actual Measure AA Expenditures         \$27,753											
Actual Measure AA Expenditures \$27,753											
	Running Balance										

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17	Combined Totals
AA 7100153										
Emergency Lighting, Fire Alarm, and Security System (119)										
Supplies		\$0	\$0	\$0		\$2,348	\$0	\$0	\$0	\$2,3
Consultants		\$0	\$0	\$0		\$0	\$16	\$0	\$0	9
Telecom Fee		\$0	\$0	\$0	\$0	\$0	\$800	\$0	\$0	\$
Maintenance Contract		\$0	\$0	\$648	\$0	\$39,700	\$0	\$2,700	\$0	\$43,
Software Suppoert		\$0	\$0	\$24,765	\$0	\$106,367	\$0	\$2,232	\$0	\$133,
Other Contract Services		\$0	\$0	\$0		\$47,695	\$0	\$4,643	\$0	\$52,
Building & Additions		\$0	\$0	\$0		\$110	\$2,648,866	\$4,129,145	\$851,247	\$7,629,
Architect		\$0	\$0	\$0		\$0	\$18,925	\$0	\$0	\$18
Enginnering		\$0	\$0	\$0		\$211,030	\$389,013	\$156,247	\$120,164	\$876
nspection & Testing		\$0	\$0	\$0		\$0	\$0	\$58,831	\$4,800	\$63
Project Management		\$0	\$0	\$0	\$0	\$51,008	\$52,044	\$79,285	\$11,130	\$193
Cap Equipment		\$0	\$0	\$0	\$0	\$89,415	\$0	\$5,871	\$0	\$95
Non-Cap Equipment		\$0	\$0	\$6,087	\$0	\$392,586	\$8,348	\$0	\$0	\$407
Total Total		\$0	\$0	\$31,500	\$0	\$940,259	\$3,118,012	\$4,438,953	\$987,341	\$9,516
Project Budget	\$11,520,794									
ess Other Funding	\$0									
Net	\$11,520,794									
Actual Measure AA Expenditures	\$9,516,066									
Running Balance	\$2,004,728									
<b>VA</b>										
Cost of Issuance (121)										
Cost of Issuance		\$0	\$0	\$0		\$0	\$285,000	\$0	\$0	\$285
otal		\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$0	\$285
Project Budget	\$500,000									
ess Other Funding	\$0									
Net	\$500,000									
Actual Measure AA Expenditures	\$285,000									
Running Balance	\$215,000									
Grand Total	1 1	\$4,900,734	\$10,935,584	\$17,864,407	\$13,113,759	\$30,388,248	\$39,049,510	\$60,741,756	\$40,602,105	\$217,596

## SMC Bond Program Contractor List as of 3-31-2017

Student Services (Measure U #0, Measure S #9, Measure AA #120):

Architect – Steinberg Architects, Morris Architects

Contractor - Minco, Bernards Brothers

Engineering – IVA, Cogent Energy Engineering, XL Fire

Inspection & Testing – Geo Labs, BTC Labs - Vertical V, Peak Survey, LPI

Rango Inc., Twining

Project Management - LPI

Replacement Health/PE/Fitness/Dance Building (Measure S #4, Measure AA #104):

Architect - Gensler Architects

Contractor – Bernards Brothers

Engineering – IVA, Glumac

Inspection & Testing – Geo Labs, Ellis Environmental, Twining, Rango Inc.

Project Management – LPI

Early Childhood Development (Measure S #5):

Architect - Carde Ten Architects

Consultant - Child Educational Center

Contractor - N/A

Engineering - N/A

Inspection & Testing – Geo Labs

Project Management - LPI

Malibu Site (Measure S #6, Measure AA #110):

Architect - Quatro Design Group

Contractor - N/A

Consultant – m2 Strategic, Parker Environmental

Engineering – Ensitu Services

Inspection & Testing – Peak Surveys, Ellis Environmental, JL Inspection

Project Management - LPI, m6 Strategic

Energy Efficiency Projects (Measure S #7, Measure AA #113):

Architect - N/A

Contractor – Compass Energy Solutions, Johnson Controls

Engineering – Compass Energy Solutions, Johnson Controls

Inspection & Testing – Ellis Environmental

Environmental Performance (Measure AA #101):

Architect - Kishimoto Architects

Contractor – SJ Amoroso Construction

Engineering – P2S Engineering

Inspection & Testing - Cannon, Peak Surveys

Project Management - LPI

Information Technology Relocation (Measure AA #102):

Architect - Morris Architects

Contractor - Minco, Bernards Brothers, Eidim AV Technology

Engineering – IVA, P2S Engineering

Inspection & Testing – Cannon, Peak Surveys, Geo Labs, Ellis Environmental, Twining, JL Inspection, Rango Inc.

Project Management – LPI, CCS Presentation

Media and Technology Complex (Measure AA #103):

Architect - Clive Wilkinson Architects, Morris Architects

Contractor – H.B. Parkco Construction, Fast Track Construction, CW Driver, Dimension Data, Key Code Media

Consultant – EEG Services

Engineering – IVA, P2S Engineering

Inspection & Testing - Twining, Geo Labs, BTC Labs - Vertical V,

JL Inspection, EEG Services, Ellis Environmental, Rango Inc., Cannon

Project Management - LPI

Madison East Wing Seismic Upgrade (Measure AA #107):

Architect – DLR Group – WWCOT, LPI

Contractor - Trimax, Bernards Brothers, Dimension Data

Engineering – IVA, Glumac

Inspection & Testing – Twining, Peak Surveys, LPI, All Group Engineering, EEG

Services, Ellis Environmental

Project Management - LPI

Business & Facilities Infrastructure (Measure AA #111):

Architect - LPI, Gwynne Pugh Urban Studio

Contractor – REC+S, Inc., Omega Construction, Concept Consultant, Inc.

Engineering – N/A

Inspection & Testing – Ellis Environmental, JL Inspection

Project Management – LPI

Community Classroom & Facility Project (Measure AA #114)

Architect – Morris Architects

Contractor – Waisman Construction, Spinitar, Trimax

Engineering – IVA

Inspection & Testing – LPI, Twining

Project Management - LPI

Satellite Campus Parking Facilities and Roadway Improvements (Measure S #8)

Architect - N/A

Contractor - N/A

Engineering – MK Engineering Group

Inspection & Testing – N/A

Project Management – LPI

Roadways, walkways, Grounds, Parking Lots, and Garages (Measure AA #116)

Architect - LPI, DLR Group - WWCOT

Contractor – Trimax, Pub Construction

Consultant – Walker Parking

Engineering – MK Engineering

Inspection & Testing – Ellis Environmental, Peak Surveys, LPI

Project Management – LPI

Emergency Lighting, Fire Alarm, and Security System (Measure AA #119)

Architect - N/A

Contractor – Red Hawk Fire and Security, Nexus

Consultant – IVA

Engineering – MDC Engineers

Inspection & Testing - Rango Inc.

Project Management - LPI

Signage Safety/Information (Measure S #15)

Architect - N/A

Contractor - Sign Excellence

Consultant – APCO

Engineering – N/A

Inspection & Testing – N/A

Project Management – LPI
