Measure U Project Schedule As of October 1, 2010

	Project Name	Completion	201	0		20	11	2	012	2	201	3	2014	
Α	Purchase of BAE Airport Site	Completed												
В	Emeritus College Facility	Completed												
С	Purchase of 1738 Pearl Street	Completed												
D	PE Temp. Bldg. Replacement	Completed												
Е	Remodel Library Village for Math	Completed												
F	SM Airport Campus Site Improvements	Completed												
G	SM Airport Campus West Building	Completed												
Н	Theater Arts Renovation	Completed												
J	Earthquake Rpl. Liberal Arts North	Completed												
J	Music Complex	Completed												
K	Earthquake Rpl. Liberal Arts South	Completed												
L	Shuttle Replacement Parking	Completed												
М	North Quad Plaza	Completed												
N	Letters & Sci Demo/Restore	Move to AA												
0	Student Services Building	February 2014												
Р	Science Complex Addition	Move to AA												
Q	Infrastructure & Safety	Completed												
R	Restroom Improvements	Completed												
S	Master Planning	Completed												
Т	14th and Pico Project	On Hold												
	* CM Airport Compus also known as Dura	dy Cito	1.		200	.	tion.							\exists
	* SM Airport Campus also known as Bun	uy Sile		10	JHS	เเนต	tion							

Measure U Bond Budget

	Project Name	Completion	Project Budget	Measure U Allocation	Other Funding	Measure U Expenditures as of 9/30/10	Measure U Expenditures as of 6/30/10	Measure U Expenditures Last Period	Total Measure U Remaining
Α	Purchase of BAE Airport Site	Completed	\$30,280,878	\$30,280,878	\$0	\$30,280,878	\$30,280,878	\$0	\$0
В	Emeritus College Facility	Completed	\$9,603,782	\$8,909,940	\$693,842	\$8,909,940	\$8,909,940	\$0	\$0
С	Purchase of 1738 Pearl Street	Completed	\$749,208	\$749,208	\$0	\$749,208	\$749,208	\$0	\$0
D	PE Temp. Bldg. Replacement	Completed	\$2,797,033	\$2,797,033	\$0	\$2,797,033	\$2,797,033	\$0	\$0
Е	Remodel Library Village for Math	Completed	\$1,458,690	\$1,458,690	\$0	\$1,458,690	\$1,458,690	\$0	\$0
F	SM Airport Campus Site Improvements	Completed	\$4,170,264	\$4,170,264	\$0	\$4,170,264	\$4,170,264	\$0	\$0
G	SM Airport Campus West Building	Completed	\$19,709,741	\$19,709,741	\$0	\$19,709,741	\$19,709,741	\$0	\$0
Н	Theater Arts Renovation	Completed	\$19,499,266	\$19,499,266	\$0	\$19,496,949	\$19,496,949	\$0	\$2,317
ı	Earthquake Rpl. Liberal Arts North	Completed	\$13,473,652	\$6,352,752	\$7,120,900	\$8,467,972	\$8,467,972	\$0	-\$2,115,220
J	Music Complex	Completed	\$4,625,047	\$2,006,934	\$2,618,113	\$2,004,434	\$2,004,434	\$0	\$2,500
K	Earthquake Rpl. Liberal Arts South	Completed	\$16,733,220	\$6,108,150	\$10,625,070	\$6,108,150	\$6,108,150	\$0	\$0
L	Shuttle Replacement Parking	Completed	\$18,969,509	\$18,969,509	\$0	\$18,969,509	\$18,969,509	\$0	\$0
М	North Quad Plaza	Completed	\$11,380,361	\$11,380,361	\$0	\$11,377,981	\$11,377,981	\$0	\$2,380
N	Letters & Sci Demo/Restore	Move to AA	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0	Student Services Building	February 2014	\$53,521,913	\$20,809,481	\$32,712,432	\$2,052,198	\$2,040,586	\$11,612	\$18,757,283
Р	Science Complex Addition	Move to AA	\$308,336	\$308,336	\$0	\$308,336	\$308,336	\$0	\$0
Q	Infrastructure & Safety	Completed	\$4,042,284	\$4,042,284	\$0	\$3,890,801	\$3,890,801	\$0	\$151,483
R	Restroom Improvements	Completed	\$17,501	\$17,501	\$0	\$17,501	\$17,501	\$0	\$0
S	Master Planning	Completed	\$2,110,430	\$2,110,430	\$0	\$2,110,430	\$2,110,430	\$0	\$0
Т	14th and Pico Project	On Hold	\$319,242	\$319,242	\$0	\$319,242	\$319,242	\$0	\$0
	Project Totals		\$213,770,357	\$160,000,000	\$53,770,357	\$143,199,257	\$143,187,645	\$11,612	\$16,800,743

FUND 42.2 As of October 1, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100010											
Purchase of BAE Airport Site (A)											
Site Acquisition		\$0	\$0	\$0	\$30,280,878					\$0	
Total		\$0	\$0	\$0	\$30,280,878	\$0	\$0	\$0	\$0	\$0	\$30,280,878
Project Budget	\$30,280,878										
Less Other Funding	\$0										
Net	\$30,280,878										
Actual Measure U Expenditures	\$30,280,878										
Running Balance	\$0										
U7100028											
Emeritus College Facility (B)											
Site Acquisition		\$8,658,675	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$8,658,675
Legal		\$14,649	\$3,009	\$20,421	\$0	\$0					
Architect		\$93,735	\$27,831	\$161	\$0						
Engineering		\$18,400	\$0								
Supply		\$0	\$4,461	\$0				\$0	\$0	\$0	
Building & Additions		\$0	\$17,496	\$0		\$0					\$21,496
Cap Equipment		\$0	\$49,406	\$0						\$0	
Non-Cap Equipment		\$0	-\$2,197	\$0						\$0	
Total		\$8,785,459	\$100,007	\$20,582	\$3,892	\$0	\$0	\$0	\$0	\$0	\$8,909,940
Project Budget	\$9,603,782										
Less Other Funding	\$693,842										
Net	\$8,909,940										
Actual Measure U Expenditures	\$8,909,940										
Running Balance	\$0										
U7100006											
1738 Pearl Street (C)		•	A= 0.4.=0.4							•	^ /
Site Acquisition		\$0	\$704,534	\$0	\$0	\$0		\$0		\$0	
Site Improvement		\$0	\$3,250	\$0							
Building & Additions		\$0	\$41,424	\$0							
Total	0=10	\$0	\$749,208	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$749,208
Project Budget	\$749,208										
Less Other Funding	\$0										
Net	\$749,208										
Actual Measure U Expenditures	\$749,208										
Running Balance	\$0										

10/8/2010 1 of 9

FUND 42.2 As of October 1, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
	<u> </u>						•				
U7100026											
PE Temporary Building Replacement (D)											
Architect		\$148,055	\$42,372	\$6,220	\$485	\$0	\$0	\$0	\$0	\$0	\$197,133
Building & Additions		\$43,866	\$1,922,493	\$415,932	\$0			\$0	\$0	\$0	\$2,382,291
Inspection & Testing		\$6,455	\$136,510	\$716	\$0			\$0	\$0	\$0	
Project Management		\$4,800	\$56,247	\$5,225	\$0			\$0	\$0	\$0	
Other Expenditures		\$763	\$0	\$6,893	\$0	\$0	\$0	\$0	\$0	\$0	
Total		\$203,939	\$2,157,622	\$434,987	\$485	\$0	\$0	\$0	\$0	\$0	\$2,797,033
Project Budget	\$2,797,033										
Less Other Funding	\$0										
Net	\$2,797,033										
Actual Measure U Expenditures	\$2,797,033										
Running Balance	\$0										
U7100310											
Remodel Library Village for Math (E)											
Moving Exp.		\$0	\$38,625	\$0		\$0	\$0	\$0	\$0	\$0	\$38,625
Building & Additions		\$0	\$1,036,490	\$115,653	\$0	\$0	\$0	\$0	\$0	\$0	\$1,152,143
Architect		\$104,992	\$27,141	\$1,340	\$486	\$0	\$0	\$0	\$0	\$0	\$133,959
Engineering		\$0	\$2,658	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,658
Inspection & Testing		\$0	\$27,083	\$25,175	\$0	\$0	\$0	\$0	\$0	\$0	\$52,258
Project Management		\$0	\$51,679	\$4,400	\$0	\$0	\$0	\$0	\$0	\$0	\$56,079
Other Expenditures		\$207	\$10,137	\$12,623	\$0	\$0	\$0	\$0	\$0	\$0	\$22,967
Total		\$105,199	\$1,193,813	\$159,191	\$486	\$0	\$0	\$0	\$0	\$0	\$1,458,690
Project Budget	\$1,458,690								•		
Less Other Funding	\$0										
Net	\$1,458,690										
Actual Measure U Expenditures	\$1,458,690										
Running Balance	\$0										

10/8/2010 2 of 9

FUND 42.2 As of October 1, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
	•		•	•							•
U7100027											
SM Airport Campus Site Improvements (F)											
Supplies		\$0	\$26,234	\$975	\$5,873	\$0		\$0	\$0	\$0	\$33,082
Misc Fees		\$0	\$25	\$0	\$0		\$0	\$0	\$0	\$0	\$34,299
Other Contract Services		\$3,860	\$11,508	\$8,434	\$1,501	\$0	T -	\$0	\$0	\$0	\$25,302
Site Improvement		\$0	\$0		\$5,790	\$7,237	\$0	\$0	\$0	\$0	\$28,209
Building & Additions		\$0	\$1,495,697	\$1,670,788	\$4,824	\$0	\$0		\$0	\$0	\$3,171,309
Architect		\$104,934	\$500	\$0	\$43,570				\$0		\$149,004
Engineering		\$35,000	\$148,304	\$950	\$10,040				\$0		\$194,294
Inspection & Testing		\$5,032	\$118,662	\$191,271	\$0		\$0	\$0	\$0		\$314,965
Project Management		\$750	\$155,798	\$38,425	\$1,365	\$220	\$0		\$0	\$0	\$196,558
Other Expenditures		\$16,587	\$1,802	\$327	\$150	\$4,375	\$0		\$0		\$23,241
Total		\$166,163	\$1,958,530	\$1,926,352	\$73,113	\$46,106	\$0	\$0	\$0	\$0	\$4,170,264
Project Budget	\$4,170,264										
Less Other Funding	\$0										
Net	\$4,170,264										
Actual Measure U Expenditures	\$4,170,264										
Running Balance	\$0										
U7110027											
SM Airport Campus West Building (G)											
Supply		\$0	\$0	\$17,650	\$28,017	\$0	\$0	\$0	\$0	\$0	\$45,667
Other Contract Services		\$0	\$0	\$0	\$3,576	\$0		\$0	\$0	\$0	\$3,576
Moving Expenses		\$0	\$0	\$180	\$15,824	\$0			\$0	\$0	\$16,004
Building & Additions		\$0	\$0	\$15,037,532	\$1,256,065	\$46,946	\$0	\$0	\$0		\$16,340,543
Architect		\$0	\$971,954		\$49,779	\$1,147	\$0		\$0	\$0	\$2,066,830
Engineering		\$0	\$2,920	\$9,800	\$5,010	\$963	\$0	\$0	\$0	\$0	\$18,693
Inspection & Testing		\$0	\$21,173	\$126,510	\$9,856	\$0	\$0	\$0	\$0	\$0	\$157,539
Project Management		\$0	\$14,450	\$313,715	\$13,956	\$0		\$0	\$0		\$342,121
Cap Equipment		\$0	\$49,795	\$326,382	\$4,792	\$0			\$0		\$380,969
Non-Cap Equipment		\$0	\$0	\$280,558	\$57,240				\$0		\$337,798
Total		\$0		\$17,156,277		\$49,056			\$0	\$0	\$19,709,741
Project Budget	\$19,709,741	7-	. ,,	. ,,	. , , ,	, -,,,				,,,	, -,,
Less Other Funding	\$0										
Net	\$19,709,741										
Actual Measure U Expenditures	\$19,709,741										
Running Balance	\$0										

10/8/2010 3 of 9

FUND 42.2 As of October 1, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
1.10,00.0	Baagot	02,00 1 11101	00/01111101	0 1/00 1 11141	00,00111141	00/01 1 11141	01700 1 11101	00/00 1 11101	00/10 1 11141	10/11	Combined Foldio
U7100025											
Theatre Arts Renovation (H)											
Supplies		\$0	\$8,904	-\$14	\$12,858	\$16,619	\$0	\$0	\$0	\$0	\$38,367
Legal		\$0	\$0	\$0	\$0			\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$0	\$0	\$14,061	\$0	\$0	\$0	\$0	\$14,061
Other Contract Services		\$0	\$0				\$0	\$5,245	\$0	\$0	\$5,245
Rental / Lease		\$0	\$1,446	\$2,200	\$0		\$0	\$0	\$0	\$0	\$3,646
Building & Additions		\$528	\$1,326,630		\$10,897,603	\$56,122	\$25,220	\$0	\$0	\$0	\$16,846,590
Architect		\$289,913	\$369,213	\$423,416	\$82,639	\$0	\$0	\$0	\$0	\$0	\$1,165,181
Engineering		\$6,174	\$2,981	\$16,606	\$2,375	\$1,250	\$0	\$0	\$0	\$0	\$29,386
Inspection & Testing		\$150	\$14,785	\$353,890	\$297,675		\$0	\$0	\$0	\$0	\$667,616
Project Management		\$150	\$45,698	\$184,219			\$230	\$0	\$0	\$0	\$439,013
Other Expenditures		\$0	\$812	\$0		\$2,267	\$0	\$0	\$0	\$0	\$5,627
Cap Equipment		\$0	\$31,638	\$0			\$0	\$0	\$0	\$0	\$97,785
Non-Cap Equipment		\$0	\$2,388	\$0		\$145,294	\$0	\$0	\$0	\$0	\$184,432
Total		\$296,915		\$5,520,804	\$11,532,803	\$311,236		\$5,245		\$0	\$19,496,949
Project Budget	\$19,499,266										
Less Other Funding	\$0										
Net	\$19,499,266										
Actual Measure U Expenditures	\$19,496,949										
Running Balance	\$2,317										
· · · · ·											
U7100110											
Earthquake Rpl. Liberal Arts North (I)											
Supplies		\$0	\$0	\$0	\$0	\$1,408	\$0	\$75	\$0	\$0	\$1,483
Legal		\$0	\$0				\$0	\$0	\$0	\$0	\$887
Other Contract Services		\$0	\$0				\$0	\$0	\$0	\$0	\$75
Building & Additions		\$265	\$0		\$5,916,281	-\$973,001	\$321,345	\$14,898	\$0	\$0	\$6,323,449
Architect		\$0	\$611,732	\$102,824	\$209,490		\$21,215	\$3,465	\$0	\$0	\$1,165,289
Engineering		\$3,248	\$4,295	\$0				\$0	\$0	\$0	\$8,043
Inspection & Testing		\$0	\$0	\$28,312	\$326,203	\$77,942	\$0	\$0	\$0	\$0	\$432,458
Project Management		\$0	\$26,072	\$33,549		\$124,222	\$255	\$1,155	\$286	\$0	\$314,475
Other Expenditures		\$0	-\$4	\$7,334	\$0			\$0	\$0	\$0	\$7,330
Cap-Equipment		\$0	\$0					\$0	\$0	\$0	\$37,935
Non-Cap Equipment		\$0	\$0		\$2,033		\$4,093	\$0	\$0	\$0	\$176,550
Total		\$3,513	\$642,095			-\$356,123	\$359,737	\$19,592	\$286	\$0	\$8,467,972
Project Budget	\$13,473,652	Received	, , , , , , , , , , , ,	, , , , , ,			, , , , , , , , , , , , , , , , , , , ,	. , -			
Less Other Funding	\$7,120,900	\$4,039,753									
·		. ,,									
Net	\$6,352,752										
Actual Measure U Expenditures	\$6,352,752 \$8,467,972										

10/8/2010 4 of 9

FUND 42.2 As of October 1, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100013, U7100047											
Music Complex (J)											
Advertising		\$0	\$0	\$436	\$0	\$0	\$0	\$0	\$0	\$0	\$436
Supplies		\$0	\$0	\$0	\$0		\$19,094	\$0	\$0	\$0	\$19,288
Consultants		\$0	\$0		\$0	\$0	\$36,000	\$0	\$0	\$0	\$36,000
Other Contract Services		\$0	\$0		\$0		\$180	\$0	\$0	\$0	\$180
Moving Services		\$0	\$0		\$0		\$6,330	\$0	\$0	\$0	\$6,330
Building & Additions		\$0	\$0			-\$737,213	\$273,531	\$0	\$0	\$0	\$1,186,509
Architect		\$0	\$187,922	\$22,500	\$37,227	\$38,448	\$4,052	\$14,356	\$0	\$0	\$304,505
Engineering		\$0	\$0	\$0	\$0		\$0	\$21,370	\$0	\$0	\$21,370
Inspection & Testing		\$0	\$0		\$19,265	\$26,238		\$0	\$0	\$0	\$111,122
Project Management		\$0	\$170	\$36,739	\$36,351	\$56,914	\$16,200	\$1,288	\$0	\$0	\$147,662
Cap Equipment		\$0	\$0		\$0		\$62,600	\$0	\$0	\$0	\$62,600
Non-Cap Equipment		\$0	\$0		\$0		\$78,582		\$0	\$0	\$108,434
Total		\$0	\$188,092	\$445,879		-\$585,566		\$37,014		\$0	\$2,004,434
Project Budget	\$4,625,047	Received	, , , , , ,	, ,,,	, , ,	, ,	, , ,	, , , , ,	* - 1	•	, , , , ,
Less Other Funding	\$2,618,113	\$2,618,113									
Net	\$2,006,934	+ ,,	1								
Actual Measure U Expenditures	\$2,004,434										
Running Balance	\$2,500										
U7100111											
Earthquake Rpl. Liberal Arts South (K)											
Supply		\$0	\$0	\$855	\$2,497	\$379	\$23,811	\$75	\$0	\$0	\$27,618
Legal		\$0	\$0	\$0	\$0	\$0	\$2,203	\$50	\$0	\$0	\$2,253
Moving Services		\$0	\$0	\$0	\$0	\$0	\$4,063	\$0	\$0	\$0	\$4,063
Consultants		\$0	\$0		\$17,265	\$41,435	\$0	\$0	\$0	\$0	\$58,700
Other Contract Services		\$0	\$0	\$6,154	\$0	\$0	\$0	\$0	\$0	\$0	\$6,154
Building & Additions		\$0	\$0		\$3,091,306	\$5,706,802	-\$4,642,459	\$0	\$91,516	\$0	\$4,273,467
Architect		\$0	\$0		-\$503,297	\$163,506	\$183,877	\$39,984	\$2,549	\$0	\$723,174
Engineering		\$0	\$0		\$150	\$5,344	\$500	\$0	\$0	\$0	\$9,119
Inspection & Testing		\$0	\$0		\$179,798	\$296,015	\$68,273	\$0	\$0	\$0	\$544,086
Project Management		\$0	\$0		\$43,989	\$262,598	\$52,690	\$1,722	\$1,278	\$0	\$362,276
Other Expenses		\$0	\$0		\$202	\$0	\$0	\$0	\$0	\$0	\$202
Cap-Equipment		\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0		\$0	\$58,726	\$45,388	-\$7,074	\$0	\$0	\$97,040
Total		\$0	\$0	\$872,991	\$2,831,909	\$6,534,806	-\$4,261,655	\$34,757	\$95,342	\$0	\$6,108,150
Project Budget	\$16,733,220	Received									
. O. E. E.	\$10,625,070	\$10,625,070									
Less Other Funding		Ψ10,020,010									
Net	\$6,108,150	Ψ10,020,010									
		Ψ10,020,07 O	l								

10/8/2010 5 of 9

FUND 42.2 As of October 1, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
	<u> </u>		•					•	•		
U7100221											
Shuttle Replacement Parking (L)											
Supplies		\$0		\$0				\$0	\$0	\$0	\$1,347
Legal		\$0	\$0	\$0	\$8,462			\$0	\$0	\$0	\$43,565
Site Acquisition		\$0	\$0	\$0		\$16,903,087	\$0		\$0	\$0	\$16,903,087
Site Improvement		\$0	\$0	\$0			\$0	\$0	\$0	\$0	\$3,027
Building & Additions		\$0	\$0	\$0	\$0		\$1,252,224	\$2,353	\$0	\$0	\$1,738,577
Architect		\$0	\$0	\$0	\$0	\$51,569	\$7,208	\$0	\$0	\$0	\$58,777
Inspection & Testing		\$0	\$0	\$0	\$0		\$41,250	\$0	\$0	\$0	\$181,072
Project Management		\$0	\$0	\$0	\$0		\$32,425	\$0	\$0	\$0	\$40,056
Total		\$0	\$0	\$0	\$8,462	\$17,624,240	\$1,334,455	\$2,353	\$0	\$0	\$18,969,509
Project Budget	\$18,969,509										
Less Other Funding	\$0										
Net	\$18,969,509										
Actual Measure U Expenditures	\$18,969,509										
Running Balance	\$0										
U7100321											
North Quad Plaza (M)											
Legal		\$0	\$0	\$0	\$0		\$3,825	\$5,604	\$0	\$0	\$9,429
Building & Additions		\$0	\$0	\$0	\$0	-\$443	\$6,130,081	\$3,634,487	\$0	\$0	\$9,764,125
Architect		\$0	\$231,055	\$8,444	\$140,048	\$435,618	\$171,225	\$68,633	\$2,901	\$0	\$1,057,924
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$186,220	\$107,477	\$328	\$0	\$294,025
Project Management		\$0	\$0	\$760	\$210	\$2,200	\$135,601	\$55,782	\$606	\$0	\$195,158
Other Expenses		\$0	\$1,900	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,900
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$55,420	\$0	\$0	\$55,420
Total		\$0	\$232,955	\$9,204	\$140,258	\$437,375	\$6,626,952		\$3,834	\$0	\$11,377,981
Project Budget	\$11,380,361										· •
Less Other Funding	\$0										
Net	\$11,380,361										
Actual Measure U Expenditures	\$11,377,981										
Running Balance	\$2,380										

10/8/2010 6 of 9

FUND 42.2 As of October 1, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100500, U7126450, U7100334, U7100142											
Student Services Building (O)											
Supplies		\$2,014	\$0		\$0		\$0	\$718	\$0	\$0	\$2,732
PC Upgrades		\$0	\$765	\$0	\$0		\$0	\$0	\$0		
Consultants		\$0	\$0		\$0		\$55,693	\$0	\$0		
Legal		\$0	\$0		\$0		\$2,775	\$31,776	\$0		\$34,588
Other Contract Services		\$210	\$0	\$0	\$0		\$17,561	\$17,495	\$18,817	\$0	\$54,084
Moving		\$7,571	\$0	\$0	\$0			\$616	\$0		
Building & Additions		\$359,141	\$2,441	\$0	\$0			\$0	\$0		
Architect		\$31,782	\$0	\$235,230	\$0			\$690,099	\$208,521		
Engineering		\$1,838	\$0		\$0			\$6,205	\$27,363		
Inspection & Testing		\$0	\$0		\$0		\$25,670	\$34,687	\$0		
Project Management		\$4,650	\$0	\$2,470	\$0		\$0	\$124,148	\$0		\$132,368
Cap Equipment		\$59,063	\$0	\$0	\$0		\$8,745	\$8,056	\$0		
Total		\$466,268	\$3,207	\$237,700	\$0	\$54,464	\$110,445	\$913,802	\$254,701	\$11,613	\$2,052,198
Project Budget	\$53,521,913	Received									
Less Other Funding	\$32,712,432	\$1,321,000									
Net	\$20,809,481										
Actual Measure U Expenditures	\$2,052,198										
Running Balance	\$18,757,283										
U7100090											
Science Complex Additional (P)											
Architect		\$0	\$0		\$0	\$246,425	\$61,911	\$0	\$0	\$0	\$308,336
Total		\$0	\$0	\$0	\$0	\$246,425	\$61,911	\$0	\$0	\$0	\$308,336
Project Budget	\$308,336							•		•	
Less Other Funding	\$0										
Net	\$308,336										
Actual Measure U Expenditures	\$308,336										
Running Balance	\$0										

10/8/2010 7 of 9

FUND 42.2 As of October 1, 2010

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
								ı		1	
U6780000, U7100022, U7100331, U7100550,											
U7100005, U7100030, U7100031, U7100029,											
U7100003, U7100008, U7100332, U7100072,											
U7100042, U7100056, U7100039											
Infrastructure & Safety (Q)		-									
Supplies		\$0	\$0	\$254	\$0	\$0	\$0	\$1,700	\$1,393	\$0	\$3,347
Consultants		\$0	\$0	\$0	\$0	\$0				\$0	
Legal		\$0	\$0	\$0	\$0	\$0		\$3,294	\$0	\$0	
Other Contract Services		\$0	\$0	\$0	\$0			\$81,445		\$0	
Building & Additions		\$681,900	\$195,175	\$20,600	\$0			\$0	\$0	\$0	
Architect		\$69,081	\$42,108	\$0	\$155,321	\$448,507	\$91,127	\$4,227	\$0	\$0	
Engineering		\$8,050	\$0	\$0	\$6,750			\$2,360	\$0	\$0	\$47,589
Inspection & Testing		\$2,241	\$4,250	\$0	\$0	\$0		\$0	\$0	\$0	\$12,298
Project Management		\$0	\$2,805	\$0	\$0	\$3,520	\$1,840	\$38	\$196	\$0	
Cap Equipment		\$0	\$0	\$343,861	\$0	\$0			\$349,531	\$0	\$1,588,563
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,216	\$0	
Other Expenses		\$0	\$785	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$785
Total		\$761,272	\$245,122	\$364,715	\$162,071	\$664,647	\$129,287	\$1,004,968	\$558,718	\$0	\$3,890,801
Project Budget	\$4,042,284										
Less Other Funding	\$0										
Net	\$4,042,284										
Actual Measure U Expenditures	\$3,890,801										
Running Balance	\$151,483										
U7100007	——										
Restroom Improvement (R)	—	Φ0	0504	Φ0	04.075	Φ0	00		00	Φ0	04.000
Supplies	—	\$0	\$564	\$0	\$1,075	\$0	\$0	\$0	\$0	\$0	\$1,639
Other Contract Services	 	\$0	\$0	\$0	\$3,803	\$0			\$0	\$0	
Building & Additions	—	\$0	\$1,305	\$0	\$7,891	\$0			\$0	\$0	\$9,196
Inspection & Testing	—	\$0	\$2,043	\$0	\$820	\$0			\$0	\$0	
Total	647.504	\$0	\$3,912	\$0	\$13,589	\$0	\$0	\$0	\$0	\$0	\$17,501
Project Budget	\$17,501										
Less Other Funding	\$0										
Net	\$17,501										
Actual Measure U Expenditures	\$17,501										
Running Balance	\$0										

10/8/2010 8 of 9

FUND 42.2 As of October 1, 2010

U7100004, U7110020 Master Planning (S) Consultants Architect Engineering Rental / Lease Postage		\$9,000	¢26 F46								
Master Planning (S) Consultants Architect Engineering Rental / Lease Postage			¢26 F46								
Consultants Architect Engineering Rental / Lease Postage			¢26 F46								
Architect Engineering Rental / Lease Postage			\$06 E46								
Engineering Rental / Lease Postage		Φ0	\$26,516	\$158,449	\$374,329	\$125,404	\$17,998	\$363,342	\$0	\$0	\$1,075,038
Rental / Lease Postage		\$0	\$17,617	\$126,433	\$104,083	\$126,701	\$346,827	\$276,985	\$0	\$0	\$998,647
Postage		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		\$0	\$0	\$6,453	\$0	\$0	\$0	\$0	\$0	\$0	\$6,453
Other Eveneses		\$0	\$0	\$30,000	\$0	\$0	\$0	\$0	\$0	\$0	\$30,000
Other Expenses		\$0	\$0	\$0	\$180	\$0	\$0	\$0	\$0	\$0	\$180
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$113	\$0	\$0	\$113
Total		\$9,000	\$44,133	\$321,335	\$478,593	\$252,105	\$364,825	\$640,439	\$0	\$0	\$2,110,430
Project Budget	\$2,110,430										
Less Other Funding	\$0										
Net	\$2,110,430										
Actual Measure U Expenditures	\$2,110,430										
Running Balance	\$0										
U7100024											
14th and Pico Project (T)											
Consultants	i	\$0	\$888	\$0	¢ο	ΦO	Φ0	ΦO	Φ.0	Φ0	0000
Architect		ΨΟ	φοσο	⊅ ∪	\$0	\$0	\$0	\$0	\$0	\$0	\$888

U7100024											
14th and Pico Project (T)											
Consultants		\$0	\$888	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$888
Architect		\$258,601	\$47,343	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$305,944
Inspection & Testing		\$12,070	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,070
Project Management		\$0	\$340	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$340
Total		\$270,671	\$48,571	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$319,242
Project Budget	\$319,242										
Less Other Funding	\$0										
Net	\$319,242										
Actual Measure U Expenditures	\$319,242										
Running Balance	\$0										

Grand Total \$11,068,400 \$10,432,055 \$28,685,697 \$54,940,416 \$25,278,771 \$5,283,853 \$6,585,573 \$912,880 \$11,613 \$143,199,258	Grand Total	\$11,068,400 \$10,	,432,055 \$28,685,697 \$54,940,	416 \$25,278,771 \$5,283,853 \$6,585,573	\$912,880 \$11,613	\$143,199,258
--	-------------	--------------------	---------------------------------	---	--------------------	---------------

Note: Project N had no expenses

10/8/2010 9 of 9

Measure S Project Schedule As of October 1, 2010

	Project Name	Completion	20	10		2	201 ⁻	1	20 ⁻	12		201	3
1	Athletic Fields Phase I, Corsair Field	Completed											
1A	Athletic Fields Phase I, John Adams	Completed											
2	Performing Arts Center	Completed											
3	Career Opportunity Center	Move to AA											
4	Replacement Health/PE/Fitness Building	June 2013											
5	Early Childhood Development/Childcare	In Planning											
6	Malibu Site Acquisition and Facility	Not Scheduled											
7	Energy Efficiency Projects	February 2013											
8	Satellite Campus Parking Facilities and Roadway Improvements	Completed											
9	Parking Garage, Grounds and Equipment - Student Services	February 2014											
10	Pico Promenade Improvements	Completed											
11	Master Planning	On-Going											
12	Other Bond Related Expenses	On-Going											
13	Adv. Architecture Related Exp for AA	Completed											
14	Real Property Acquisition	On-Going											
15	Signage Safety/Information	On-Going											\blacksquare
			In	Pla	ınn	ing			In (Cons	truc	tion	

Measure S Bond Budget

	Project Name	Completion	Project Budget	Measure S Allocation	Other Funding	Measure S Expenditures as of 9/30/10	Measure S Expenditures as of 6/30/10	Measure S Expenditures Last Period	Total Measure S Remaining
1	Athletic Fields Phase I, Corsair Field	Completed	\$4,440,768	\$4,373,238	\$67,530	\$4,372,238	\$4,372,238	\$0	\$1,000
1A	Athletic Fields Phase I, John Adams	Completed	\$2,970,807	\$2,970,807	\$0	\$2,969,807	\$2,969,807	\$0	\$1,000
2	Performing Arts Complex	Completed	\$40,664,881	\$37,672,305	\$2,992,576	\$37,608,541	\$37,608,541	\$0	\$63,764
3	Career Opportunity Center	Move to AA	\$0	\$0	\$0	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	June 2013	\$33,831,088	\$4,598,771	\$29,232,317	\$772,976	\$772,976	\$0	\$3,825,795
5	Early Childhood Development/Childcare	In Planning	\$11,318,000	\$7,000,000	\$4,318,000	\$9,200	\$9,200	\$0	\$6,990,800
6	Malibu Site Acquisition and Facility	Not Scheduled	\$31,069,031	\$25,000,000	\$6,069,031	\$5,230,992	\$5,230,992	\$0	\$19,769,008
7	Energy Efficiency Projects	February 2013	\$1,293,570	\$1,293,570	\$0	\$473,704	\$473,704	\$0	\$819,866
8	Satellite Campus Parking Facilities and Roadway Improvements	Completed	\$4,876,424	\$4,876,424	\$0	\$3,778,324	\$3,772,789	\$5,535	\$1,098,100
9	Parking Garage, Grounds and Equipment - Student Services	February 2014	\$53,143,653	\$52,690,653	\$453,000	\$14,403,411	\$14,359,174	\$44,237	\$38,287,242
10	Pico Promenade Improvements	Completed	\$1,018,009	\$1,018,009	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	On-Going	\$750,000	\$750,000	\$0	\$680,281	\$658,143	\$22,138	\$69,719
12	Other Bond Related Expenses	On-Going	\$600,000	\$600,000	\$0	\$60,048	\$51,985	\$8,063	\$539,952
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	On-Going	\$50,000	\$50,000	\$0	\$45,597	\$45,597	\$0	\$4,403
15	Signage Safety/Information	On-Going	\$606,223	\$606,223	\$0	\$188,483	\$32,225	\$156,258	\$417,740
	Project Totals		\$186,632,454	\$143,500,000	\$43,132,454	\$71,611,611	\$71,375,380	\$236,231	\$71,888,389

MEASURE S EXPENDITURES

FUND 42.3 As of October 1, 2010

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
•				·	L	•	<u> </u>		<u> </u>
S7100019									
Athletic Field Phase I, Corsair Field (1)									
Legal		\$0	\$0	\$0	\$301	\$175	\$0	\$0	\$476
Other Contract Services		\$0	\$0	\$0	\$0		\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$300,380	\$2,579,095	\$0	\$0	\$2,879,475
Architect		\$27,332	\$43,815	\$197,557	\$252,736	\$279,173	\$26,563	\$0	\$827,176
Inspection & Testing		\$0	\$0	\$0	\$23,411	\$57,585	\$640	\$0	\$81,636
Project Management		\$0	\$0	\$0	\$9,871	\$42,374	\$565	\$0	\$52,810
Cap Equipment		\$0	\$0	\$0	\$0		\$35,271	\$0	\$518,288
Non-Cap Equipment		\$0	\$0		\$0		\$10,312	\$0	
Total		\$27,332	\$43,815	\$197,557	\$586,699	\$3,443,485	\$73,350	\$0	\$4,372,238
Project Budget	\$4,440,768								
Less Other Funding	\$67,530	\$67,530							
Net	\$4,373,238								
Actual Measure S Expenditures	\$4,372,238								
Running Balance	\$1,000								
S7100038	1								
Athletic Field Phase I, John Adams (1A)									
Legal		\$0	\$0	\$0	\$75	\$0	\$0	\$0	\$75
Consultants		\$0	\$0	\$0	\$0		\$0	\$0	\$0
Supplies		\$0	\$0	\$0	\$0		\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$16,556		\$0	\$0	\$1,411,817
Architect		\$0	\$5,807	\$93,941	\$12,150	\$31,818	\$0	\$0	\$143,715
Inspection & Testing		\$0	\$2,874	\$3,207	\$0		\$0	\$0	\$56,066
Project Management		\$0	\$0		\$10,921	\$45,170	\$38	\$0	\$56,128
Cap Equipment		\$0	\$0	\$0	\$0		\$0	\$0	\$1,290,672
Non-Cap Equipment		\$0	\$0	\$0	\$0		\$0	\$0	\$11,334
Total		\$0	\$8,681	\$97,148	\$39,701	\$2,824,239	\$38	\$0	
Project Budget	\$2,970,807	, -	. ,					•	. , ., ., .,
Less Other Funding	\$0								
Net	\$2,970,807								
Actual Measure S Expenditures	\$2,969,807								
Running Balance	\$1,000								

10/8/2010 1 of 7

FUND 42.3 As of October 1, 2010

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
	3								
S7100012									
Performing Arts Center (2)									
Consultants		\$0	\$0	\$0	\$121,790	\$76,639	\$0	\$0	\$198,429
Other Expenses		\$0	\$0	\$4,269	\$0	\$22,729	\$22	\$0	\$27,020
Supplies		\$0	\$0		\$14,565	\$5,810		\$0	\$20,375
Legal		\$0	\$0	\$34,329	\$275,667	\$492,731	\$15,629	\$0	\$818,356
Advertising		\$0	\$0		\$320	\$0	\$0	\$0	\$320
Building & Additions		\$7,784,151	\$10,292,986	\$8,930,813	\$2,991,903	\$1,629,990	\$50,000	\$0	\$31,679,843
Architect		\$0	\$811,312	\$182,457	\$412,309	\$121,588	\$108	\$0	\$1,527,774
Engineering		\$0	\$3,600		\$1,500	\$9,650	\$0	\$0	\$20,000
Inspection & Testing		\$104,308	\$722,685	\$411,193	\$210,381	\$22,256	\$0	\$0	\$1,470,823
Project Management		\$31,984	\$155,732	\$248,876	\$263,690	\$47,915	\$3,244	\$0	\$751,441
Cap Equipment		\$0	\$0	\$130,218	\$292,565	\$342,693	\$0	\$0	\$765,476
Non-Cap Equipment		\$0	\$0		\$93,106	\$220,455	\$0	\$0	\$328,685
Total		\$7,920,443	\$11,986,315	\$9,962,528	\$4,677,797	\$2,992,455	\$69,003	\$0	\$37,608,541
Project Budget	\$40,664,881	Received							
Less Other Funding	\$2,992,576	\$2,992,576							
Net	\$37,672,305								
Actual Measure S Expenditures	\$37,608,541								
Running Balance	\$63,764								
S7100033, S7100144									
Replacement Health/PE/Fitness Building (4)									
Supplies		\$0	\$0	\$0	\$0	\$0	\$163	\$0	\$163
Legal		\$0	\$0		\$0	\$1,413	\$75	\$0	\$1,488
Other Contract Services		\$0	\$0		\$0	\$253	\$165	\$0	\$418
Repair Facility		\$0	\$4,861	\$0	\$0		\$0	\$0	\$4,861
Supplies		\$4,809	\$288	\$0	\$0		\$0	\$0	\$5,097
Building & Additions		\$0	\$0		\$0	\$112,410	\$526,552	\$0	\$638,962
Architect		\$0	\$0		\$0	\$0	\$41,044	\$0	\$41,044
Inspection & Testing		\$0	\$0		\$0		\$14,363	\$0	\$20,881
Project Management		\$0	\$0		\$0		\$23,425	\$0	\$32,495
Other Contract Services		\$1,634	\$25,934	\$0	\$0	\$0	\$0	\$0	\$27,568
Total		\$6,443	\$31,083	\$0	\$0	\$129,663	\$605,787	\$0	\$772,976
Project Budget	\$33,831,088								
Less Other Funding	\$29,232,317								
Net	\$4,598,771								
Actual Measure S Expenditures	\$772,976								
Running Balance	\$3,825,795								

10/8/2010 2 of 7

FUND 42.3 As of October 1, 2010

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/09 Einal	08/09 Final	00/10 Final	10/11	Combined Totals
Flojects	Buuget	04/03 Filial	03/00 Fillal	00/07 Fillal	07/00 Fillal	00/09 Fillal	09/10 Fillal	10/11	Combined Totals
S7100045									
Early Childhood Development/Childcare (5)									
Consultants		\$0	\$0	\$0	\$9,200	\$0	\$0	\$0	\$9,200
Total		\$0	\$0	\$0			\$0	\$0	\$9,200
Project Budget	\$11,318,000	Received		-					
Less Other Funding	\$4,318,000	\$0							
Net	\$7,000,000								
Actual Measure S Expenditures	\$9,200								
Running Balance	\$6,990,800								
S7100077, S7100015									
Malibu Site Acquisition and Facilities (6)									
Consultants		\$0	\$0	\$0	\$0	\$30,000	\$0	\$0	\$30,000
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Legal		\$0	\$27,722	\$16,787	\$6,159	\$504	\$0	\$0	\$51,172
Building & Additions		\$0	\$0	\$0		\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0		\$0	\$0	\$0	\$0
Inspection & Testing		\$4,388	\$3,750	\$141,462	\$0	\$0	\$0	\$0	\$149,600
Project Management		\$0	\$0	\$220	\$0	\$0	\$0	\$0	\$220
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Expenses		\$0	\$2,500,000	\$0	\$0	\$2,500,000		\$0	\$5,000,000
Total		\$4,388	\$2,531,472	\$158,468	\$6,159	\$2,530,504	\$0	\$0	\$5,230,992
Project Budget	\$31,069,031								
Less Other Funding	\$6,069,031								
Net	\$25,000,000								
Actual Measure S Expenditures	\$5,230,992								
Running Balance	\$19,769,008								

10/8/2010 3 of 7

FUND 42.3 As of October 1, 2010

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
	, J			l .	l.		l l		
S7100043, S7100066									
Energy Efficiency Projects (7)									
Legal		\$0	\$0	\$0	\$0	\$988	\$0	\$0	\$988
Building & Additions		\$0	\$0		\$0	\$106,921	\$355,294	\$0	\$462,215
Engineering		\$0	\$0			\$0	\$0	\$0	
Inspection & Testing		\$0	\$0				\$0	\$0	
Project Management		\$0	\$0		\$0	\$0	\$0	\$0	
Total		\$0	\$0	\$0	\$10,500	\$107,910	\$355,294	\$0	\$473,704
Project Budget	\$1,293,570								
Less Other Funding	\$0								
Net	\$1,293,570								
Actual Measure S Expenditures	\$473,704								
Running Balance	\$819,866								
S7100091, S7100092									
Satellite Campus Parking Facilities and F	Roadway Improvem	nents (8)							
Legal		\$0	\$0		\$300	\$175	\$0	\$0	
Other Contract Services		\$0	\$0		\$300	\$0	\$0	\$0	
Advertising		\$0	\$0				\$0	\$0	
Consultants		\$0	\$0			\$0	\$0	\$0	
Supplies		\$0	\$0		\$0	\$0	\$0	\$0	
Building & Additions		\$0	\$0		\$278,178	\$1,860,152	\$449,543	\$3,624	\$2,591,497
Architect		\$0	\$0		\$324,864	\$136,911	\$34,490	\$0	\$821,184
Inspection & Testing		\$0	\$0		\$31,100	\$185,947	\$28,218	\$0	\$245,266
Project Management		\$0	\$0		\$18,288	\$64,880	\$31,137	\$1,911	\$116,216
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$3,387	\$0	
Total		\$0	\$0	\$324,919	\$653,031	\$2,248,065	\$546,775	\$5,535	\$3,778,324
Project Budget	\$4,876,424								
Less Other Funding	\$0								
Net	\$4,876,424								
Actual Measure S Expenditures	\$3,778,324								
Running Balance	\$1,098,100								

10/8/2010 4 of 7

MEASURE S EXPENDITURES

FUND 42.3 As of October 1, 2010

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100142									
Parking Garage and Grounds - Student Service	es (9)								
Supplies		\$0	\$0	\$0	\$0	\$1,745	\$0	\$0	\$1,745
Consultants		\$0	\$0	\$0	\$0	\$20,700	\$0	\$0	\$20,700
Legal		\$0	\$0	\$0	\$0	\$2,154	\$17,486	\$0	\$19,640
Other Contract Services		\$0	\$0	\$0	\$0	\$1,508	\$10,952	\$26	\$12,486
Building & Additions		\$0	\$0	\$0	\$0	\$2,555,940	\$5,925,152	\$0	\$8,481,092
Architect		\$0	\$0	\$0	\$2,266,766	\$2,674,054	\$0	\$3,500	\$4,944,320
Engineering		\$0	\$0	\$0	\$0	\$4,813	\$38,330	\$3,166	\$46,308
Inspection & Testing		\$0	\$0	\$0	\$0	\$131,009	\$161,847	\$1,800	\$294,657
Project Management		\$0	\$0	\$0	\$0	\$158,766	\$373,559	\$35,745	\$568,070
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$14,393	\$0	\$14,393
Total		\$0	\$0	\$0	\$2,266,766	\$5,550,689	\$6,541,719	\$44,237	\$14,403,411
Project Budget	\$53,143,653	Received							
Less Other Funding	\$453,000	\$0							
Net	\$52,690,653		•						
Actual Measure S Expenditures	\$14,403,411								
Running Balance	\$38,287,242								

S7100044									
Pico Promenade Improvements (10)									
Building & Additions		\$0	\$0	\$0	\$690	\$883,401	\$0	\$0	\$884,091
Architect		\$0	\$0	\$0	\$69,190	\$28,540	\$864	\$0	\$98,595
Inspection & Testing		\$0	\$0	\$0	\$0	\$7,591	\$0	\$0	\$7,591
Project Management		\$0	\$0	\$0	\$2,185	\$25,548	\$0	\$0	\$27,733
Total		\$0	\$0	\$0	\$72,066	\$945,080	\$864	\$0	\$1,018,009
Project Budget	\$1,018,009								
Less Other Funding	\$0								
Net	\$1,018,009								
Actual Measure S Expenditures	\$1,018,009								
Running Balance	\$0								

10/8/2010 5 of 7

FUND 42.3 As of October 1, 2010

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100004									
Master Planning (11)									
Consultants		\$0	\$0	\$0	\$0	\$0	\$441,549	\$6,479	\$448,028
Printing		\$0	\$0	\$0	\$0		\$4,157	\$0	
Advertising		\$0	\$0		\$0		\$3,000	\$0	
Other Contract Services		\$0	\$0		\$0			\$200	
Architect		\$0	\$0	\$0	\$0		\$192,358	\$4,220	\$196,578
Project Management		\$0	\$0		\$0			\$8,396	
Other Expenses		\$0	\$0		\$0			\$2,842	\$2,842
Total		\$0	\$0		\$0			\$22,137	
Project Budget	\$750,000	, -	* -	* -	* -	* -	, , , , , ,	· · · · · ·	, , , , , ,
Less Other Funding	\$0								
Net	\$750,000								
Actual Measure S Expenditures	\$680,281								
Running Balance	\$69,719								
, J	+ /	I.							
S7100048									
Other Bond Related Expenses (12)									
Supplies		\$0	\$0	\$0	\$0	\$0	\$3.638	\$0	\$3,638
Legal		\$0	\$0		\$0		\$8,917	\$489	\$9,406
Advertising		\$0	\$0 \$0	\$0	\$0		\$2,278	Ψ 1 03	
Other Contract Services		\$0	\$0		\$0		\$17,206	\$6,184	
Moving Services		\$0	\$0		\$0		\$400	\$0	
Project Management		\$0	\$0		\$0		\$17,747	\$1,390	
Total		\$0	\$ 0					\$8,063	
Project Budget	\$600.000	ΨΟ	ΨΟ	ΨΟ	ΨΟ	Ψ1,000	ψ30,103	ψ0,003	ψ00,040
Less Other Funding	\$0								
Net	\$600,000								
Actual Measure S Expenditures	\$60,048								
Running Balance	\$539,952								
Ituning Balance	ψ009,902								
S7100049		ı		ı	ı	ı	ı		I
Adv Architecture Related Exp for AA (13)									
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0 \$0		\$0 \$0		\$0	\$0 \$0	
Architect		\$0	\$0 \$0		\$0 \$0		\$0	\$0 \$0	\$0
		\$0	\$0 \$0		\$0 \$0		\$0 \$0	\$0 \$0	\$0
Engineering		\$0	\$0 \$0		\$0		-\$45,734	\$0 \$0	
Inspection & Testing									\$0
Project Management		\$0	\$0 \$0		\$0 \$0		\$0 \$45.734	\$0 \$0	
Total	00	\$0	\$0	\$0	\$0	\$45,734	-\$45,734	\$0	\$0
Project Budget	\$0	-							
Less Other Funding	\$0 \$0								
Net	\$0 \$0								
Actual Measure S Expenditures	\$0 \$0								
Running Balance	\$0								

10/8/2010 6 of 7

FUND 42.3 As of October 1, 2010

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100057									
Real Property Acquisition (14)									
Other Contract Services		\$0			\$0	\$0	\$18,721	\$0	\$18,721
Architect		\$0		\$0				\$0	
Engineering		\$0						\$0	
Inspection & Testing		\$0	\$0		7 -			\$0	
Project Management		\$0						\$0	
Total		\$0	\$0	\$0	\$0	\$0	\$45,597	\$0	\$45,597
Project Budget	\$50,000								
Less Other Funding	\$0								
Net	\$50,000								
Actual Measure S Expenditures	\$45,597								
Running Balance	\$4,403								
S7100072									
Campus Signage (15)									
Consultants		\$0					\$32,225	\$0	\$32,225
Other Contract Services		\$0	\$0	\$0			\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Inspection & Testing		\$0					\$0	\$0	
Project Management		\$0	\$0	\$0			\$0	\$0	\$0
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$156,258	\$156,258
			\$0	\$0	\$0	\$0	\$32,225	\$156,258	\$188,483
Total		\$0	ΨU	ΨΟ					
	\$606,223	\$0	\$ 0	Ψ.	+-				
Total	\$606,223 \$0		φυ	μ ψυ	7.				
Total Project Budget			\$0	ψυ	**				
Total Project Budget Less Other Funding	\$0		<u> </u> \$0	1 40	, , , ,				

	Grand Total		\$7,958,606	\$14,601,366	\$10,740,621	\$8,321,918	\$20,819,624	\$8,933,245	\$236,230	\$71,611,610
--	-------------	--	-------------	--------------	--------------	-------------	--------------	-------------	-----------	--------------

Note: Project 3 had no expenses

10/8/2010 7 of 7

Measure AA Project Schedule As of October 1, 2010

	Project Name	Completion	2010)	2	2011	2	2012		20	013	2014	ļ	20	15	2016	
101	Environmental Performance - Central Plant	July 2013															П
102	Infrastructure & Technology - Information Technology Relocation	August 2013															
103	Media and Technology Complex - Academy Site	February 2014															
104	Replacement Health/PE/Fitness/Dance Building with Central Plant	September 2013															
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	August 2015															
106	Replacement Math and Science Extension Building	August 2016															
107	Madison East Wing Seismic Upgrade	June 2013															
108	Renovation of Corsair Stadium	November 2016												<u>.</u>			
109	Career Opportunity and Advancement Center (Bundy)	Not Scheduled															
110	Malibu Center	Not Scheduled															
111	Business & Facilities Infrastructure	December 2011															
112	Master Planning, Program Management, Overhead	On-Going															
113	Energy Efficiency Projects	On-Going															
114	Community Classroom & Facility Projects	December 2011															
115	Real Property Acquisition	On-Going															
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	On-Going															
				ln	Pla	nning	I	n Cc	nst	ructio	on					工	

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget As of October 1, 2010

	Project Name	Completion	Project Budget	Measure AA Allocation	Other Funding	Measure AA Expenditures as of 9/30/10	Measure AA Expenditures as of 6/30/10	Measure AA Expenditures Last Period	Total Measure AA Remaining
101	Environmental Performance - Central Plant	December 2012	\$4,882,119	\$4,882,119	\$0	\$48,500	\$48,500	\$0	\$4,833,619
102	Infrastructure & Technology - Information Technology Relocation	December 2012	\$13,287,218	\$13,287,218	\$0	\$199,438	\$148,800	\$50,638	\$13,087,780
103	Media and Technology Complex - Academy Site	August 2013	\$61,480,824	\$57,700,824	\$3,780,000	\$ 3,191,526	\$ 2,321,599	\$869,927	\$54,509,298
104	Replacement Health/PE/Fitness/Dance Building with Central Plant	June 2013	\$39,983,011	\$35,384,240	\$4,598,771	\$350,279	\$328,056	\$22,223	\$35,033,961
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	July 2015	\$34,026,480	\$34,026,480	\$0	\$0	\$0	\$0	\$34,026,480
106	Replacement Math and Science Extension Building	May 2015	\$108,103,000	\$68,259,000	\$40,134,000	\$0	\$0	\$0	\$68,259,000
107	Madison East Wing Seismic Upgrade	June 2012	\$12,292,000	\$12,292,000	\$0	\$186,154	\$81,630	\$104,524	\$12,105,846
108	Renovation of Corsair Stadium	November 2016	\$11,203,000	\$11,203,000	\$0	\$0	\$0	\$0	\$11,203,000
109	Career Opportunity and Advancement Center (Bundy)	December 2016	\$41,391,000	\$29,384,000	\$12,007,000	\$0	\$0	\$0	\$29,384,000
110	Malibu Center	November 2014	\$31,069,031	\$6,069,031	\$25,000,000	\$0	\$0	\$0	\$6,069,031
111	Business & Facilities Infrastructure	December 2011	\$6,140,952	\$6,140,952	\$0	\$0	\$0	\$0	\$6,140,952
112	Master Planning, Program Management, Overhead	On-Going	\$1,650,000	\$1,650,000	\$0	\$0	\$0	\$0	\$1,650,000
113	Energy Efficiency Projects	On-Going	\$5,150,136	\$5,150,136	\$0	\$0	\$0	\$0	\$5,150,136
114	Community Classroom & Facility Projects	December 2011	\$3,221,000	\$3,221,000	\$0	\$15,828	\$135	\$15,693	\$3,205,172
115	Real Property Acquisition	On-Going	\$6,000,000	\$6,000,000	\$0	\$1,748,667	\$1,748,667	\$0	\$4,251,333
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	On-Going	\$350,000	\$350,000	\$0	\$231,758	\$223,347	\$8,411	\$118,242
	Project Totals		\$380,229,771	\$295,000,000	\$85,519,771	\$5,972,150	\$4,900,734	\$1,071,416	\$289,027,850

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100062				
Environmental Performance - Central Plant (101)				
Legal		\$0	\$0	\$0
Other Contract Services		\$0	\$0	
Consultants		\$0	\$0	\$0
Building & Additions		\$0	\$0	
Architect		\$0	\$0	
Engineering		\$48,500	\$0	
Inspection & Testing		\$0	\$0	
Project Management		\$0	\$0	
Cap Equipment		\$0	\$0	
Non-Cap Equipment		\$0	\$0	
Total		\$48,500	\$0	\$48,500
Project Budget	\$4,882,119			
Less Other Funding	\$0			
Net	\$4,882,119			
Actual Measure AA Expenditures	\$48,500			
Running Balance	\$4,833,619			
AA 7100063				<u> </u>
Infrastructure & Technology - IT Relocation (102)				
Legal		\$0	\$0	\$0
Consultants		\$0	\$0	
Supplies		\$0	\$0	
Building & Additions		\$0	\$0	
Architect		\$105,049	\$35,000	\$140,049
Inspection & Testing		\$10,291	\$0	
Project Management		\$33,460	\$15,638	\$49,098
Cap Equipment		\$0	\$0	
Non-Cap Equipment		\$0	\$0	
Total		\$148,800	\$50,638	\$199,438
Project Budget	\$13,287,218			
Less Other Funding	\$0			
Net	\$13,287,218			
Actual Measure AA Expenditures	\$199,438			
Running Balance	\$13,087,780			

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100061				
Media and Technology Complex - Academy Site (103)				
Consultants		\$0	\$0	\$0
Supplies		\$0	\$0	\$0
Legal		\$16,903	\$0	\$16,903
Other Contract Services		\$3,993	\$1,140	\$5,134
Advertising		\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0
Architect		\$2,097,553	\$815,994	\$2,913,547
Engineering		\$16,459	\$4,516	\$20,976
Inspection & Testing		\$64,905	\$0	\$64,905
Project Management		\$121,786	\$48,277	\$170,063
Cap Equipment		\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0
Total		\$2,321,599	\$869,927	\$3,191,526
Project Budget	\$61,480,824	Received		
Less Other Funding	\$3,780,000	\$357,933		
Net	\$57,700,824			
Actual Measure AA Expenditures	\$3,191,526			
Running Balance	\$54,509,298			
AA 7100060	<u> </u>			
Repl. Health/PE/Fitness/Dance Building with Central Plant (104)				
Consultants		\$0	\$0	\$0
Supplies		\$0	\$0	\$0
Other Contract Services		\$120	\$0	\$120
Building & Additions		\$0	\$0	\$0
Architect		\$256,076	\$0	\$256,076
Inspection & Testing		\$36,892	\$0	\$36,892
Project Management		\$34,968	\$22,223	\$57,191
Total		\$328,056	\$22,223	\$350,279
Project Budget	\$39,983,011	· · · · · · · · · · · · · · · · · · ·	· ·	. ,
Less Other Funding	\$4,598,771			
Net	\$35,384,240			
Actual Measure AA Expenditures	\$350,279			
Running Balance	\$35,033,961			

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100047				
Madison East Wing Seismic Upgrade (107)				
Consultants		\$0	\$0	\$0
Supplies		\$0	\$0	\$0
Legal		\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0
Architect		\$76,073	\$88,417	\$164,490
Inspection & Testing		\$0	\$0	\$0
Project Management		\$5,557	\$16,107	\$21,664
Other Contract Services		\$0	\$0	\$0
Other Expenses		\$0	\$0	\$0
Total		\$81,630	\$104,524	\$186,154
Project Budget	\$12,292,000			
Less Other Funding	\$0			
Net	\$12,292,000			
Actual Measure AA Expenditures	\$186,154			
Running Balance	\$12,105,846			
AA 7100064				
Community Classroom & Facility Projects (114)				
Building & Additions		\$0	\$0	\$0
Architect		\$0	\$7,846	\$7,846
Engineering		\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0
Project Management		\$135	\$7,847	\$7,982
Total		\$135	\$15,693	\$15,828
Project Budget	\$3,221,000		. ,	. , , , , , , , , , , , , , , , , , , ,
Less Other Funding	\$0			
Net	\$3,221,000			
Actual Measure AA Expenditures	\$15,828			
Running Balance	\$3,205,172			

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100057				
Real Property Acquisition (115)				
Legal		\$0	\$0	\$(
Site Acquisition		\$1,739,979	\$0	\$1,739,97
Inspection & Testing		\$8,689	\$0	\$8,68
Project Management		\$0	\$0	\$
Total		\$1,748,667	\$0	\$1,748,66
Project Budget	\$6,000,000			
Less Other Funding	\$0			
Net	\$6,000,000			
Actual Measure AA Expenditures	\$1,748,667			
Running Balance	\$4,251,333			
•				
AA 7100058				
Roadways, Walkways, Grounds, Parking Lots, and Garages (116)				
Legal		\$0	\$0	\$
Other Contract Services		\$218	\$750	\$96
Building & Additions		\$185,345	\$0	\$185,34
Inspection & Testing		\$13,380	\$2,880	\$16,26
Project Management		\$24,404	\$4,781	\$29,18
Total		\$223,347	\$8,411	\$231,75
Project Budget	\$350,000			
Less Other Funding	\$0			
Net	\$350,000			
Actual Measure AA Expenditures	\$231,758			
Running Balance	\$118,242			
	•			
Grand Total		\$4,900,734	\$1,071,417	\$5,972,15


SANTA MONICA COMMUNITY COLLEGE DISTRICT Bond Sales / Expenses Report As of October 1, 2010

Measure U Bond \$160,000,000		
Bond Issue Date		Amount
	2002	\$25,000,000
	2004	\$21,999,971
	2005	\$89,999,923
	2007	\$11,999,987
	2010	\$10,998,992
Total Available		\$159,998,873
Expenses as of 9-30-10		\$143,199,258
Total Available Remaining		\$16,799,615
Unsold Bond Amount		\$1,127
Total Available as of 10-1-10		\$16,800,742

M 0 D 1 0 1 10 500 000 (4)		
Measure S Bond \$143,500,000 (1)		
Bond Issue Date		Amount
	2005	\$58,000,000
	2007	\$8,500,000
	2009	\$56,997,857
Total Available		\$123,497,857
Expenses as of 9-30-10		\$71,611,610
Total Available Remaining		\$51,886,247
Unsold Bond Amount		\$20,002,143
Total Available as of 10-1-10		\$71,888,390

Measure AA Bond \$295,000,000	
Bond Issue Date	Amount
2010	\$100,000,000
Total Available	\$100,000,000
Expenses as of 9-30-10	\$5,972,151
Total Available Remaining	\$94,027,849
Unsold Bond Amount	\$195,000,000
Total Available as of 10-1-10	\$289,027,849

Total Bond	\$598,500,000
Total Available	\$383,496,730
Total Expenses as of 9-30-10	\$220,783,019
Total Available Remaining	\$162,713,711
Total Unsold Bond	\$215,003,270

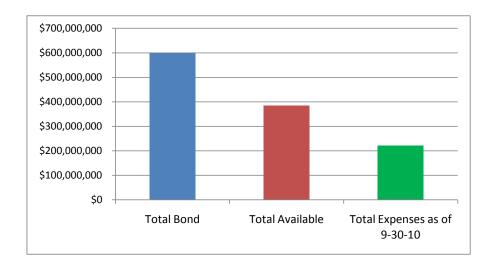

Interest	Measure U	Measure S	Measure AA
As of 6-30-10	\$5,694,648	\$7,329,902	\$512,487
Arbitrage Payment as of 6-30-10	\$0	\$393,004	\$0
Available Interest as of 6-30-10	\$5,694,648	\$6,936,898	\$512,487

Cost of Issuance Refund	Measure U	Measure S
As of 6-30-10	\$20,688	\$35,575
