# SANTA MONICA COMMUNITY COLLEGE DISTRICT


# Measure U Project Schedule As of June 30, 2011

	Project Name	Completion	20	10			20 <sup>-</sup>	11	2	012		201	3		20	14
А	Purchase of BAE Airport Site	Completed														
В	Emeritus College Facility	Completed														
С	Purchase of 1738 Pearl Street	Completed														
D	PE Temp. Bldg. Replacement	Completed														
E	Remodel Library Village for Math	Completed														
F	SM Airport Campus Site Improvements	Completed														
G	SM Airport Campus West Building	Completed														
Н	Theater Arts Renovation	Completed														
I	Earthquake Rpl. Liberal Arts North	Completed														
J	Music Complex	Completed														
К	Earthquake Rpl. Liberal Arts South	Completed														
L	Shuttle Replacement Parking	Completed														
М	North Quad Plaza	Completed														
Ν	Letters & Sci Demo/Restore	Move to AA														
0	Student Services Building	October 2014														
Р	Science Complex Addition	Move to AA														
Q	Infrastructure & Safety	Completed														
R	Restroom Improvements	Completed														
S	Master Planning	Completed														
Т	14th and Pico Project	On Hold														
	* CM Aiment Compute also known as Durate	Cito		1					 		 -			_		
	* SM Airport Campus also known as Bundy	SILE		m	U01	IST	ucti	บท								

# SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure U Bond Budget

As of June 30, 2011

	Project Name	Completion	Project Budget	Measure U Allocation	Other Funding	Measure U Expenditures as of 6/30/11	Measure U Expenditures as of 3/31/11	Measure U Expenditures Last Period	Total Measure U Remaining
Α	Purchase of BAE Airport Site	Completed	\$30,280,878	\$30,280,878	\$0	\$30,280,878	\$30,280,878	\$0	\$0
В	Emeritus College Facility	Completed	\$9,603,782	\$8,909,940	\$693,842	\$8,909,940	\$8,909,940	\$0	\$0
С	Purchase of 1738 Pearl Street	Completed	\$749,208	\$749,208	\$0	\$749,208	\$749,208	\$0	\$0
D	PE Temp. Bldg. Replacement	Completed	\$2,797,033	\$2,797,033	\$0	\$2,797,033	\$2,797,033	\$0	\$0
E	Remodel Library Village for Math	Completed	\$1,458,690	\$1,458,690	\$0	\$1,458,690	\$1,458,690	\$0	\$0
F	SM Airport Campus Site Improvements	Completed	\$4,170,264	\$4,170,264	\$0	\$4,170,264	\$4,170,264	\$0	\$0
G	SM Airport Campus West Building	Completed	\$19,709,741	\$19,709,741	\$0	\$19,709,741	\$19,709,741	\$0	\$0
Н	Theater Arts Renovation	Completed	\$19,497,949	\$19,497,949	\$0	\$19,496,949	\$19,496,949	\$0	\$1,000
1	Earthquake Rpl. Liberal Arts North	Completed	\$12,507,725	\$6,352,752	\$6,154,973	\$7,633,209	\$7,633,209	\$0	-\$1,280,457
J	Music Complex	Completed	\$4,623,547	\$2,005,434	\$2,618,113	\$2,005,116	\$2,004,434	\$682	\$318
K	Earthquake Rpl. Liberal Arts South	Completed	\$16,733,220	\$6,108,150	\$10,625,070	\$6,108,150	\$6,108,150	\$0	\$0
L	Shuttle Replacement Parking	Completed	\$18,969,509	\$18,969,509	\$0	\$18,969,509	\$18,969,509	\$0	\$0
М	North Quad Plaza	Completed	\$11,388,463	\$11,388,463	\$0	\$11,388,463	\$11,388,463	\$0	\$0
Ν	Letters & Sci Demo/Restore	Move to AA	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0	Student Services Building	October 2014	\$53,521,913	\$20,816,196	\$32,708,239	\$2,082,330	\$2,081,098	\$1,232	\$18,733,866
Р	Science Complex Addition	Move to AA	\$308,336	\$308,336	\$0	\$308,336	\$308,336	\$0	\$0
Q	Infrastructure & Safety	Completed	\$4,030,284	\$4,030,284	\$0	\$3,948,796	\$3,930,803	\$17,993	\$81,488
R	Restroom Improvements	Completed	\$17,501	\$17,501	\$0	\$17,501	\$17,501	\$0	\$0
S	Master Planning	Completed	\$2,110,430	\$2,110,430	\$0	\$2,110,430	\$2,110,430	\$0	\$0
Т	14th and Pico Project	On Hold	\$319,242	\$319,242	\$0	\$319,242	\$319,242	\$0	\$0
	Project Totals		\$212,800,237	\$160,000,000	\$52,800,237	\$142,463,785	\$142,443,878	\$19,907	\$17,536,215

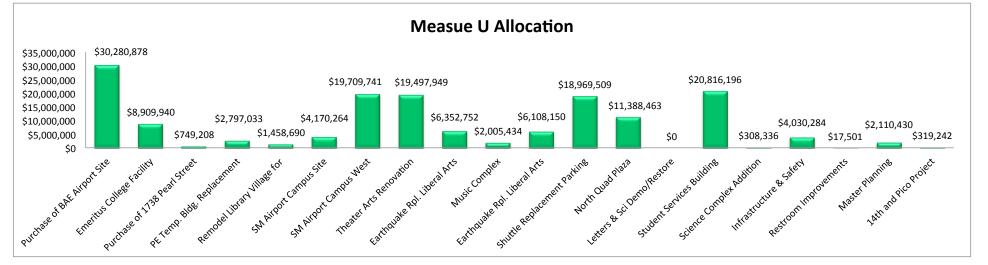

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100010											
Purchase of BAE Airport Site (A)											
Site Acquisition		\$0	\$0		\$30,280,878		\$0	\$0	\$0	\$0	\$30,280,878
Total		\$0	\$0	\$0	\$30,280,878	\$0	\$0	\$0	\$0	\$0	\$30,280,878
Project Budget	\$30,280,878										
Less Other Funding	\$0										
Net	\$30,280,878										
Actual Measure U Expenditures	\$30,280,878										
Running Balance	\$0										
U7100028											
Emeritus College Facility (B)											
Site Acquisition		\$8,658,675	\$0	\$0	\$0	\$0		\$0			\$8,658,675
Legal		\$14,649	\$3,009	\$20,421	\$0	\$0	\$0	\$0			\$38,078
Architect		\$93,735	\$27,831	\$161	\$0			\$0		\$0	\$121,727
Engineering		\$18,400	\$0	\$0	\$0			\$0			\$18,400
Supply		\$0	\$4,461	\$0	\$0	\$0		\$0		\$0	\$4,461
Building & Additions		\$0	\$17,496	\$0	\$4,000	\$0		\$0		\$0	\$21,496
Cap Equipment		\$0	\$49,406	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$49,406
Non-Cap Equipment		\$0	-\$2,197	\$0	-\$108			\$0		\$0	-\$2,305
Total		\$8,785,459	\$100,007	\$20,582	\$3,892	\$0	\$0	\$0	\$0	\$0	\$8,909,940
Project Budget	\$9,603,782	Received	•								
Less Other Funding*	\$693,842	\$693,842		* Other Fundin	g Source:						
Net	\$8,909,940			Emeritus Colle	ge Foundation	\$693,842 receiv	/ed				
Actual Measure U Expenditures	\$8,909,940				-						
Running Balance	\$0										
ŭ											
U7100006											
1738 Pearl Street (C)											
Site Acquisition		\$0	\$704,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$704,534
Site Improvement		\$0	\$3,250	\$0	\$0		\$0	\$0			\$3,250
Building & Additions		\$0	\$41,424	\$0	\$0			\$0			\$41,424
Total		\$0	\$749,208	\$0	\$0	\$0	\$0	\$0		\$0	\$749,208
Project Budget	\$749,208		,	• -							,
Less Other Funding	\$0										
Net	\$749,208										
Actual Measure U Expenditures	\$749,208										
Running Balance	\$0										
	•										

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100026											
PE Temporary Building Replacement (D)											
Architect		\$148.055	\$42,372	\$6,220	\$485	\$0	\$0	\$0	\$0	\$0	\$197,133
Building & Additions		\$43,866	\$1,922,493	\$415,932		\$0	\$0			\$0	\$2,382,291
Inspection & Testing		\$6,455				\$0	\$0			\$0	\$143,681
Project Management		\$4,800	\$56,247	\$5,225	\$0	\$0	\$0			\$0	\$66,272
Advertising and Moving Expenses		\$763		\$6,893		\$0	\$0		\$0	\$0	\$7,656
Total		\$203,939	\$2,157,622	\$434,987	\$485	\$0			\$0	\$0	\$2,797,033
Project Budget	\$2,797,033										
Less Other Funding	\$0										
Net	\$2,797,033										
Actual Measure U Expenditures	\$2,797,033										
Running Balance	\$0										
-											
U7100310											
Remodel Library Village for Math (E)											
Moving Exp.		\$0		\$0		\$0	\$0			\$0	\$38,625
Building & Additions		\$0		\$115,653		\$0	\$0			\$0	\$1,152,143
Architect		\$104,992		\$1,340		\$0	\$0			\$0	\$133,959
Engineering		\$0		\$0		\$0	\$0			\$0	\$2,658
Inspection & Testing		\$0	\$27,083	\$25,175		\$0	\$0			\$0	\$52,258
Project Management		\$0	\$51,679	\$4,400		\$0	\$0			\$0	\$56,079
Advertising and Moving Expenses		\$207	\$10,137	\$12,623		\$0	\$0	\$0		\$0	\$22,967
Total		\$105,199	\$1,193,813	\$159,191	\$486	\$0	\$0	\$0	\$0	\$0	\$1,458,690
Project Budget	\$1,458,690										
Less Other Funding	\$0										
Net	\$1,458,690										
Actual Measure U Expenditures	\$1,458,690										
Running Balance	\$0										


Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100027											
SM Airport Campus Site Improvements (F)											
Supplies		\$0	\$26,234	\$975	\$5,873	\$0	\$0		\$0		\$33,082
Misc Fees		\$0	\$25	\$0	\$0		\$0	\$0	\$0	\$0	\$34,299
Other Contract Services		\$3,860	\$11,508	\$8,434	\$1,501	\$0	\$0		\$0		\$25,302
Site Improvement		\$0	\$0	\$15,182	\$5,790	\$7,237	\$0		\$0	\$0	\$28,209
Building & Additions		\$0	\$1,495,697	\$1,670,788	\$4,824	\$0	\$0		\$0	\$0	\$3,171,309
Architect		\$104,934	\$500	\$0	\$43,570		\$0		\$0	\$0	\$149,004
Engineering		\$35,000	\$148,304	\$950	\$10,040	\$0	\$0			\$0	\$194,294
Inspection & Testing		\$5,032	\$118,662	\$191,271	\$0		\$0		\$0	\$0	\$314,965
Project Management		\$750	\$155,798	\$38,425	\$1,365		\$0	\$0	\$0	\$0	\$196,558
City Fees, Advertising and Security System		\$16,587	\$1,802	\$327	\$150	\$4,375	\$0	\$0	\$0	\$0	\$23,241
Total		\$166,163	\$1,958,530	\$1,926,352	\$73,113	\$46,106	\$0	\$0	\$0	\$0	\$4,170,264
Project Budget	\$4,170,264										
Less Other Funding	\$0										
Net	\$4,170,264										
Actual Measure U Expenditures	\$4,170,264										
Running Balance	\$0										
U7110027											
SM Airport Campus West Building (G)											
Supply		\$0	\$0	\$17,650	\$28,017	\$0	\$0	\$0	\$0	\$0	\$45,667
Other Contract Services		\$0	\$0	\$0	\$3,576	\$0	\$0	\$0	\$0	\$0	\$3,576
Moving Expenses		\$0	\$0	\$180	\$15,824	\$0	\$0	\$0	\$0	\$0	\$16,004
Building & Additions		\$0	\$0	\$15,037,532	\$1,256,065	\$46,946	\$0	\$0	\$0	\$0	\$16,340,543
Architect		\$0	\$971.954	\$1.043.950	\$49.779	\$1,147	\$0	\$0	\$0	\$0	\$2,066,830
Engineering		\$0	\$2,920	\$9,800	\$5,010	\$963	\$0		\$0	\$0	\$18,693
Inspection & Testing		\$0	\$21,173	\$126,510	\$9,856		\$0		\$0	\$0	\$157,539
Project Management		\$0	\$14,450	\$313,715	\$13,956		\$0	\$0	\$0	\$0	\$342,121
Cap Equipment		\$0	\$49,795	\$326,382	\$4,792		\$0	\$0	\$0	\$0	\$380,969
Non-Cap Equipment		\$0	\$0	\$280,558	\$57,240		\$0		\$0	\$0	\$337,798
Total		\$0		\$17,156,277	\$1,444,115		\$0				\$19,709,741
Project Budget	\$19,709,741	+-1	. ,,	. , ,	.,,,,	, ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,	+-1	<b>*</b> -	, , , , , , , , , , , , , , , , , , ,		, , , , , ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,
Less Other Funding	\$0										
Net	\$19,709,741										
Actual Measure U Expenditures	\$19,709,741										
Running Balance	\$0										
i tanining Dalarioo	ψŬ										

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
										-	
U7100025											
Theatre Arts Renovation (H)											
Supplies		\$0	\$8,904	-\$14	\$12,858	\$16,619	\$0	\$0		\$0	\$38,367
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	
Moving Services		\$0	\$0	\$0	\$0	\$14,061	\$0	\$0	\$0	\$0	\$14,061
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$5,245	\$0	\$0	\$5,245
Rental / Lease		\$0	\$1,446	\$2,200	\$0	\$0	\$0	\$0		\$0	\$3,646
Building & Additions		\$528	\$1,326,630	\$4,540,487	\$10,897,603	\$56,122	\$25,220	\$0	\$0	\$0	\$16,846,590
Architect		\$289,913	\$369,213	\$423,416	\$82,639	\$0	\$0	\$0	\$0	\$0	\$1,165,181
Engineering		\$6,174	\$2,981	\$16,606	\$2,375	\$1,250	\$0	\$0	\$0	\$0	\$29,386
Inspection & Testing		\$150	\$14,785	\$353,890	\$297,675	\$1,116	\$0	\$0	\$0	\$0	\$667,616
Project Management		\$150	\$45,698	\$184,219	\$193,898	\$14,818	\$230	\$0	\$0	\$0	\$439,013
Cleaning, Storage and Installation		\$0	\$812	\$0	\$2,548	\$2,267	\$0	\$0	\$0	\$0	\$5,627
Cap Equipment		\$0	\$31,638	\$0	\$6,458	\$59,689	\$0	\$0		\$0	\$97,785
Non-Cap Equipment		\$0	\$2,388	\$0	\$36,749	\$145,294	\$0	\$0	\$0	\$0	\$184,432
Total		\$296,915	\$1,804,496	\$5,520,804	\$11,532,803	\$311,236	\$25,450	\$5,245	\$0	\$0	
Project Budget	\$19,497,949										
Less Other Funding	\$0										
Net	\$19,497,949										
Actual Measure U Expenditures	\$19,496,949										
Running Balance	\$1,000										
U7100110											
Earthguake Rpl. Liberal Arts North (I)											
Supplies		\$0	\$0	\$0	\$0	\$1,408	\$0	\$75	\$0	\$0	\$1,483
Legal		\$0	\$0	\$0	\$0	\$887	\$0	\$0	\$0	\$0	\$887
Other Contract Services		\$0	\$0	\$0	\$0	\$75	\$0	\$0	\$0	\$0	\$75
Building & Additions		\$265	\$0	\$1,043,660	\$5,916,281	-\$973,001	\$321,345	\$14,898	\$0	-\$834,764	\$5,488,685
Architect		\$0	\$611,732	\$102,824	\$209,490	\$216,563	\$21,215	\$3,465	\$0	\$0	\$1,165,289
Engineering		\$3,248	\$4,295	\$0	\$250	\$0	\$250	\$0	\$0	\$0	\$8,043
Inspection & Testing		\$0	\$0	\$28,312	\$326,203	\$77,942	\$0	\$0	\$0	\$0	\$432,458
Project Management		\$0	\$26,072	\$33,549	\$128,937	\$124,222	\$255	\$1,155		\$0	\$314,475
Advertising and Fees		\$0	-\$4	\$7,334	\$0	\$0	\$0	\$0	\$0	\$0	\$7,330
Cap-Equipment		\$0	\$0	\$0	\$0	\$25,356	\$12,579	\$0		\$0	\$37,935
Non-Cap Equipment		\$0	\$0	\$0			\$4,093	\$0		\$0	\$176,550
Total		\$3,513	\$642,095	\$1,215,679	\$6,583,194	-\$356,123	\$359,737	\$19,592		-\$834,764	\$7,633,209
Project Budget	\$12,507,725	Received	,,,,,,,,	. , .,	, ,		, , -	,			. ,,
Less Other Funding*	\$6,154,973			* Other Fundin	g Source:						
Net	\$6,352,752				Ionica \$4,039,7	53 received					
Actual Measure U Expenditures	\$7,633,209					\$834,764 receiv	ed				
Running Balance	-\$1,280,457			. ,,-		. ,					
	÷ .,= : : ; . • :										

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100013, U7100047	1										
Music Complex (J)											
Advertising		\$0	\$0	\$436	\$0	\$0	\$0	\$0	\$0	\$0	\$436
Supplies		\$0	\$0 \$0	<u>φ+80</u> \$0	\$0	\$194	\$19.094	\$0 \$0	\$0 \$0	\$0 \$0	\$19,288
Consultants		\$0	\$0	\$0			\$36,000	\$0 \$0	\$0 \$0	\$0 \$0	\$36.000
Other Contract Services		\$0	\$0 \$0	\$0			\$180	\$0 \$0	\$0 \$0	\$0 \$0	\$180
Moving Services		\$0	\$0	\$0	\$0	\$0	\$6.330	\$0	\$0	\$0	\$6.330
Building & Additions		\$0	\$0	\$356,464	\$1,293,726	-\$737,213	\$273,531	\$0	\$0	\$0	\$1,186,509
Architect		\$0	\$187,922	\$22,500	\$37,227	\$38,448	\$4,052	\$14,356	\$0	\$681	\$305,186
Engineering		\$0	\$0	\$0		\$0	\$0	\$21,370	\$0	\$0	\$21,370
Inspection & Testing		\$0	\$0	\$29,740		\$26,238	\$35,880	\$0	\$0	\$0	\$111.122
Project Management		\$0	\$170	\$36,739		\$56,914	\$16,200	\$1,288	\$0	\$0	\$147.662
Cap Equipment		\$0	\$0	\$0			\$62,600	\$0	\$0	\$0	\$62,600
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$29,852	\$78,582	\$0	\$0	\$0	\$108,434
Total		\$0	\$188,092	\$445,879			\$532,447	\$37,014	\$0		\$2,005,116
Project Budget	\$4,623,547	Received			, , ,						. ,,
Less Other Funding*	\$2,618,113	\$2,618,113		* Other Fundin	g Source:						
Net	\$2,005,434				ice \$2,618,113	received					
Actual Measure U Expenditures	\$2,005,116										
Running Balance	\$318										
• • •											
U7100111											
Earthquake Rpl. Liberal Arts South (K)											
Supply		\$0	\$0	\$855	\$2,497	\$379	\$23,811	\$75	\$0	\$0	\$27,618
Legal		\$0	\$0	\$0	\$0	\$0	\$2,203	\$50	\$0	\$0	\$2,253
Moving Services		\$0	\$0	\$0	\$0	\$0	\$4,063	\$0	\$0	\$0	\$4,063
Consultants		\$0	\$0	\$0		\$41,435	\$0	\$0	\$0	\$0	\$58,700
Other Contract Services		\$0	\$0	\$6,154	\$202	\$0	\$0	\$0	\$0	\$0	\$6,356
Building & Additions		\$0	\$0	\$26,302	\$3,091,306	\$5,706,802	-\$4,642,459	\$0	\$91,516	\$0	\$4,273,467
Architect		\$0	\$0	\$836,555	-\$503,297	\$163,506	\$183,877	\$39,984	\$2,549	\$0	\$723,174
Engineering		\$0	\$0	\$3,125	\$150	\$5,344	\$500	\$0	\$0	\$0	\$9,119
Inspection & Testing		\$0	\$0	\$0	\$179,798	\$296,015	\$68,273	\$0	\$0	\$0	\$544,086
Project Management		\$0	\$0	\$0	\$43,989	\$262,598	\$52,690	\$1,722	\$1,278	\$0	\$362,276
Cap-Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$58,726	\$45,388	-\$7,074	\$0	\$0	\$97,040
Total		\$0	\$0	\$872,991	\$2,831,909	\$6,534,806	-\$4,261,655	\$34,757	\$95,342	\$0	\$6,108,150
Project Budget	\$16,733,220	Received									
Less Other Funding*	\$10,625,070	\$10,625,070		* Other Fundin	g Source:						
Net	\$6,108,150				,0 Ionica \$6,167,0						
Actual Measure U Expenditures	\$6,108,150			State of Califor	nia \$4,458,000	received					
Running Balance	\$0										

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
					1				1		
U7100221											
Shuttle Replacement Parking (L)			<b>^</b>				<b>6</b> 4 0 47				<b>*</b> 4.047
Supplies		\$0		\$0		\$0	\$1,347	\$0		\$0	\$1,347
Legal		\$0	\$0	\$0		\$35,103	\$0			\$0	\$43,565
Site Acquisition		\$0	\$0	\$0			\$0			\$0	\$16,903,087
Site Improvement		\$0	\$0	\$0			\$0			\$0	\$3,027
Building & Additions		\$0	\$0	\$0			\$1,252,224	\$2,353		\$0	\$1,738,577
Architect		\$0		\$0			\$7,208			\$0	\$58,777
Inspection & Testing		\$0		\$0			\$41,250	\$0		\$0	\$181,072
Project Management		\$0					\$32,425	\$0		\$0	\$40,056
Total		\$0	\$0	\$0	\$8,462	\$17,624,240	\$1,334,455	\$2,353	\$0	\$0	\$18,969,509
Project Budget	\$18,969,509										
Less Other Funding	\$0										
Net	\$18,969,509										
Actual Measure U Expenditures	\$18,969,509										
Running Balance	\$0										
U7100321											
North Quad Plaza (M)											
Legal		\$0		\$0		\$0	\$3,825			\$0	\$9,429
Building & Additions		\$0	\$0	\$0		-\$443	\$6,130,081	\$3,634,487	\$0	\$0	\$9,764,125
Architect		\$0	\$231,055	\$8,444	\$140,048	\$435,618	\$171,225	\$68,633	\$2,901	\$10,483	\$1,068,407
Engineering		\$0	\$0	\$0		\$0	\$0			\$0	\$0
Inspection & Testing		\$0	\$0	\$0		\$0	\$186,220	\$107,477	\$328	\$0	\$294,025
Project Management		\$0	\$0	\$760	\$210	\$2,200	\$135,601	\$55,782	\$606	\$0	\$195,158
Printing		\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,900
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$55,420	\$0	\$0	\$55,420
Total		\$0	\$232,955	\$9,204	\$140,258	\$437,375	\$6,626,952	\$3,927,402	\$3,834	\$10,483	\$11,388,463
Project Budget	\$11,388,463										
Less Other Funding	\$0										
Net	\$11,388,463										
Actual Measure U Expenditures	\$11,388,463										
Running Balance	\$0										

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals	
U7100500, U7126450, U7100334, U7100142												
Student Services Building (O)												
Supplies		\$2,014	\$0	\$0	\$0	\$0	\$0	\$718	\$0	\$0	\$2,732	
PC Upgrades		\$0	\$765	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$765	
Consultants		\$0	\$0		\$0	\$9,334	\$55,693	\$0	\$0	\$0	\$65,027	
Legal		\$0	\$0	\$0	\$0	\$38	\$2,775	\$31,776	\$0	\$0	\$34,588	
Other Contract Services		\$210	\$0	\$0	\$0	\$0	\$17,561	\$17,495	\$18,817	-\$70	\$54,014	
Moving		\$7,571	\$0	\$0	\$0	\$0	\$0	\$616	\$0	\$0	\$8,187	
Building & Additions		\$359,141	\$2,441	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$361,582	
Architect		\$31,782	\$0	\$235,230	\$0	\$43,992	\$0	\$690,099	\$208,521	\$38,643	\$1,248,268	
Engineering		\$1,838	\$0	\$0	\$0	\$0	\$0	\$6,205	\$27,363	\$3,171	\$38,576	
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$25,670	\$34,687	\$0	\$0	\$60,358	
Project Management		\$4,650	\$0	\$2,470	\$0	\$1,100	\$0	\$124,148	\$0	\$0	\$132,368	
Cap Equipment		\$59,063	\$0	\$0	\$0	\$0	\$8,745	\$8,056	\$0	\$0	\$75,864	
Total		\$466,268	\$3,207	\$237,700	\$0	\$54,464	\$110,445	\$913,802	\$254,701	\$41,744	\$2,082,330	
Project Budget	\$53,521,913	Received										
Less Other Funding*	\$32,705,717											
Net	\$20,816,196			District Capital	Funds \$10,208	,069 commited						
Actual Measure U Expenditures	\$2,082,330											
Running Balance	\$18,733,866											

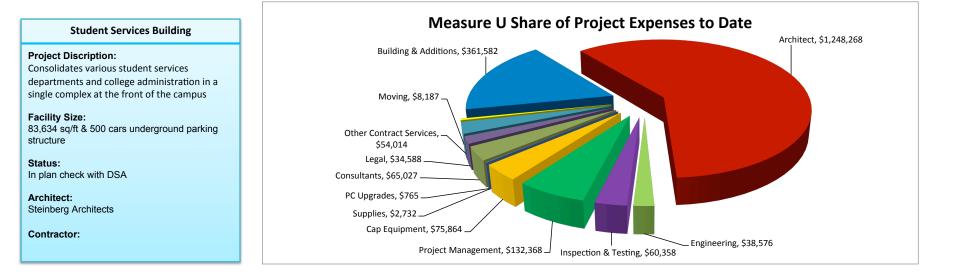

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100090											
Science Complex Additional (P)											
Architect		\$0	\$0	\$0	\$0	\$246,425	\$61,911	\$0	\$0	\$0	\$308,336
Total		\$0	\$0	\$0	\$0	\$246,425	\$61,911	\$0	\$0	\$0	\$308,336
Project Budget	\$308,336								-		
Less Other Funding	\$0										
Net	\$308,336										
Actual Measure U Expenditures	\$308,336										
Running Balance	\$0										
U6780000, U7100022, U7100331, U7100550,											
U7100005, U7100030, U7100031, U7100029,											
U7100003, U7100008, U7100332, U7100072,											
U7100042, U7100056, U7100039											
Infrastructure & Safety (Q)											
Supplies		\$0	\$0	\$254	\$0	\$0		\$1,700	\$1,393	\$0	\$3,347
Consultants		\$0	\$0	\$0	\$0	\$0		\$16,734	\$0	\$0	\$16,734
Maintenance Agreement		\$0	\$0	\$0	\$0			\$0	\$0	\$14,673	\$14,673
Legal		\$0	\$0	\$0	\$0			\$3,294	\$0	\$0	\$6,821
Other Contract Services		\$0	\$0	\$0	\$0			\$81,445	\$203,383	\$3,320	\$295,973
Building & Additions		\$681,900	\$195,175	\$20,600	\$0		\$733	\$0	\$0	\$0	\$1,099,028
Architect		\$69,081	\$42,108	\$0	\$155,321	\$448,507	\$91,127	\$4,227	\$0	\$0	\$810,370
Engineering		\$8,050	\$0	\$0	\$6,750	\$12,000	\$18,429	\$2,360	\$0	\$0	\$47,589
Inspection & Testing		\$2,241	\$4,250	\$0	\$0	\$0		\$0	\$0	\$0	\$12,298
Project Management		\$0	\$2,805	\$0	\$0	\$3,520	\$1,840	\$38	\$196	\$0	\$8,399
Cap Equipment		\$0	\$0	\$343,861	\$0	\$0		\$895,171	\$349,531	\$40,002	\$1,628,565
Non-Cap Equipment		\$0	\$0	\$0	\$0			\$0	\$4,216	\$0	\$4,216
Advertising		\$0	\$785	\$0	\$0			\$0	\$0	\$0	\$785
Total		\$761,272	\$245,122	\$364,715	\$162,071	\$664,647	\$129,287	\$1,004,968	\$558,718	\$57,995	\$3,948,796
Project Budget	\$4,030,284										
Less Other Funding	\$0										
Net	\$4,030,284										
Actual Measure U Expenditures	\$3,948,796										
Running Balance	\$81,488										

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
U7100007											
Restroom Improvement (R)											
Supplies		\$0	\$564	\$0	\$1,075	\$0	\$0	\$0	\$0	\$0	\$1,639
Other Contract Services		\$0	\$0	\$0	\$3,803	\$0 \$0	\$0	\$0		\$0	\$3,803
Building & Additions		\$0	\$1,305	\$0	\$7,891	\$0	\$0	\$0		\$0	\$9,196
Inspection & Testing		\$0	\$2,043	\$0	\$820	\$0	\$0	\$0		\$0	\$2,863
Total		\$0	\$3,912	\$0		\$0	\$0			\$0	\$17.501
Project Budget	\$17,501										
Less Other Funding	\$0										
Net	\$17,501										
Actual Measure U Expenditures	\$17,501										
Running Balance	\$0										
	, +·										
U7100004. U7110020			[						I		
Master Planning (S)											
Consultants		\$9,000	\$26,516	\$158,449	\$374,329	\$125,404	\$17,998	\$363,342	\$0	\$0	\$1,075,038
Architect		\$0	\$17,617	\$126,433	\$104,083	\$126,701	\$346,827	\$276,985	\$0 \$0	\$0 \$0	\$998,647
Rental / Lease		\$0	\$0	\$6,453	\$0	\$0	\$0	\$0		\$0 \$0	\$6,453
Postage		\$0	\$0 \$0	\$30,000	\$0	\$0 \$0	\$0	\$0	\$0	\$0 \$0	\$30,000
Reimbursement to SMC		\$0	\$0	\$0	\$180	\$0 \$0	\$0	\$0 \$0		\$0 \$0	\$180
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$113		\$0	\$113
Total		\$9,000	\$44,133	\$321,335	\$478,593	\$252,105	\$364,825	\$640,439		\$0	\$2,110,430
Project Budget	\$2,110,430	++,	÷ .,	<i>+,</i>	<b>,</b> , .,	<i> </i>	<i>+•••</i> ,•=•	<i>,</i>		+-	<i>,</i> ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,
Less Other Funding	\$0										
Net	\$2,110,430										
Actual Measure U Expenditures	\$2,110,430										
Running Balance	\$0										
· · · · · · · · · · · · · · · · · · ·	, , , , , , , , , , , , , , , , , , ,										
U7100024											
14th and Pico Project (T)											
Consultants		\$0	\$888	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$888
Architect		\$258,601	\$47,343	\$0	\$0	\$0	\$0	\$0		\$0	\$305,944
Inspection & Testing		\$12,070	\$0	\$0	\$0	\$0 \$0	\$0	\$0	\$0	\$0 \$0	\$12,070
Project Management		\$0	\$340	\$0	\$0	\$0	\$0	\$0		\$0	\$340
Total		\$270,671	\$48,571	\$0			\$0			\$0	\$319,242
Project Budget	\$319,242		+,5. 1	֥	֥	ţ,	֥	ţ.	<b>*</b> *	ţ.	÷ • • • • • • • • •
Less Other Funding	\$0										
Net	\$319,242										
Actual Measure U Expenditures	\$319,242										
Running Balance	\$0										
	ц ФФ	l.									
Grand Total		\$11.068.400	\$10.432.055	\$28,685,697	\$54,940,416	\$25,278,771	\$5,283,853	\$6,585,573	\$912,880	-\$723,860	\$142,463,786
		<i><i><i>w</i>11,000,400</i></i>	÷10,402,300	<i>~_0,000,001</i>	<i>~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~~</i>	<i>~20,210,111</i>	<i>40,200,000</i>	<i>40,000,010</i>	<b>\$512,500</b>	-4120,000	ψιτε,του,/00

Note: Project N had no expenses

# SANTA MONICA COMMUNITY COLLEGE DISTRICT

# Measure S Project Schedule As of June 30, 2011


	Project Name	Completion	20	10			201	1	20 <sup>,</sup>	12		2	2013	2	2014	ļ
1	Athletic Fields Phase I, Corsair Field	Completed														
1A	Athletic Fields Phase I, John Adams	Completed														
2	Performing Arts Center	Completed														
3	Career Opportunity Center	Move to AA														
4	Replacement Health/PE/Fitness Building	September 2014					,	·								
5	Early Childhood Development/Childcare	In Planning														
6	Malibu Site Acquisition and Facility	Not Scheduled														
7	Energy Efficiency Projects	On-Going														
8	Satellite Campus Parking Facilities and Roadway Improvements	Completed														
9	Parking Garage, Grounds and Equipment - Student Services	October 2014					, i	, i								
10	Pico Promenade Improvements	Completed														
11	Master Planning	On-Going														
12	Other Bond Related Expenses	On-Going														
13	Adv. Architecture Related Exp for AA	Completed														
14	Real Property Acquisition	On-Going														
15	Signage Safety/Information	On-Going														
			In	Plar	nnir	ng			In (	Con	stru	uctic	n			

# SANTA MONICA COMMUNITY COLLEGE DISTRICT


#### Measure S Bond Budget

As of June 30, 2011


	Project Name	Completion	Project Budget	Measure S Allocation	Other Funding	Measure S Expenditures as of 6/30/11	Measure S Expenditures as of 3/31/11	Measure S Expenditures Last Period	Total Measure S Remaining
1	Athletic Fields Phase I, Corsair Field	Completed	\$4,440,768	\$4,373,238	\$67,530	\$4,372,535	\$4,372,535	\$0	\$703
1A	Athletic Fields Phase I, John Adams	Completed	\$2,970,807	\$2,970,807	\$0	\$2,969,807	\$2,969,807	\$0	\$1,000
2	Performing Arts Complex	Completed	\$40,603,541	\$37,610,965	\$2,992,576	\$37,610,571	\$37,608,541	\$2,030	\$394
3	Career Opportunity Center	Move to AA	\$0	\$0	\$0	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	September 2014	\$40,200,333	\$4,816,093	\$35,384,240	\$772,976	\$772,976	\$0	\$4,043,117
5	Early Childhood Development/Childcare	In Planning	\$11,318,000	\$7,000,000	\$4,318,000	\$10,446	\$10,446	\$0	\$6,989,554
6	Malibu Site Acquisition and Facility	Not Scheduled	\$31,069,031	\$25,000,000	\$6,069,031	\$5,233,682	\$5,230,992	\$2,690	\$19,766,318
7	Energy Efficiency Projects	On-Going	\$1,293,570	\$1,076,248	\$217,322	\$293,361	\$293,361	\$0	\$782,887
8	Satellite Campus Parking Facilities and Roadway Improvements	Completed	\$4,875,000	\$4,875,000	\$0	\$3,820,983	\$3,820,689	\$294	\$1,054,017
9	Parking Garage, Grounds and Equipment - Student Services	October 2014	\$53,143,653	\$52,690,653	\$453,000	\$14,668,516	\$14,598,721	\$69,795	\$38,022,137
10	Pico Promenade Improvements	Completed	\$1,018,009	\$1,018,009	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	On-Going	\$750,000	\$750,000	\$0	\$708,583	\$708,583	\$0	\$41,417
12	Other Bond Related Expenses	On-Going	\$662,764	\$662,764	\$0	\$114,917	\$97,403	\$17,514	\$547,847
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	On-Going	\$50,000	\$50,000	\$0	\$45,597	\$45,597	\$0	\$4,403
15	Signage Safety/Information	On-Going	\$606,223	\$606,223	\$0	\$236,289	\$222,732	\$13,557	\$369,934
	Project Totals		\$193,001,699	\$143,500,000	\$49,501,699	\$71,876,272	\$71,770,392	\$105,880	\$71,623,728

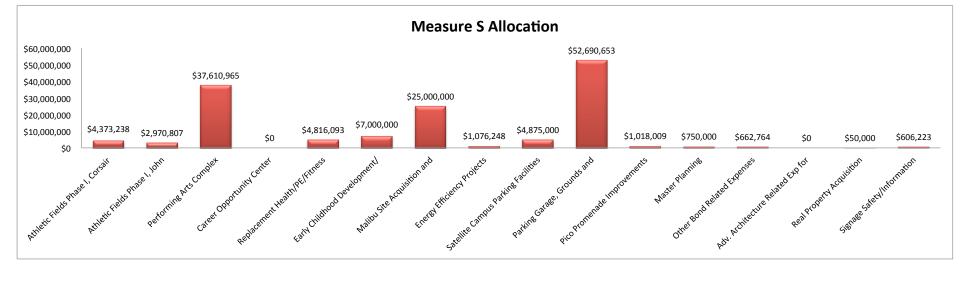

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100019									
Athletic Field Phase I, Corsair Field (1)									
Legal		\$0	\$0	\$0	\$301	\$175	\$0	\$0	\$476
Building & Additions		\$0	\$0	\$0	\$300,380	\$2,579,095	\$0	\$0	\$2,879,475
Architect		\$27,332	\$43,815	\$197,557	\$252,736	\$279,173	\$26,563	\$0	\$827,176
Inspection & Testing		\$0	\$0	\$0	\$23,411	\$57,585	\$640	\$296	\$81,932
Project Management		\$0	\$0	\$0	\$9,871	\$42,374	\$565	\$0	\$52,810
Cap Equipment		\$0	\$0	\$0	\$0	\$483,017	\$35,271	\$0	\$518,288
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$2,066	\$10,312	\$0	\$12,378
Total		\$27,332	\$43,815	\$197,557	\$586,699	\$3,443,485	\$73,350	\$296	\$4,372,535
Project Budget	\$4,440,768	Received						-	
Less Other Funding*	\$67,530	\$67,530							
Net	\$4,373,238		* Other Funding	g Source:					
Actual Measure S Expenditures	\$4,372,535		Metropolitan W	ater District \$6	7,530 received				
Running Balance	\$703								

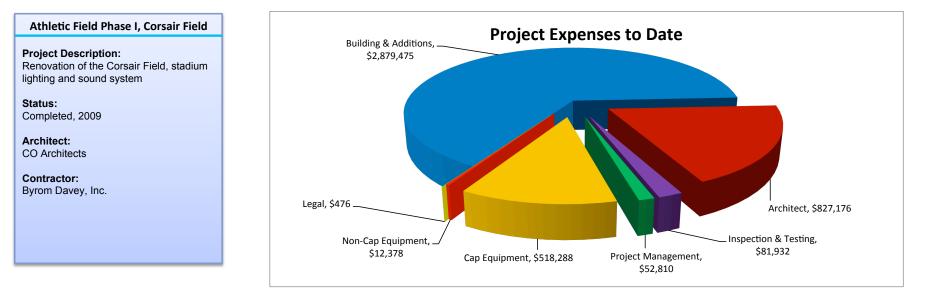

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100038									
Athletic Field Phase I, John Adams (1A)									
Legal		\$0	\$0	\$0	\$75	\$0	\$0	\$0	\$75
Building & Additions		\$0	\$0	\$0	\$16,556	\$1,395,261	\$0	\$0	\$1,411,817
Architect		\$0	\$5,807	\$93,941	\$12,150	\$31,818	\$0	\$0	\$143,715
Inspection & Testing		\$0	\$2,874	\$3,207	\$0	\$49,984	\$0	\$0	\$56,066
Project Management		\$0	\$0	\$0	\$10,921	\$45,170	\$38	\$0	\$56,128
Cap Equipment		\$0	\$0	\$0	\$0	\$1,290,672	\$0	\$0	\$1,290,672
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$11,334	\$0	\$0	\$11,334
Total		\$0	\$8,681	\$97,148	\$39,701	\$2,824,239	\$38	\$0	\$2,969,807
Project Budget	\$2,970,807								
Less Other Funding	\$0								
Net	\$2,970,807								
Actual Measure S Expenditures	\$2,969,807								
Running Balance	\$1,000								

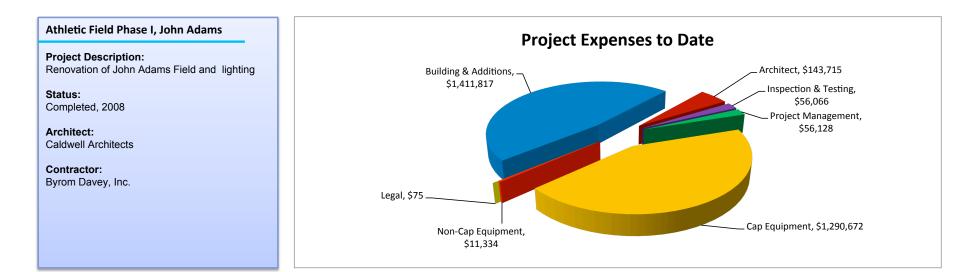

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	Combined Totals						
								-				
57100012												
Performing Arts Center (2)												
Consultants		\$0	\$0	\$0	\$121,790		\$0	\$0	\$198,429			
Other Contract Services		\$0	\$0	\$4,269	\$0	\$22,729	\$22	\$68	\$27,088			
Supplies		\$0	\$0	\$0	\$14,565	\$5,810	\$0	\$0	\$20,375			
egal		\$0	\$0	\$34,329	\$275,667	\$492,731	\$15,629	\$0	\$818,356			
Advertising		\$0										
Building & Additions		\$7,784,151										
Architect		\$0										
Engineering		\$0	\$3,600		\$1,500	\$9,650	\$0	\$0	\$20,000			
nspection & Testing		\$104,308	\$722,685	\$411,193	\$210,381	\$22,256	\$0	\$0	\$1,470,823			
Project Management		\$31,984	\$155,732	\$248,876		\$47,915	\$3,244	\$0	\$751,441			
Cap Equipment		\$0	\$0	\$130,218	\$292,565	\$342,693	\$0	\$0	\$765,476			
Ion-Cap Equipment		\$0	\$0	\$15,124	\$93,106	\$220,455	\$0	\$0	\$328,685			
otal		\$7,920,443	\$11,986,315	\$9,962,528	\$4,677,797	\$2,992,455	\$69,003	\$2,030	\$37,610,571			
Project Budget	\$40,603,541	Received										
ess Other Funding*	\$2,992,576	\$2,992,576	S S S S S S S S S S S S S S S S S S S									
let	\$37,610,965			Madison Project	ct Foundation \$	52,992,576 rece	eived					
Actual Measure S Expenditures	\$37,610,571											
Running Balance	\$394											

# Performing Arts Center


# Project Description:

Construction of a state-of-the-art 499 seat performing arts theater

Status: Completed, 2008

Architect: Renzo Zecchetto


Contractor: FTR International

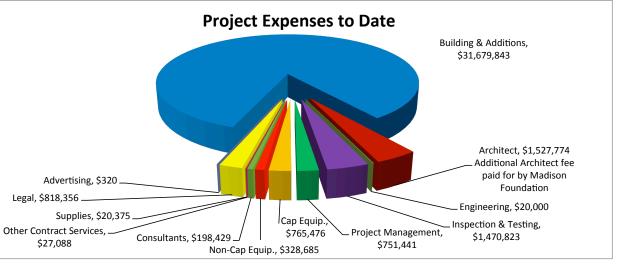

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100033, S7100144	-					1	г г		
Replacement Health/PE/Fitness Building (4)									
Supplies		\$0	\$0	\$0	\$0	\$0	\$163	\$0	\$163
Legal		\$0 \$0	\$0 \$0	\$0 \$0	\$0			\$0 \$0	
Other Contract Services		\$1,634	\$25,934	\$0 \$0	\$0			\$0 \$0	
Repair Facility		\$0	\$4,861	\$0 \$0	\$0			\$0 \$0	
Supplies		\$4,809	\$288	\$0 \$0	\$0			\$0	
Building & Additions		\$0 \$0	<u>پ200</u> \$0	\$0 \$0	\$0			\$0 \$0	
Architect		\$0 \$0	\$0 \$0	\$0 \$0	\$0			\$0 \$0	
Inspection & Testing		\$0 \$0	\$0 \$0	\$0 \$0	\$0			\$0 \$0	\$20,881
Project Management		\$0 \$0	\$0 \$0		\$0			\$0 \$0	\$32,495
Total		\$6,443	\$31,083	\$0 \$0				\$0 \$0	
Project Budget	\$40,200,333		φ <b>31,00</b> 3	ψŪ	ψυ	\$125,005	\$003,707	ψŪ	\$112,510
Less Other Funding*	\$35,384,240			* Other Fundin	a Source:				
Net	\$4,816,093			Measure AA \$3		nated			
Actual Measure S Expenditures	\$772,976			Measure AA at	5,504,240 allu	JCaleu			
Running Balance	\$4,043,117								
	\$4,043,117								
S7100045									
Early Childhood Development/Childcare (5)									
Consultants		\$0	\$0	\$0	\$9,200	\$0	\$0	\$0	\$9,200
Project Management		\$0	\$0	\$0	\$0			\$1,246	
Total		\$0			\$9,200			\$1,246	
Project Budget	\$11,318,000	Received		· · ·					
Less Other Funding*	\$4,318,000			* Other Fundin	a Source:				
Net	\$7,000,000			City of Santa M		000 commited			
Actual Measure S Expenditures	\$10,446			- · <b>,</b> - · · ·	, ,,				
Running Balance	\$6,989,554								
	, - , ,	I							
S7100077, S7100015									
Malibu Site Acquisition and Facilities (6)									
Consultants		\$0	\$0		\$0			\$0	
Legal		\$0	\$27,722	\$16,787	\$6,159		\$0	\$0	
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Architect		\$0	\$0	\$0	\$0			\$0	
Inspection & Testing		\$4,388	\$3,750	\$141,462	\$0	\$0		\$0	
Project Management		\$0	\$0	\$220	\$0			\$2,690	\$2,910
Other Contract Services		\$0	\$0		\$0			\$0	
Storm/Waste Water Treatment Center		\$0	\$2,500,000	\$0	\$0	\$2,500,000	\$0	\$0	
Total		\$4,388			\$6,159		\$0	\$2,690	\$5,233,682
Project Budget	\$31,069,031			· · ·					
Less Other Funding*	\$6,069,031			* Other Fundin	g Source:				
Net	\$25,000,000			Measure AA \$6		ated			
Actual Measure S Expenditures	<b>AF</b> 000 000				. ,				
	\$5,233,682								

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
07/000/0 07/00000						1			
S7100043, S7100066									
Energy Efficiency Projects (7)		<u> </u>	<u> </u>	¢0	<u> </u>	¢000	<b>*</b> 0	<b>*</b> 0	¢000
Legal		\$0 \$0	\$0		\$0 \$0		\$0	\$0	\$988
Building & Additions		\$0	\$0	\$0		1 ] -	\$355,294	-\$180,342 \$0	\$281,873
Engineering		\$0	\$0 \$0	\$0		\$0	\$0		\$10,500
Inspection & Testing		\$0	\$0 \$0				\$0	\$0 \$0	\$0 \$0
Project Management Total		\$0 <b>\$0</b>	\$0 <b>\$0</b>	\$0 <b>\$0</b>	\$0		\$0		τ. <del>.</del>
	¢4 000 570		\$U	\$0	\$10,500	\$107,910	\$355,294	-\$180,342	\$293,361
Project Budget Less Other Funding*	\$1,293,570 \$217,322	Received \$217,322		* Other Fundin	a Couroo				
Net		\$217,322		* Other Fundin SCE & The Ga		Oreceived			
Actual Measure S Expenditures	\$1,076,248 \$293,361			SUE & THE Ga	S CO. \$217,32	z received			
Running Balance	\$782,887								
S7100091, S7100092									
Satellite Campus Parking Facilities and Roadway I	mprovements (	8)							
Legal		\$0	\$0		\$300	\$175	\$0	\$0	\$475
Other Contract Services		\$0	\$0	\$0	\$300	\$0	\$0	\$0	\$300
Advertising		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Supplies		\$0	\$0	\$0	\$0		\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$278,178	\$1,860,152	\$449,543	\$37,777	\$2,625,651
Architect		\$0	\$0	\$324,919	\$324,864	\$136,911	\$34,490	\$1,397	\$822,582
Inspection & Testing		\$0	\$0	\$0		\$185,947	\$28,218	\$360	\$245,626
Project Management		\$0	\$0			\$64,880	\$31,137	\$8,659	\$122,964
Non-Cap Equipment		\$0	\$0		1 -		\$3,387	\$0	\$3,387
Total		\$0	\$0	\$324,919	\$653,031	\$2,248,065	\$546,775	\$48,194	\$3,820,983
Project Budget	\$4,875,000								
Less Other Funding	\$0								
Net	\$4,875,000								
Actual Measure S Expenditures	\$3,820,983								
Running Balance	\$1,054,017								

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals				
S7100142													
Parking Garage and Grounds - Student Services (9	)												
Supplies		\$0	\$0	\$0	\$0	\$1,745	\$0	\$0	\$1,745				
Consultants		\$0	\$0	\$0	\$0	\$20,700	\$0	\$0	\$20,700				
Legal		\$0	\$0 \$0 \$0 \$2,154 \$17,486 \$4,337 \$										
Other Contract Services		\$0	\$0	\$0 \$0 \$1,508 \$10,952 \$1,863									
Building & Additions		\$0	\$0 \$0 \$2,555,940 \$5,925,152 \$1,447 \$8,48										
Architect		\$0	\$0	\$0	\$2,266,766	\$2,674,054	\$0	\$33,778	\$4,974,598				
Engineering		\$0	\$0	\$0	\$0	\$4,813	\$38,330	\$42,968	\$86,110				
Inspection & Testing		\$0	\$0	\$0	\$0	\$131,009	\$161,847	\$50,305	\$343,161				
Project Management		\$0	\$0	\$0	\$0	\$158,766	\$373,559	\$174,645	\$706,970				
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$14,393	\$0	\$14,393				
Total		\$0	\$0	\$0	\$2,266,766	\$5,550,689	\$6,541,719	\$309,342	\$14,668,516				
Project Budget	\$53,143,653	Received											
Less Other Funding*	\$453,000	\$0											
Net	\$52,690,653			State of Califor	nia \$453,000 a	llocated							
Actual Measure S Expenditures	\$14,668,516												
Running Balance	\$38,022,137												

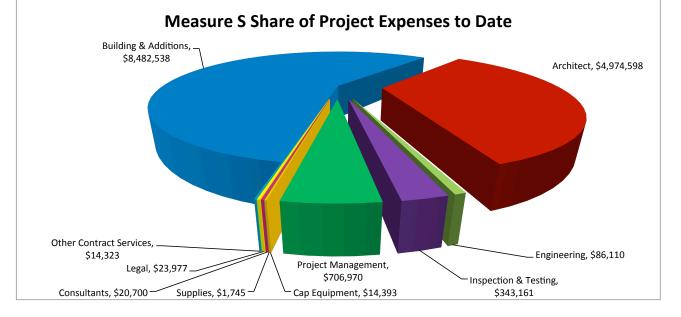

# Parking Garage and Grounds - Student Services

# Project Description:

Consolidates various student services departments and college administration in a single complex at the front of the campus

# Facility Size:

83,634 sq/ft & 500 cars underground parking structure

Status: Phase 1 completed Phase 2 in plan check with DSA

Architect: Steinberg Architects

Contractor:

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
1-									
S7100044									
Pico Promenade Improvements (10)									
Building & Additions		\$0	\$0	\$0	\$690		\$0	\$0	\$884,091
Architect		\$0	\$0	\$0	\$69,190		\$864	\$0	
Inspection & Testing		\$0	\$0	\$0	\$0		\$0	\$0	\$7,591
Project Management		\$0	\$0	\$0	\$2,185	\$25,548	\$0	\$0	\$27,733
Total		\$0	\$0	\$0	\$72,066	\$945,080	\$864	\$0	\$1,018,009
Project Budget	\$1,018,009								
Less Other Funding	\$0								
Net	\$1,018,009								
Actual Measure S Expenditures	\$1,018,009								
Running Balance	\$0								
S7100004					1	1			
Master Planning (11)									
Consultants		\$0	\$0	\$0	\$0	\$0	\$441,549	\$13,320	\$454,869
Printing		\$0 \$0	\$0	\$0		\$0	\$4,157	<u>φ13,320</u> \$0	\$4,157
Advertising		\$0 \$0	\$0	\$0	\$0		\$3,000	\$0 \$0	\$3,000
Other Contract Services		\$0 \$0	\$0	\$0	\$0	\$0		\$200	\$642
Architect		\$0 \$0	\$0 \$0	\$0		\$0		\$24,736	\$217,094
Project Management		\$0 \$0	\$0 \$0	\$0	\$0	\$0		\$9,341	\$25,979
Filling Fees		\$0 \$0	\$0 \$0	\$0	\$0	\$0	\$0	\$2,842	\$2,842
Total		\$0	\$0	\$0	\$0		\$658,143	\$50,439	
Project Budget	\$750.000	<b>*</b> •1	<u><u></u></u>	÷.	<b>\$</b>	, <del>, , ,</del> ,	<i>vvvvvvvvvvvvv</i>	400,100	\$100,000
Less Other Funding	\$0								
Net	\$750,000								
Actual Measure S Expenditures	\$708,583								
Running Balance	\$41,417								
	φ,								
S7100048									
Other Bond Related Expenses (12)									
Supplies		\$0	\$0	\$0			\$3,638	\$0	\$3,638
Legal		\$0	\$0	\$0	\$0	\$0	\$8,917	\$11,469	\$20,386
Software License		\$0	\$0	\$0	\$0		\$0	\$1,997	\$1,997
Advertising		\$0	\$0	\$0	\$0		\$2,278	\$0	\$2,278
Other Contract Services		\$0	\$0	\$0			\$17,206	\$23,342	\$42,348
Moving Services		\$0	\$0	\$0		\$0	\$400	\$0	\$400
Project Management		\$0	\$0	\$0	\$0	\$0		\$13,179	
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$10,086	\$10,086
Non-Cap Equipment		\$0	\$0	\$0				\$2,860	
Total		\$0	\$0	\$0	\$0	\$1,800	\$50,185	\$62,932	\$114,917
Project Budget	\$662,764								
Less Other Funding	\$0								
Net	\$662,764								
Actual Measure S Expenditures	\$114,917								
Running Balance	\$547,847								

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100049									
Adv Architecture Related Exp for AA (13)									
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0				\$0	\$0	\$0
Architect		\$0	\$0		\$0		\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0		\$0	\$0	\$0
Inspection & Testing		\$0	\$0		\$0		-\$45,734	\$0	\$0
Project Management		\$0	\$0		\$0		\$0	\$0	\$0
Total		\$0	\$0	\$0	\$0	\$45,734	-\$45,734	\$0	\$0
Project Budget	\$0								
Less Other Funding	\$0	l							
Net	\$0	i i							
Actual Measure S Expenditures	\$0	l							
Running Balance	\$0	i							
					-				
S7100057		į							
Real Property Acquisition (14)									
Other Contract Services		\$0	\$0				. ,	\$0	\$18,721
Architect		\$0	\$0		\$0		\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0		\$6,336	\$0	\$6,336
Project Management		\$0	\$0		\$0	\$0	\$20,540	\$0	\$20,540
Total		\$0	\$0	\$0	\$0	\$0	\$45,597	\$0	\$45,597
Project Budget	\$50,000	1							
Less Other Funding	\$0	l							
Net	\$50,000	i							
Actual Measure S Expenditures	\$45,597	l							
Running Balance	\$4,403	l							

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11	Combined Totals
S7100072									
Campus Signage (15)									
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$303	\$303
Consultants		\$0	\$0	\$0	\$0	\$0	\$32,225	\$23,725	\$55,950
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$187	\$187
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$638	\$638
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$22,953	\$22,953
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$156,258	\$156,258
Total		\$0	\$0	\$0	\$0	\$0	\$32,225	\$204,064	\$236,289
Project Budget	\$606,223			_					
Less Other Funding	\$0								
Net	\$606,223								
Actual Measure S Expenditures	\$236,289								
Running Balance	\$369,934								

Grand Total	\$7,958,606	\$14,601,366	\$10,740,621	\$8,321,918	\$20,819,624	\$8,933,245	\$500,891	\$71,876,271


Note: Project 3 had no expenses

# SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Project Schedule As of June 30, 2011

	Project Name	Completion	2	2010		20	011	201	2	2	013	20	14	2015	20	16
101	Environmental Performance - Central Plant Connections	September 2014														
102	Infrastructure & Technology - Information Technology Relocation	February 2014														
103	Media and Technology Complex - Academy Site	September 2014														
104	Replacement Health/PE/Fitness/Dance Building with Central Plant	September 2014														
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	December 2016											•			
106	Replacement Math and Science Extension Building	December 2016														
107	Madison East Wing Seismic Upgrade	August 2013														
108	Renovation of Corsair Stadium	Not Scheduled														
109	Career Opportunity and Advancement Center (Bundy)	Not Scheduled														
110	Malibu Center	Not Scheduled														
111	Business & Facilities Infrastructure	On-Going														
112	Master Planning, Program Management, Overhead	On-Going														
113	Energy Efficiency Projects	On-Going														
114	Community Classroom & Facility Projects	December 2011														
115	Real Property Acquisition	On-Going														
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	On-Going														
					In P	lann	ing	In C	onsti	uctio	n					


#### SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget As of June 30, 2011

	Project Name	Completion	Project Budget	Measure AA Allocation	Other Funding	Measure AA Expenditures as of 6/30/11	Measure AA Expenditures as of 3/31/11	Measure AA Expenditures Last Period	Total Measure AA Remaining
101	Environmental Performance - Central Plant Connections	September 2014	\$4,882,119	\$4,882,119	\$0	\$62,550	\$51,132	\$11,418	\$4,819,569
102	Infrastructure & Technology - Information Technology Relocation	February 2014	\$13,287,218	\$13,287,218	\$0	\$586,547	\$376,009	\$210,538	\$12,700,671
103	Media and Technology Complex - Academy Site	September 2014	\$61,480,824	\$57,700,824	\$3,780,000	\$5,015,125	\$4,881,617	\$133,508	\$52,685,699
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	September 2014	\$40,200,333	\$35,384,240	\$4,816,093	\$1,846,819	\$1,234,609	\$612,210	\$33,537,421
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	December 2016	\$34,026,480	\$34,026,480	\$0	\$0	\$0	\$0	\$34,026,480
106	Replacement Math and Science Extension Building	December 2016	\$108,103,000	\$68,259,000	\$40,134,000	\$0	\$0	\$0	\$68,259,000
107	Madison East Wing Seismic Upgrade	August 2013	\$12,292,000	\$12,292,000	\$0	\$619,810	\$467,035	\$152,775	\$11,672,190
108	Renovation of Corsair Stadium	Not Scheduled	\$11,203,000	\$11,203,000	\$0	\$35,299	\$13,714	\$21,585	\$11,167,701
109	Career Opportunity and Advancement Center (Bundy)	Not Scheduled	\$41,391,000	\$29,384,000	\$12,007,000	\$0	\$0	\$0	\$29,384,000
110	Malibu Center	Not Scheduled	\$31,069,031	\$6,069,031	\$25,000,000	\$0	\$0	\$0	\$6,069,031
111	Business & Facilities Infrastructure	On-Going	\$6,140,952	\$6,140,952	\$0	\$133,238	\$130,172	\$3,066	\$6,007,714
112	Master Planning, Program Management, Overhead	On-Going	\$1,650,000	\$1,650,000	\$0	\$0	\$0	\$0	\$1,650,000
113	Energy Efficiency Projects	On-Going	\$4,650,136	\$4,150,136	\$0	\$0	\$0	\$0	\$4,150,136
114	Community Classroom & Facility Projects	December 2011	\$3,221,000	\$3,221,000	\$0	\$577,172	\$288,970	\$288,202	\$2,643,828
115	Real Property Acquisition	On-Going	\$6,000,000	\$6,000,000	\$0	\$5,757,895	\$5,781,653	-\$23,758	\$242,105
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	On-Going	\$350,000	\$350,000	\$0	\$251,152	\$240,787	\$10,365	\$98,848
117	Infrastructure & Technology - Technology	On-Going	\$500,000	\$500,000	\$0	\$216,896	\$216,896	\$0	\$283,104
118	Infrastructure & Technology - Utility	On-Going	\$500,000	\$500,000	\$0	\$20,219	\$2,760	\$17,459	\$479,781
	Project Totals		\$380,947,093	\$295,000,000	\$85,737,093	\$15,122,722	\$13,685,354	\$1,437,368	\$279,877,278

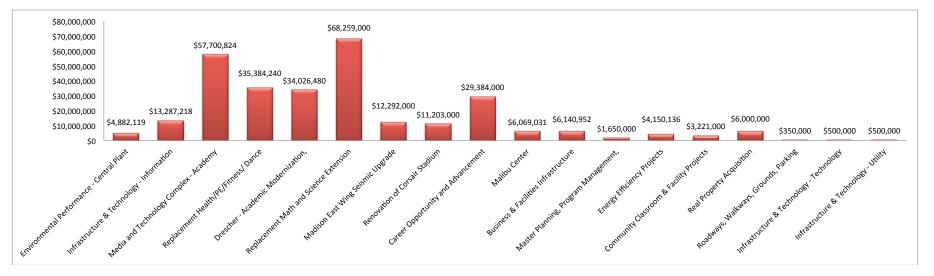


Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100062				
Environmental Performance - Central Plant Connections (101)				
Legal		\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0
Consultants		\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0
Architect		\$0	\$385	\$385
Engineering		\$48,500	\$0	\$48,500
Inspection & Testing		\$0	\$0	\$0
Project Management		\$0	\$13,665	\$13,665
Cap Equipment		\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0
Total		\$48,500	\$14,050	\$62,550
Project Budget	\$4,882,119			
Less Other Funding	\$0			
Net	\$4,882,119			
Actual Measure AA Expenditures	\$62,550			
Running Balance	\$4,819,569			


Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100063				
Infrastructure & Technology - IT Relocation (102)				
Legal		\$0	\$0	\$0
Consultants		\$0	\$0	\$0
Supplies		\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0
Architect		\$105,049	\$355,748	\$460,797
Inspection & Testing		\$10,291	\$8,468	\$18,759
Project Management		\$33,460	\$73,532	\$106,992
Cap Equipment		\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0
Total		\$148,800	\$437,747	\$586,547
Project Budget	\$13,287,218			
Less Other Funding	\$0			
Net	\$13,287,218			
Actual Measure AA Expenditures	\$586,547			
Running Balance	\$12,700,671			

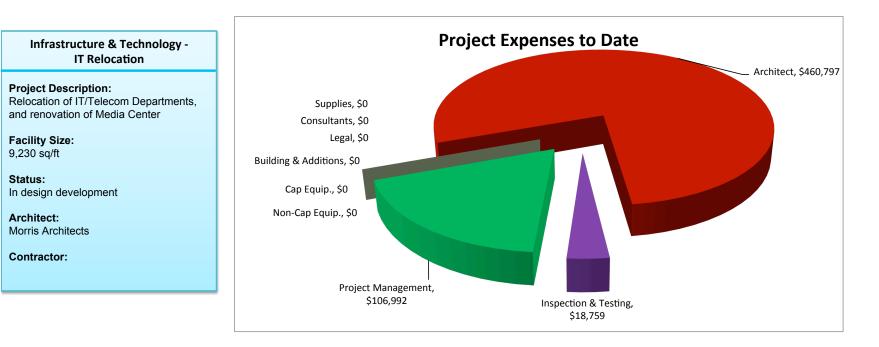


Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100061				
Media and Technology Complex - Academy Site (103)				
Consultants		\$0	\$0	\$0
Supplies		\$0	\$0	\$0
Legal		\$16,903	\$0	\$16,903
Other Contract Services		\$3,993	\$5,446	\$9,439
Advertising		\$0	\$0	\$0
Building & Additions		\$0	\$538	\$538
Architect		\$2,097,553	\$2,408,588	\$4,506,141
Engineering		\$16,459	\$26,553	\$43,012
Inspection & Testing		\$64,905	\$22,628	\$87,533
Project Management		\$121,786	\$229,773	\$351,558
Cap Equipment		\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0
Total		\$2,321,599	\$2,693,526	\$5,015,125
Project Budget	\$61,480,824	Received		
Less Other Funding*	\$3,780,000			
Net	\$57,700,824	0,824 * Other Funding Source:		
Actual Measure AA Expenditures		\$5,015,125 KCRW Foundation \$3,780,000 commited,		
Running Balance	\$52,685,700	\$803,412 received	1	

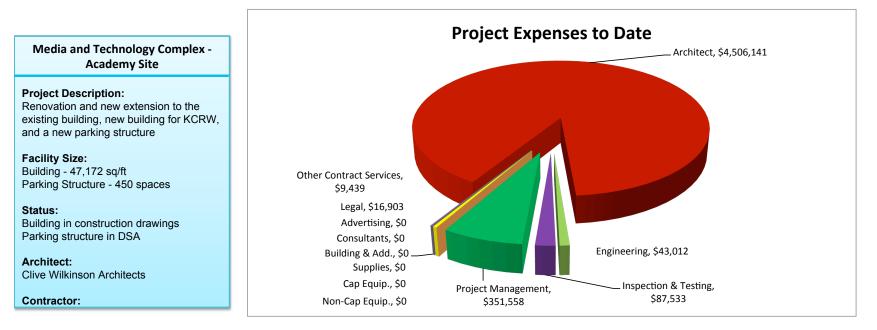

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100060				
Repl. Health/PE/Fitness/Dance Building with Central Plant (104)				
Consultants		\$0	\$0	\$0
Supplies		\$0	\$0	\$0
Other Contract Services		\$120	\$38	\$158
Building & Additions		\$0	\$0	\$0
Architect		\$256,076	\$1,399,227	\$1,655,303
Engineering		\$0	\$8,507	\$8,507
Inspection & Testing		\$36,892	\$490	\$37,382
Project Management		\$34,968	\$110,502	\$145,470
Total		\$328,056	\$1,518,764	\$1,846,819
Project Budget	\$40,200,333			
Less Other Funding*	\$4,816,093	* Other Funding So	urce:	
Net	\$35,384,240	Measure S \$4,816,	093 allocated	
Actual Measure AA Expenditures	\$1,846,819	]		
Running Balance	\$33,537,421	]		

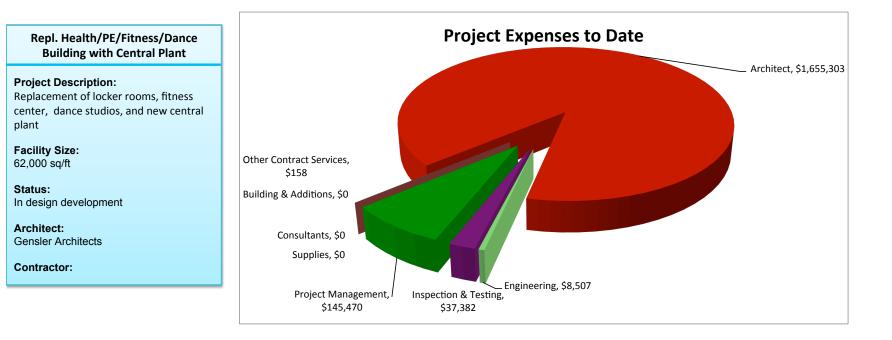

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100047				
Madison East Wing Seismic Upgrade (107)				
Consultants		\$0	\$0	\$0
Supplies		\$0	\$0	\$0
Legal		\$0	\$0	\$0
Other Contract Services		\$0	\$350	\$350
Building & Additions		\$0	\$656	\$656
Architect		\$76,073	\$398,050	\$474,123
Inspection & Testing		\$0	\$18,408	\$18,408
Project Management		\$5,557	\$120,716	\$126,273
Total		\$81,630	\$538,180	\$619,810
Project Budget	\$12,292,000	•		
Less Other Funding	\$0			
Net	\$12,292,000			
Actual Measure AA Expenditures	\$619,810			
Running Balance	\$11,672,190			

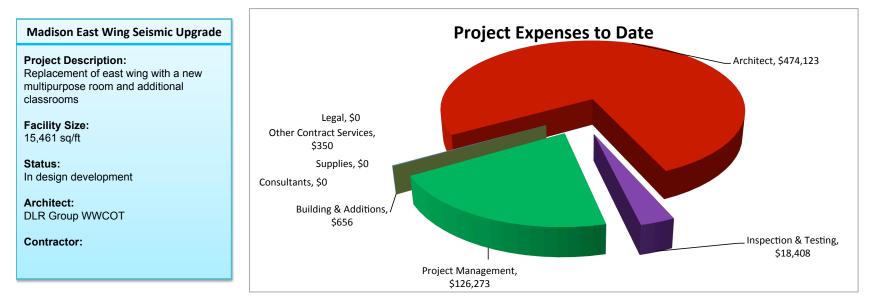

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100068				
Renovation to Corsair Stadium (108)				
Other Contract Services		\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0
Architect		\$0	\$30,759	\$30,759
Engineering		\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0
Project Management		\$0	\$4,540	\$4,540
Total		\$0	\$35,299	\$35,299
Project Budget	\$11,203,000			
Less Other Funding	\$0			
Net	\$11,203,000			
Actual Measure AA Expenditures	\$35,299			
Running Balance	\$11,167,701			
AA 7100067				
Business & Facilities Infrastructure (111)				
Other Contract Services		\$0	\$6,289	\$6,289
Building & Additions		\$0	\$34,672	\$34,672
Architect		\$0	\$0 \$0	\$04,072
Engineering		\$0	\$0 \$0	\$0 \$0
Inspection & Testing		\$0	\$0 \$0	\$0 \$0
Project Management		\$0	\$3,073	\$3,073
Non-Cap Equipment		\$0	\$89,204	\$89,204
Total		\$0	\$133,238	\$133.238
Project Budget	\$6,140,952	ΨΟ	\$155,250	φ133,230
Less Other Funding	\$0,140,352			
Net	\$6,140,952			
Actual Measure AA Expenditures	\$133,238			
Running Balance	\$6,007,714			
	\$0,007,714			
AA 7100064				
Community Classroom & Facility Projects (114)				
Other Contract Services		\$0	\$2,989	\$2,989
Building & Additions		\$0	\$191,851	\$191,851
Architect		\$0	\$247,460	\$247,460
Engineering		\$0	\$2,208	\$2,208
Inspection & Testing		\$0	\$27,883	\$27,883
Project Management		\$135	\$104,647	\$104,782
Total		\$135	\$577,037	\$577,172
Project Budget	\$3,221,000			
Less Other Funding	\$0			
Net	\$3,221,000			
Actual Measure AA Expenditures	\$577,172			
Running Balance	\$2,643,828			

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100057				
Real Property Acquisition (115)				
Legal		\$0	\$0	\$0
Other Contract Services		\$0	\$39	\$39
Site Acquisition		\$1,739,979	\$4,001,204	\$5,741,182
Inspection & Testing		\$8,689	\$7,986	\$16,674
Project Management		\$0	\$0	\$0
Total		\$1,748,667	\$4,009,228	\$5,757,895
Project Budget	\$6,000,000			
Less Other Funding	\$0			
Net	\$6,000,000			
Actual Measure AA Expenditures	\$5,757,895			
Running Balance	\$242,105			
AA 7100058				
Roadways, Walkways, Grounds, Parking Lots, and Garages (116)		<u> </u>	<b>*</b> 0	
Legal	_	\$0	\$0	\$0
Other Contract Services		\$218	\$770	\$988
Building & Additions		\$185,345	\$6,731	\$192,076
Inspection & Testing		\$13,380	\$7,865	\$21,245
Project Management		\$24,404	\$12,439	\$36,843
Total		\$223,347	\$27,804	\$251,152
Project Budget	\$350,000			
Less Other Funding	\$0			
Net	\$350,000			
Actual Measure AA Expenditures	\$251,152			
Running Balance	\$98,848			
AA 7100069				
Infrastructure & Technology - Technology (117)				
Maintenance Contract		\$0	\$9,472	\$9,472
Building & Additions		\$0	\$0 \$0	\$0,472
Architect		\$0	\$0 \$0	\$0 \$0
Inspection & Testing		\$0	\$0 \$0	\$0 \$0
Project Management		\$0	\$0 \$0	\$0 \$0
Cap Equipment		\$0	\$207,423	\$207,423
Non-Cap Equipment		\$0 \$0	<del>\$207,423</del> \$0	<u>\$207,423</u> \$0
Total		\$0 <b>\$0</b>	\$216.896	\$216,896
Project Budget	\$500,000	40 j	φ210,030	ψ2 10,090
Less Other Funding	\$500,000			
Net	\$500,000			
Actual Measure AA Expenditures	\$216,896			
Running Balance	\$283,104			

Projects	Budget	09/10 Final	10/11	Combined Totals
AA 7100069				
Infrastructure & Technology - Utility (118)				
Sofeware License		\$0	\$12,000	\$12,000
Legal		\$0	\$0	\$(
Building & Additions		\$0	\$0	\$(
Architect		\$0	\$0	\$(
Inspection & Testing		\$0	\$4,979	\$4,979
Project Management		\$0	\$3,240	\$3,240
Cap Equipment		\$0	\$0	\$(
Non-Cap Equipment		\$0	\$0	\$(
Total		\$0	\$20,219	\$20,219
Project Budget	\$500,000			
Less Other Funding	\$0			
Net	\$500,000			
Actual Measure AA Expenditures	\$20,219			
Running Balance	\$479,781			
Grand Total		\$4,900,734	\$10,221,988	\$15,122,722


# SANTA MONICA COMMUNITY COLLEGE DISTRICT Bond Sales / Expenses Report As of June 30, 2011

Measure U Bond \$160,000,000	
Bond Issue Date	Amount
2002	\$25,000,000
2004	\$21,999,971
2005	\$89,999,923
2007	\$11,999,987
2010	\$10,998,992
Total Available	\$159,998,873
Expenses as of 6-30-11	\$142,463,785
Total Available Remaining	\$17,535,088
Unsold Bond Amount	\$1,127
Total Available as of 7-1-11	\$17,536,215

Measure S Bond \$143,500,000 (1)		
Bond Issue Date		Amount
	2005	\$58,000,000
	2007	\$8,500,000
	2009	\$56,997,857
Total Available		\$123,497,857
Expenses as of 6-30-11		\$71,876,272
Total Available Remaining		\$51,621,585
Unsold Bond Amount		\$20,002,143
Total Available as of 7-1-11		\$71,623,728

Measure AA Bond \$295,000,000	
Bond Issue Date	Amount
2010	\$100,000,000
Total Available	\$100,000,000
Expenses as of 6-30-11	\$15,122,722
Total Available Remaining	\$84,877,278
Unsold Bond Amount	\$195,000,000
Total Available as of 7-1-11	\$279,877,278

Total Bond	\$598,500,000
Total Available	\$383,496,730
Total Expenses as of 6-30-11	\$229,462,779
Total Available Remaining	\$154,033,951
Total Unsold Bond	\$215,003,270

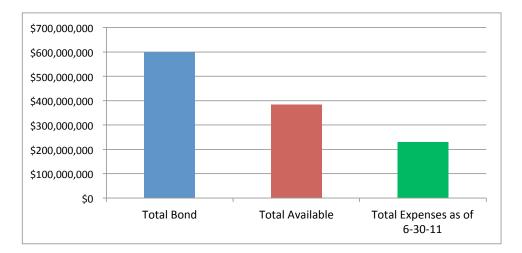

Interest	Measure U	Measure S	Measure AA
As of 6-30-10	\$5,694,648	\$7,329,902	\$512,487
Arbitrage Payment as of 6-30-10	\$0	\$393,004	\$0
Available Interest as of 6-30-10	\$5,694,648	\$6,936,898	\$512,487

	Cost of Issuance Refund	Measure U	Measure S
,	As of 6-30-10	\$20,688	\$35,575

(1) Original Bond \$135,000,000.00, refunding on 2-15-07 received additional \$8,500,000.00
