
Measure U Bond Budget

	Project Name	Completion	Project Budget	Measure U Allocation	Other Funding	Measure U Expenditures as of 12/31/11	Measure U Expenditures as of 9/30/11	Measure U Expenditures Last Period	Total Measure U Remaining
Α	Purchase of BAE Airport Site	Completed	\$30,280,878	\$30,280,878	\$0	\$30,280,878	\$30,280,878	\$0	\$0
В	Emeritus College Facility	Completed	\$9,603,782	\$8,909,940	\$693,842	\$8,909,940	\$8,909,940	\$0	\$0
С	Purchase of 1738 Pearl Street	Completed	\$749,208	\$749,208	\$0	\$749,208	\$749,208	\$0	\$0
D	PE Temp. Bldg. Replacement	Completed	\$2,797,033	\$2,797,033	\$0	\$2,797,033	\$2,797,033	\$0	\$0
E	Remodel Library Village for Math	Completed	\$1,458,690	\$1,458,690	\$0	\$1,458,690	\$1,458,690	\$0	\$0
F	SM Airport Campus Site Improvements	Completed	\$4,170,264	\$4,170,264	\$0	\$4,170,264	\$4,170,264	\$0	\$0
G	SM Airport Campus West Building	Completed	\$19,709,741	\$19,709,741	\$0	\$19,709,741	\$19,709,741	\$0	\$0
Н	Theater Arts Renovation	Completed	\$19,496,949	\$19,496,949	\$0	\$19,496,949	\$19,496,949	\$0	\$0
I	Earthquake Rpl. Liberal Arts North	Completed	\$12,507,725	\$6,352,752	\$6,154,973	\$7,633,209	\$7,633,209	\$0	-\$1,280,457
J	Music Complex	Completed	\$4,623,547	\$2,005,434	\$2,618,113	\$2,005,341	\$2,005,116	\$225	\$93
K	Earthquake Rpl. Liberal Arts South	Completed	\$16,733,220	\$6,108,150	\$10,625,070	\$6,108,150	\$6,108,150	\$0	\$0
L	Shuttle Replacement Parking	Completed	\$18,969,509	\$18,969,509	\$0	\$18,969,509	\$18,969,509	\$0	\$0
M	North Quad Plaza	Completed	\$11,388,463	\$11,388,463	\$0	\$11,388,463	\$11,388,463	\$0	\$0
N	Letters & Sci Demo/Restore	Move to AA	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0	Student Services Building	May 2015	\$53,525,435	\$20,817,196	\$32,708,239	\$2,101,036	\$2,087,584	\$13,452	\$18,716,160
Р	Science Complex Addition	Move to AA	\$308,336	\$308,336	\$0	\$308,336	\$308,336	\$0	\$0
Q	Infrastructure & Safety	Completed	\$4,030,284	\$4,030,284	\$0	\$3,991,516	\$3,961,776	\$29,740	\$38,768
R	Restroom Improvements	Completed	\$17,501	\$17,501	\$0	\$17,501	\$17,501	\$0	\$0
S	Master Planning	Completed	\$2,110,430	\$2,110,430	\$0	\$2,110,430	\$2,110,430	\$0	\$0
Т	14th and Pico Project	On Hold	\$319,242	\$319,242	\$0	\$319,242	\$319,242	\$0	\$0
	Project Totals		\$212,800,237	\$160,000,000	\$52,800,237	\$142,525,436	\$142,482,019	\$43,417	\$17,474,564

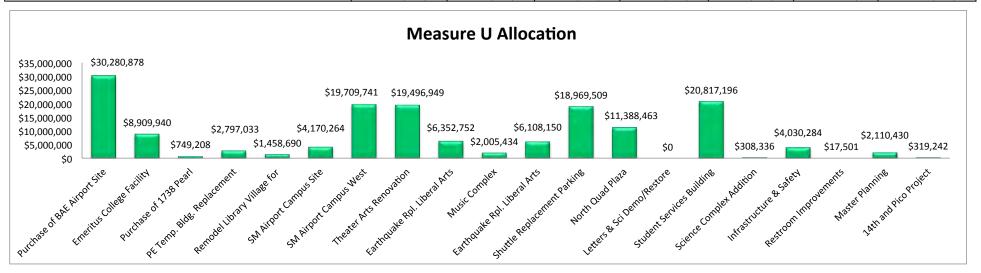

Measure U Project Schedule As of December 31, 2011

	Project Name	Completion	2	2011			2012	2	201	3	20	14	20	015	
Α	Purchase of BAE Airport Site	Completed													
В	Emeritus College Facility	Completed													
С	Purchase of 1738 Pearl Street	Completed													
D	PE Temp. Bldg. Replacement	Completed													
Е	Remodel Library Village for Math	Completed													
F	SM Airport Campus Site Improvements	Completed													
G	SM Airport Campus West Building	Completed													
Н	Theater Arts Renovation	Completed													
I	Earthquake Rpl. Liberal Arts North	Completed													
J	Music Complex	Completed													
K	Earthquake Rpl. Liberal Arts South	Completed													
L	Shuttle Replacement Parking	Completed													
М	North Quad Plaza	Completed													
N	Letters & Sci Demo/Restore	Move to AA													
0	Student Services Building	May 2015													
Р	Science Complex Addition	Move to AA													\Box
Q	Infrastructure & Safety	Completed													
R	Restroom Improvements	Completed													
S	Master Planning	Completed													\Box
Т	14th and Pico Project	On Hold													\Box
	* SM Airport Campus also known as Bundy	Site		ln (Cor	nstri	uctio	n							

MEASURE U EXPENDITURES FUND 42.2

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
U7100010												
Purchase of BAE Airport Site (A)												
Site Acquisition		\$0	\$0		\$30,280,878			\$0			\$0	\$30,280,878
Total		\$0	\$0	\$0	\$30,280,878	\$0	\$0	\$0	\$0	\$0	\$0	\$30,280,878
Project Budget	\$30,280,878											
Less Other Funding	\$0											
Net	\$30,280,878											
Actual Measure U Expenditures	\$30,280,878											
Running Balance	\$0											
U.W. (00000												
U7100028												
Emeritus College Facility (B)												
Site Acquisition		\$8,658,675	\$0	\$0	\$0						\$0	\$8,658,675
Legal		\$14,649	\$3,009	\$20,421	\$0						\$0	\$38,078
Architect		\$93,735	\$27,831	\$161	\$0			\$0			\$0	\$121,727
Engineering		\$18,400	\$0	\$0	\$0						\$0	\$18,400
Supply		\$0	\$4,461	\$0	\$0			\$0		\$0	\$0	\$4,461
Building & Additions		\$0	\$17,496	\$0	\$4,000	\$0		\$0		\$0	\$0	\$21,496
Cap Equipment		\$0	\$49,406	\$0	\$0						\$0	\$49,406
Non-Cap Equipment		\$0	-\$2,197	\$0	-\$108			\$0			\$0	-\$2,305
Total		\$8,785,459	\$100,007	\$20,582	\$3,892	\$0	\$0	\$0	\$0	\$0	\$0	\$8,909,940
Project Budget	\$9,603,782	Received		_						-		
Less Other Funding*	\$693,842	\$693,842		* Other Funding								
Net	\$8,909,940			Emeritus Colle	ge Foundation	\$693,842 receiv	ved					
Actual Measure U Expenditures	\$8,909,940				_							
Running Balance	\$0											
U7100006												
1738 Pearl Street (C)												
Site Acquisition		\$0	\$704,534	\$0	\$0						\$0	\$704,534
Site Improvement		\$0	\$3,250	\$0	\$0	\$0	\$0	\$0			\$0	\$3,250
Building & Additions		\$0	\$41,424	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$41,424
Total		\$0	\$749,208	\$0							\$0	\$749,208
Project Budget	\$749,208		. , ,	, , ,			•					,
Less Other Funding	\$0											
Net	\$749,208											
Actual Measure U Expenditures	\$749,208											
Running Balance	\$0											
	ΨΟ											

MEASURE U EXPENDITURES

FUND 42.2

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
	-		-	-	-	-	-					
U7100026												
PE Temporary Building Replacement (D)												
Architect		\$148,055	\$42,372	\$6,220	\$485	\$0	\$0	\$0	\$0	\$0	\$0	\$197,133
Building & Additions		\$43,866	\$1,922,493	\$415,932	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,382,291
Inspection & Testing		\$6,455	\$136,510	\$716	\$0	\$0	\$0	\$0	\$0		\$0	\$143,681
Project Management		\$4,800	\$56,247	\$5,225	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$66,272
Advertising and Moving Expenses		\$763	\$0	\$6,893		\$0	\$0	\$0	\$0	\$0	\$0	\$7,656
Total		\$203,939	\$2,157,622	\$434,987	\$485	\$0	\$0	\$0	\$0	\$0	\$0	\$2,797,033
Project Budget	\$2,797,033											
Less Other Funding	\$0											
Net	\$2,797,033											
Actual Measure U Expenditures	\$2,797,033											
Running Balance	\$0											
U7100310												
Remodel Library Village for Math (E)												
Moving Exp.		\$0	\$38,625	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$38,625
Building & Additions		\$0	\$1,036,490	\$115,653	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,152,143
Architect		\$104,992	\$27,141	\$1,340			\$0	\$0	\$0	\$0	\$0	\$133,959
Engineering		\$0	\$2,658	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,658
Inspection & Testing		\$0	\$27,083	\$25,175		\$0	\$0	\$0	\$0	\$0	\$0	\$52,258
Project Management		\$0	\$51,679	\$4,400	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$56,079
Advertising and Moving Expenses		\$207	\$10,137	\$12,623	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$22,967
Total		\$105,199	\$1,193,813	\$159,191	\$486	\$0	\$0	\$0	\$0	\$0	\$0	\$1,458,690
Project Budget	\$1,458,690											
Less Other Funding	\$0											
Net	\$1,458,690											
Actual Measure U Expenditures	\$1,458,690											
Running Balance	\$0											

MEASURE U EXPENDITURES

FUND 42.2 As of December 31, 2011

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
U7100027												
SM Airport Campus Site Improvements (F)												
Supplies		\$0	\$26,234	\$975	\$5,873	\$0				\$0	\$0	\$33,082
Misc Fees		\$0	\$25	\$0	\$0	. ,	\$0	\$0		\$0	\$0	\$34,299
Other Contract Services		\$3,860	\$11,508	\$8,434	\$1,501	\$0				\$0	\$0	\$25,302
Site Improvement		\$0	\$0	\$15,182	\$5,790	\$7,237	\$0			\$0	\$0	\$28,209
Building & Additions		\$0	\$1,495,697	\$1,670,788	\$4,824	\$0		\$0		\$0	\$0	\$3,171,309
Architect		\$104,934	\$500	\$0	\$43,570					\$0	\$0	\$149,004
Engineering		\$35,000	\$148,304	\$950	\$10,040	\$0		\$0		\$0	\$0	\$194,294
Inspection & Testing		\$5,032	\$118,662	\$191,271	\$0	\$0	\$0	\$0		\$0	\$0	\$314,965
Project Management		\$750	\$155,798	\$38,425	\$1,365		\$0	\$0		\$0	\$0	\$196,558
City Fees, Advertising and Security System		\$16,587	\$1,802	\$327	\$150					\$0	\$0	\$23,241
Total		\$166,163	\$1,958,530	\$1,926,352	\$73,113	\$46,106	\$0	\$0	\$0	\$0	\$0	\$4,170,264
Project Budget	\$4,170,264											
Less Other Funding	\$0											
Net	\$4,170,264											
Actual Measure U Expenditures	\$4,170,264											
Running Balance	\$0											
•	'											
U7110027												
SM Airport Campus West Building (G)												
Supply		\$0	\$0	\$17,650	\$28,017	\$0	\$0	\$0	\$0	\$0	\$0	\$45,667
Other Contract Services		\$0	\$0	\$0	\$3,576			\$0		\$0	\$0	\$3,576
Moving Expenses		\$0	\$0	\$180	\$15.824	\$0		\$0		\$0	\$0	\$16,004
Building & Additions		\$0	\$0	\$15,037,532	\$1,256,065	\$46,946				\$0	\$0	\$16,340,543
Architect		\$0	\$971,954	\$1,043,950	\$49,779		\$0	\$0		\$0	\$0	\$2,066,830
Engineering		\$0	\$2,920	\$9.800	\$5,010	\$963	\$0	\$0		\$0	\$0	\$18.693
Inspection & Testing		\$0	\$21,173	\$126,510	\$9,856	\$0				\$0	\$0	\$157,539
Project Management		\$0	\$14,450	\$313,715	\$13,956	\$0		\$0		\$0	\$0	\$342,121
Cap Equipment		\$0	\$49,795	\$326,382	\$4,792	\$0		\$0		\$0	\$0	\$380,969
Non-Cap Equipment		\$0	\$0	\$280,558	\$57,240			\$0		\$0	\$0	\$337,798
Total		\$0	\$1,060,292		\$1,444,115	\$49,056				\$0	\$0	
Project Budget	\$19,709,741	401	7.,000,202	÷ , . • • , =	<i>ϕ</i> .,,	Ţ.5,000		- 40		Ψ0	Ψ0	Ţ.c,. co,i -i
Less Other Funding	\$0											
Net	\$19,709,741											
Actual Measure U Expenditures	\$19,709,741											
Running Balance	\$0											
Talling Balarioc	ا ﴿ ا											

MEASURE U EXPENDITURES

FUND 42.2 As of December 31, 2011

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
		•		•								
U7100025												
Theatre Arts Renovation (H)												
Supplies		\$0	\$8,904	-\$14	\$12,858	\$16,619	\$0				\$0	
Legal		\$0	\$0	\$0	\$0		\$0				\$0	
Moving Services		\$0	\$0	\$0	\$0	\$14,061	\$0				\$0	
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0				\$0	
Rental / Lease		\$0	\$1,446	\$2,200	\$0		\$0	\$0	\$0	\$0	\$0	\$3,646
Building & Additions		\$528	\$1,326,630	\$4,540,487	\$10,897,603	\$56,122	\$25,220	\$0			\$0	
Architect		\$289,913	\$369,213	\$423,416	\$82,639	\$0	\$0	\$0	\$0	\$0	\$0	\$1,165,181
Engineering		\$6,174	\$2,981	\$16,606	\$2,375	\$1,250	\$0	\$0	\$0	\$0	\$0	
Inspection & Testing		\$150	\$14,785	\$353,890	\$297,675	\$1,116	\$0	\$0	\$0	\$0	\$0	\$667,616
Project Management		\$150	\$45,698	\$184,219	\$193,898		\$230	\$0	\$0	\$0	\$0	\$439,013
Cleaning, Storage and Installation		\$0	\$812	\$0	\$2,548	\$2,267	\$0	\$0	\$0	\$0	\$0	\$5,627
Cap Equipment		\$0	\$31,638	\$0	\$6,458	\$59,689	\$0	\$0	\$0	\$0	\$0	\$97,785
Non-Cap Equipment		\$0	\$2,388	\$0	\$36,749	\$145,294	\$0	\$0	\$0	\$0	\$0	\$184,432
Total		\$296,915	\$1,804,496	\$5,520,804	\$11,532,803	\$311,236	\$25,450	\$5,245	\$0	\$0	\$0	\$19,496,949
Project Budget	\$19,496,949				•							
Less Other Funding	\$0											
Net	\$19,496,949											
Actual Measure U Expenditures	\$19,496,949											
Running Balance	\$0											
· · · · · · · · · · · · · · · · · · ·	•		-					-	-	-	-	
U7100110			1									
Earthquake Rpl. Liberal Arts North (I)								1				
Supplies		\$0	\$0	\$0	\$0	\$1,408	\$0	\$75	\$0	\$0	\$0	\$1,483
Legal		\$0	\$0	\$0	\$0		\$0				\$0	
Other Contract Services		\$0	\$0	\$0	\$0		\$0				\$0	
Building & Additions		\$265	\$0	\$1,043,660	\$5,916,281	-\$973,001	\$321,345	\$14,898			\$0	
Architect		\$0	\$611.732	\$102.824	\$209,490	\$216,563	\$21,215			\$0	\$0	
Engineering		\$3,248	\$4,295	\$0	\$250	\$0	\$250	\$0			\$0	
Inspection & Testing		\$0	\$0	\$28.312	\$326,203	\$77,942	\$0				\$0	
Project Management		\$0	\$26,072	\$33,549	\$128,937	\$124,222	\$255	\$1,155			\$0	
Advertising and Fees		\$0	-\$4	\$7,334	\$0		\$0				\$0	
Cap-Equipment		\$0	\$0	\$0	\$0		\$12,579			\$0	\$0	
Non-Cap Equipment		\$0	\$0	\$0	\$2,033	\$170,425	\$4,093	\$0			\$0	
Total		\$3,513	\$642,095			-\$356,123	\$359,737	\$19,592			\$0	
Project Budget	\$12,507,725	Received	,,,,,,,	. , .,	, -,,	,	, ,	,,,,,,		, 1		. ,,
Less Other Funding*	\$6,154,973	\$4,874,517		* Other Funding	Source:							ļ
Net	\$6,352,752	, ,,		City of Santa M		53 received						
Actual Measure U Expenditures	\$7,633,209			FEMA \$2,115.2	20 commited.	\$834,764 receiv	ed					İ

MEASURE U EXPENDITURES

FUND 42.2 As of December 31, 2011

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
U7100013. U7100047	1 1						I					
Music Complex (J)												
Advertising		\$0	\$0	\$436	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$436
Supplies		\$0	\$0	\$0	\$0	\$194					\$0	
Consultants		\$0	\$0	\$0	\$0	\$0			\$0		\$0	
Other Contract Services		\$0	\$0	\$0	\$0	\$0			\$0		\$0	\$180
Moving Services		\$0	\$0	\$0	\$0	\$0	\$6,330		\$0	\$0	\$0	
Building & Additions		\$0	\$0	\$356,464	\$1,293,726	-\$737,213	\$273,531		\$0	\$0	\$0	
Architect		\$0	\$187,922	\$22,500	\$37,227	\$38,448	\$4,052	\$14,356	\$0	\$681	\$225	\$305,411
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$21,370	\$0	\$0	\$0	\$21,370
Inspection & Testing		\$0	\$0	\$29,740	\$19,265	\$26,238	\$35,880	\$0	\$0	\$0	\$0	\$111,122
Project Management		\$0	\$170	\$36,739	\$36,351	\$56,914	\$16,200	\$1,288	\$0	\$0	\$0	\$147,662
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$62,600	\$0	\$0	\$0	\$0	\$62,600
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$29,852	\$78,582	\$0	\$0	\$0	\$0	\$108,434
Total		\$0	\$188,092	\$445,879	\$1,386,568	-\$585,566	\$532,447	\$37,014	\$0	\$681	\$225	\$2,005,341
Project Budget	\$4,623,547	Received	•									
Less Other Funding*	\$2,618,113	\$2,618,113	,	Other Funding	g Source:							
Net	\$2,005,434			Prop T Refinan	ce \$2,618,113	received						
Actual Measure U Expenditures	\$2,005,341											
Running Balance	\$93											
U7100111												
Earthquake Rpl. Liberal Arts South (K)												
Supply		\$0	\$0	\$855	\$2,497	\$379			\$0	\$0	\$0	\$27,618
Legal		\$0	\$0	\$0	\$0	\$0	\$2,203	\$50	\$0	\$0	\$0	\$2,253
Moving Services		\$0	\$0	\$0	\$0	\$0		\$0	\$0		\$0	
Consultants		\$0	\$0	\$0	\$17,265	\$41,435			\$0		\$0	\$58,700
Other Contract Services		\$0		\$6,154	\$202	\$0			\$0		\$0	
Building & Additions		\$0	\$0	\$26,302	\$3,091,306	\$5,706,802			\$91,516		\$0	\$4,273,467
Architect		\$0	\$0	\$836,555	-\$503,297	\$163,506		\$39,984	\$2,549	\$0	\$0	
Engineering		\$0	\$0	\$3,125	\$150	\$5,344			\$0		\$0	
Inspection & Testing		\$0	\$0	\$0	\$179,798	\$296,015			\$0		\$0	
Project Management		\$0	\$0	\$0	\$43,989	\$262,598			\$1,278	\$0	\$0	
Cap-Equipment		\$0	\$0	\$0	\$0	\$0			\$0		\$0	
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$58,726			\$0		\$0	
Total		\$0	\$0	\$872,991	\$2,831,909	\$6,534,806	-\$4,261,655	\$34,757	\$95,342	\$0	\$0	\$6,108,150
Project Budget	\$16,733,220	Received										
Less Other Funding*	\$10,625,070	\$10,625,070		* Other Funding								
Net	\$6,108,150				Ionica \$6,167,0							
Actual Measure U Expenditures	\$6,108,150		;	State of Califor	nia \$4,458,000	received						
Running Balance	\$0											

SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE U EXPENDITURES

FUND 42.2

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
U7100221												
Shuttle Replacement Parking (L)												
Supplies		\$0	\$0	\$0	\$0		\$1,347	\$0			\$0	\$1,347
Legal		\$0	\$0	\$0	\$8,462	\$35,103	\$0	\$0		\$0	\$0	\$43,565
Site Acquisition		\$0	\$0	\$0	\$0		\$0	\$0			\$0	\$16,903,087
Site Improvement		\$0	\$0	\$0	\$0		\$0	\$0			\$0	\$3,027
Building & Additions		\$0	\$0	\$0	\$0		\$1,252,224	\$2,353	\$0		\$0	\$1,738,577
Architect		\$0	\$0	\$0	\$0		\$7,208	\$0			\$0	\$58,777
Inspection & Testing		\$0	\$0	\$0	\$0		\$41,250	\$0			\$0	\$181,072
Project Management		\$0	\$0	\$0	\$0		\$32,425	\$0			\$0	\$40,056
Total		\$0	\$0	\$0	\$8,462	\$17,624,240	\$1,334,455	\$2,353	\$0	\$0	\$0	\$18,969,509
Project Budget	\$18,969,509	-		-	-				-			
Less Other Funding	\$0											
Net	\$18,969,509											
Actual Measure U Expenditures	\$18,969,509											
Running Balance	\$0											
U7100321												
North Quad Plaza (M)												
Legal		\$0	\$0	\$0	\$0		\$3,825	\$5,604			\$0	\$9,429
Building & Additions		\$0	\$0	\$0	\$0	-\$443	\$6,130,081	\$3,634,487	\$0		\$0	\$9,764,125
Architect		\$0	\$231,055	\$8,444	\$140,048	\$435,618	\$171,225	\$68,633	\$2,901	\$10,483	\$0	\$1,068,407
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$186,220	\$107,477	\$328	\$0	\$0	\$294,025
Project Management		\$0	\$0	\$760	\$210	\$2,200	\$135,601	\$55,782	\$606	\$0	\$0	\$195,158
Printing		\$0	\$1,900	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,900
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$55,420	\$0	\$0	\$0	\$55,420
Total		\$0	\$232,955	\$9,204	\$140,258	\$437,375	\$6,626,952	\$3,927,402	\$3,834	\$10,483	\$0	\$11,388,463
Project Budget	\$11,388,463			•							•	
Less Other Funding	\$0											
Net	\$11,388,463											
Actual Measure U Expenditures	\$11,388,463											
Running Balance	\$0											

MEASURE U EXPENDITURES

FUND 42.2 As of December 31, 2011

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
•	' '									-		
U7100500, U7126450, U7100334, U7100142												
Student Services Building (O)												
Supplies		\$2,014	\$0	\$0	\$0	\$0	\$0	\$718	\$0	\$0	\$0	\$2,732
PC Upgrades		\$0	\$765	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$765
Consultants		\$0	\$0	\$0	\$0	\$9,334	\$55,693	\$0	\$0	\$0	\$0	\$65,027
Legal		\$0	\$0	\$0	\$0	\$38	\$2,775	\$31,776	\$0	\$0	\$0	\$34,588
Other Contract Services		\$210	\$0	\$0	\$0	\$0	\$17,561	\$17,495	\$18,817	-\$70	\$0	\$54,014
Moving		\$7,571	\$0	\$0	\$0	\$0	\$0	\$616	\$0	\$0	\$0	\$8,187
Building & Additions		\$359,141	\$2,441	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$361,582
Architect		\$31,782	\$0	\$235,230	\$0	\$43,992	\$0	\$690,099	\$208,521	\$38,643	\$18,706	\$1,266,974
Engineering		\$1,838	\$0	\$0	\$0	\$0	\$0	\$6,205	\$27,363	\$3,171	\$0	\$38,576
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$25,670	\$34,687	\$0	\$0	\$0	\$60,358
Project Management		\$4,650	\$0	\$2,470	\$0	\$1,100	\$0	\$124,148	\$0	\$0	\$0	\$132,368
Cap Equipment		\$59,063	\$0	\$0	\$0	\$0	\$8,745	\$8,056	\$0	\$0	\$0	\$75,864
Total		\$466,268	\$3,207	\$237,700	\$0	\$54,464	\$110,445	\$913,802	\$254,701	\$41,744	\$18,706	\$2,101,036
Project Budget	\$53,521,913	Received		* Other Fundin	g Source:					-		
Less Other Funding*	\$32,705,717	\$1,321,000		State of Califor	nia \$16,803,00	0 allocated, \$1,3	321,000 receive	ed				
Net	\$20,816,196			District Capital	Funds \$10,208	,069 commited						
Actual Measure U Expenditures	\$2,101,036			Measure U Inte	erest \$5,694,64	8 allocated						
Running Balance	\$18,715,160											

Student Services Building

Project Discription:


Consolidates various student services departments and college administration in a single complex at the front of the campus

Facility Size: 83,634 sq/ft & 500 cars underground parking structure

In plan check with DSA

Architect:

Steinberg Architects

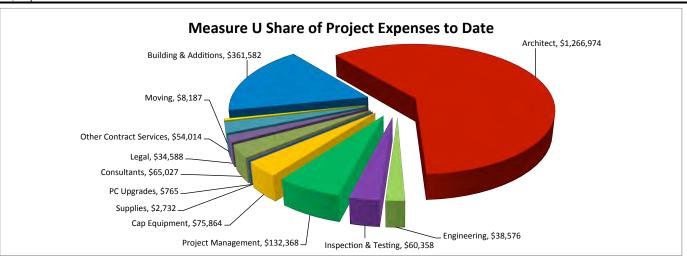

MEASURE U EXPENDITURES FUND 42.2

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
,	J											
U7100090												
Science Complex Additional (P)												
Architect		\$0	\$0	\$0	\$0	\$246,425	\$61,911	\$0	\$0	\$0	\$0	\$308,336
Total		\$0	\$0	\$0	\$0		\$61,911	\$0	\$0		\$0	\$308,336
Project Budget	\$308,336	, ,	,			,	, , ,					, ,
Less Other Funding	\$0											
Net	\$308,336											
Actual Measure U Expenditures	\$308,336											
Running Balance	\$0											
U6780000, U7100022, U7100331, U7100550,												
U7100005, U7100030, U7100031, U7100029,												
U7100003, U7100008, U7100332, U7100072,												
U7100042, U7100056, U7100039												
Infrastructure & Safety (Q)												
Supplies		\$0	\$0	\$254	\$0	\$0	\$0	\$1,700	\$1,393	\$0	\$0	\$3,347
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$16,734	\$0	\$0	\$0	\$16,734
Maintenance Agreement		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$14,673	\$12,979	\$27,653
Legal		\$0	\$0	\$0	\$0	\$0	\$3,527	\$3,294	\$0	\$0	\$0	\$6,821
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$7,825	\$81,445	\$203,383	\$3,320	\$0	\$295,973
Building & Additions		\$681,900	\$195,175	\$20,600	\$0	\$200,620	\$733	\$0	\$0	\$0	\$0	\$1,099,028
Architect		\$69,081	\$42,108	\$0	\$155,321	\$448,507	\$91,127	\$4,227	\$0	\$0	\$0	\$810,370
Engineering		\$8,050	\$0	\$0	\$6,750	\$12,000	\$18,429	\$2,360	\$0	\$0	\$0	\$47,589
Inspection & Testing		\$2,241	\$4,250	\$0	\$0		\$5,807	\$0	\$0	\$0	\$0	\$12,298
Project Management		\$0	\$2,805	\$0	\$0		\$1,840	\$38	\$196	\$0	\$0	\$8,399
Cap Equipment		\$0	\$0	\$343,861	\$0		\$0	\$895,171	\$349,531	\$40,002	\$0	\$1,628,565
Non-Cap Equipment		\$0	\$0	\$0	\$0		\$0		\$4,216	\$0	\$29,740	\$33,956
Advertising		\$0	\$785	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$785
Total		\$761,272	\$245,122	\$364,715	\$162,071	\$664,647	\$129,287	\$1,004,968	\$558,718	\$57,995	\$42,720	\$3,991,516
Project Budget	\$4,030,284											
Less Other Funding	\$0											
Net	\$4,030,284											
Actual Measure U Expenditures	\$3,991,516											
Running Balance	\$38,768											

SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE U EXPENDITURES

FUND 42.2


As of December 31, 2011

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
				·								
U7100007												
Restroom Improvement (R)												
Supplies		\$0	\$564	\$0	\$1,075	\$0	\$0	\$0		\$0	\$0	\$1,639
Other Contract Services		\$0	\$0	\$0	\$3,803	\$0	\$0	\$0		\$0	\$0	\$3,803
Building & Additions		\$0	\$1,305	\$0	\$7,891	\$0	\$0	\$0		\$0	\$0	\$9,196
Inspection & Testing		\$0	\$2,043	\$0	\$820	\$0	\$0	\$0		\$0	\$0	\$2,863
Total		\$0	\$3,912	\$0	\$13,589	\$0	\$0	\$0	\$0	\$0	\$0	\$17,501
Project Budget	\$17,501											
Less Other Funding	\$0											
Net	\$17,501											
Actual Measure U Expenditures	\$17,501											
Running Balance	\$0											
U7100004, U7110020												
Master Planning (S)												
Consultants		\$9,000	\$26,516	\$158,449	\$374,329	\$125,404	\$17,998	\$363,342	\$0	\$0	\$0	\$1,075,038
Architect		\$0	\$17,617	\$126,433	\$104,083	\$126,701	\$346.827	\$276,985		\$0	\$0	\$998.647
Rental / Lease		\$0	\$0	\$6,453	\$0	\$0	\$0	\$0		\$0	\$0	\$6,453
Postage		\$0	\$0	\$30,000	\$0	\$0	\$0	\$0		\$0	\$0	\$30,000
Reimbursement to SMC		\$0	\$0	\$0	\$180	\$0	\$0	\$0		\$0	\$0	\$180
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$113		\$0	\$0	\$113
Total		\$9,000	\$44,133	\$321,335	\$478,593	\$252,105	\$364,825	\$640,439		\$0	\$0	\$2,110,430
Project Budget	\$2,110,430	+=,===	*,	+	4 11 0,000	+,	+ ,	*****	**	7-1	**	+-,,
Less Other Funding	\$0											
Net	\$2,110,430											
Actual Measure U Expenditures	\$2,110,430											
Running Balance	\$0											
Training Balance	ΨΟ											
U7100024		1				1						
14th and Pico Project (T)												
Consultants		\$0	\$888	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$888
Architect		\$258,601	\$47,343	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$305,944
Inspection & Testing		\$12,070	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$12,070
Project Management		\$12,070	\$340	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		\$0	\$0 \$0	\$340
Total		\$270,671	\$48,571	\$0	\$0	\$0	\$0	\$0		\$0 \$0	\$0	\$319,242
	\$319,242	\$270,071	\$40,57 I	Ψ 0]	φυ	Ψ0	φυ	40	φ0	φ0	Ψυ	Ψ313,242
Project Budget Less Other Funding	\$319,242											
Net	\$319,242											
Actual Measure U Expenditures	\$319,242											
Running Balance	\$0											
		A11.000 (==1				A	A= 000 5=="	AA		4-00 01	****	A
Grand Total		\$11,068,400	\$10,432,055	\$28,685,697	\$54,940,416	\$25,278,771	\$5,283,853	\$6,585,573	\$912,880	-\$723,860	\$61,651	\$142,525,436

Note: Project N had no expenses

Measure S Bond Budget

	Project Name	Completion	Project Budget	Measure S Allocation	Other Funding	Measure S Expenditures as of 12/31/11	Measure S Expenditures as of 9/30/11	Measure S Expenditures Last Period	Total Measure S Remaining
1	Athletic Fields Phase I, Corsair Field	Completed	\$4,440,768	\$4,373,238	\$67,530	\$4,372,535	\$4,372,535	\$0	\$703
1A	Athletic Fields Phase I, John Adams	Completed	\$2,970,807	\$2,970,807	\$0	\$2,969,807	\$2,969,807	\$0	\$1,000
2	Performing Arts Complex	Completed	\$40,603,541	\$37,610,965	\$2,992,576	\$37,610,571	\$37,610,571	\$0	\$394
3	Career Opportunity Center	Move to AA	\$0	\$0	\$0	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	May 2014	\$40,200,333	\$4,816,093	\$35,384,240	\$790,589	\$790,589	\$0	\$4,025,504
5	Early Childhood Development/Childcare	May 2015	\$11,318,000	\$7,000,000	\$4,318,000	\$12,504	\$11,524	\$980	\$6,987,496
6	Malibu Site Acquisition and Facility	Not Scheduled	\$31,069,031	\$25,000,000	\$6,069,031	\$5,289,063	\$5,235,922	\$53,141	\$19,710,937
7	Energy Efficiency Projects	On-Going	\$1,293,570	\$1,076,248	\$217,322	\$293,361	\$293,361	\$0	\$782,887
8	Satellite Campus Parking Facilities and Roadway Improvements	Completed	\$4,875,000	\$4,875,000	\$0	\$3,820,983	\$3,820,983	\$0	\$1,054,017
9	Parking Garage, Grounds and Equipment - Student Services	May 2015	\$53,143,653	\$52,690,653	\$453,000	\$15,018,400	\$14,968,445	\$49,955	\$37,672,253
10	Pico Promenade Improvements	Completed	\$1,018,009	\$1,018,009	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	On-Going	\$750,000	\$750,000	\$0	\$708,583	\$708,583	\$0	\$41,417
12	Other Bond Related Expenses	On-Going	\$662,764	\$662,764	\$0	\$151,310	\$124,645	\$26,665	\$511,454
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	On-Going	\$50,000	\$50,000	\$0	\$45,597	\$45,597	\$0	\$4,403
15	Signage Safety/Information	On-Going	\$606,223	\$606,223	\$0	\$236,289	\$236,289	\$0	\$369,934
	Project Totals		\$193,001,699	\$143,500,000	\$49,501,699	\$72,337,601	\$72,206,860	\$130,741	\$71,162,399

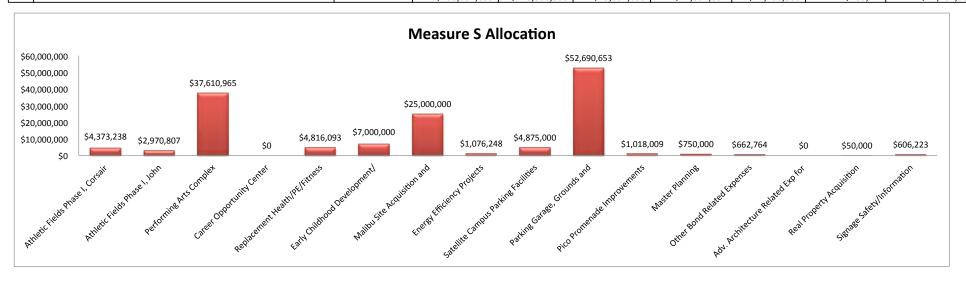

Measure S Project Schedule As of December 31, 2011

	Project Name	Completion	2011	2012	2013	2014	2015
1	Athletic Fields Phase I, Corsair Field	Completed					
1A	Athletic Fields Phase I, John Adams	Completed					
2	Performing Arts Center	Completed					
3	Career Opportunity Center	Move to AA					
4	Replacement Health/PE/Fitness Building	May 2014					
5	Early Childhood Development/Childcare	May 2015					
6	Malibu Site Acquisition and Facility	Not Scheduled					
7	Energy Efficiency Projects	On-Going					
8	Satellite Campus Parking Facilities and Roadway Improvements	Completed					
9	Parking Garage, Grounds and Equipment - Student Services	May 2015					
10	Pico Promenade Improvements	Completed					
11	Master Planning	On-Going					
12	Other Bond Related Expenses	On-Going					
13	Adv. Architecture Related Exp for AA	Completed					
14	Real Property Acquisition	On-Going					
15	Signage Safety/Information	On-Going					
			In Planni	ing	In Constru	uction	

MEASURE S EXPENDITURES

FUND 42.3

As of December 31, 2011

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
			-				•			•
S7100019										
Athletic Field Phase I, Corsair Field (1)										
Legal		\$0	\$0	\$0	\$301	\$175	\$0	\$0	\$0	\$476
Building & Additions		\$0	\$0	\$0	\$300,380	\$2,579,095	\$0	\$0	\$0	\$2,879,475
Architect		\$27,332	\$43,815	\$197,557	\$252,736	\$279,173	\$26,563	\$0	\$0	\$827,176
Inspection & Testing		\$0	\$0	\$0	\$23,411	\$57,585	\$640	\$296	\$0	\$81,932
Project Management		\$0	\$0	\$0	\$9,871	\$42,374	\$565	\$0	\$0	\$52,810
Cap Equipment		\$0	\$0	\$0	\$0	\$483,017	\$35,271	\$0	\$0	\$518,288
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$2,066	\$10,312	\$0	\$0	\$12,378
Total		\$27,332	\$43,815	\$197,557	\$586,699	\$3,443,485	\$73,350	\$296	\$0	\$4,372,535
Project Budget	\$4,440,768	Received								
Less Other Funding*	\$67,530	\$67,530								
Net	\$4,373,238		* Other Funding	g Source:						
Actual Measure S Expenditures	\$4,372,535		Metropolitan W	ater District \$6	7,530 received					
Running Balance	\$703									

Athletic Field Phase I, Corsair Field

Project Description:

Renovation of the Corsair Field, stadium lighting and sound system

Status:


Completed, 2009

Architect:

CO Architects

Contractor:

Byrom Davey, Inc.

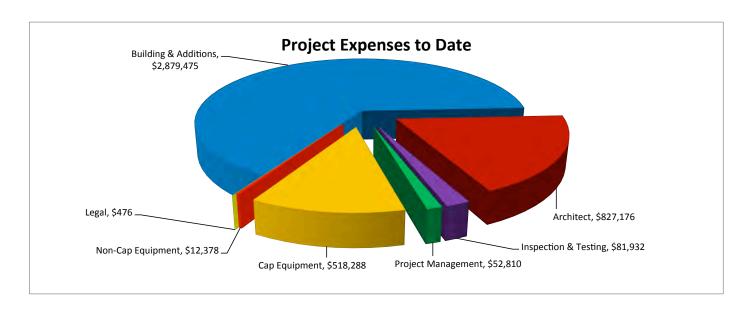

MEASURE S EXPENDITURES

FUND 42.3 As of December 31, 2011

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
					•	-	•	•		
S7100038										
Athletic Field Phase I, John Adams (1A)										
Legal		\$0	\$0	\$0	\$75	\$0	\$0	\$0	\$0	\$75
Building & Additions		\$0	\$0	\$0	\$16,556	\$1,395,261	\$0	\$0	\$0	\$1,411,817
Architect		\$0	\$5,807	\$93,941	\$12,150	\$31,818	\$0	\$0	\$0	\$143,715
Inspection & Testing		\$0	\$2,874	\$3,207	\$0	\$49,984	\$0	\$0	\$0	\$56,066
Project Management		\$0	\$0	\$0	\$10,921	\$45,170	\$38	\$0	\$0	\$56,128
Cap Equipment		\$0	\$0	\$0	\$0	\$1,290,672	\$0	\$0	\$0	\$1,290,672
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$11,334	\$0	\$0	\$0	\$11,334
Total		\$0	\$8,681	\$97,148	\$39,701	\$2,824,239	\$38	\$0	\$0	\$2,969,807
Project Budget	\$2,970,807							_		
Less Other Funding	\$0									
Net	\$2,970,807									
Actual Measure S Expenditures	\$2,969,807									
Running Balance	\$1,000									

Athletic Field Phase I, John Adams

Project Description:

Renovation of John Adams Field and lighting

Status:


Completed, 2008

Architect:

Caldwell Architects

Contractor:

Byrom Davey, Inc.

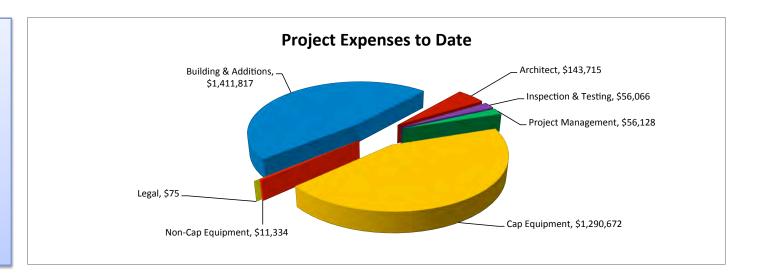

MEASURE S EXPENDITURES

FUND 42.3

As of December 31, 2011

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
S7100012										
Performing Arts Center (2)										
Consultants		\$0	\$0	\$0	\$121,790	\$76,639	\$0	\$0	\$0	\$198,429
Other Contract Services		\$0	\$0	\$4,269	\$0	\$22,729	\$22	\$68	\$0	\$27,088
Supplies		\$0	\$0	\$0	\$14,565	\$5,810	\$0	\$0		\$20,375
Legal		\$0	\$0	\$34,329	\$275,667	\$492,731	\$15,629	\$0	\$0	\$818,356
Advertising		\$0	\$0	\$0	\$320	\$0	\$0	\$0		\$320
Building & Additions		\$7,784,151	\$10,292,986	\$8,930,813	\$2,991,903	\$1,629,990	\$50,000	\$0	\$0	\$31,679,843
Architect		\$0	\$811,312	\$182,457	\$412,309	\$121,588	\$108	\$1,962	\$0	\$1,529,736
Engineering		\$0	\$3,600	\$5,250	\$1,500	\$9,650	\$0	\$0	\$0	\$20,000
Inspection & Testing		\$104,308	\$722,685	\$411,193	\$210,381	\$22,256	\$0	\$0	\$0	\$1,470,823
Project Management		\$31,984	\$155,732	\$248,876	\$263,690	\$47,915	\$3,244	\$0		\$751,441
Cap Equipment		\$0	\$0	\$130,218	\$292,565	\$342,693	\$0	\$0	\$0	\$765,476
Non-Cap Equipment		\$0	\$0	\$15,124	\$93,106	\$220,455	\$0	\$0	\$0	\$328,685
Total		\$7,920,443	\$11,986,315	\$9,962,528	\$4,677,797	\$2,992,455	\$69,003	\$2,030	\$0	\$37,610,571
Project Budget	\$40,603,541	Received								
Less Other Funding*	\$2,992,576	\$2,992,576		* Other Fundin						
Net	\$37,610,965			Madison Projec	ct Foundation \$	2,992,576 rece	eived			
Actual Measure S Expenditures	\$37,610,571									
Running Balance	\$394									

Performing Arts Center

Project Description:

Construction of a state-of-the-art 499 seat performing arts theater

Status:


Completed, 2008

Architect:

Renzo Zecchetto

Contractor:

FTR International

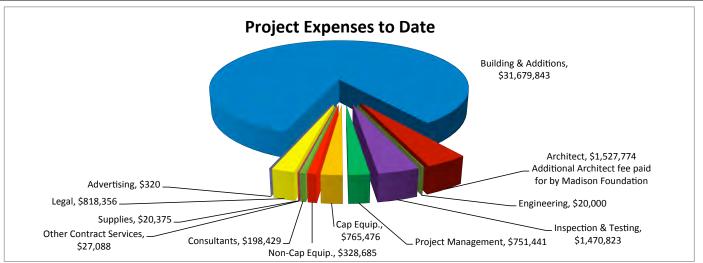

MEASURE S EXPENDITURES

FUND 42.3

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals	
S7100033, S7100144											
Replacement Health/PE/Fitness Building (4)											
Supplies		\$0	\$0	\$0	\$0	\$0	\$163	\$0	\$0	\$163	
Legal		\$0	\$0	\$0	\$0	\$1,413	\$75	\$0	\$0	\$1,488	
Other Contract Services		\$1,634	\$25,934	\$0		\$253	\$165	\$0	\$0	\$27,985	
Repair Facility		\$0	\$4,861	\$0			\$0	\$0	\$0	\$4,861	
Supplies		\$4,809	\$288	\$0			\$0	\$0	\$0	\$5,097	
Building & Additions		\$0	\$0	\$0			\$526,552		\$0	\$638,962	
Architect		\$0	\$0	\$0	\$0	\$0	\$41,044	\$0	\$0	\$41,044	
Inspection & Testing		\$0	\$0	\$0		\$6,518	\$14,363	\$0	\$0	\$20,881	
Project Management		\$0	\$0	\$0	\$0	\$9,070	\$23,425	\$0	\$0	\$32,495	
Cap Equipment		\$0	\$0	\$0			\$0	* -	\$0	\$17,613	
Total		\$6,443	\$31,083	\$0	\$0		\$605,787	\$17,613	\$0	\$790,589	
Project Budget	\$40,200,333	7-,	, , - 20	+-	70	,,	, ,	,,	7-1	Ţ: 22 ,300	
Less Other Funding*	\$35,384,240	•		* Other Fundin	g Source:						
Net	\$4,816,093			Measure AA \$3		cated					
Actual Measure S Expenditures	\$790,589										
Running Balance	\$4,025,504										
<u> </u>											
S7100045											
Early Childhood Development/Childcare (5)											
Consultants		\$0	\$0	\$0	\$9,200	\$0	\$0	\$0	\$0	\$9,200	
Project Management		\$0	\$0	\$0			\$0	\$1,246	\$2,058	\$3,304	
Total		\$0	\$0						\$2,058	\$12,504	
Project Budget	\$11,318,000	Received							,		
Less Other Funding*	\$4,318,000	\$0		* Other Fundin	g Source:						
Net	\$7,000,000			City of Santa N	Ionica \$4,318,0	000 commited					
Actual Measure S Expenditures	\$12,504			•							
Running Balance	\$6,987,496										
S7100077, S7100015											
Malibu Site Acquisition and Facilities (6)											
Consultants		\$0	\$0	\$0	\$0	\$30,000	\$0	\$0	\$4,778	\$34,778	
Legal		\$0	\$27,722	\$16,787	\$6,159	\$504	\$0	\$0	\$0	\$51,172	
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Inspection & Testing		\$4,388	\$3,750	\$141,462	\$0	\$0	\$0		\$37,730	\$187,329	
Project Management		\$0	\$0	\$220	\$0	\$0	\$0	\$2,886	\$12,537	\$15,643	
Other Contract Services		\$0	\$0	\$0	\$0		\$0	\$0	\$141	\$141	
Storm/Waste Water Treatment Center		\$0	\$2,500,000	\$0	\$0	\$2,500,000	\$0	\$0	\$0	\$5,000,000	
Total		\$4,388	\$2,531,472	\$158,468	\$6,159	\$2,530,504	\$0	\$2,886	\$55,185	\$5,289,063	
Project Budget	\$31,069,031										
Less Other Funding*	\$6,069,031			* Other Fundin	g Source:						
Net	\$25,000,000			Measure AA \$6							
Actual Measure S Expenditures	\$5,289,063										
Running Balance	\$19,710,937										

MEASURE S EXPENDITURES

FUND 42.3

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
C7100042 C7100066			-						ı	
S7100043, S7100066 Energy Efficiency Projects (7)										
		\$0	\$0	\$0	\$0	\$988	\$0	\$0	\$0	\$988
Legal Building & Additions		\$0 \$0	\$0 \$0	\$0 \$0		\$106,921	\$355,294	-\$180,342	\$0 \$0	\$281,873
Engineering		\$0 \$0	\$0 \$0	\$0 \$0		\$100,921	\$355,294	-\$160,342 \$0	\$0 \$0	\$10,500
Inspection & Testing		\$0 \$0	\$0 \$0	\$0 \$0	\$10,500	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$10,500
		\$0 \$0	\$0 \$0	\$0 \$0		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0
Project Management Total		\$0 \$0	\$0 \$0	\$0		\$107,910		-\$180,342	\$0 \$0	
Project Budget	\$1.293.570	Received	ψU	ψŪ	\$10,500	\$107,910	\$355,∠94	-\$100,342	\$ 0	\$293,361
, 0	, , , -			* 041 5	. 0					
Less Other Funding*	\$217,322	\$217,322		* Other Fundin	g Source:	O				
Net	\$1,076,248			SCE & The Ga	s Co. \$217,322	z receivea				
Actual Measure S Expenditures	\$293,361									
Running Balance	\$782,887									
S7100091, S7100092										
Satellite Campus Parking Facilities and Roadway I	mprovements (
Legal		\$0	\$0	\$0	\$300	\$175	\$0	\$0	\$0	\$475
Other Contract Services		\$0	\$0	\$0	\$300	\$0	\$0	\$0	\$0	\$300
Advertising		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$278,178	\$1,860,152	\$449,543	\$37,777	\$0	\$2,625,651
Architect		\$0	\$0	\$324,919	\$324,864	\$136,911	\$34,490	\$1,397	\$0	\$822,582
Inspection & Testing		\$0	\$0	\$0	\$31,100	\$185,947	\$28,218	\$360	\$0	\$245,626
Project Management		\$0	\$0	\$0	\$18,288	\$64,880	\$31,137	\$8,659	\$0	\$122,964
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$3,387	\$0	\$0	\$3,387
Total		\$0		\$324,919	\$653,031	\$2,248,065	\$546,775	\$48,194	\$0	\$3,820,983
Project Budget	\$4,875,000				·				•	
Less Other Funding	\$0									
Net	\$4,875,000									
Actual Measure S Expenditures	\$3,820,983									
Running Balance	\$1,054,017									

MEASURE S EXPENDITURES

FUND 42.3

As of December 31, 2011

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
S7100142										
Parking Garage and Grounds - Student Services (9))									
Supplies		\$0	\$0	\$0	\$0	\$1,745	\$0	\$0	\$648	\$2,393
Consultants		\$0	\$0	\$0	\$0	\$20,700	\$0	\$0	\$0	\$20,700
Legal		\$0	\$0	\$0	\$0	\$2,154	\$17,486	\$4,800	\$1,603	\$26,043
Other Contract Services		\$0	\$0	\$0	\$0	\$1,508	\$10,952	\$1,986	\$0	\$14,446
Building & Additions		\$0	\$0	\$0	\$0	\$2,555,940	\$5,925,152	\$78,717	\$77,320	\$8,637,129
Architect		\$0	\$0	\$0	\$2,266,766	\$2,674,054	\$0	\$37,111	\$75,163	\$5,053,094
Engineering		\$0	\$0	\$0	\$0	\$4,813	\$38,330	\$42,968		\$98,898
Inspection & Testing		\$0	\$0	\$0	\$0	\$131,009	\$161,847	\$54,069		\$360,950
Project Management		\$0	\$0	\$0	\$0	\$158,766	\$373,559	\$184,088	\$62,561	\$778,974
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$14,393	\$0	\$0	\$14,393
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	. ,	\$11,381
Total		\$0	\$0	\$0	\$2,266,766	\$5,550,689	\$6,541,719	\$403,737	\$255,488	\$15,018,400
Project Budget	\$53,143,653	Received								
Less Other Funding*	\$453,000	\$0		* Other Fundin						
Net	\$52,690,653			State of Califor	nia \$453,000 a	llocated				
Actual Measure S Expenditures	\$15,018,400									
Running Balance	\$37,672,253									



Project Description:

Consolidates various student services departments and college administration in a single complex at the front of the campus

Facility Size:


83,634 sq/ft & 500 cars underground parking structure

Status:

Phase 1 completed Phase 2 in plan check with DSA

Architect:

Steinberg Architects

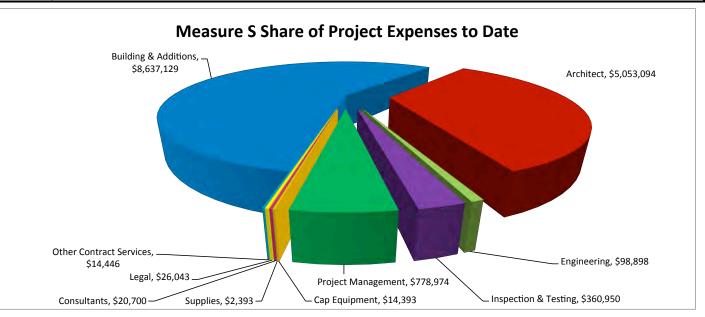

MEASURE S EXPENDITURES

FUND 42.3 As of December 31, 2011

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/06 Final	Uo/U9 Finai	09/10 Final	10/11 Final	11/12	Combined rotals
S7100044								1	1	
Pico Promenade Improvements (10)										
Building & Additions		\$0	\$0	\$0	\$690	\$883,401	\$0	\$0	\$0	\$884,091
Architect		\$0 \$0	\$0 \$0	\$0 \$0			\$864	\$0 \$0	\$0	\$98,595
Inspection & Testing		\$0 \$0	\$0 \$0				\$004		\$0 \$0	\$7,591
Project Management		\$0 \$0	\$0 \$0	\$0 \$0				\$0 \$0	\$0	\$27,733
Total		\$0					\$8 64	\$0 \$0	\$0	\$1,018,009
Project Budget	\$1,018,009	ΨΟ	ΨΟΙ	ΨΟ	ψ1 Z,000	\$343,000	\$004	ΨΟ	ΨΟΙ	\$1,010,009
Less Other Funding	\$0									
Net	\$1,018,009									
Actual Measure S Expenditures	\$1,018,009									
Running Balance	\$1,010,003									
Turining Balarice	ΨΟ									
S7100004						T			1	
Master Planning (11)						-				
Consultants		\$0	\$0	\$0	\$0	\$0	\$441,549	\$13,320	\$0	\$454,869
Printing		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0	\$4,157	\$13,320	\$0 \$0	\$4,157
Advertising		\$0 \$0	\$0 \$0	\$0 \$0				\$0	\$0 \$0	\$3,000
Other Contract Services		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0	\$3,000	\$200	\$0 \$0	\$5,000 \$642
Architect		\$0 \$0	\$0 \$0	\$0 \$0				\$24,736	\$0	\$217,094
Project Management		\$0 \$0	\$0 \$0				\$16.638	\$9,341	\$0 \$0	\$25,979
Filling Fees		\$0 \$0	\$0 \$0					\$2,842	\$0 \$0	\$2,842
Total		\$0 \$0			\$0 \$0	\$0 \$0		\$50,439	\$0 \$0	\$708,583
Project Budget	\$750,000	\$ 0	Ψ0	φυ	φυ	40	\$000,140	\$50,455	Ψ 0]	\$100,303
Less Other Funding	\$7,50,000									
Net	\$750,000									
Actual Measure S Expenditures	\$708,583									
Running Balance	\$41,417									
Turning Balance	Ψ+1,+17									
S7100048									1	
Other Bond Related Expenses (12)										
Lease/Rental		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,620	\$3,620
Supplies		\$0 \$0	\$0 \$0	\$0 \$0		\$0			\$0,020	\$3,638
Legal		\$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0		\$15,649	\$2,682	\$27,248
Software License		\$0	\$0	\$0	\$0	\$0	\$0,517	\$1,997	\$0	\$1,997
Advertising		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0	\$2,278	\$0	\$0 \$0	\$2,278
Other Contract Services		\$0 \$0	\$0	\$0	\$0		\$17,206	\$23,558	\$15,491	\$58,055
Moving Services		\$0	\$0			\$1,500	\$400	\$0	\$15,491	\$400
Project Management		\$0	\$0	\$0	\$0		\$17,747	\$13,179	\$8,785	\$39,710
Cap Equipment		\$0 \$0	\$0			\$0			\$0,700	\$10,086
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0			\$1,418	\$4,278
Total		\$0			\$0	\$1,800			\$31,997	\$151,310
Project Budget	\$662,764	ΨΟ	ΨΟΙ	Ψ0		. .,000	400,100	¥0.,520	ψο.,σοι	\$101,010
Less Other Funding	\$0									
Net	\$662,764									
Actual Measure S Expenditures	\$151,310									
Running Balance	\$511,454									
Training Balance	Ψ511,454									

MEASURE S EXPENDITURES

FUND 42.3 As of December 31, 2011

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
S7100049										
Adv Architecture Related Exp for AA (13)										
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0 \$0
Other Contract Services		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$45,734		\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0 \$0
Total		\$0	\$0	\$0	\$0	\$45,734	-\$45,734	\$0	\$0	\$0
Project Budget	\$0									
Less Other Funding	\$0									
Net	\$0									
Actual Measure S Expenditures	\$0 \$0									
Running Balance	\$0									
S7100057										
Real Property Acquisition (14)										
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$18,721	\$0	\$0	\$18,721
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$6,336		\$0	\$6,336
Project Management		\$0	\$0	\$0		\$0	\$20,540	\$0	\$0	\$20,540
Total		\$0	\$0	\$0	\$0	\$0	\$45,597	\$0	\$0	\$45,597
Project Budget	\$50,000									
Less Other Funding	\$0									
Net	\$50,000									
Actual Measure S Expenditures	\$45,597									
Running Balance	\$4,403									

MEASURE S EXPENDITURES

FUND 42.3 As of December 31, 2011

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12	Combined Totals
S7100072										
Campus Signage (15)										
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$303	\$0	\$303
Consultants		\$0	\$0	\$0	\$0	\$0	\$32,225	\$23,725	\$0	\$55,950
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$187	\$0	\$187
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$638	\$0	\$638
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$22,953	\$0	\$22,953
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$156,258	\$0	\$156,258
Total		\$0	\$0	\$0	\$0	\$0	\$32,225	\$204,064	\$0	\$236,289
Project Budget	\$606,223									
Less Other Funding	\$0	1								
Net	\$606,223	1								
Actual Measure S Expenditures	\$236,289	1								
Running Balance	\$369,934	1								

\$8,321,918 \$20,819,624

\$8,933,245

\$617,492

\$344,728


\$72,337,600

\$7,958,606 \$14,601,366 \$10,740,621

Grand Total

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget As of December 31, 2011

	Project Name	Completion	Project Budget	Measure AA Allocation	Other Funding	Measure AA Expenditures as of 12/31/11	Measure AA Expenditures as of 9/30/11	Measure AA Expenditures Last Period	Total Measure AA Remaining
101	Environmental Performance - Central Plant Connections	September 2014	\$4,882,119	\$4,882,119	\$0	\$91,218	\$79,070	\$12,148	\$4,790,901
102	Infrastructure & Technology - Information Technology Relocation	November 2013	\$13,287,218	\$13,287,218	\$0	\$1,010,690	\$795,905	\$214,785	\$12,276,528
103	Media and Technology Complex - Academy Site	October 2014	\$61,480,824	\$57,700,824	\$3,780,000	\$5,357,689	\$5,204,123	\$153,566	\$52,343,135
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	May 2014	\$40,200,333	\$35,384,240	\$4,816,093	\$2,562,739	\$2,047,442	\$515,297	\$32,821,501
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	December 2016	\$34,026,480	\$34,026,480	\$0	\$0	\$0	\$0	\$34,026,480
106	Replacement Math and Science Extension Building	December 2016	\$108,103,000	\$68,259,000	\$40,134,000	\$0	\$0	\$0	\$68,259,000
107	Madison East Wing Seismic Upgrade	August 2013	\$12,292,000	\$12,292,000	\$0	\$1,301,368	\$716,850	\$584,518	\$10,990,632
108	Renovation of Corsair Stadium	Not Scheduled	\$2,415,898	\$2,415,898	\$0	\$35,299	\$35,299	\$0	\$2,380,599
109	Career Opportunity and Advancement Center (Bundy)	Not Scheduled	\$41,391,000	\$29,384,000	\$12,007,000	\$0	\$0	\$0	\$29,384,000
110	Malibu Center	Not Scheduled	\$31,069,031	\$6,069,031	\$25,000,000	\$0	\$0	\$0	\$6,069,031
111	Business & Facilities Infrastructure	On-Going	\$6,140,952	\$6,140,952	\$0	\$170,874	\$149,002	\$21,872	\$5,970,078
112	Master Planning, Program Management, Overhead	On-Going	\$1,650,000	\$1,650,000	\$0	\$0	\$0	\$0	\$1,650,000
113	Energy Efficiency Projects	On-Going	\$4,150,136	\$4,150,136	\$0	\$0	\$0	\$0	\$4,150,136
114	Community Classroom & Facility Projects	December 2011	\$3,221,000	\$3,221,000	\$0	\$2,001,263	\$1,288,838	\$712,425	\$1,219,737
115	Real Property Acquisition	On-Going	\$14,787,102	\$14,787,102	\$0	\$14,787,102	\$5,764,895	\$9,022,207	\$0
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	On-Going	\$350,000	\$350,000	\$0	\$395,682	\$268,591	\$127,091	-\$45,682
117	Infrastructure & Technology - Technology	On-Going	\$500,000	\$500,000	\$0	\$302,259	\$235,840	\$66,419	\$197,741
118	Infrastructure & Technology - Utility	On-Going	\$500,000	\$500,000	\$0	\$20,219	\$20,219	\$0	\$479,781
	Project Totals		\$380,447,093	\$295,000,000	\$85,737,093	\$28,036,402	\$16,606,074	\$11,430,328	\$266,963,598

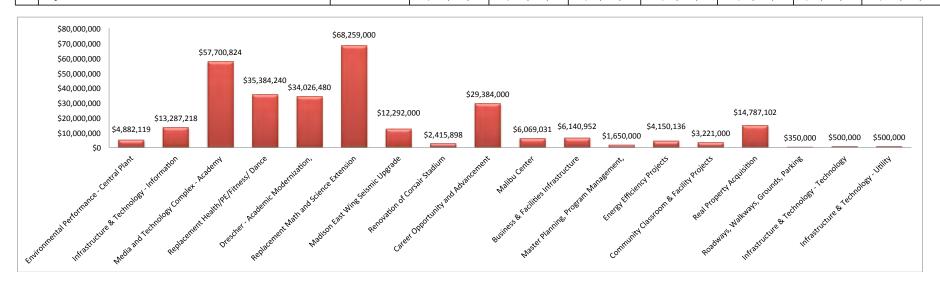

Measure AA Project Schedule As of December 31, 2011

	Project Name	Completion	2	011		2	012	201	13		2014	ļ	2	015		201	16
101	Environmental Performance - Central Plant Connections	September 2014															\prod
102	Infrastructure & Technology - Information Technology Relocation	November 2013															
103	Media and Technology Complex - Academy Site	October 2014															
104	Replacement Health/PE/Fitness/Dance Building with Central Plant	May 2014															
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	December 2016															
106	Replacement Math and Science Extension Building	December 2016															
107	Madison East Wing Seismic Upgrade	August 2013															
108	Renovation of Corsair Stadium	Not Scheduled															
109	Career Opportunity and Advancement Center (Bundy)	Not Scheduled															
110	Malibu Center	Not Scheduled															
111	Business & Facilities Infrastructure	On-Going															
112	Master Planning, Program Management, Overhead	On-Going															
113	Energy Efficiency Projects	On-Going															
114	Community Classroom & Facility Projects	December 2011															
115	Real Property Acquisition	On-Going															
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	On-Going															
117	Infrastructure & Technology - Technology	On-Going															
118	Infrastructure & Technology - Utility	On-Going															
					In F	Plann	ing	In C	Const	ructio	on				丄		

SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE AA EXPENDITURES FUND 42.4

Projects	Budget	09/10 Final	10/11 Final	11/12	Combined Totals
AA 7100062					
Environmental Performance - Central Plant Connections (101)					
Legal		\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0
Consultants		\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0
Architect		\$0	\$385	\$0	\$385
Engineering		\$48,500	\$0	\$4,000	\$52,500
Inspection & Testing		\$0	\$0	\$0	\$0
Project Management		\$0	\$17,263	\$21,070	\$38,333
Cap Equipment		\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0
Total		\$48,500	\$17,648	\$25,070	\$91,218
Project Budget	\$4,882,119		-		
Less Other Funding	\$0				
Net	\$4,882,119				
Actual Measure AA Expenditures	\$91,218				
Running Balance	\$4,790,901				

Projects	Budget	09/10 Final	10/11 Final	11/12	Combined Totals
		•	•		
AA 7100063					
Infrastructure & Technology - IT Relocation (102)					
Legal		\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$1,679	\$1,679
Supplies		\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0
Architect		\$105,049	\$482,261	\$246,773	\$834,083
Engineering		\$0	\$0	\$2,738	\$2,738
Inspection & Testing		\$10,291	\$8,793	\$14,248	\$33,332
Project Management		\$33,460	\$76,290	\$29,108	\$138,858
Cap Equipment		\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0
Total		\$148,800	\$567,344	\$294,546	\$1,010,690
Project Budget	\$13,287,218		-	-	
Less Other Funding	\$0				
Net	\$13,287,218				
Actual Measure AA Expenditures	\$1,010,690				
Running Balance	\$12,276,528				

Infrastructure & Technology -**IT Relocation**

Project Description:Relocation of IT/Telecom Departments, and renovation of Media Center

Facility Size:


9,230 sq/ft

Status:

In design development

Architect:

Morris Architects

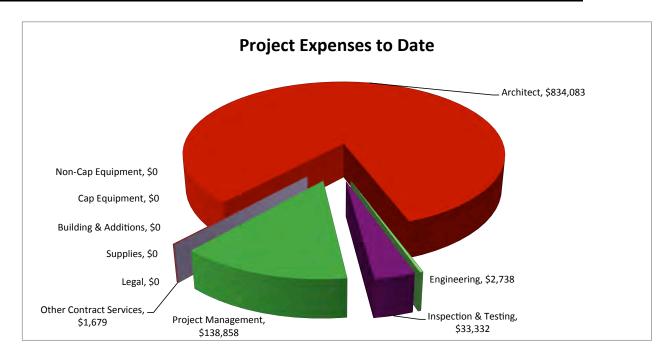

Projects	Budget	09/10 Final	10/11 Final	11/12	Combined Totals
AA 7100061					
Media and Technology Complex - Academy Site (103)					
Consultants		\$0	\$0	\$0	
Supplies		\$0	\$0	\$0	\$0
Legal		\$16,903	\$0	\$0	\$16,903
Other Contract Services		\$3,993	\$5,763	\$6,473	\$16,229
Advertising		\$0	\$0	\$0	\$0
Building & Additions		\$0	\$538	\$0	\$538
Architect		\$2,097,553	\$2,508,588	\$128,287	\$4,734,427
Engineering		\$16,459	\$29,293	\$7,408	\$53,160
Inspection & Testing		\$64,905	\$27,527	\$139	\$92,571
Project Management		\$121,786	\$233,826	\$88,249	\$443,860
Cap Equipment		\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0
Total		\$2,321,599	\$2,805,534	\$230,556	\$5,357,689
Project Budget	\$61,480,824	Received	· · · · ·		
Less Other Funding*	\$3,780,000	\$803,412			
Net	\$57,700,824	* Other Funding So	ource:		
Actual Measure AA Expenditures	\$5,357,689	KCRW Foundation	\$3,780,000 commi	ted,	
Running Balance		\$803,412 received			

Media and Technology Complex - Academy Site

Project Description:

Renovation and new extension to the existing building, new building for KCRW, and a new parking structure

Facility Size:


Building - 47,172 sq/ft Parking Structure - 450 spaces

Status:

Building in construction drawings Parking structure in DSA

Architect:

Clive Wilkinson Architects

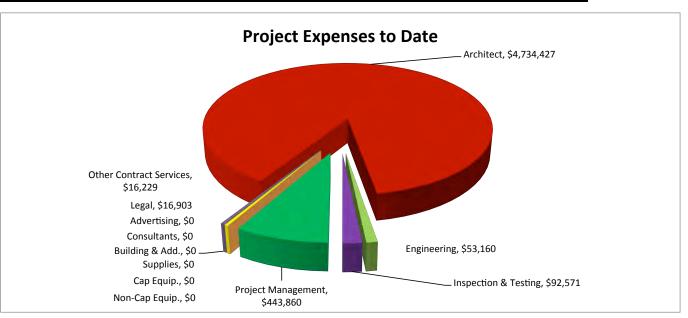

Projects	Budget	09/10 Final	10/11 Final	11/12	Combined Totals
AA 7100060					
Repl. Health/PE/Fitness/Dance Building with Central Plant (104)					
Consultants		\$0	\$0	\$0	\$0
Supplies		\$0	\$0	\$0	\$0
Other Contract Services		\$120	\$38	\$112	\$270
Building & Additions		\$0	\$0	\$0	\$0
Architect		\$256,076	\$1,568,564	\$477,213	\$2,301,853
Engineering		\$0	\$8,507	\$4,844	\$13,351
Inspection & Testing		\$36,892	\$490	\$11,617	\$48,999
Project Management		\$34,968	\$113,379	\$49,919	\$198,266
Total		\$328,056	\$1,690,978	\$543,705	\$2,562,739
Project Budget	\$40,200,333				
Less Other Funding*	\$4,816,093	* Other Funding So	urce:		
Net	\$35,384,240	Measure S \$4,816,	093 allocated		
Actual Measure AA Expenditures	\$2,562,739				
Running Balance	\$32,821,501				

Repl. Health/PE/Fitness/Dance Building with Central Plant

Project Description:

Replacement of locker rooms, fitness center, dance studios, and new central plant

Facility Size:


62,000 sq/ft

Status:

In design development

Architect:

Gensler Architects

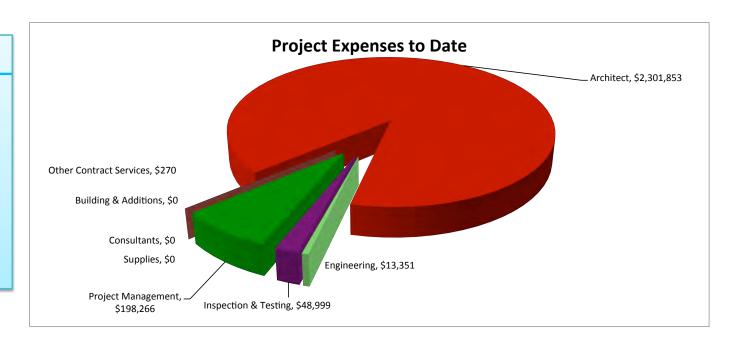

Projects	Budget	09/10 Final	10/11 Final	11/12	Combined Totals
AA 7100047					
Madison East Wing Seismic Upgrade (107)					
Consultants		\$0	\$0	\$0	\$0
Supplies		\$0	\$0	\$0	\$0
Legal		\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$364	\$698	\$1,061
Building & Additions		\$0	\$656	\$269,350	\$270,006
Architect		\$76,073	\$398,050	\$263,271	\$737,394
Engineering		\$0	\$0	\$2,623	\$2,623
Inspection & Testing		\$0	\$19,848	\$11,489	\$31,337
Project Management		\$5,557	\$128,878	\$66,485	\$200,920
Non-Cap Equipment		\$0	\$0	\$58,027	\$58,027
Total		\$81,630	\$547,796	\$671,942	\$1,301,368
Project Budget	\$12,292,000			•	
Less Other Funding	\$0				
Net	\$12,292,000				
Actual Measure AA Expenditures	\$1,301,368				
Running Balance	\$10,990,632				

Madison East Wing Seismic Upgrade

Project Description:

Replacement of east wing with a new multipurpose room and additional classrooms

Facility Size:


15,461 sq/ft

Status:

In design development

Architect:

DLR Group WWCOT

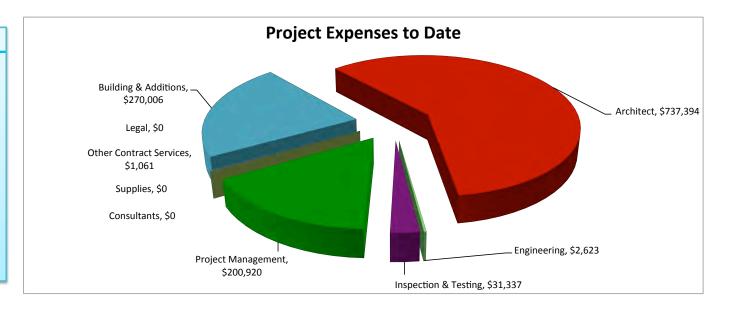

Projects	Budget	09/10 Final	10/11 Final	11/12	Combined Totals
AA 7400000		1		ı	
AA 7100068 Renovation to Corsair Stadium (108)					
Other Contract Services		\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0 \$0	\$0 \$0	\$0
Architect		\$0	\$30,759	\$0 \$0	\$30,759
Engineering		\$0 \$0	\$0,739 \$0	\$0 \$0	\$00,738
Inspection & Testing		\$0	\$0 \$0	\$0	\$0
Project Management		\$0	\$4,540	\$0	\$4,540
Total		\$0	\$35,299	\$0	\$35,299
Project Budget	\$2,415,898	Ψ	Ψ00,200	ΨΟ	Ψ00,200
Less Other Funding	\$0				
Net	\$2,415,898				
Actual Measure AA Expenditures	\$35,299				
Running Balance	\$2,380,599				
AA 7100067 Business & Facilities Infrastructure (111)					
Other Contract Services		\$0	\$6,289	\$0	\$6,289
Building & Additions		\$0	\$34.672	\$0 \$0	\$34,672
Architect		\$0 \$0	\$0	\$0 \$0	\$34,072
Engineering		\$0	\$0 \$0	\$0 \$0	\$0
Inspection & Testing		\$0	\$0 \$0	\$0	\$0
Project Management		\$0	\$3,073	\$37,636	\$40,709
Non-Cap Equipment		\$0	\$89,204	\$0	\$89,204
Total		\$0	\$133,238	\$37,636	\$170,874
Project Budget	\$6,140,952	+ •	\$100,200	ψο.,,σοσ	\$110,01
Less Other Funding	\$0				
Net	\$6,140,952				
Actual Measure AA Expenditures	\$170,874				
Running Balance	\$5,970,078				
AA 7100064		1		1	
Community Classroom & Facility Projects (114)					
Legal		\$0	\$0	\$150	\$150
Other Contract Services		\$0 \$0	\$3,720	\$1.454	\$5,174
Building & Additions		\$0	\$434,578	\$959,476	\$1,394,054
Architect		\$0	\$263,833	\$28,222	\$292,055
Engineering		\$0	\$3,220	\$1,958	\$5,178
Inspection & Testing		\$0 \$0	\$41,002	\$61,505	\$102,507
Project Management		\$135	\$117,247	\$84,764	\$202,146
Total		\$135	\$863,599	\$1,137,529	\$2,001,263
Project Budget	\$3,221,000	\$100	4000,000	ψ.,.σ.,σ2σ	4 2,001,200
Less Other Funding	\$0				
Net	\$3,221,000				
Actual Measure AA Expenditures	\$2,001,263				
Running Balance	\$1,219,737				

Projects	Budget	09/10 Final	10/11 Final	11/12	Combined Totals
			•		
AA 7100057					
Real Property Acquisition (115)					
Legal		\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$39	\$7,000	\$7,039
Site Acquisition		\$1,739,979	\$4,001,204	\$9,022,207	\$14,763,389
Inspection & Testing		\$8,689	\$7,986	\$0	
Project Management		\$0	\$0	\$0	
Total		\$1,748,667	\$4,009,228	\$9,029,207	\$14,787,102
Project Budget	\$14,787,102				
Less Other Funding	\$0				
Net	\$14,787,102				
Actual Measure AA Expenditures	\$14,787,102				
Running Balance	\$0				
•					
AA 7100058, 7100151					
Roadways, Walkways, Grounds, Parking Lots, and Garages (116)					
Legal		\$0	\$0	\$0	\$0
Other Contract Services		\$218	\$770	\$122	\$1,110
Building & Additions		\$185,345	\$6,731	\$112,984	\$305,060
Inspection & Testing		\$13,380	\$7,865	\$12,119	
Project Management		\$24,404	\$12,439	\$19,306	\$56,149
Total		\$223,347	\$27,804	\$144,530	\$395,682
Project Budget	\$350,000				
Less Other Funding	\$0				
Net	\$350,000				
Actual Measure AA Expenditures	\$395,682				
Running Balance	-\$45,682				
		Ī			
AA 7100069					
Infrastructure & Technology - Technology (117)		00	A0 470	* 40.000	055 770
Maintenance Contract		\$0	\$9,472	\$46,300	\$55,773
Building & Additions		\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0
Project Management		\$0	\$0	\$0	\$0
Cap Equipment		\$0	\$207,423	\$39,063	\$246,487
Non-Cap Equipment		\$0	\$0	\$0	\$0
Total		\$0	\$216,896	\$85,364	\$302,259
Project Budget	\$500,000				
Less Other Funding	\$0				
Net	\$500,000				
Actual Measure AA Expenditures	\$302,259				
Running Balance	\$197,741				

SANTA MONICA COMMUNITY COLLEGE DISTRICT MEASURE AA EXPENDITURES FUND 42.4

Projects	Budget	09/10 Final	10/11 Final	11/12	Combined Totals
AA 7100069					
Infrastructure & Technology - Utility (118)					
Sofeware License		\$0	\$12,000	\$0	\$12,000
Legal		\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0
Architect		\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$4,979	\$0	\$4,979
Project Management		\$0	\$3,240	\$0	\$3,240
Cap Equipment		\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0
Total		\$0	\$20,219	\$0	\$20,219
Project Budget	\$500,000		<u> </u>		
Less Other Funding	\$0				
Net	\$500,000				
Actual Measure AA Expenditures	\$20,219				
Running Balance	\$479,781				
Grand Total		\$4,900,734	\$10,935,584	\$12,200,085	\$28,036,402


SANTA MONICA COMMUNITY COLLEGE DISTRICT Bond Sales / Expenses Report As of December 31, 2011

Measure U Bond \$160,000,000		
Bond Issue Date		Amount
	2002	\$25,000,000
	2004	\$21,999,971
	2005	\$89,999,923
	2007	\$11,999,987
	2010	\$10,998,992
Total Available		\$159,998,873
Expenses as of 12-31-11		\$142,525,436
Total Available Remaining		\$17,473,437
Unsold Bond Amount		\$1,127
Total Available as of 1-1-12		\$17,474,564

Measure S Bond \$143,500,000 (1)		
Bond Issue Date		Amount
	2005	\$58,000,000
	2007	\$8,500,000
	2009	\$56,997,857
Total Available		\$123,497,857
Expenses as of 12-31-11		\$72,337,601
Total Available Remaining		\$51,160,256
Unsold Bond Amount		\$20,002,143
Total Available as of 1-1-12		\$71,162,399

Measure AA Bond \$295,000,000	
Bond Issue Date	Amount
2010	\$100,000,000
Total Available	\$100,000,000
Expenses as of 12-31-11	\$28,036,402
Total Available Remaining	\$71,963,598
Unsold Bond Amount	\$195,000,000
Total Available as of 1-1-12	\$266,963,598

\$598,500,000
\$383,496,730
\$242,899,439
\$140,597,291
\$215,003,270

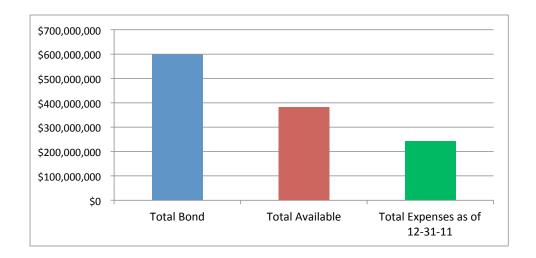

Interest	Measure U	Measure S	Measure AA
As of 6-30-11	\$5,996,729	\$8,106,718	\$1,715,719
Arbitrage Payment as of 6-30-11	\$0	\$393,004	\$0
Available Interest as of 6-30-11	\$5,996,729	\$7,713,714	\$1,715,719

Cost of Issuance Refund	Measure U	Measure S
As of 6-30-11	\$20,688	\$35,575
