



Santa Monica Community College District Citizens' Bond Oversight Committee ANNUAL REPORT, 2017-2018

Submitted to the Santa Monica Community College District BOARD OF TRUSTEES

- Barry Snell, Chair
- Dr. Margaret Quiñones-Perez, Vice-Chair
- Dr. Susan Aminoff
- Dr. Nancy Greenstein
- Dr. Louise Jaffe, Chair
- Dr. Andrew Walzer
- Rob Rader
- Charlene Alex Boyd, Student Trustee

CITIZENS' BOND OVERSIGHT COMMITTEE

Sonya Sultan, Chair Jeffrey Graham Sion Roy Sharon Barovsky Michael Dubin Alfred Barrett Garrison Finley

Staff Support

Charlie Yen, Director Facilities Finance Elaine Polachek, Interim EVP Christopher Bonvenuto, Chief Director, Business Services Ramin Nematollahi, Committee Coordinator

TABLE OF CONTENTS



Santa Monica Community College District CITIZENS' BOND OVERSIGHT COMMITTEE ANNUAL REPORT, 2017-2018

| Statement of Compliance | |
|---|----|
| Measure U | 3 |
| Measure S | 4 |
| Measure AA | 5 |
| Citizens' Bond Oversight Committee Proceedings and Activities | 6 |
| Minutes of Meetings | |
| July 19, 2017 | 7 |
| October 25, 2017 | 10 |
| January 24, 2018 | 12 |
| April 25, 2018 | 16 |
| SMC Capital Outlay Program – Bond Project Descriptions and Project Status | 19 |
| SMC Capital Construction Budget Summary as of June 30, 2018 | 27 |
| Bond Sales/Expenses Report | 28 |
| Bond Budgets | |
| Measure U | 29 |
| Measure S | 31 |
| Measure AA | |
| Measure V | 35 |
| Measure U Reports | |
| Project Schedule | |
| Expenditures | 38 |
| Measure S Reports | |
| Project Schedule | |
| Expenditures | 48 |
| Measure AA Reports | |
| Project Schedule | |
| Expenditures | 58 |
| Measure V Reports | |
| Project Schedule | |
| Expenditures | 69 |
| | |
| SMC Bond Program Contractor List | 73 |



Santa Monica Community College District Citizens' Bond Oversight Committee

ANNUAL REPORT, 2017-2018

STATEMENT OF COMPLIANCE MEASURE U FUNDS

This Annual Report is submitted to the Board of Trustees by the Santa Monica Community College District Citizens' Bond Oversight Committee.

The Committee advises that, to the best of its knowledge, the Santa Monica Community College District is in compliance with the requirements in Article XIIIA, Section 1(b)(3) of the California Constitution. In particular, bond revenue has been expended only for the purposes so described in Measure U and no funds were used for any teacher or administrative salaries or other operating expenses as prohibited by Article XIIIA, Section 1(b)(3)(a) of the California Constitution.

Respectfully Submitted: Sony Fox Subtain

Date: Oct 10, 2018

Chair Citizens' Bond Oversight Committee



Santa Monica Community College District Citizens' Bond Oversight Committee

ANNUAL REPORT, 2017-2018

STATEMENT OF COMPLIANCE MEASURE S FUNDS

This Annual Report is submitted to the Board of Trustees by the Santa Monica Community College District Citizens' Bond Oversight Committee.

The Committee advises that, to the best of its knowledge, the Santa Monica Community College District is in compliance with the requirements in Article XIIIA, Section 1(b)(3) of the California Constitution. In particular, bond revenue has been expended only for the purposes so described in Measure S and no funds were used for any teacher or administrative salaries or other operating expenses as prohibited by Article XIIIA, Section 1(b)(3)(a) of the California Constitution.

Respectfully Submitted: Song Fol Quelle

Date: Oct 10,2018

Chair Citizens' Bond Oversight Committee



Santa Monica Community College District Citizens' Bond Oversight Committee

ANNUAL REPORT, 2017-2018

STATEMENT OF COMPLIANCE MEASURE AA FUNDS

This Annual Report is submitted to the Board of Trustees by the Santa Monica Community College District Citizens' Bond Oversight Committee.

The Committee advises that, to the best of its knowledge, the Santa Monica Community College District is in compliance with the requirements in Article XIIIA, Section 1(b)(3) of the California Constitution. In particular, bond revenue has been expended only for the purposes so described in Measure AA and no funds were used for any teacher or administrative salaries or other operating expenses as prohibited by Article XIIIA, Section 1(b)(3)(a) of the California Constitution.

Respectfully Submitted: Sony FySulf

Date:

Chair Citizens' Bond Oversight Committee



Santa Monica Community College District Citizens' Bond Oversight Committee

ANNUAL REPORT, 2017-2018

CITIZENS' BOND OVERSIGHT COMMITTEE PROCEEDINGS AND ACTIVITIES

Meetings of the Citizens' Bond Oversight Committee

The Committee conducts its meetings in accordance with provisions of the Ralph M. Brown Public Meetings Act, Government Code Sections 54950 *et seq*. Meeting notices and agendas are sent to members of the Committee within the required period of time and are also posted at eight Santa Monica College campus locations and satellite sites.

Meeting notices, agendas, minutes and all documents and reports received by the Committee members are a matter of public record and made available on the SMC website: http://www.smc.edu/CBOC

The SMC Bond Program website is located at: www.smcbondprogram.com

Minutes of the quarterly meetings are included on the following pages.



Santa Monica Community College District
Citizens' Bond Oversight Committee
MEETING – July 19, 2017
MINUTES

A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee was held on Wednesday, **July 19, 2017 at 8 a.m.** in Drescher 300---E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

1. CALL TO ORDER: 8:10 a.m.

2. ROLL CALL --- Members

- Sonya Sultan, Chair --- Present
- Katherine Reuter, Vice-Chair --- Absent
- Jeffrey Graham Absent
- Sion Roy --- Present
- Sharon Barovsky --- Absent
- Michael Dubin Absent

Others Present:

- Cassandra Santiago-Amzallag Student Representative Present (To be presented for approval at the August Board of Trustees meeting)
- Chris Bonvenuto, Chief Director, Business Services
- Greg Brown, Director Facilities Planning
- Don Girard, Senior Director, Government Relations/Institutional Communications
- Ramin Nematollahi, Citizens' Bond Oversight Committee Coordinator
- Charlie Yen, Director Contracts
- Emil Zordilla, Assistant Director, Facilities Planning
- Elizabeth Chavira Project Manager/Construction Manager– Vanir
- Gustavo Ripalda Project Manager/Construction Manager Vanir

3. APPROVAL OF MINUTES

Action was not taken due to lack of guorum.

4. REPORTS and DISCUSSION

A. SMC Bond Capital Construction Budget Summary.

Charlie Yen, discussed the SMC bond Capital Constructer Budget Summary as of June 30, 2017.

- **Core Performance Center**: Second phase, has started with the older-locker-rooms and bathrooms being renovated, and is scheduled to be completed by early quarter of 2018.
- Center for Media and Design: The project is continuing as planned and fall occupancy is expected. KCRW will most likely move in later in the fall due to their technological requirements.
- Student Services Building: Construction is proceeding as planned and completion date is 2019.
- Malibu Campus: Currently awaiting the finalization of lease from Los Angeles County.

 Bidding for the project will take place in the summer of 2017 with construction to begin in

- fall of 2017. Completion date is last quarter of 2019.
- Early Childhood Education Center: Awaiting coastal commission approval. Bidding for the project is expected in the summer of 2017 with construction to commence fall 2017. The project is schedule to be completed fall of 2018.
- B. Measure U, S and AA and Bond Sales Expense Reports

The SMC Bond Capital Construction Budget Summary as of June 30, 2017 reports the following:

Measure U Budget: \$160,000,000 Measure S Budget: \$143,500,000 Measure AA Budget: \$295,000,000 \$345,000,000 Measure V Budget: Interest \$ 21,495,870 Other Funding Received: \$ 26,228,381 Other Funding Pending: \$ 52,594,548 **Total Budget:** \$ 1,043,818,799 Estimate at Completion: \$ 1,043,818,799 **Bond Funds Remaining:** \$ 462,892,008

- Measure U: Total Measure U Expenditures last period were \$105,155; total remaining funds are \$1,939,510; no budget variance.
- Measure S: Total Measure S Expenditures last period were \$4,328,007; total remaining funds are \$47,078,885; no budget variance.
- Measure AA: Total Measure AA Expenditures last period were \$8,530,284; total remaining funds are \$68,873,613; no budget variance.
- The Bond Sales/Expense Report

Indicates total bond amounts, bond issue dates/amounts unsold bond amount and total available as of June 30, 2017.

 Total Bond:
 \$598,500,000

 Total Available:
 \$528,492,559

 Total Expenses:
 \$480,607,992

 Total Available Remaining:
 \$117,884,567

 Total Unsold Bond:
 \$7,441

- Measure S Bond: \$20,000,000.00 (\$20 Million) was sold, April 2017.
- Measure AA bond: \$50,000,000.00 (\$50 Million was sold, April 2017.

The SMC Bond Construction Program Contractor List as of June 30, 2017 was included in the packet.

C. PRESENTATION OF THE DRAFT OF FACILITIES MASTER PLAN

Greg Brown, discussed a draft update of the SMC Educational Facilities Master Plan ("Master Plan"), a

set of strategies first adopted by the Board of Trustees in 1998 that have guided the development of facilities on our campuses and have presented SMC's needs to the public during bond campaigns.

Greg discussed that the last update of the Master Plan was in 2010, and a number of projects funded by voter-approved Measures U, S, and AA—the IT Building, the East Wing of the Performing Arts Campus, Student Services, and others—were included in that plan. The draft plan presented to the Board was based on the 2010 Master Plan, and took into account the new projects approved by Measure V, the \$345 million bond approved by voters in November 2016. These projects include a new Art complex to be housed at the new acquired property of the former YWCA, a renovation of the Business Building, an outdoor classroom, and a facelift of the 'frontage of Santa Monica College' on Pico Boulevard.

The campus build out is a 9 phase-multi-step process that has a 10 year time-frame. The new square footage footprint would be an increase of 1.88% or approximately 18,000 square feet.

In spring 2017, these new projects were discussed with the DPAC Facilities Committee and their comments were considered in putting together the draft plan. The public discussion of the draft plan also mentioned the Math/Science addition, for which partial funding has been received through the Governor's approved state budget.

The intent is to revise the plan and present it to the College and various constituency groups this fall.

7. SCHEDULE OF MEETINGS, 2017--2018

Wednesday, October 25, 2017 Wednesday, January 24, 2018 Wednesday, April 25, 2018 Wednesday, July 25, 2018

8. ADJOURNMENT: 9:07 am

The next meeting of the Citizens' Bond Oversight Committee will be held on **Wednesday, October 25, 2017 at 8 a.m. in Drescher Hall Room 300---E (the Loft) at Santa Monica College**, 1900 Pico Boulevard, Santa Monica, California.

Current information on all bond construction projects is available at: http://smcbondprogram.com and at http://smcbondprogram.com



Santa Monica Community College District
Citizens' Bond Oversight Committee
MEETING – October 25, 2017
MINUTES

A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee was held on Wednesday, October 25, 2017 at 8 a.m. in NOTE LOCATION CHANGE: Drescher 300-E (the Loft), 1900 Pico, Santa Monica, CA 90405. Meeting was held at: Center for Media Design Conference Room 216, 1660 Stewart Street, Santa Monica, CA 90404.

- CALL TO ORDER: 8:06 a.m.
 PUBLIC COMMENTS: None
- 3. ROLL CALL:
 - Sonya Sultan, Chair Present
 - Katherine Reuter, Vice-Chair Present
 - Sharon Barovsky Absent
 - Michael Dubin Present
 - Jeffrey Graham Absent
 - Sion Roy Absent
 - o Cassandra Santiago-Amzallag AS representative Present

Others Present:

- Elaine Polachek, Executive Vice President, Santa Monica College
- Don Girard, Senior Director, Government Relations/Institutional Communications
- Greg Brown, Director Facilities
- Chris Bonvenuto, Chief Director, Business Services
- Ramin Nematollahi, Citizens' Bond Oversight Committee Coordinator
- Charlie Yen, Director, Contracts
- Emil Zordilla, Assistant Director, Facilities Planning

3. APPROVAL OF MINUTES:

The minutes for the Citizens' Bond Oversight Committee Meeting of April 26, 2017 and July 19, 2017 were approved as is. *Motion was made by Katherine Reuter and seconded by Michael Dubin and unanimously approved.*

4. CITIZEN'S BOND OVERSIGHT COMMITTEE ANNUAL REPORT, 2016-2017:

The Annual Report 2016-2017 was approved as presented. *Motion was made by Katherine Reuter and seconded Michael Dubin and unanimously approved.*

5. REPORTS and DISCUSSION

- I. SMC Bond Construction Projects Update: Greg Brown, Director of Facilities, Charlie Yen, Director of Contracts, and Emil Zordilla, Assistant Director, Facilities Planning, gave an overview of bond construction projects:
 - **Center for Media and Design:** The building is open for operation, and will have an official grand opening on December 2nd. The KCRW building will be open for operation in spring 2018.
 - Core Performance Center: Formerly known as Center Health/P.E./Fitness/Central Plant, first phase is complete and building is open to occupancy. The second phase which will focus on updating the training room, weight room and additional facilities will be completed in early 2018.
 - **Student Services Building**: All framing for the building is complete and a "topping off" ceremony took place. The building is projected to be completed late 2019.
 - **Malibu Campus**: All approvals have been received. Currently awaiting approval from County of Los Angeles expected fall of 2017.

10

- **Early Childhood Education Center**: The coastal commission unanimously approved the plans, construction start spring of 2018.
- Math & Sciences: The building extension and upgrade would qualify for up to \$40 million in State funding, which requires a local match. The building will contain an upgraded planetarium and a community lab for all ages, including a nutrition and culinary lab in support of the College's nutrition program. Canon design has been selected to provide architectural design, anticipated in May of 2018.
- Measure U, S and AA and Bond Sales Expenses Reports (reports included with agenda)
- The SMC Bond Capital Construction Budget Summary as of September 30, 2017 reports the following:

| Measure U Budget: | \$160,000,000 |
|-------------------------|---------------|
| Measure S Budget: | \$143,500,000 |
| Measure AA Budget | \$295,000,000 |
| Other Funding Received: | \$ 26,736,062 |
| Other Funding Pending: | \$ 52,594,548 |
| Total Budget: | \$677,830,610 |
| Estimate at Completion: | \$677,830,610 |
| Bond Funds Remaining: | \$99,704,270 |

- **Measure U**: Total Measure U expenditures last period were \$2,362,100; total remaining funds are \$1,127; no budget variance.
- Measure S: Total expenditures last period were \$186,893 total remaining funds are \$43,050,473;
- **Measure AA**: Total expenditures last period were \$4,032,012; total remaining funds are \$56,660,112; no budget variance.
- The Bond Sales/Expenses Report indicates total bond amounts, bond issue dates/amounts, unsold bond amount and total available as of September 30, 2017.

| Total Bond: | \$598,500,000 |
|----------------------------|---------------|
| Total Available: | \$598,500,000 |
| Total Expenses: | \$498,788,289 |
| Total Available Remaining: | \$ 99,704,270 |
| Total Unsold Bond: | \$ 7,441 |

- The SMC Bond Construction Program Contractor List as of September 30, 2017 was presented for information.
- Current information on all bond construction projects is available at: http://smcbondprogram.com and at http://smcbondprogram.com and at http://smcbondprogram.com and at http://smcbondprogram.com and at http://smcbondprogram.com and at http://smcbondprogram.com

6. SCHEDULE OF MEETINGS FUTURE MEETINGS, 2017-2018

Wednesdays at 8 a.m.

- ✓ January 24, 2018
- ✓ April 25, 2018
- ✓ July 25, 2018

7. ADJOURNMENT: 9:06 AM

The next meeting of the Citizens' Bond Oversight Committee will be held on Wednesday, January 24, 2018 at 8 a.m. in Drescher 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.



Santa Monica Community College District
Citizens' Bond Oversight Committee
MEETING – January 24, 2018
MINUTES

A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee was held on Wednesday, **January 24, 2018 at 8 a.m.** in Drescher 300---E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

5. CALL TO ORDER: 8:05 a.m.

6. ROLL CALL --- Members

- Sonya Sultan, Chair --- Absent
- Katherine Reuter, Vice---Chair --- Present
- Jeffrey Graham Present
- Sion Roy --- Present
- Sharon Barovsky --- Present
- Michael Dubin --- Absent
- Cassandra Santiago-Amzallag –Present

Others Present:

- Alicia Herrera Varinek, Trine, Day & Company (VTD)– CPA
- Dr. Kathryn E. Jeffery, Superintendent/President
- Elaine Polachek, Interim Executive Vice President
- Don Girard, Senior Director, Government Relations/Institutional Communications
- Chris Bonvenuto, Chief Director, Business Services
- Ramin Nematollahi, Citizens' Bond Oversight Committee Coordinator
- Charlie Yen, Director --- Contracts
- Emil Zordilla, Assistant Director, Facilities Planning

Community Member(s) Present:

Stacy Dalgleish

7. APPROVAL OF MINUTES

The minutes of the Citizens' Bond Oversight Committee meeting of October 25, 2017 were approved as is. *Motion was made by Katherine Reuter and seconded by Sion Roy and unanimously approved by the committee.*

8. CONFLICT OF INTEREST FORM

Members completed and endorsed forms. The forms are on file. Members absent from meeting will mail in forms.

9. REPORTS and DISCUSSION

Ms. Alicia Herrera, Auditor for Varinek, Trine, Day & Company presented the 2016-2017 Financial and Performance Audit Reports.

D. Santa Monica Community College District

Measure U, Measure S, Measure AA General Obligation Bonds Financial and Performance Audit, June 30, 2017

She reviewed the Opinion of the findings which state:

"In our opinion, the financial statements referred to above present fairly, in all material respects, the financial position of Measure U, Measure S, Measure AA General Obligation Bond Funds (Measure U, Measure S, and Measure AA) of the District as of June 30, 2017, and the respective changes in financial position for the year then ended in accordance with accounting principles generally accepted in the Unites State of America." (Page 3, of the SMCCD, Measure U, Measure S & Measure AA General Obligation Bonds Financial And Performance Audits – June 30, 2017 – Varinek, Trine, Day & Co. LLP)

She reiterated the "unmodified opinion", which is the highest mark that can be received for a financial and performance audit. She further reviewed, **The Statement of Revenues**, **Expenditures**, **and Changes in Fund Balance** on page 5 and discussed the "**None Reported**" findings on Financial Statement Findings on page 17.

E. Santa Monica Community College District

Measure U, Measure S, Measure AA General Obligation Bonds Performance Audit June 30, 2016

Ms. Herrera discussed the procedures performed for the performance audit. A sample of expenditures was selected starting July 1, 2016 and ending June 30, 2017, and supporting documentation was reviewed to ensure that funds were properly expended on specific project list. The dollar value of transactions tested totaled \$50,600,727, which represent 63 percent of the total expenditures of \$79,817,120. (Page 4, of the SMCCD, Measure U, Measure S & Measure AA General Obligation Bonds Performance Audits – June 30, 2017 – Varinek, Trine, Day & Co. LLP)

Based on this testing, Varinek, Trine, Day & Co. LLP, verified that funds from Measures U, Measures S, and Measures AA general Obligation Bond Funds (Measure U, Measure S, Measure AA) were expended for the construction, renovation, funding and equipment of District facilities constituting authorized bond projects.

Conclusion:

"The results of our test indicated that, in all significant respect, the Santa Monica Community College District has properly accounted for the expenditures held in the Measure, U, Measure S, and Measure AA general Obligation Bond Funds (Measure U, Measure S, Measure AA) and such expenditures were made for authorized bond projects. There were no salaries of administrative charged to the Measure U, Measure S, and Measure AA General Obligation Bond Funds for District general administration or operations." (Page 4, of the SMCCD, Measure U, Measure S & Measure AA General Obligation Bonds Performance Audits – June 30, 2017 – Varinek, Trine, Day & Co. LLP)

Ms. Herrera also discussed the "none reported" comment regarding the Schedule of Findings and Questioned Costs – Page 5, (June 30, 2017) and reiterated that "There were no audit findings reported in the prior year's Schedule of Findings and Questioned Costs."

Motion was made by Sion Roy to accept the report as is and seconded by Jeffrey Graham and unanimously approved by the committee.

F. SMC Bond Capital Construction Budget Summary as of December 31, 2017.

Emil Zordilla, Assistant Director, Facilities planning, gave a visual presentation of the bond construction project:

- **Center for Media and Design**: The project had its grand opening December 2, 2017. KCRW is set to occupy space spring of 2018.
- East Wing Performing Arts Center: The PAC is completed.
- Core Performance Center: Is completed and currently hosting classes.
- **Student Services Building**: Structural steel is completely assembled and the building envelope is being installed, completion by 2018/2019.
- Malibu Campus: All regulatory agency approvals have been attained. Project to break ground in July 2018.
- Santa Monica Early Childhood Lab School: All regulatory agencies approvals have been attained and ground breaking Spring 2018.
- Math & Science Building Extension: The design phase is being finalized, and early renderings were shared with the committee. The design is to be completed summer of 2018 and submitted for DSA approval.
- G. Measure U, S and AA and Bond Sales Expense Reports

The SMC Bond Capital Construction Budget Summary as of December 31, 2017 reports the following:

| Measure U Budget: | \$160,000,000 |
|--------------------------------|---------------|
| Measure S Budget: | \$143,500,000 |
| Measure AA Budget: | \$295,000,000 |
| Other Funding Received: | \$ 26,741,995 |
| Other Funding Pending: | \$ 52,594,548 |
| Total Budget: | \$698,766,706 |
| Estimate at Completion: | \$698,590,482 |
| Bond Funds Remaining: | \$88,233,955 |

- Measure U: Total Measure U Expenditures last period were \$0; total remaining funds are \$1,127.00; no budget variance.
- Measure S: Total Measure S Expenditures last period were \$4,057,782; total remaining funds are \$38,992,691; no budget variance.
- Measure AA: Total Measure AA Expenditures last period were \$7,412,494; total remaining funds are \$49,247,618; no budget variance.

The committee requested a "more detailed financial report" and one will be provided at a subsequent meeting.

The Bond Sales/Expense Report indicates total bond amounts, bond issue dates/amounts unsold bond amount and total available as of December 31, 2017.

| Total Bond: | \$598,500,000 |
|-----------------------------------|---------------|
| Total Available: | \$528,492,559 |
| Total Expenses: | \$510,258,564 |
| Total Available Remaining: | \$ 88,233,995 |
| Total Unsold Bond: | \$ 7,441 |

- The SMC Bond Construction Program Contractor List as of December 31, 2017 was included in the packet.
- Current information on all bond construction projects is available at: http://smcbondprogram.com and at http://www.smc.edu/CBOC

9. SCHEDULE OF MEETINGS, 2017-2018

Wednesday, April 25, 2018 at 8 a.m. Wednesday, July 25, 2018 at 8 a.m.

10. ADJOURNMENT: 9:05 am

The next meeting of the Citizens' Bond Oversight Committee will be held on Wednesday, April 25, 2018 at 8 a.m. in Drescher Hall Room 300---E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.



Santa Monica Community College District
Citizens' Bond Oversight Committee
MEETING – April 25, 2018
MINUTES

A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee was held on Wednesday, **April 25**, **2018 at 8 a.m.** in Drescher 300---E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

10. CALL TO ORDER: 8:07 a.m.

11. ROLL CALL --- Members

- Sonya Sultan, Chair --- Present
- Katherine Reuter, Vice-Chair --- Present
- Jeffrey Graham Absent
- Sion Roy --- Absent
- Sharon Barovsky --- Present
- Michael Dubin Present
- Cassandra Santiago-Amzallag Present

Others Present:

- Chris Bonvenuto, Chief Director, Business Services
- Don Girard, Senior Director, Government Relations/Institutional Communications
- Ramin Nematollahi, Citizens' Bond Oversight Committee Coordinator
- Charlie Yen -- Director of Facilities Planning

12. APPROVAL OF MINUTES

The minutes of the Citizens' Bond Oversight Committee meeting of January 25, 2018 were approved as is. *Motion was made by Michael Dubin and seconded by Katherine Reuter and unanimously approved by the committee.*

13. REPORTS and DISCUSSION

H. SMC Bond Capital Construction Budget Summary as of March 31, 2018.

Charlie Yen, Director of Facilities Planning, discussed the SMC bond Capital Constructer Budget Summary as of March 31, 2018.

- Center for Media and Design: The project is progressing as 90% complete. KCRW
 has started to move in their equipment and it may take 6 months for the move to be
 complete.
- Core Performance Center: Phase 2 (renovation of older building is now complete). Building is currently occupied and in use.
- **Student Services Building**: Construction is proceeding as planned and completion date is set for Spring/Summer 2019.
- Malibu Campus: A sewer line realignment has caused a delay. The bid should go to

the board in August with a breaking ground of construction in September. Completion is planned for Spring 2021.

- Early Childhood Education Center: Construction to break ground June 2018, and expected completion date is 2020. Due to Aluminum/Steel tariffs price for construction was higher than expected.
- Math & Science Building: Currently at the development phase. Due to financing being matched by the state, each step must be approved by the state.

I. Bond Sales & Measure V

Chris Bonvenuto, Chief Director, Business Services, discussed the recent bond sales and refunding of the Build America Bonds. He discussed structuring the sale to generate specific premiums, so that the first year assessment and would not impact the property owners tax liability until 2019/2020. He shared that with SMC's bond rating and a cooperative market a \$1.9 million savings was generated for the taxpayer. He further clarified achieving a repayment ratio of 1.77 to 1 on the Measure V. Sonya Sultan, the chair, and the committee expressed their gratitude to Chris and Charlie and their teams for all their work in saving the tax payers money!

J. Measure U, S and AA and Bond Sales Expense Reports

The SMC Bond Capital Construction Budget Summary as of March 31, 2018 reports the following:

Measure U Budget: \$160,000,000 \$143,500,000 Measure S Budget: Measure AA Budget: \$295,000,000 Interest \$ 22,867,238 Other Funding Received: \$ 26,741,995 Other Funding Pending: \$ 52,594,548 **Total Budget:** \$ 700,703,781 \$ 700,703,781 Estimate at Completion: **Bond Funds Remaining:** \$ **59,872,153**

- **Measure U**: Total Measure U Expenditures last period were **\$0**; total remaining funds are **\$1,127**; no budget variance.
- Measure S: Total Measure S Expenditures last period were \$10,480,443; total remaining funds are

\$28,512,248; no budget variance.

- Measure AA: Total Measure AA Expenditures last period were \$17,881,399; total remaining funds are \$31,366,219; no budget variance.
- The Bond Sales/Expense Report

Indicates total bond amounts, bond issue dates/amounts unsold bond amount and total available as of March 31, 2018.

 Total Bond:
 \$598,500,000

 Total Available:
 \$528,492,559

 Total Expenses:
 \$538,620,408

 Total Available Remaining:
 \$ 59,872,151

 Total Unsold Bond:
 \$ 7,441

• The SMC Bond Construction Program Contractor List as of March 31, 2018 was included in the packet.

K. <u>INFORMATION – EXPIRING TERMS OF MEMBERS OF THE CITIZENS' BOND OVERSIGHT</u> COMMITTEE

The term of the following member(s) of the Citizens' Bond Oversight Committee is expiring effective **June 30, 2018** and is not eligible for reappointment:

• The associate student representative will be selected in September.

The term of the following member(s) of the Citizens' Bond Oversight Committee is expiring effective **June 30, 2018** and is eligible for reappointment:

Jeffrey Graham, Local Business

The term of the following member(s) of the Citizens' Bond Oversight Committee is expiring effective **June 30, 2018** and is not eligible for reappointment, as they will have termed out having served 3 consecutive terms:

• Katharine Reuter, Senior Citizens' Organization

The Board of Trustees will follow a recruitment and application process to appoint/reappoint members to fill the vacancies.

11. SCHEDULE OF MEETINGS, 2017---2018

Wednesday, July 25, 2018 at 8 a.m.

12. ADJOURNMENT: 9:08 am

The next meeting of the Citizens' Bond Oversight Committee will be held on **Wednesday**, **July 25, 2018 at 8 a.m. in Drescher Hall Room 300---E (the Loft) at Santa Monica College**, 1900 Pico Boulevard, Santa Monica, California.

Current information on all bond construction projects is available at: http://smcbondprogram.com and at http://www.smc.edu/CBOC



SANTA MONICA COMMUNITY COLLEGE DISTRICT

Capital Outlay Program

Bond Project Report

July 2018

Prepared by SMC Facilities Planning

Introduction

The District's capital outlay program consists of larger non-maintenance projects that are generally over \$100,000, typically financed by local taxpayer approved bonds. The capital projects include new buildings, replacement buildings, renovations, property acquisition, parking, site work, landscaping, infrastructure, security, and technology.

Over the last several decades, Santa Monica and Malibu voters have approved five safety and modernization bond measures in support of the college's career and academic programs:

| Proposition T | 1992 | \$ 23,000,000 |
|---------------|------|---------------|
| Measure U | 2002 | \$160,000,000 |
| Measure S | 2004 | \$135,000,000 |
| Measure AA | 2008 | \$295,000,000 |
| Measure V | 2016 | \$345,000,000 |

By way of background, local bonds financed the original Main Campus, built in the 1950s and 1960s. However, in subsequent years until 1992, the District depended primarily on limited state funding, so only a few large projects were built. After the 1994 Northridge Earthquake and the extensive damage to the Main Campus, the District received federal FEMA support for rebuilding which started the current era of major construction on the campus.

In addition to the local bonds listed above, there has been significant financial support from federal, state and city sources along with the District's own capital funds.

The 1998 Facilities Master plan was a major effort in guiding the modernization and development of the Main Campus after the Northridge earthquake. Additional facility assessments were conducted in 2001, 2002, and 2003. In 2007, a master plan was added for the development of the Bundy Campus. In 2010, an update of the Facilities Master Plan was completed to address other safety and modernization improvements on the Main Campus and to incorporate the satellite campuses.

A new Facilities Master Plan Update is currently underway and will be completed in 2019 to guide the progress in completing Measure AA projects and new projects under Measure V.

Highlights of the completed projects include the purchase of the Bundy Campus and Emeritus College, and the construction of the Theatre Arts, Broad Stage, HSS Building, Campus Quad and Information Technology.

Projects completed in 2017:

Core Performance Center

Music Hall at the SMC Performing Arts Center

Center for Media and Design

Projects expected to start construction in 2018:

Malibu Campus Santa Monica Early Childhood Lab School

Projects expected to be completed in 2019:

Student Services

| Project | Funding Source Total Cost | | Status 6/30/18 |
|--|---------------------------|---------------|---------------------------|
| Purchase of Bundy Site | U | \$30,280,878 | Completed 2002 |
| Emeritus College | U, SMC Foundation | \$9,603,782 | Completed 2003 |
| Purchase of 1738 Pearl Street | U | \$749,208 | Completed 2003 |
| Library Renovation & Expansion | T, State, FEMA | \$23,600,000 | Completed 2003 |
| PE/Dance/Athletics Office Relocation | U | \$2,797,033 | Completed 2004 |
| Math Complex | U | \$1,458,690 | Completed 2004 |
| Bundy Campus West Building | U | \$23,291,387 | Completed 2005 |
| Malibu Storm Water Infrastructure P-I | S | \$2,500,000 | Completed 2005 |
| Renovation of Theatre Arts | U | \$19,544,314 | Completed 2006 |
| Music Complex - Performing Arts | U | \$4,623,547 | Completed 2007 |
| HSS North/South | U, State, FEMA, City | \$29,240,945 | Completed 2006/7 |
| Shuttle Parking Acquisition & Constr. | U | \$18,969,509 | Completed 2007 |
| Malibu Storm Water Infrastructure P-II | S | \$2,500,000 | Completed 2008 |
| Broad Stage - Performing Arts | S, SMC Foundation | \$40,690,201 | Completed 2008 |
| Athletic Fields - John Adams | S | \$2,969,807 | Completed 2008 |
| Main Campus Quad | U | \$11,388,463 | Completed 2008 |
| Bundy New Driveway & Signal | S | \$3,825,841 | Completed 2009 |
| Athletic Fields - Corsair Field | S | \$4,440,065 | Completed 2009 |
| Pico Phase I - Lot 6 & Structures | S | \$1,018,009 | Completed 2009 |
| Infrastructure & Safety Phase I | U | \$4,003,084 | Completed 2010 |
| Purchase of 1516 Pico Blvd. | AA | \$1,748,667 | Completed 2010 |
| Purchase of 1510 Pico Blvd. | AA | \$4,009,228 | Completed 2011 |
| Purchase of 919 Santa Monica Blvd. | AA | \$9,029,287 | Completed 2011 |
| Bundy/Airport Classroom Relocations | AA | \$3,162,183 | Completed 2012 |
| Library Village Relocation & Bike Park | AA | \$1,448,275 | Completed 2013 |
| Bundy/Airport Parking | AA | \$2,035,375 | Completed 2013 |
| Information Technology | AA | \$23,978,879 | Completed 2015 |
| Purchase of 2019 14 th Street | AA | \$5,013,226 | Completed 2017 |
| Central Plant Loop Connections | AA | \$11,206,164 | Competed 2017 |
| East Wing - Performing Arts Center | AA | \$30,108,816 | Completed 2017 |
| Purchase of 1530 Pico Blvd. | AA | \$4,821,600 | Completed 2018 |
| Security and Fire Alarm Upgrade | AA | \$11,520,794 | Finish Fall 2018 |
| Health, PE, Fitness, Dance, Cent. Plant | S, AA | \$58,272,030 | Finish Fall 2018 |
| Center for Media & Design | AA | \$130,549,713 | Finish Fall 2018 |
| Student Services | U, S, AA | \$130,224,164 | Under Construction |
| Child Development Center | AA, V, City of SM | \$30,925,693 | Under Construction |
| Malibu Campus | S, AA | \$50,000,000 | Start Const. 2018 |
| Math and Science | AA, V, State | \$124,958,336 | DSA review Aug. 18 |

Projects Under Construction or Recently Completed

Center for Media & Design (Academy Campus)

Project Description: This project includes the construction of a new 440-space Parking Structure. Also includes major renovation of the existing 50,000 SF AET building, a new 30,000 SF addition to the existing AET building, a new 33,000 SF building for the KCRW radio station, a new central courtyard, and new landscaping.

Current Progress: Parking Structure and the Academic Building are complete and occupied. KCRW building is substantially completed and occupied. The project is currently in closeout phase.

Project Schedule: Parking Structure and Academic Buildings early fall 2017; KCRW early fall 2018

Estimated Project Cost: \$130,549,713

Funding Sources: Measure AA, KCRW Foundation

Core Performance Center (Replacement Health, Fitness, Dance, and PE Building and Central Plant)

Project Description: The project consists of the demolition of the existing 1958 Locker Room building and replacing it with a new three-story 66,000 SF complex. The new building consists of athletic facilities, fitness center with climbing wall, fitness studios and dance studios.

Since this building is located in the center of campus, it is an ideal location for the central cooling plant which is an energy efficiency project designed to generate chilled water for efficiently for air cooling in buildings throughout the main campus.

Current Progress: Project is in closeout phase.

Project Schedule: Phase 1 Completed; Phase 2 completed late fall 2017

Estimated Project Cost: \$58,272,030

Funding Sources: Measure S, AA, State and Utility Energy Incentives

Security and Fire Alarm

Project Description: To better protect student and staff during emergency situations the college is upgrading all its security systems, including access control, video surveillance, and intrusion alarms as well as its fire alarm and mass notification systems to newer digital technologies.

Current Progress: Currently working on programming and testing of the system, and the installation of the remaining security devices at various buildings.

Project Schedule: Fire alarm complete, security in construction with summer 2018 completion.

Estimated Project Cost: \$11,520,794 **Funding Sources:** Measure AA

Central Plant Building Connections

Project Description: To connect and retrofit individual buildings to the chilled water loop from the Central Plant. Buildings include Business, HSS, Library and Science.

Project Schedule: Completed summer 2017

Estimated Project Cost: \$11,206,164

Funding Sources: Measure

Student Services Building

Project Description: The new Student Services building will facilitate the centralization of all Student Services operations that are presently dispersed throughout the campus and housed in temporary buildings. This project provides office and service space for approximately 25 Student Services functions. The new building will be sited near the Pico Boulevard main entrance to the SMC campus and thereby provide immediate access for students and members of the college community.

This proposed project also includes accommodation for vehicular access/egress, and underground parking, all in compliance with the Master Plan goal to provide more below grade vehicle parking at the main campus.

Current Progress: Currently working on the building façade, mechanical / electrical / plumbing system, interior dry wall, ceilings and site work.

Project Schedule: In construction, completion spring 2019.

Estimated Project Cost: \$\$130,224,164 **Funding Sources:** Measure S, U, AA, and V

Projects in Pre-Construction Phase

Malibu Site Campus

Project Description: In the 1970s and early 1980s, Santa Monica College offered about 70 general education classes and several non-credit classes in Malibu throughout a semester. Today, the program is limited to a few classes offered in school district buildings.

The recommended site acquisition and facility will be a classroom facility to provide general education classes, science, art and Emeritus College classes. There is also an interpretive center to highlight natural environment and history of Malibu and a Sheriff's sub-station. The District has worked cooperatively with the City of Malibu and the County of Los Angeles in planning a site at the Malibu Civic Center.

Current Progress: Phase 1, which includes the demolition of the existing building and ground stabilization, will start fall 2018. Phase 2 will commence late spring 2019

Project Schedule: Construction start in fall 2018

Estimated Project Cost: \$50,000,000 **Funding Sources:** Measure S, V

Santa Monica Early Childhood Lab School

Project Description: SMC currently has no dedicated childcare facility and offers lab instruction though various local childcare providers. The District lacks a teaching laboratory facility in Early Childhood Education available at many other community colleges. This project provides for a childcare center for the community plus college instructional facilities. The City of Santa Monica is a partner in this project, providing the site at the Civic Center and a portion of the building funds.

Current Progress: Project is under construction, paving demolition is completed. The contractor will start the foundation excavation in July.

Project Schedule: Pending approval by the Coastal Commission, construction start in Spring 2018.

Estimated Project Cost: \$30,925,693

Funding Sources: Measure S, V, and City of Santa Monica

Classrooms Relocation - Temporary Classroom Village

Project Description: As part of the new Math and Science project, the District requires temporary classroom space for students and teachers that will be displaced during the construction of the new Math and Science building. This temporary village will be located in the existing Admission Complex, and Parking Lot 2.

Current Progress: Design team has been selected and we are expecting the project to be approved in

DSA by spring 2019

Project Schedule: Construction start in summer 2019

Estimated Project Cost: \$4,900,000

Funding Sources: Measure V

Projects in Active Design Phases

None

Future Projects (Measure V)

The following projects were included in the 2016 Measure V Bond language and will be further developed during the Facilities Master Plan Update process:

Science and Math Extension. Santa Monica College is renowned for its science and allied health programs; however, the existing labs for Life, Physical and Earth Sciences are at capacity; also, the current facility for the Math Department consists of temporary trailers and lacks the infrastructure for smart classrooms or support for the use of modern technology for instructional use. Consolidating Math and Science programs into a new Science Extension building supports interdisciplinary interaction. The building extension would qualify for up to \$40 million in State funding, which requires a local match. The building will contain an upgraded planetarium and a community lab for all ages, including a nutrition and culinary lab in support of the College's nutrition program. The project is currently under review by DSA.

Replacement of Temporary Classrooms. Bond proceeds would be used to replace the 1994 temporary trailer Math Village classroom complex with permanent First Year Experience classrooms, student support study space and instructional support labs. These trailers were rushed into service following the 1994 Northridge Earthquake and have exceeded their time of usable service. Additionally, proceeds would be used to replace the 1984 modular English as a Second Language classroom building. This modular building lacks fire sprinklers, is poorly ventilated and has also exceeded its time of usable service.

Upgrading, Renovation or Replacement of Two 1950's Buildings. The 1952 Liberal Arts building has the poorest Facility Condition Index rating on the College's main campus, lacks fire sprinklers and does not have an elevator. The 1952 Letters & Science building has the second poorest Facility Condition Index rating on the main campus, and also lacks both fire sprinklers and an elevator.

Renovation of Business Building. The 1981 Business Building is overdue for renovation. The building houses a large number of computer classrooms and labs.

Replacement of Campus Police Station. The current police facility is antiquated and undersized. Applying bond proceeds to the replacement, construction, renovation and relocation of the campus police station and including a public space for community and neighborhood use will improve public and campus safety.

Upgrading, Renovation or Replacement of Art Building. An upgraded, renovated or newly constructed art structure will replace aging building systems and improve space distribution for the many disciplines within the Art Department. The College is eligible to receive up to \$10 million in State funding for this project, which requires a local match.

Landscaping/ Water Conservation Improvements and Completing Pico Boulevard Frontage Improvements. Applying bond proceeds for landscaping improvements, including landscaping improvements to complete the main campus Pico Boulevard frontage, will improve water conservation through water reclamation and installation of drought resistant landscaping.

Completing Master Plan Improvements at the Santa Monica College Performing Arts Center Campus. Construction at the Performing Arts Center campus has proceeded in phases, in coordination with available funding. The first phase added the Broad Stage and the Edye Second Space theaters. The second phase has added an East Wing rehearsal hall and music performance labs. The final phase, to be funded from bond proceeds, will include an underground three-level parking structure to replace most of the existing surface parking, along with an above-ground art gallery and green-space plaza. The theaters at the Performing Arts Center are among the most heavily used theaters in Los Angeles County.

Designing and Installing an Outdoor Classroom. The design, construction, installation and improvement of a venue for outdoor plays and class lectures.

Converting Library Interiors. Conversion of existing Library floor space used for book stacks to construct and install additional student study areas, tutoring and collaborative learning spaces that will support student success.

Making Environmental Performance Improvements. Bond funds will be used to upgrade District facilities to achieve energy or resource use efficiency and water conservation and achieve sustainability for District operations.

Upgrading Technology Infrastructure. Bond proceeds will be applied to renovate, replace, upgrade, acquire, install and integrate major site, building and utility systems, equipment and related infrastructure, including lighting, electrical, wiring and related infrastructure for modern technology, classroom instructional technology, communications and security technology (including security cameras and monitoring systems), data, voice, public address and audio-visual communication, energy efficiency, management monitoring systems, networks, fixtures, controls and equipment, cable infrastructure, network expansion, wireless access points and other communications and administrative systems.

COMMUNITY JOINT USE PROJECTS

Providing for a Joint Use Project with the City of Santa Monica. The College will provide up to \$20 million in bond funds for the expansion of the City of Santa Monica's Memorial Park to accommodate soccer and/or other field sports for use by College students and the general public.

Providing for a Joint Use Project with the Santa Monica-Malibu Unified School District. The Johns Adams Middle School Auditorium, adjacent to the College's main campus, has suffered earthquake damage and is no longer in service. The College will make available up to \$20 million bond funds as

needed to assist the School District in renovating or replacing the auditorium with a seating capacity of approximately 750, for joint use.

Providing for City of Malibu Infrastructure and Community Educational Facilities. The College will provide up to \$25 million in funding enhancements to its instructional presence in Malibu in partnership with the City of Malibu.

| | | | | | Dauget Juin | mary as of 6- | | | | | | |
|---------------------------------------|---|---------------------|---------------------|----------------------|------------------------------|---------------|--------------------------|--------------------------|---------------|------------------------|-------------|-------------------------|
| Project Number | Project Name | Measure U Budget | Measure S Budget | Measure AA Budget | Measure V Budget | Interest | Other Funding Received * | Other Funding Pending ** | Total Budget | Estimate at Completion | Status | Bond Funds Remaining |
| U-A | Purchase of BAE Airport Site | \$30,280,878 | | Dauget | Budget | | RECEIVED | renaing | \$30,280,878 | | Completed | \$(|
| U-B | Emeritus College Facility | \$8,909,940 | | | | | \$693,842 | | \$9,603,782 | | Completed | \$ |
| U-C | Purchase of 1738 Pearl Street | \$749,208 | | | | | φοσο,ο : Ξ | | \$749,208 | · · · · · | Completed | \$(|
| U-D | PE Temp. Bldg. Replacement | \$2,797,033 | | | | | | | \$2,797,033 | | Completed | \$(|
| U-E | Remodel Library Village for Math | \$1,458,690 | | | | | | | \$1,458,690 | | Completed | \$(|
| U-F | SM Airport Campus Site Improvements | \$4,170,264 | | | | | | | \$4,170,264 | \$4,170,264 | Completed | \$(|
| U-G | SM Airport Campus West Building | \$19,709,741 | | | | | | | \$19,709,741 | | Completed | \$(|
| U-H | Theater Arts Renovation | \$19,544,314 | | | | | | | \$19,544,314 | | Completed | \$(|
| U-I | Earthquake Rpl. Liberal Arts North | \$6,011,584 | | | | | \$6,496,141 | | \$12,507,725 | | Completed | \$(|
| U-K | Earthquake Rpl. Liberal Arts South | \$6,108,150 | | | | | \$10,625,070 | | \$16,733,220 | | Completed | \$(|
| U-L | Shuttle Replacement Parking | \$18,969,509 | | | | | ψ10,020,070 | | \$18,969,509 | | Completed | \$(|
| U-M | North Quad Plaza | \$11,388,463 | | | | | | | \$11,388,463 | | Completed | \$(|
| U-Q | Infrastructure & Safety | \$4,003,084 | | | | | | | \$4,003,084 | | Completed | \$(|
| U-R | Restroom Improvements | \$17,501 | | | | | | | \$17,501 | | Completed | \$(|
| S-1 | Athletic Fields Phase I, Corsair Field | Ų17,501 | \$4,372,535 | | | | \$67,530 | | \$4,440,065 | · · · | Completed | \$(|
| S-1A | Athletic Fields Phase I, John Adams | | \$2,969,807 | | | | ψ07,550 | | \$2,969,807 | | Completed | \$(|
| S-10 | Pico Promenade Improvements, Phase I | | \$1,018,009 | | | | | | \$1,018,009 | | Completed | \$(|
| S-13 | Adv. Architecture Related Exp for AA | | \$0 | | | | | | \$0 | | Completed | \$(|
| AA-114 | Community Classroom & Facility Projects | | ΨO | \$3,162,183 | | | | | \$3,162,183 | | Completed | \$(|
| U-T | 14th and Pico Project | \$319,242 | | 75,102,105 | | | | | \$319,242 | | Completed | \$(|
| U-N | Letters & Sci Demo/Restore | \$0 | | | | | | | \$0 | | Completed | \$(|
| AA-108 | Renovation of Corsair Stadium | ÇÜ | | \$35,299 | | | | | \$35,299 | 1.1 | Completed | \$(|
| S-2 | Performing Arts Complex | | \$37,697,625 | 733,233 | | | \$2,992,576 | | \$40,690,201 | | Completed | \$(|
| U-J | Music Complex | \$2,011,371 | \$37,037,023 | | | | \$2,618,113 | | \$4,629,484 | | Completed | \$(|
| S-3, AA-109 | Career Opportunity Center | 72,011,371 | | \$0 | | | \$2,010,113 | | \$4,023,484 | | Completed | \$(|
| AA-118 | Infrastructure & Technology - Utility | | | \$27,753 | | | | | \$27,753 | | Completed | \$(|
| AA-111 | Business & Facilities Infrastructure | | | \$1,968,124 | | | | | \$1,968,124 | \$1,968,124 | Completed | \$(|
| AA-117 | Infrastructure & Technology - Technology | | | \$2,434,417 | | | | | \$2,434,417 | | Completed | \$(|
| S-7, AA-113 | Energy Efficiency Projects | | \$293,361 | \$3,016,773 | | | \$708,637 | | \$4,018,771 | | Completed | \$(|
| S-15 | Signage Safety/Information | | \$706,713 | 75,010,775 | | | \$708,037 | | \$706,713 | | Completed | \$(|
| AA-102 | Infrastructure & Technology - Information Technology Relocation | | \$700,713 | \$23,140,771 | | | \$19,798 | | \$23,160,569 | | Completed | \$(|
| S-8, AA-116 | Satellite Campus Parking Facilities and Roadway | | \$3,891,747 | \$2,130,670 | | | \$19,790 | | \$6,022,417 | | Completed | \$(|
| AA-107 | Madison East Wing Seismic Upgrade | | \$3,631,747 | \$30,143,816 | | | | | \$30,143,816 | | Completed | \$2,463 |
| S-4, AA-104 | Replacement Health/PE/Fitness Central Plant Building | | \$11,603,383 | \$46,459,800 | | | \$208,847 | | \$58,272,030 | | Completed | \$2,016,130 |
| AA-104 | Environmental Performance - Central Plant Connections | | \$11,005,565 | \$11,206,164 | | | \$200,047 | | \$11,206,164 | | Completed | \$454,802 |
| S-14, AA-115 | Real Property Acquisition | | \$45,597 | \$24,859,475 | | | | | \$24,905,072 | | Completed | \$221,089 |
| AA-103 | Media and Technology Complex - Academy Site | | \$45,597 | \$123,714,322 | | | \$990,441 | \$5,844,950 | \$130,549,713 | | | \$1,000,000 |
| AA-103 AA-119 | | | | \$123,714,322 | | | \$990,441 | \$3,644,930 | \$130,349,713 | | | \$225,995 |
| | Emergency Lighting, Fire Alarm, and Security System | ¢21 121 12E | \$45,595,322 | | ¢22.624.000 | \$21,681,308 | \$1,321,000 | | \$11,320,794 | | | \$37,274,57 |
| | Student Services Building | 321,131,133 | | 30,670,490 | 4 | | \$1,521,000 | \$6,661,598 | | | | \$22,016,984 |
| S-5, V-104 S-6, AA-110, V-103 | Early Childhood Development/Childcare Malibu Site Acquisition and Facility | | \$8,858,578 | | \$15,405,517 \$25,000,000 | | | \$0,001,598 | \$50,000,000 | | | \$39,576,562 |
| <u> </u> | · | \$2,110,430 | \$25,000,000 | \$833,427 | \$450,000 | | | | \$4,110,285 | | | \$450,000 |
| | Master Planning Replacement Math and Science Extension Building | \$2,110,430 | | \$833,427 | | | | \$40,088,000 | | - ' ' | In Design | \$450,000 |
| U-P, AA-106, V-101 AA-105, V-110 | Drescher - Academic Modernization, Bookstore, Pico Promenade II | \$5U8,33b | | \$2,244,008 | | | | \$40,088,000 | \$124,958,336 | | In Design | \$80,252,858 |
| | · · · · · · · · · · · · · · · · · · · | | | 280,082 | \$13,000,000 \$24,000,000 | | | \$8,914,000 | \$13,005,082 | | In Planning | |
| V-105 | Art Building Replacement | | | | | | | · · · · | \$32,914,000 | | In Planning | \$23,999,816 |
| V-106 | Business Building Renovation | | | | \$12,547,000 | | | \$12,470,000 | \$25,017,000 | | In Planning | \$12,547,000 |
| V-107 | Air Conditioning | | | | \$10,777,654 | | | | \$10,777,654 | | In Design | \$10,355,324 |
| V-108 | ADA | | | | \$4,000,000 | | | | \$4,000,000 | | In Planning | \$4,000,00 |
| V-111 | Outdoor Classroom | | | | \$10,000,000 | | | | \$10,000,000 | | In Planning | \$9,900,000 |
| V-112 | SMMUSD Situ of South Marrian | | | | \$20,000,000 | | | | \$20,000,000 | | In Design | \$20,000,000 |
| V-113 | City of Santa Monica | | | | \$20,000,000 | | | | \$20,000,000 | | In Planning | \$20,000,000 |
| V-114 | Classrooms Relocation | | 6505 55- | | \$4,900,000 | | | | \$4,900,000 | | In Planning | \$4,900,000 |
| S-12, V-120 | Other Bond Related Expenses | | \$609,282 | | \$300,000 | | | | \$909,282 | | In Planning | \$488,72 |
| V-115 | TBD | | 44 | ** | \$39,876,928 | | | | \$39,876,928 | | In Planning | \$39,876,928 |
| S-16, AA-121, V-121 | Cost of Issuance | | \$119,470 | \$498,026 | | 40.0== | | | \$1,417,496 | | In Planning | \$508,723 |
| AA-122, V-122 | Management Reserve | | | \$724,435 | \$28,000,000 | \$3,877,925 | | | \$32,602,360 | | In Planning | \$28,724,435 |
| · · · · · · · · · · · · · · · · · · · | Unissuable | \$1,127 | \$2,143 | \$4,171 | l | | | | \$7,441 | \$7,441 | On-Going | |

* City of SM: \$10,206,823; FEMA: \$1,962,572; State: \$5,779,000; Prop T: 2,618,113; DWP: \$86,245; SCE: \$844,284; Gas Co.: \$106,262; Madison Foundation: \$2,992,576; KCRW: \$958,462; Emeritus College Foundation: \$693,842; Bond Interest and Cost of Issuance Refund: \$21,476,400

8/

^{**} City of SM: 6,661,598; KCRW: \$5,844,950; State: \$40,088,000

SANTA MONICA COMMUNITY COLLEGE DISTRICT Bond Sales / Expenses Report As of June 30, 2018


| Measure U Bond \$160,000,000 | | |
|------------------------------|------|---------------|
| Bond Issue Date | | Amount |
| | 2002 | \$25,000,000 |
| | 2004 | \$21,999,971 |
| | 2005 | \$89,999,923 |
| | 2007 | \$11,999,987 |
| | 2010 | \$10,998,992 |
| Total Available | | \$159,998,873 |
| Expenses as of 6-30-18 | | \$159,998,873 |
| Total Available Remaining | | \$0 |
| | | |
| Unsold Bond Amount | | \$1,127 |
| Total Available as of 7-1-18 | | \$1,127 |

| Measure S Bond \$143,500,000 (1 |) | |
|---------------------------------|------|---------------|
| Bond Issue Date | | Amount |
| | 2005 | \$58,000,000 |
| | 2007 | \$8,500,000 |
| | 2009 | \$56,997,857 |
| | 2017 | \$20,000,000 |
| Total Available | | \$143,497,857 |
| Expenses as of 6-30-18 | | \$122,120,920 |
| Total Available Remaining | | \$21,376,937 |
| - | | · |
| Unsold Bond Amount | | \$2,143 |
| Total Available as of 7-1-18 | | \$21,379,080 |
| | | |

| Measure AA Bond \$295,000,000 | | |
|-------------------------------|------|---------------|
| Bond Issue Date | | Amount |
| | 2010 | \$100,000,000 |
| | 2014 | \$144,995,829 |
| | 2017 | \$50,000,000 |
| Total Available | | \$294,995,829 |
| Expenses as of 6-30-18 | | \$286,500,922 |
| Total Available Remaining | | \$8,494,907 |
| | | |
| Unsold Bond Amount | | \$4,171 |
| Total Available as of 7-1-18 | | \$8,499,078 |
| | | |

| Measure V Bond \$345,000,000 | | |
|------------------------------|------|---------------|
| Bond Issue Date | | Amount |
| | 2018 | \$180,000,000 |
| Total Available | | \$180,000,000 |
| Expenses as of 6-30-18 | | \$3,079,439 |
| Total Available Remaining | | \$176,920,561 |
| | | |
| Unsold Bond Amount | | \$165,000,000 |
| Total Available as of 7-1-18 | | \$341,920,561 |

| Total Bond | \$943,500,000 |
|------------------------------|---------------|
| Total Available | \$778,492,559 |
| Total Expenses as of 6-30-18 | \$571,700,154 |
| Total Available Remaining | \$206,792,405 |
| Total Unsold Bond | \$165,007,441 |

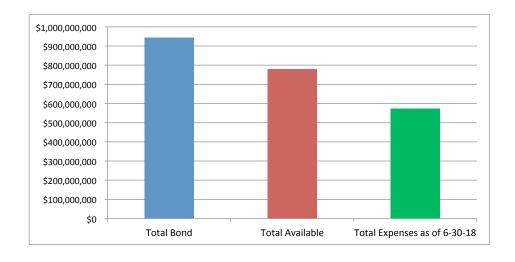

| Interest | Measure U | Measure S | Measure AA | Measure V |
|---------------------------------------|-------------|--------------|-------------|-----------|
| As of 6-30-18 | \$7,034,168 | \$11,417,370 | \$6,375,323 | \$676,109 |
| Expenditure / Arbitrage as of 6-30-18 | \$7,034,168 | \$9,141,589 | \$0 | \$0 |
| Available Interest as of 6-30-18 | \$0 | \$2,275,781 | \$6,375,323 | \$676,109 |


| Cost of Issuance Refund | Measure U | Measure S |
|---------------------------|-----------|-----------|
| As of 6-30-17 | \$20,688 | \$35,575 |
| Expenditure as of 6-30-18 | \$20,688 | \$0 |
| Available as of 6-30-18 | \$0 | \$35,575 |

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure U Bond Budget

As of June 30, 2018

| | Project Name | Completion | Project Budget | Measure U Allocation | Other Funding | Measure U Expenditures as of 6/30/18 | Measure U Expenditures as of 3/31/18 | Measure U Expenditures Last Period | Total Measure U Remaining |
|---|-------------------------------------|------------|-------------------|-------------------------|---------------|--|--|--|------------------------------|
| Α | Purchase of BAE Airport Site | Completed | \$30,280,878 | \$30,280,878 | \$0 | \$30,280,878 | \$30,280,878 | \$0 | \$0 |
| В | Emeritus College Facility | Completed | \$9,603,782 | \$8,909,940 | \$693,842 | \$8,909,940 | \$8,909,940 | \$0 | \$0 |
| С | Purchase of 1738 Pearl Street | Completed | \$749,208 | \$749,208 | \$0 | \$749,208 | \$749,208 | \$0 | \$0 |
| D | PE Temp. Bldg. Replacement | Completed | \$2,797,033 | \$2,797,033 | \$0 | \$2,797,033 | \$2,797,033 | \$0 | \$0 |
| Е | Remodel Library Village for Math | Completed | \$1,458,690 | \$1,458,690 | \$0 | \$1,458,690 | \$1,458,690 | \$0 | \$0 |
| F | SM Airport Campus Site Improvements | Completed | \$4,170,264 | \$4,170,264 | \$0 | \$4,170,264 | \$4,170,264 | \$0 | \$0 |
| G | SM Airport Campus West Building | Completed | \$19,709,741 | \$19,709,741 | \$0 | \$19,709,741 | \$19,709,741 | \$0 | \$0 |
| Н | Theater Arts Renovation | Completed | \$19,544,314 | \$19,544,314 | \$0 | \$19,544,314 | \$19,544,314 | \$0 | \$0 |
| I | Earthquake Rpl. Liberal Arts North | Completed | \$12,507,725 | \$6,011,584 | \$6,496,141 | \$6,011,584 | \$6,011,584 | \$0 | \$0 |
| J | Music Complex | Completed | \$4,629,484 | \$2,011,371 | \$2,618,113 | \$2,011,371 | \$2,011,371 | \$0 | \$0 |
| K | Earthquake Rpl. Liberal Arts South | Completed | \$16,733,220 | \$6,108,150 | \$10,625,070 | \$6,108,150 | \$6,108,150 | \$0 | \$0 |
| L | Shuttle Replacement Parking | Completed | \$18,969,509 | \$18,969,509 | \$0 | \$18,969,509 | \$18,969,509 | \$0 | \$0 |
| М | North Quad Plaza | Completed | \$11,388,463 | \$11,388,463 | \$0 | \$11,388,463 | \$11,388,463 | \$0 | \$0 |
| N | Letters & Sci Demo/Restore | Completed | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| 0 | Student Services Building | March 2019 | \$130,224,164 | \$21,131,135 | \$109,093,029 | \$21,131,135 | \$21,131,135 | \$0 | \$0 |
| Р | Science Complex Addition | Completed | \$124,958,336 | \$308,336 | \$124,650,000 | \$308,336 | \$308,336 | \$0 | \$0 |
| Q | Infrastructure & Safety | Completed | \$4,003,084 | \$4,003,084 | \$0 | \$4,003,084 | \$4,003,084 | \$0 | \$0 |
| R | Restroom Improvements | Completed | \$17,501 | \$17,501 | \$0 | \$17,501 | \$17,501 | \$0 | \$0 |
| S | Master Planning | Completed | \$2,110,430 | \$2,110,430 | \$0 | \$2,110,430 | \$2,110,430 | \$0 | \$0 |
| Т | 14th and Pico Project | Completed | \$319,242 | \$319,242 | \$0 | \$319,242 | \$319,242 | \$0 | \$0 |
| U | Unissuable Bond | Completed | \$1,127 | \$1,127 | \$0 | \$0 | \$0 | \$0 | \$1,127 |
| | Project Totals | | \$414,175,068 | \$160,000,000 | \$254,176,195 | \$159,998,873 | \$159,998,873 | \$0 | \$1,127 |

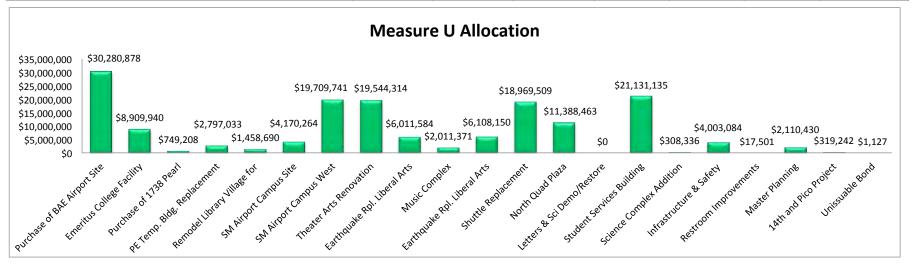

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure U Bond Budget History

as of June 30, 2018


| | Project Name | Completion | Preliminary Measure U | Measure U Budget as of | Measure U Budget as of | Variance | Measure U Remaining as of |
|-----|-------------------------------------|------------|--------------------------|---------------------------|---------------------------|----------|------------------------------|
| | | | Budget | 3/31/18 | 6/30/18 | | 6/30/18 |
| Α | Purchase of BAE Airport Site | Completed | \$30,000,000 | \$30,280,878 | \$30,280,878 | \$0 | \$0 |
| В | Emeritus College Facility | Completed | \$8,883,381 | \$8,909,940 | \$8,909,940 | \$0 | \$0 |
| С | Purchase of 1738 Pearl Street | Completed | \$749,208 | \$749,208 | \$749,208 | \$0 | \$0 |
| D | PE Temp. Bldg. Replacement | Completed | \$2,673,247 | \$2,797,033 | \$2,797,033 | \$0 | \$0 |
| Е | Remodel Library Village for Math | Completed | \$1,425,565 | \$1,458,690 | \$1,458,690 | \$0 | \$0 |
| F | SM Airport Campus Site Improvements | Completed | \$6,200,000 | \$4,170,264 | \$4,170,264 | \$0 | \$0 |
| G | SM Airport Campus West Building | Completed | \$20,071,124 | \$19,709,741 | \$19,709,741 | \$0 | \$0 |
| Н | Theater Arts Renovation | Completed | \$16,992,296 | \$19,544,314 | \$19,544,314 | \$0 | \$0 |
| - 1 | Earthquake Rpl. Liberal Arts North | Completed | \$5,352,752 | \$6,011,584 | \$6,011,584 | \$0 | \$0 |
| J | Music Complex | Completed | \$4,802,537 | \$2,011,371 | \$2,011,371 | \$0 | \$0 |
| K | Earthquake Rpl. Liberal Arts South | Completed | \$2,863,566 | \$6,108,150 | \$6,108,150 | \$0 | \$0 |
| L | Shuttle Replacement Parking | Completed | \$17,256,000 | \$18,969,509 | \$18,969,509 | \$0 | \$0 |
| М | North Quad Plaza | Completed | \$3,939,759 | \$11,388,463 | \$11,388,463 | \$0 | \$0 |
| N | Letters & Sci Demo/Restore | Completed | \$1,192,250 | \$0 | \$0 | \$0 | \$0 |
| 0 | Student Services Building | March 2019 | \$23,952,004 | \$21,131,135 | \$21,131,135 | \$0 | \$0 |
| Р | Science Complex Addition | Completed | \$10,613,910 | \$308,336 | \$308,336 | \$0 | \$0 |
| Q | Infrastructure & Safety | Completed | \$5,000,000 | \$4,003,084 | \$4,003,084 | \$0 | \$0 |
| R | Restroom Improvements | Completed | \$400,000 | \$17,501 | \$17,501 | \$0 | \$0 |
| S | Master Planning | Completed | \$500,000 | \$2,110,430 | \$2,110,430 | \$0 | \$0 |
| Т | 14th and Pico Project | Completed | \$14,662,000 | \$319,242 | \$319,242 | \$0 | \$0 |
| U | Unissuable Bond | Completed | \$0 | \$1,127 | \$1,127 | \$0 | \$1,127 |
| | Project Totals | | \$177,529,599 | \$160,000,000 | \$160,000,000 | \$0 | \$1,127 |

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure S Bond Budget

As of June 30, 2018

| | Project Name | Completion | Project Budget | Measure S Allocation | Other Funding | Measure S Expenditures as of 6/30/18 | Measure S Expenditures as of 3/31/18 | Measure S Expenditures Last Period | Total Measure S Remaining |
|----|--|---------------|----------------|-------------------------|---------------|--|--|--|------------------------------|
| 1 | Athletic Fields Phase I, Corsair Field | Completed | \$4,440,065 | \$4,372,535 | \$67,530 | \$4,372,535 | \$4,372,535 | \$0 | \$0 |
| 1A | Athletic Fields Phase I, John Adams | Completed | \$2,969,807 | \$2,969,807 | \$0 | \$2,969,807 | \$2,969,807 | \$0 | \$0 |
| 2 | Performing Arts Complex | Completed | \$40,690,201 | \$37,697,625 | \$2,992,576 | \$37,697,625 | \$37,697,625 | \$0 | \$0 |
| 3 | Career Opportunity Center | Completed | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| 4 | Replacement Health/PE/Fitness Building | Completed | \$58,272,030 | \$11,603,383 | \$46,668,647 | \$11,603,383 | \$11,603,383 | \$0 | \$0 |
| 5 | Early Childhood Development/Childcare | June 2020 | \$30,925,693 | \$8,858,578 | \$22,067,115 | \$2,247,111 | \$1,171,232 | \$1,075,879 | \$6,611,467 |
| 6 | Malibu Site Acquisition and Facility | December 2021 | \$25,000,000 | \$25,000,000 | \$0 | \$10,423,438 | \$9,792,887 | \$630,551 | \$14,576,562 |
| 7 | Energy Efficiency Projects | Completed | \$510,683 | \$293,361 | \$217,322 | \$293,361 | \$293,361 | \$0 | \$0 |
| 8 | Satellite Campus Parking Facilities and Roadway Improvements | Deferred | \$7,022,417 | \$3,891,747 | \$3,130,670 | \$3,891,747 | \$3,891,747 | \$0 | \$0 |
| 9 | Parking Garage, Grounds and Equipment - Student Services | March 2019 | \$130,224,164 | \$45,595,322 | \$84,628,842 | \$45,595,322 | \$40,171,892 | \$5,423,430 | \$0 |
| 10 | Pico Promenade Improvements | Completed | \$1,018,009 | \$1,018,009 | \$0 | \$1,018,009 | \$1,018,009 | \$0 | \$0 |
| 11 | Master Planning | Completed | \$716,428 | \$716,428 | \$0 | \$716,428 | \$716,428 | \$0 | \$0 |
| 12 | Other Bond Related Expenses | On-Going | \$609,282 | \$609,282 | \$0 | \$420,373 | \$417,066 | \$3,307 | \$188,909 |
| 13 | Adv. Architecture Related Exp for AA | Completed | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| 14 | Real Property Acquisition | Completed | \$45,597 | \$45,597 | \$0 | \$45,597 | \$45,597 | \$0 | \$0 |
| 15 | Signage Safety/Information | Completed | \$706,713 | \$706,713 | \$0 | \$706,713 | \$706,713 | \$0 | \$0 |
| 16 | Cost of Issuance | Completed | \$119,470 | \$119,470 | \$0 | \$119,470 | \$119,470 | \$0 | \$0 |
| 17 | Unissuable Bond | Completed | \$2,143 | \$2,143 | \$0 | \$0 | \$0 | \$0 | \$2,143 |
| | Project Totals | | \$303,270,559 | \$143,500,000 | \$159,772,702 | \$122,120,919 | \$114,987,752 | \$7,133,167 | \$21,379,081 |

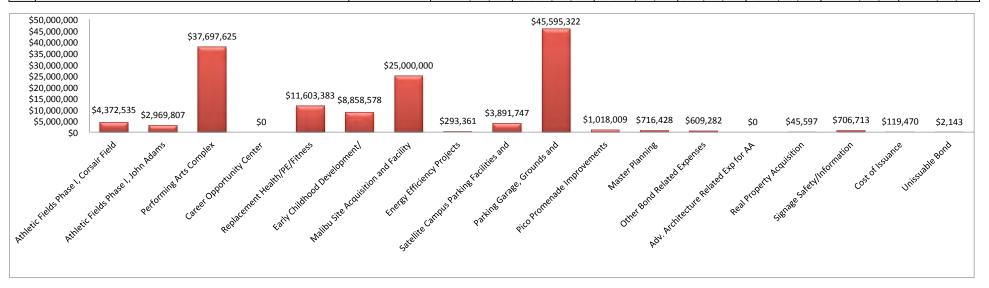


SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure S Bond Budget History

as of June 30, 2018

| | Project Name | Completion | Preliminary Measure S Budget | Measure S Budget as of 3/31/18 | Measure S Budget as of 6/30/18 | Variance | Measure S Remaining as of 6/30/18 |
|----|--|---------------|------------------------------------|--------------------------------------|--------------------------------------|----------|---|
| 1 | Athletic Fields Phase I, Corsair Field | Completed | \$1,800,000 | \$4,372,535 | \$4,372,535 | \$0 | \$0 |
| 1A | Athletic Fields Phase I, John Adams | Completed | \$35,200,000 | \$2,969,807 | \$2,969,807 | \$0 | \$0 |
| 2 | Performing Arts Complex | Completed | \$24,000,000 | \$37,697,625 | \$37,697,625 | \$0 | \$0 |
| 3 | Career Opportunity Center | Completed | \$20,000,000 | \$0 | \$0 | \$0 | \$0 |
| 4 | Replacement Health/PE/Fitness Building | Completed | \$20,000,000 | \$11,603,383 | \$11,603,383 | \$0 | \$0 |
| 5 | Early Childhood Development/Childcare | June 2020 | \$7,000,000 | \$8,858,578 | \$8,858,578 | \$0 | \$6,611,467 |
| 6 | Malibu Site Acquisition and Facility | December 2021 | \$25,000,000 | \$25,000,000 | \$25,000,000 | \$0 | \$14,576,562 |
| 7 | Energy Efficiency Projects | Completed | \$2,000,000 | \$293,361 | \$293,361 | \$0 | \$0 |
| 8 | Satellite Campus Parking Facilities and Roadway Improvements | Deferred | \$0 | \$3,891,747 | \$3,891,747 | \$0 | \$0 |
| 9 | Parking Garage, Grounds and Equipment - Student Services | March 2019 | \$0 | \$45,595,322 | \$45,595,322 | \$0 | \$0 |
| 10 | Pico Promenade Improvements, Phase I | Completed | \$0 | \$1,018,009 | \$1,018,009 | \$0 | \$0 |
| 11 | Master Planning | Completed | \$0 | \$716,428 | \$716,428 | \$0 | \$0 |
| 12 | Other Bond Related Expenses | On-Going | \$0 | \$609,282 | \$609,282 | \$0 | \$188,909 |
| 13 | Adv. Architecture Related Exp for AA | Completed | \$0 | \$0 | \$0 | \$0 | \$0 |
| 14 | Real Property Acquisition | Completed | \$0 | \$45,597 | \$45,597 | \$0 | \$0 |
| 15 | Signage Safety/Information | Completed | \$0 | \$706,713 | \$706,713 | \$0 | \$0 |
| 16 | Cost of Issuance | Completed | \$0 | \$119,470 | \$119,470 | \$0 | \$0 |
| 17 | Unissuable Bond | Completed | \$0 | \$2,143 | \$2,143 | \$0 | \$2,143 |
| | Project Totals | | \$135,000,000 | \$143,500,000 | \$143,500,000 | \$0 | \$21,379,081 |

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget As of June 30, 2018

| | Project Name | Completion | Project Budget | Measure AA Allocation | Other Funding | Measure AA Expenditures as of 6/30/18 | Measure AA Expenditures as of 3/31/18 | Measure AA Expenditures Last Period | Total Measure AA Remaining |
|-----|--|----------------|----------------|--------------------------|---------------|---|---|---|-------------------------------|
| 101 | Environmental Performance - Central Plant Connections | Completed | \$11,206,164 | \$11,206,164 | \$0 | \$10,751,362 | \$10,749,286 | \$2,076 | \$454,802 |
| 102 | Infrastructure & Technology - Information Technology Relocation | Completed | \$23,160,569 | \$23,140,771 | \$19,798 | \$23,140,771 | \$23,140,771 | \$0 | \$0 |
| 103 | Media and Technology Complex - Academy Site | Completed | \$130,549,713 | \$123,714,322 | \$6,835,391 | \$122,714,322 | \$105,809,692 | \$16,904,630 | \$1,000,000 |
| 104 | Replacement Health/PE/Fitness/ Dance Building with Central Plant | Completed | \$58,272,030 | \$46,459,800 | \$11,812,230 | \$44,443,670 | \$42,134,118 | \$2,309,552 | \$2,016,130 |
| 105 | Drescher - Academic Modernization, Bookstore, Pico Promenade | Deferred | \$13,005,082 | \$5,082 | \$13,000,000 | \$5,082 | \$5,082 | \$0 | \$0 |
| 106 | Replacement Math and Science Extension Building | September 2022 | \$124,958,336 | \$2,244,008 | \$122,714,328 | \$2,098,878 | \$1,903,715 | \$195,163 | \$145,130 |
| 107 | Madison East Wing Seismic Upgrade | Completed | \$30,143,816 | \$30,143,816 | \$0 | \$30,141,353 | \$29,974,072 | \$167,281 | \$2,463 |
| 108 | Renovation of Corsair Stadium | Completed | \$35,299 | \$35,299 | \$0 | \$35,299 | \$35,299 | \$0 | \$0 |
| 109 | Career Opportunity and Advancement Center (Bundy) | Completed | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| 110 | Malibu Center | December 2021 | \$25,000,000 | \$0 | \$25,000,000 | \$0 | \$0 | \$0 | \$0 |
| 111 | Business & Facilities Infrastructure | Completed | \$1,968,124 | \$1,968,124 | \$0 | \$1,968,124 | \$1,968,124 | \$0 | \$0 |
| 112 | Master Planning, Program Management, Overhead | On-Going | \$833,427 | \$833,427 | \$0 | \$833,427 | \$792,034 | \$41,393 | \$0 |
| 113 | Energy Efficiency Projects | Completed | \$3,508,088 | \$3,016,773 | \$491,315 | \$3,016,773 | \$3,016,773 | \$0 | \$0 |
| 114 | Community Classroom & Facility Projects | Completed | \$3,162,183 | \$3,162,183 | \$0 | \$3,162,183 | \$3,162,183 | \$0 | \$0 |
| 115 | Real Property Acquisition | Completed | \$24,859,475 | \$24,859,475 | \$0 | \$24,638,386 | \$24,716,127 | -\$77,741 | \$221,089 |
| 116 | Roadways, Walkways, Grounds, Parking Lots, and Garages | Completed | \$7,022,417 | \$2,130,670 | \$4,891,747 | \$2,130,670 | \$2,130,670 | \$0 | \$0 |
| 117 | Infrastructure & Technology - Technology | Completed | \$2,434,417 | \$2,434,417 | \$0 | \$2,434,417 | \$2,434,417 | \$0 | \$0 |
| 118 | Infrastructure & Technology - Utility | Completed | \$27,753 | \$27,753 | \$0 | \$27,753 | \$27,753 | \$0 | \$0 |
| 119 | Emergency Lighting, Fire Alarm, and Security System | On-Going | \$11,520,794 | \$11,520,794 | \$0 | \$11,294,799 | \$11,135,639 | \$159,160 | \$225,995 |
| 120 | Student Services | March 2019 | \$130,224,164 | \$6,870,490 | \$123,353,674 | \$3,165,626 | \$0 | \$3,165,626 | \$3,704,864 |
| 121 | Cost of Issuance | Completed | \$498,026 | \$498,026 | \$0 | \$498,026 | \$498,026 | \$0 | \$0 |
| 122 | Management Reserve | On-Going | \$724,435 | \$724,435 | \$0 | \$0 | \$0 | \$0 | \$724,435 |
| 123 | Unissuable Bond | Completed | \$4,171 | \$4,171 | \$0 | \$0 | \$0 | \$0 | \$4,171 |
| | Project Totals | | \$602,389,877 | \$295,000,000 | \$308,118,483 | \$286,500,921 | \$263,633,781 | \$22,867,140 | \$8,499,079 |



SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget History as of June 30, 2018


| | | | Preliminary | Measure AA | Measure AA | | Measure AA |
|-----|--|----------------|---------------|---------------|---------------|---------------|--------------|
| | Project Name | Completion | Measure AA | Budget as of | Budget as of | Variance | Remaining as |
| | | | Budget | 3/31/18 | 6/30/18 | | of 6/30/18 |
| 101 | Environmental Performance - Central Plant Connections | Completed | \$12,034,042 | \$11,206,164 | \$11,206,164 | \$0 | \$454,802 |
| 102 | Infrastructure & Technology - Information Technology Relocation | Completed | \$13,287,218 | \$23,140,771 | \$23,140,771 | \$0 | \$0 |
| | Media and Technology Complex - Academy Site | Completed | \$57,480,824 | \$106,219,665 | \$123,714,322 | \$17,494,657 | \$1,000,000 |
| 104 | Replacement Health/PE/Fitness/ Dance Building with Central Plant | Completed | \$29,232,317 | \$46,459,800 | \$46,459,800 | \$0 | \$2,016,130 |
| 105 | Drescher - Academic Modernization, Bookstore, Pico Promenade II | Deferred | \$34,026,480 | \$5,082 | \$5,082 | \$0 | \$0 |
| 106 | Replacement Math and Science Extension Building | September 2022 | \$68,259,000 | \$2,244,008 | \$2,244,008 | \$0 | \$145,130 |
| 107 | Madison East Wing Seismic Upgrade | Completed | \$6,146,000 | \$30,108,816 | \$30,143,816 | \$35,000 | \$2,463 |
| 108 | Renovation of Corsair Stadium | Completed | \$11,203,000 | \$35,299 | \$35,299 | \$0 | \$0 |
| 109 | Career Opportunity and Advancement Center (Bundy) | Completed | \$32,384,000 | \$0 | \$0 | \$0 | |
| 110 | Malibu Center | December 2021 | \$6,069,031 | \$0 | \$0 | \$0 | |
| 111 | Business & Facilities Infrastructure | Completed | \$17,506,952 | \$1,968,124 | \$1,968,124 | \$0 | |
| 112 | Master Planning, Program Management, Overhead | On-Going | \$2,000,000 | \$825,000 | \$833,427 | \$8,427 | |
| 113 | Energy Efficiency Projects | Completed | \$5,371,136 | \$3,016,773 | \$3,016,773 | \$0 | |
| 114 | Community Classroom & Facility Projects | Completed | \$0 | \$3,162,183 | \$3,162,183 | \$0 | \$0 |
| 115 | Real Property Acquisition | Completed | \$0 | \$24,902,902 | \$24,859,475 | -\$43,427 | \$221,089 |
| 116 | Roadways, Walkways, Grounds, Parking Lots, and Garages | Completed | \$0 | \$2,130,670 | \$2,130,670 | \$0 | |
| 117 | Infrastructure & Technology - Technology | Completed | \$0 | \$2,434,417 | \$2,434,417 | \$0 | \$0 |
| 118 | Infrastructure & Technology - Utility | Completed | \$0 | \$27,753 | \$27,753 | \$0 | \$0 |
| 119 | Emergency Lighting, Fire Alarm, and Security System | On-Going | \$0 | \$11,520,794 | \$11,520,794 | \$0 | \$225,995 |
| 120 | Student Services | March 2019 | \$0 | \$24,365,147 | \$6,870,490 | -\$17,494,657 | \$3,704,864 |
| 121 | Cost of Issuance | Completed | \$0 | \$498,026 | \$498,026 | \$0 | \$0 |
| 122 | Management Reserve | On-Going | \$0 | \$724,435 | \$724,435 | \$0 | \$724,435 |
| 123 | Unissuable Bond | Completed | \$0 | \$4,171 | \$4,171 | \$0 | \$4,171 |
| | Project Totals | | \$295,000,000 | \$295,000,000 | \$295,000,000 | \$0 | \$8,499,079 |

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure V Bond Budget

As of June 30, 2018

| | Project Name | Completion | Project Budget | Measure V Allocation | Other Funding | Measure V Expenditures as of 6/30/18 | Measure V Expenditures as of 3/31/18 | Measure V Expenditures Last Period | Total Measure V Remaining |
|-----|---|----------------|-------------------|-------------------------|---------------|--|--|--|------------------------------|
| 101 | Replacement Math and Science Extension Building | September 2022 | \$124,958,336 | \$82,317,992 | \$42,640,344 | \$2,210,264 | \$0 | \$2,210,264 | \$80,107,728 |
| 102 | Student Services | March 2019 | \$130,224,164 | \$33,624,909 | \$96,599,255 | \$55,202 | \$0 | \$55,202 | \$33,569,707 |
| 103 | Malibu Center | December 2021 | \$50,000,000 | \$25,000,000 | \$25,000,000 | \$0 | \$0 | \$0 | \$25,000,000 |
| 104 | Early Childhood Development/Childcare | June 2020 | \$30,925,693 | \$15,405,517 | \$15,520,176 | \$0 | \$0 | \$0 | \$15,405,517 |
| 105 | Art Building Replacement | September 2022 | \$32,914,000 | \$24,000,000 | \$8,914,000 | \$184 | \$0 | \$184 | \$23,999,816 |
| 106 | Business Building Renovation | December 2023 | \$25,017,000 | \$12,547,000 | \$12,470,000 | \$0 | \$0 | \$0 | \$12,547,000 |
| 107 | Air Conditioning | December 2019 | \$10,777,654 | \$10,777,654 | \$0 | \$422,330 | \$0 | \$422,330 | \$10,355,324 |
| 108 | ADA | On-Going | \$4,000,000 | \$4,000,000 | \$0 | \$0 | \$0 | \$0 | \$4,000,000 |
| 109 | Master Planning | December 2019 | \$450,000 | \$450,000 | \$0 | \$0 | \$0 | \$0 | \$450,000 |
| 110 | Drescher Hall Modernization | On-Going | \$13,005,082 | \$13,000,000 | \$5,082 | \$0 | \$0 | \$0 | \$13,000,000 |
| 111 | Outdoor Classroom | June 2022 | \$10,000,000 | \$10,000,000 | \$0 | \$100,000 | \$0 | \$100,000 | \$9,900,000 |
| 112 | SMMUSD | August 2021 | \$20,000,000 | \$20,000,000 | \$0 | \$0 | \$0 | \$0 | \$20,000,000 |
| 113 | City of Santa Monica | On-Going | \$20,000,000 | \$20,000,000 | \$0 | \$0 | \$0 | \$0 | \$20,000,000 |
| 114 | Classrooms Relocation | On-Going | \$4,900,000 | \$4,900,000 | \$0 | \$0 | \$0 | \$0 | \$4,900,000 |
| 115 | TBD | On-Going | \$39,876,928 | \$39,876,928 | \$0 | \$0 | \$0 | \$0 | \$39,876,928 |
| 120 | Other Bond Related Expenses | On-Going | \$300,000 | \$300,000 | \$0 | \$184 | \$0 | \$184 | \$299,816 |
| 121 | Cost of Issuance | On-Going | \$800,000 | \$800,000 | | \$291,277 | \$0 | \$291,277 | \$508,723 |
| 122 | Management Reserve | On-Going | \$28,000,000 | \$28,000,000 | | \$0 | \$0 | \$0 | \$28,000,000 |
| 123 | Unissuable Bond | On-Going | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| | Project Totals | | \$546,148,857 | \$345,000,000 | \$201,148,857 | \$3,079,441 | \$0 | \$3,079,441 | \$341,920,559 |

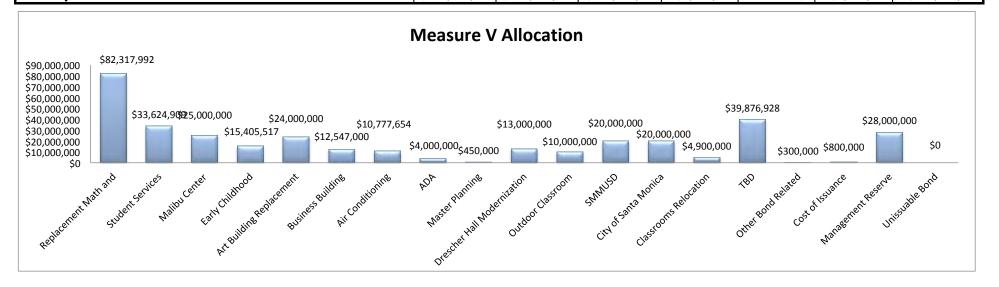

SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure V Bond Budget History

as of June 30, 2018

| | Project Name | Completion | Preliminary Measure V | Measure V Budget as of | Measure V Budget as of | Variance | Measure V Remaining as |
|-----|---|----------------|--------------------------|---------------------------|---------------------------|---------------|---------------------------|
| | | | Budget | 3/31/18 | 6/30/18 | | of 6/30/18 |
| 101 | Replacement Math and Science Extension Building | September 2022 | \$82,317,992 | \$82,317,992 | \$82,317,992 | \$0 | \$80,107,728 |
| 102 | Student Services | March 2019 | \$21,130,252 | \$21,130,252 | \$33,624,909 | \$12,494,657 | \$33,569,707 |
| 103 | Malibu Center | December 2021 | \$25,000,000 | \$25,000,000 | \$25,000,000 | \$0 | \$25,000,000 |
| 104 | Early Childhood Development/Childcare | June 2020 | \$15,405,517 | \$15,405,517 | \$15,405,517 | \$0 | \$15,405,517 |
| 105 | Art Building Replacement | September 2022 | \$24,000,000 | \$24,000,000 | \$24,000,000 | \$0 | \$23,999,816 |
| 106 | Business Building Renovation | December 2023 | \$12,547,000 | \$12,547,000 | \$12,547,000 | \$0 | \$12,547,000 |
| 107 | Air Conditioning | December 2019 | \$10,777,654 | \$10,777,654 | \$10,777,654 | \$0 | \$10,355,324 |
| 108 | ADA | On-Going | \$4,000,000 | \$4,000,000 | \$4,000,000 | \$0 | \$4,000,000 |
| 109 | Master Planning | December 2019 | \$450,000 | \$450,000 | \$450,000 | \$0 | \$450,000 |
| 110 | Drescher Hall Modernization | On-Going | \$13,000,000 | \$13,000,000 | \$13,000,000 | \$0 | \$13,000,000 |
| 111 | Outdoor Classroom | June 2022 | \$10,000,000 | \$10,000,000 | \$10,000,000 | \$0 | \$9,900,000 |
| 112 | SMMUSD | August 2021 | \$20,000,000 | \$20,000,000 | \$20,000,000 | \$0 | \$20,000,000 |
| 113 | City of Santa Monica | On-Going | \$20,000,000 | \$20,000,000 | \$20,000,000 | \$0 | \$20,000,000 |
| 114 | Classrooms Relocation | On-Going | | \$4,900,000 | \$4,900,000 | \$0 | \$4,900,000 |
| 115 | TBD | On-Going | \$57,271,585 | \$52,371,585 | \$39,876,928 | -\$12,494,657 | \$39,876,928 |
| 120 | Other Bond Related Expenses | On-Going | \$300,000 | \$300,000 | \$300,000 | \$0 | \$299,816 |
| 121 | Cost of Issuance | On-Going | \$800,000 | \$800,000 | \$800,000 | \$0 | \$508,723 |
| 122 | Management Reserve | On-Going | \$28,000,000 | \$28,000,000 | \$28,000,000 | \$0 | \$28,000,000 |
| 123 | Unissuable Bond | On-Going | \$0 | \$0 | \$0 | \$0 | \$0 |
| | Project Totals | | \$345,000,000 | \$345,000,000 | \$345,000,000 | \$0 | \$341,920,559 |

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure U Project Schedule As of June 30, 2018

| | Project Name | Completion | 2014 | 2015 | 2016 | 2017 | 2018 | 2019 |
|-----|---|------------|--------|------------|------|------|------|------|
| Α | Purchase of BAE Airport Site | Completed | | | | | | |
| В | Emeritus College Facility | Completed | | | | | | |
| С | Purchase of 1738 Pearl Street | Completed | | | | | | |
| D | PE Temp. Bldg. Replacement | Completed | | | | | | |
| Е | Remodel Library Village for Math | Completed | | | | | | |
| F | SM Airport Campus Site Improvements | Completed | | | | | | |
| G | SM Airport Campus West Building | Completed | | | | | | |
| Н | Theater Arts Renovation | Completed | | | | | | |
| - 1 | Earthquake Rpl. Liberal Arts North | Completed | | | | | | |
| J | Music Complex | Completed | | | | | | |
| K | Earthquake Rpl. Liberal Arts South | Completed | | | | | | |
| L | Shuttle Replacement Parking | Completed | | | | | | |
| М | North Quad Plaza | Completed | | | | | | |
| N | Letters & Sci Demo/Restore | Completed | | | | | | |
| 0 | Student Services Building | March 2019 | | | | | | |
| Р | Science Complex Addition | Completed | | | | | | |
| Q | Infrastructure & Safety | Completed | | | | | | |
| R | Restroom Improvements | Completed | | | | | | |
| S | Master Planning | Completed | | | | | | |
| Т | 14th and Pico Project | Completed | | | | | | |
| U | Unissuable Bond | Completed | | | | | | |
| | * SM Airport Campus also known as Bundy | Site | In Cor | nstruction | | | | |

| Projects | Budget | 02/03 Final | 03/04 Final | 04/05 Final | 05/06 Final | 06/07 Final | 07/08 Final | 08/09 Final | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|--------------------------------------|--------------|-------------|-------------|------------------|---------------|------------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-----------------|
| U7100010 | | | | | | | | | | | | 1 | | | | | | |
| Purchase of BAE Airport Site (A) | | | | | | | | | | | | | | | | | | |
| Site Acquisition | | \$0 | \$0 | 60 | \$30,280,878 | 60 | 60 | 60 | - 60 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | \$30,280,878 |
| Total | | \$0 \$0 | \$0 \$0 | | \$30,280,878 | | \$0 \$0 | \$0 \$0 | | | | | | | | | | |
| Project Budget | \$30,280,878 | \$0 | \$0] | Φ U | \$30,200,070 | \$ 0 | ŞU | ψU | \$ 0 | ψU | ŞU | \$0 | ŞU | \$ 0 | \$0 |) (| ار \$0 | \$30,280,878 |
| Less Other Funding | \$30,280,878 | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| Net Actual Measure U Expenditures | \$30,280,878 | | | | | | | | | | | | | | | | | |
| | \$30,280,878 | | | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | | | |
| U7100028 | | | | | | | | | | | | | | | | | | |
| Emeritus College Facility (B) | | | | | | | | | | | | | | | | | | |
| Site Acquisition | | \$8.658.675 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$8,658,675 |
| Legal | | \$14,649 | \$3,009 | \$20,421 | \$0 | | | | | | | | | | | | | |
| Architect | | \$93,735 | \$27.831 | \$161 | \$0 | | \$0 | | | | | \$0 | | | | | | |
| Engineering | | \$18,400 | \$0 | \$0 | | \$0 | \$0 | | \$0 | \$0 | | \$0 | | | | | \$0 | \$18,400 |
| Supply | | \$0 | \$4,461 | \$0 | | | | | | | | | | | | | | |
| Building & Additions | | \$0 | \$17,496 | \$0 | | | | | | | | | \$0 | | | | | |
| Cap Equipment | | \$0 | \$49,406 | \$0 | \$0 | \$0 | \$0 | | \$0 | | \$0 | \$0 | | | | | | \$49,406 |
| Non-Cap Equipment | | \$0 | -\$2,197 | \$0 | | | | | | | | | \$0 | | | | | |
| Total | | \$8,785,459 | \$100,007 | \$20,582 | | | | | | | | | | | | | | |
| Project Budget | \$9,603,782 | Received | *, | 7, | 7-, | | | | | | ** | | ** | | | | | 72,222,232 |
| Less Other Funding* | \$693,842 | \$693,842 | | * Other Funding | Source: | | | | | | | | | | | | | |
| Net | \$8,909,940 | φοσο,σ ιΣ | | Emeritus Collec | | \$693 842 receiv | ed | | | | | | | | | | | |
| Actual Measure U Expenditures | \$8,909,940 | | | Zillolitao oollo | go i oundudon | ,000,012100011 | ou | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | | | |
| rtanning Balance | , ,,, | | | | | | | | | | | | | | | | | |
| U7100006 | | | 1 | | | | | | | | | | | | | | | 1 |
| 1738 Pearl Street (C) | | | | | | | | | | | | | | | | | | |
| Site Acquisition | | \$0 | \$704,534 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$704,534 |
| Site Improvement | | \$0 | \$3,250 | \$0 | | | | | | | | | | | | | | |
| Building & Additions | | \$0 | \$41,424 | \$0 | | | | \$0 | | | | | | | | | | |
| Total | | \$0 | \$749,208 | \$0 | \$0 | \$0 \$0 | \$0 | | | | | \$0 | \$0 | | \$0 | | \$0 | \$749,208 |
| Project Budget | \$749,208 | **- | , | **- | ** | | ** | ** | | ** | ** | | ** | | | | | ,= |
| Less Other Funding | \$0 | | | | | | | | | | | | | | | | | |
| Net | \$749,208 | | | | | | | | | | | | | | | | | |
| Actual Measure U Expenditures | \$749,208 | | | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | | | |

| Projects | Budget | 02/02 Einal | 02/04 Einal | 04/0E Final | 0E/06 Einel | 06/07 Final | 07/00 Einal | 09/00 Einal | 00/40 Einel | 10/11 Final | 44/42 Einal | 42/42 Einal | 42/44 Einel | 14/4E Einel | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|---------------------------------------|-------------|--------------|--------------|--------------|--------------|--------------|--------------|--------------|---------------|--------------|--------------|--------------|--------------|--------------|--------------|--------------|--------------|-----------------|
| Frojects | Buugei | 02/03 Filial | 03/04 Fillal | 04/05 Fillal | 05/06 Fillal | 06/07 Fillal | 07/00 Fillal | 00/09 Fillal | US/ IU FIIIAI | 10/11 Fillal | 11/12 Fillal | 12/13 Fillal | 13/14 FIIIdi | 14/15 Fillal | 15/16 Fillal | 10/17 Fillal | 17/10 Fillal | Combined rotals |
| U7100026 | | | | | | | | | | | | | | | | | | |
| PE Temporary Building Replacement (D) | | | | | | | | | | | | | | | | | | |
| Architect | | \$148,055 | \$42,372 | \$6,220 | \$485 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$197,133 |
| Building & Additions | | \$43,866 | \$1,922,493 | \$415,932 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | | | \$0 | | \$0 | \$2,382,291 |
| Inspection & Testing | | \$6,455 | \$136,510 | \$716 | \$0 | \$0 | \$0 | \$0 | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$143,681 |
| Project Management | | \$4,800 | \$56,247 | \$5,225 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$66,272 |
| Advertising and Moving Expenses | | \$763 | \$0 | \$6,893 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | \$0 | | \$0 | \$7,656 |
| Total | | \$203,939 | \$2,157,622 | \$434,987 | \$485 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$2,797,033 |
| Project Budget | \$2,797,033 | | | | | , | | | | | | | | | | | - | |
| Less Other Funding | \$0 | | | | | | | | | | | | | | | | | |
| Net | \$2,797,033 | | | | | | | | | | | | | | | | | |
| Actual Measure U Expenditures | \$2,797,033 | | | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| U7100310 | | | | | | | | | | | | | | | | | | |
| Remodel Library Village for Math (E) | | | | | | | | | | | | | | | | | | |
| Moving Exp. | | \$0 | \$38,625 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | | | | | \$38,625 |
| Building & Additions | | \$0 | \$1,036,490 | \$115,653 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | | | |
| Architect | | \$104,992 | \$27,141 | \$1,340 | \$486 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | | | | | \$133,959 |
| Engineering | | \$0 | \$2,658 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | | | | | \$2,658 |
| Inspection & Testing | | \$0 | \$27,083 | \$25,175 | \$0 | \$0 | \$0 | \$0 \$0 | \$0 | \$0 | | \$0 | | \$0 | \$0 | | \$0 | |
| Project Management | | \$0 | \$51,679 | \$4,400 | \$0 | \$0 | \$0 | | | \$0 | | | | | | | | \$56,079 |
| Advertising and Moving Expenses | | \$207 | \$10,137 | \$12,623 | \$0 | \$0 | \$0 | \$0 | | \$0 | | | | | | | | |
| Total | | \$105,199 | \$1,193,813 | \$159,191 | \$486 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$1,458,690 |
| Project Budget | \$1,458,690 | | | | | | | | | | | | | | | | | |
| Less Other Funding | \$0 | | | | | | | | | | | | | | | | | |
| Net | \$1,458,690 | | | | | | | | | | | | | | | | | |
| Actual Measure U Expenditures | \$1,458,690 | | | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | | | |

| Projects | Budget | 02/03 Final | 03/04 Final | 04/05 Einal | 05/06 Final | 06/07 Final | 07/08 Einal | 09/09 Einal | 00/10 Einal | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|--|--------------|---------------|---------------|---|---------------|---------------|---------------|---------------|---------------|---------------|---------------|---------------|---------------|---------------|---------------|---------------|---------------|-----------------|
| Flojects | Duuget | 02/03 i iiiai | 03/04 I IIIai | 04/03 1 11101 | 03/00 i iiiai | 00/07 I IIIai | 07/00 1 11141 | 00/03 1 11101 | 03/10 I IIIai | 10/11 I IIIai | 11/12 I IIIai | 12/13 1 11101 | 13/14 1 11101 | 14/13 1 11101 | 13/10 1 11141 | 10/17 I IIIai | 17/10 1 11101 | Combined Totals |
| U7100027 | | | | | | | | | | | | | | | | | | |
| SM Airport Campus Site Improvements (F) | | | | | | | | | | | | | | | | | | |
| Supplies | | \$0 | \$26,234 | \$975 | \$5,873 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$33.082 |
| Misc Fees | _ | \$0 | | | \$0 | \$34,274 | \$0 | \$0 | \$0 | \$0 | | | | | | | | \$34,299 |
| Other Contract Services | | \$3,860 | \$11,508 | \$8,434 | | \$0 | \$0 | \$0 | \$0 | \$0 | | | | | | | | \$25,302 |
| Site Improvement | | \$0 | | \$15,182 | | \$7,237 | \$0 | \$0 | \$0 | \$0 | | | | | | | | \$28,209 |
| Building & Additions | | \$0 | | | \$4.824 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | | | | | |
| Architect | | \$104.934 | \$500 | | \$43,570 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | | | | | |
| Engineering | | \$35,000 | \$148,304 | | \$10,040 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | | | | | \$194,294 |
| Inspection & Testing | 1 | \$5.032 | \$118,662 | | | \$0 | \$0 | \$0 | \$0 | \$0 | | | | | | | | |
| Project Management | | \$750 | \$155,798 | \$38,425 | \$1,365 | \$220 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | \$0 | \$0 | | \$196,558 |
| City Fees, Advertising and Security System | | \$16.587 | \$1,802 | | \$150 | \$4,375 | \$0 | \$0 | \$0 | \$0 | | | | | | | \$0 | \$23,241 |
| Total | | \$166,163 | \$1,958,530 | | | \$46,106 | \$0 | \$0 | \$0 | \$0 | | | | | | | | |
| Project Budget | \$4,170,264 | | , , , | ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,, | , | , | | | | | | | | | | | | |
| Less Other Funding | \$0 | 1 | | | | | | | | | | | | | | | | Į. |
| Net | \$4,170,264 | 1 | | | | | | | | | | | | | | | | Į. |
| Actual Measure U Expenditures | \$4,170,264 | | | | | | | | | | | | | | | | | Į. |
| Running Balance | \$0 | ī | | | | | | | | | | | | | | | | Į. |
| | • | | | | | | | | | | | | | | | | | |
| U7110027 | | | | | | | | | | | | | | | | | | |
| SM Airport Campus West Building (G) | | | | | | | | | | | | | | | | | | |
| Supply | | \$0 | \$0 | \$17,650 | \$28,017 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$45,667 |
| Other Contract Services | | \$0 | | | \$3,576 | \$0 | \$0 | \$0 | \$0 | \$0 | | | \$0 | | | | \$0 | \$3,576 |
| Moving Expenses | | \$0 | | | \$15,824 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | | | \$0 | | \$16,004 |
| Building & Additions | | \$0 | | | | \$46,946 | \$0 | \$0 | \$0 | \$0 | | | | | | | | \$16,340,543 |
| Architect | | \$0 | | | \$49,779 | \$1,147 | \$0 | \$0 | \$0 | \$0 | | | | | | | | |
| Engineering | | \$0 | | \$9,800 | \$5,010 | \$963 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | \$0 | \$0 | \$18,693 |
| Inspection & Testing | | \$0 | | \$126,510 | \$9,856 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | | | | | \$157,539 |
| Project Management | | \$0 | | \$313,715 | | \$0 | \$0 | \$0 | \$0 | \$0 | | | | | | | | \$342,121 |
| Cap Equipment | | \$0 | | \$326,382 | \$4,792 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | | | | | \$380,969 |
| Non-Cap Equipment | | \$0 | | \$280,558 | \$57,240 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | | | | | \$337,798 |
| Total | | \$0 | \$1,060,292 | \$17,156,277 | \$1,444,115 | \$49,056 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$19,709,741 |
| Project Budget | \$19,709,741 | | | | | | | | | | | | | | | | | |
| Less Other Funding | \$0 | 1 | | | | | | | | | | | | | | | | ļ |
| Net | \$19,709,741 | | | | | | | | | | | | | | | | | ļ |
| Actual Measure U Expenditures | \$19,709,741 | | | | | | | | | | | | | | | | | ļ |
| Running Balance | \$0 |) | | | | | | | | | | | | | | | | |

| Projects | Budget | 02/03 Final | 03/04 Final | 04/05 Final | 05/06 Final | 06/07 Final | 07/08 Final | 08/09 Final | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|--|-----------------------------|---|---|--|--|---|--|--|---|--|---|---|---|---|---|--|---|--|
| | | | | | | | | | | | | | | | | | | |
| U7100025 | | | | | | | | | | | | | | | | | | |
| Theatre Arts Renovation (H) | | | | | | | | | | | | | | | | | | |
| Supplies | | \$0 | \$8,904 | -\$14 | \$12,858 | \$16,619 | \$0 | \$0 | \$0 | \$0 | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$38,367 |
| Legal | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | \$0 | \$0 | | \$0 | | \$0 |
| Moving Services | | \$0 | \$0 | | \$0 | \$14,061 | \$0 | \$0 | \$0 | \$0 | | | \$0 | | | | | \$14,061 |
| Other Contract Services | | \$0 | \$0 | | \$0 | \$0 | \$0 | \$5,245 | \$0 | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$5,245 |
| Rental / Lease | | \$0 | \$1,446 | \$2,200 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$3,646 |
| Building & Additions | | \$528 | \$1,326,630 | \$4,540,487 | \$10,897,603 | \$56,122 | \$25,220 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$16,846,590 |
| Architect | | \$289,913 | \$369,213 | \$423,416 | \$82,639 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$47,365 | \$0 | \$0 | \$0 | \$0 | \$1,212,545 |
| Engineering | | \$6,174 | \$2,981 | \$16,606 | \$2,375 | \$1,250 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$29,386 |
| Inspection & Testing | | \$150 | \$14,785 | \$353,890 | \$297,675 | \$1,116 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$667,616 |
| Project Management | | \$150 | \$45,698 | \$184,219 | \$193,898 | \$14,818 | \$230 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$439,013 |
| Cleaning, Storage and Installation | | \$0 | \$812 | \$0 | \$2,548 | \$2,267 | \$0 | \$0 | \$0 | \$0 | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$5,627 |
| Cap Equipment | | \$0 | \$31,638 | \$0 | \$6,458 | \$59,689 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$97,785 |
| Non-Cap Equipment | | \$0 | \$2,388 | \$0 | \$36,749 | \$145,294 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$184,432 |
| Total | | \$296,915 | \$1,804,496 | \$5,520,804 | \$11,532,803 | \$311,236 | \$25,450 | \$5,245 | \$0 | \$0 | \$0 | \$0 | \$47,365 | \$0 | \$0 | \$0 | \$0 | \$19,544,314 |
| Project Budget | \$19,544,314 | | | | | | | | | | | | | | | | | |
| Less Other Funding | \$0 | | | | | | | | | | | | | | | | | |
| Net | \$19,544,314 | | | | | | | | | | | | | | | | | |
| Actual Measure U Expenditures | \$19,544,314 | | | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| U7100110 | | | | | | | | | | | | | | | | | | |
| Earthquake Rpl. Liberal Arts North (I) | | | | | | | | | | | | | | | | | | |
| Supplies | | \$0 | \$0 | \$0 | \$0 | \$1,408 | \$0 | | | | | | | | | | I I | |
| Legal | | \$0 | \$0 | \$0 | | | | \$75 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$1.483 |
| Other Contract Services | | | | | 801 | \$887 | | | | | | | | | | | | |
| Building & Additions | | \$0 | \$0 | | \$0 \$0 | \$887 \$75 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$887 |
| | | \$0 \$265 | \$0 \$0 | \$0 | | | | | | | \$0 | \$0 \$0 | | \$0 \$0 | \$0 \$0 | | \$0 \$0 | |
| Architect | | \$265 | \$0 | \$0 \$1,043,660 | \$0 \$5,916,281 | \$75 -\$973,001 | \$0 \$0 \$321,345 | \$0 \$0 \$14,898 | \$0 \$0 \$0 | \$0 \$0 -\$834,764 | \$0 \$0 \$0 | \$0 \$0 -\$1,127,809 | \$0 \$0 \$0 | \$0 \$0 \$0 | \$0 \$0 \$0 | \$0 \$0 -\$493,816 | \$0 \$0 \$0 | \$887 \$75 \$3,867,060 |
| Architect Engineering | | \$265 \$0 | \$0 \$611,732 | \$0 | \$0 \$5,916,281 \$209,490 | \$75 | \$0 \$0 \$321,345 \$21,215 | \$0 \$0 \$14,898 \$3,465 | \$0 \$0 \$0 \$0 | \$0 \$0 -\$834,764 \$0 | \$0 \$0 \$0 \$0 | \$0 \$0 -\$1,127,809 \$0 | \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 | \$0 \$0 -\$493,816 \$0 | \$0 \$0 \$0 \$0 | \$887 \$75 \$3,867,060 \$1,165,289 |
| Engineering | | \$265 \$0 \$3,248 | \$0 | \$0 \$1,043,660 \$102,824 \$0 | \$0 \$5,916,281 \$209,490 \$250 | \$75 -\$973,001 \$216,563 \$0 | \$0 \$0 \$321,345 \$21,215 \$250 | \$0 \$0 \$14,898 \$3,465 \$0 | \$0 \$0 \$0 \$0 \$0 | \$0 \$0 -\$834,764 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 | \$0 \$0 -\$1,127,809 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 | \$0 \$0 -\$493,816 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 | \$887 \$75 \$3,867,060 \$1,165,289 \$8,043 |
| Engineering Inspection & Testing | | \$265 \$0 \$3,248 \$0 | \$0 \$611,732 \$4,295 \$0 | \$0 \$1,043,660 \$102,824 \$0 \$28,312 | \$0 \$5,916,281 \$209,490 \$250 \$326,203 | \$75 -\$973,001 \$216,563 \$0 \$77,942 | \$0 \$0 \$321,345 \$21,215 \$250 \$0 | \$0 \$0 \$14,898 \$3,465 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 -\$834,764 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 | \$0 \$0 -\$1,127,809 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 -\$493,816 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 |
| Engineering Inspection & Testing Project Management | | \$265 \$0 \$3,248 \$0 \$0 | \$0 \$611,732 \$4,295 \$0 \$26,072 | \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 | \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 | \$75 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 | \$0 \$0 \$321,345 \$21,215 \$250 \$0 \$255 | \$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$286 | \$0 \$0 -\$834,764 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 -\$493,816 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 \$314,475 |
| Engineering Inspection & Testing Project Management Advertising and Fees | | \$265 \$0 \$3,248 \$0 \$0 \$0 | \$0 \$611,732 \$4,295 \$0 \$26,072 -\$4 | \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 | \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 | \$75 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 | \$0 \$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0 | \$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$286 \$0 | \$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 -\$493,816 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 \$314,475 |
| Engineering Inspection & Testing Project Management Advertising and Fees Cap-Equipment | | \$265 \$0 \$3,248 \$0 \$0 | \$0 \$611,732 \$4,295 \$0 \$26,072 | \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 | \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$0 | \$75 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 \$0 \$25,356 | \$0 \$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0 \$12,579 | \$0 \$0 \$14,898 \$3,465 \$0 \$1,155 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$286 \$0 | \$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 -\$493,816 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 \$314,475 \$7,330 \$37,935 |
| Engineering Inspection & Testing Project Management Advertising and Fees Cap-Equipment Non-Cap Equipment | | \$265 \$0 \$3,248 \$0 \$0 \$0 \$0 \$0 | \$0 \$611,732 \$4,295 \$0 \$26,072 -\$4 \$0 | \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 \$0 \$0 | \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$0 \$2,033 | \$75 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 \$0 \$25,356 \$170,425 | \$0 \$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0 \$12,579 \$4,093 | \$0 \$0 \$14,898 \$3,465 \$0 \$1,155 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$286 \$0 \$0 | \$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 -\$493,816 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 \$314,475 \$7,330 \$37,935 \$176,550 |
| Engineering Inspection & Testing Project Management Advertising and Fees Cap-Equipment Non-Cap Equipment Total | \$12 507 725 | \$265 \$0 \$3,248 \$0 \$0 \$0 \$0 \$0 \$0 \$3,513 | \$0 \$611,732 \$4,295 \$0 \$26,072 -\$4 \$0 | \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 \$0 \$0 | \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$0 | \$75 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 \$0 \$25,356 | \$0 \$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0 \$12,579 | \$0 \$0 \$14,898 \$3,465 \$0 \$1,155 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$286 \$0 | \$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 -\$493,816 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 \$314,475 \$7,330 \$37,935 |
| Engineering Inspection & Testing Inspection & Testing Project Management Advertising and Fees Cap-Equipment Non-Cap Equipment Total Project Budget | \$12,507,725 \$6.496.141 | \$265 \$0 \$3,248 \$0 \$0 \$0 \$0 \$0 \$3,513 Received | \$0 \$611,732 \$4,295 \$0 \$26,072 -\$4 \$0 \$0 \$642,095 | \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 \$0 \$0 \$1,215,679 | \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$0 \$2,033 \$6,583,194 | \$75 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 \$0 \$25,356 \$170,425 | \$0 \$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0 \$12,579 \$4,093 | \$0 \$0 \$14,898 \$3,465 \$0 \$1,155 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$286 \$0 \$0 | \$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 -\$493,816 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 \$314,475 \$7,330 \$37,935 \$176,550 |
| Engineering Inspection & Testing Project Management Advertising and Fees Cap-Equipment Non-Cap Equipment Total Project Budget Less Other Funding* | \$6,496,141 | \$265 \$0 \$3,248 \$0 \$0 \$0 \$0 \$0 \$0 \$3,513 | \$0 \$611,732 \$4,295 \$0 \$26,072 -\$4 \$0 \$0 \$642,095 | \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 \$0 \$0 \$1,215,679 | \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$2,033 \$6,583,194 Source: | \$75 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 \$0 \$25,356 \$170,425 -\$356,123 | \$0 \$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0 \$12,579 \$4,093 | \$0 \$0 \$14,898 \$3,465 \$0 \$1,155 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$286 \$0 \$0 | \$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 -\$493,816 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 \$314,475 \$7,330 \$37,935 \$176,550 |
| Engineering Inspection & Testing Inspection & Testing Project Management Advertising and Fees Cap-Equipment Non-Cap Equipment Total Project Budget | | \$265 \$0 \$3,248 \$0 \$0 \$0 \$0 \$0 \$3,513 Received | \$0 \$611,732 \$4,295 \$0 \$26,072 -\$4 \$0 \$0 \$642,095 | \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 \$0 \$0 \$1,215,679 | \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$2,033 \$6,583,194 Source: nica \$4,039,753 | \$75 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 \$0 \$25,356 \$170,425 -\$356,123 | \$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0 \$12,579 \$4,033 \$359,737 | \$0 \$0 \$14,898 \$3,465 \$0 \$1,155 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$286 \$0 \$0 | \$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 -\$493,816 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 \$314,475 \$7,330 \$37,935 \$176,550 |

| Projects | Budget | 02/03 Final | 03/04 Final | 04/05 Final | 05/06 Final | 06/07 Final | 07/08 Final | 08/09 Final | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|--|---|--------------|-------------|-------------------|------------------|-------------|--------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-----------------|
| | | | | | ' | • | | • | | | | | | | | | | |
| U7100013, U7100047 | | | | | | | | | | | | | | | | | | |
| Music Complex (J) | | | | | | | | | | | | | | | | | | |
| Advertising | | \$0 | \$0 | | \$0 | | \$0 | \$0 | | \$0 | | | | \$0 | | | | \$436 |
| Supplies | | \$0 | \$0 | \$0 | \$0 | \$194 | \$19,094 | \$0 | \$0 | \$0 | | \$0 | | \$0 | \$0 | | | \$19,288 |
| Consultants | | \$0 | \$0 | | \$0 | | \$36,000 | \$0 | | \$0 | | | | \$0 | | | | \$36,000 |
| Other Contract Services | | \$0 | \$0 | | \$0 | | \$180 | \$0 | | \$0 | | | | \$0 | | | | \$180 |
| Moving Services | | \$0 | \$0 | \$0 | \$0 | \$0 | \$6,330 | \$0 | | \$0 | | \$0 | | \$0 | | | | \$6,330 |
| Building & Additions | | \$0 | \$0 | | | -\$737,213 | \$273,531 | \$0 | \$0 | \$0 | | | | \$0 | | | | \$1,186,509 |
| Architect | | \$0 | \$187,922 | \$22,500 | \$37,227 | \$38,448 | \$4,052 | \$14,356 | | \$681 | | \$3,992 | | \$0 | | | | |
| Engineering | | \$0 | \$0 | | \$0 | \$0 | \$0 | \$21,370 | \$0 | \$0 | | | | \$0 | | | | \$21,370 |
| Inspection & Testing | | \$0 | \$0 | \$29,740 | \$19,265 | \$26,238 | \$35,880 | \$0 | \$0 | \$0 | | | | \$0 | | | | \$111,122 |
| Project Management | | \$0 | \$170 | \$36,739 | \$36,351 | \$56,914 | \$16,200 | \$1,288 | \$0 | \$0 | | | | \$0 | | | | \$147,662 |
| Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$0 | \$62,600 | \$0 | \$0 | \$0 | | | | \$0 | | | | \$62,600 |
| Non-Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$29,852 | \$78,582 | \$0 | \$0 | \$0 | | | | \$0 | | | | \$108,434 |
| Total | | \$0 | \$188,092 | \$445,879 | \$1,386,568 | -\$585,566 | \$532,447 | \$37,014 | \$0 | \$681 | \$225 | \$3,992 | \$2,038 | \$0 | \$0 | \$0 | \$0 | \$2,011,371 |
| Project Budget | \$4,629,484 | Received | | | | | | | | | | | | | | | | |
| Less Other Funding* | \$2,618,113 | \$2,618,113 | | * Other Funding | Source: | | | | | | | | | | | | | |
| Net | \$2,011,371 | | | Prop T Refinance | e \$2,618,113 re | eceived | | | | | | | | | | | | |
| Actual Measure U Expenditures | \$2,011,371 | | | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| U7100111 | | | | | | | | | | | | | | | | | | |
| Earthquake Rpl. Liberal Arts South (K) | | | | | | | | | | | | | | | | | | |
| Supply | | \$0 | \$0 | \$855 | \$2,497 | \$379 | \$23,811 | \$75 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$27,618 |
| Legal | | \$0 | \$0 | | \$0 | \$0 | \$2,203 | \$50 | \$0 | \$0 | | | | \$0 | | | | \$2,253 |
| Moving Services | | \$0 | \$0 | \$0 | \$0 | \$0 | \$4,063 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$4,063 |
| Consultants | | \$0 | \$0 | \$0 | \$17,265 | \$41,435 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$58,700 |
| Other Contract Services | | \$0 | \$0 | \$6,154 | \$202 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | \$0 | \$0 | \$0 | | |
| Building & Additions | | \$0 | \$0 | \$26,302 | \$3,091,306 | \$5,706,802 | -\$4,642,459 | \$0 | \$91,516 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$4,273,467 |
| Architect | | \$0 | \$0 | | -\$503,297 | \$163,506 | \$183,877 | \$39,984 | \$2,549 | \$0 | | | | \$0 | | | | \$723,174 |
| Engineering | | \$0 | \$0 | | \$150 | \$5,344 | \$500 | \$0 | \$0 | \$0 | | | | \$0 | | | | \$9,119 |
| Inspection & Testing | | \$0 | \$0 | \$0 | \$179,798 | \$296,015 | \$68,273 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$544,086 |
| Project Management | | \$0 | \$0 | | \$43,989 | \$262,598 | \$52,690 | \$1,722 | \$1,278 | \$0 | | | | \$0 | | | | \$362,276 |
| Cap-Equipment | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | \$0 | \$0 | | \$0 | \$0 |
| Non-Cap Equipment | | \$0 | \$0 \$0 | \$0 | \$0 | \$58,726 | \$45,388 | -\$7,074 | \$0 | \$0 | \$0 | \$0 | | \$0 | \$0 | \$0 | | \$97,040 |
| Total | | \$0 | \$0 | | \$2,831,909 | | -\$4,261,655 | \$34,757 | \$95,342 | \$0 | | | | \$0 | | | | |
| Project Budget | \$16,733,220 | Received | | . , , , | , , | | , , | | | | | | | | | | | , , |
| Less Other Funding* | \$10,625,070 | \$10,625,070 | | * Other Funding | Source: | | | | | | | | | | | | | |
| Net | \$6,108,150 | | | City of Santa Mo | | 0 received | | | | | | | | | | | | |
| Actual Measure U Expenditures | \$6,108,150 | | | State of Californ | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | . , .,, | | | | | | | | | | | | | |
| • • • | , ,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,, | | | | | | | | | | | | | | | | | |

| Projects | Budget | 02/03 Final | 03/04 Final | 04/05 Final | 05/06 Final | 06/07 Final | 07/08 Final | 08/09 Final | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|---------------------------------|--------------|-------------|-------------|-------------|-------------|--------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-----------------|
| • | | | | | | | | | | | | | | | | | | |
| U7100221 | | | | | | | | | | | | | | | | | | |
| Shuttle Replacement Parking (L) | | | | | | | | | | | | | | | | | | |
| Supplies | | \$0 | \$0 | \$0 | \$0 | \$0 | \$1,347 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$1,347 |
| Legal | | \$0 | \$0 | \$0 | \$8,462 | \$35,103 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$43,565 |
| Site Acquisition | | \$0 | \$0 | \$0 | \$0 | \$16,903,087 | \$0 | \$0 | \$0 | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$16,903,087 |
| Site Improvement | | \$0 | \$0 | \$0 | \$0 | \$3,027 | \$0 | \$0 | \$0 | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$3,027 |
| Building & Additions | | \$0 | \$0 | | \$0 | \$484,000 | \$1,252,224 | \$2,353 | \$0 | \$0 | | | \$0 | \$0 | \$0 | \$0 | | \$1,738,577 |
| Architect | | \$0 | \$0 | | \$0 | \$51,569 | \$7,208 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$58,777 |
| Inspection & Testing | | \$0 | \$0 | | \$0 | \$139,822 | \$41,250 | \$0 | \$0 | \$0 | | | \$0 | \$0 | \$0 | \$0 | | \$181,072 |
| Project Management | | \$0 | | | \$0 | \$7,631 | \$32,425 | \$0 | \$0 | \$0 | | | \$0 | \$0 | \$0 | \$0 | | \$40,056 |
| Total | | \$0 | \$0 | \$0 | \$8,462 | \$17,624,240 | \$1,334,455 | \$2,353 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$18,969,509 |
| Project Budget | \$18,969,509 | | | | | | | | | | | | | | | | | |
| Less Other Funding | \$0 | | | | | | | | | | | | | | | | | |
| Net | \$18,969,509 | | | | | | | | | | | | | | | | | |
| Actual Measure U Expenditures | \$18,969,509 | | | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| U7100321 | | | | | | | | | | | | | | | | | | |
| North Quad Plaza (M) | | | | | | | | | | | | | | | | | | |
| Legal | | \$0 | \$0 | | \$0 | \$0 | \$3,825 | \$5,604 | \$0 | \$0 | | | \$0 | \$0 | \$0 | \$0 | | \$9,429 |
| Building & Additions | | \$0 | \$0 | | \$0 | -\$443 | \$6,130,081 | \$3,634,487 | \$0 | \$0 | | | \$0 | \$0 | \$0 | \$0 | | \$9,764,125 |
| Architect | | \$0 | \$231,055 | \$8,444 | \$140,048 | \$435,618 | \$171,225 | \$68,633 | \$2,901 | \$10,483 | \$0 | | \$0 | \$0 | \$0 | \$0 | | \$1,068,407 |
| Engineering | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | \$0 | \$0 | \$0 | \$0 | | \$0 |
| Inspection & Testing | | \$0 | \$0 | | \$0 | \$0 | \$186,220 | \$107,477 | \$328 | \$0 | | | \$0 | \$0 | \$0 | | | |
| Project Management | | \$0 | \$0 | | \$210 | \$2,200 | \$135,601 | \$55,782 | \$606 | \$0 | | | \$0 | \$0 | \$0 | \$0 | | \$195,158 |
| Printing | | \$0 | \$1,900 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | \$0 | \$0 | \$0 | \$0 | | \$1,900 |
| Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$55,420 | \$0 | \$0 | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$55,420 |
| Total | | \$0 | \$232,955 | \$9,204 | \$140,258 | \$437,375 | \$6,626,952 | \$3,927,402 | \$3,834 | \$10,483 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$11,388,463 |
| Project Budget | \$11,388,463 | | | | | | | | | | | | | | | | | |
| Less Other Funding | \$0 | | | | | | | | | | | | | | | | | |
| Net | \$11,388,463 | | | | | | | | | | | | | | | | | |
| Actual Measure U Expenditures | \$11,388,463 | | | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | | | |

| Desir etc | Dudmak | 00/02 Final | 02/04 Final | 04/05 5: | 05/00 Final | 00/07 Final | 07/00 Final | 00/00 Final | 00/40 5: | 40/44 Final | 44/40 Final | 40/40 Final | 40/44 Final | 4445 5: | AF/AC Final | 40/47 Final | 47/40 Final | Combined Totals |
|--|---------------|-------------|-------------|-------------------|------------------|------------------|---------------|--------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|--------------|-------------|-----------------|
| Projects | Budget | 02/03 Final | U3/U4 FINAI | 04/05 Final | 05/06 Finai | 06/07 Final | 07/08 Final | 08/09 Finai | 09/10 Final | 10/11 Finai | 11/12 Finai | 12/13 Finai | 13/14 Finai | 14/15 Final | 15/16 Finai | 16/17 Final | 17/18 Final | Combined Totals |
| U7100500, U7126450, U7100334, U7100142 | | | | | | | | | | | | | | | 1 | | | |
| Student Services Building (O) | | | | | | | | | | | | | | | | | | |
| Supplies | | \$2,014 | \$0 | \$0 | \$0 | \$0 | \$0 | \$718 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$2,732 |
| PC Upgrades | | \$0 | \$765 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$765 |
| Consultants | | \$0 | \$0 | \$0 | \$0 | \$9,334 | \$55,693 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$65,027 |
| Legal | | \$0 | \$0 | \$0 | \$0 | \$38 | \$2,775 | \$31,776 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$34,588 |
| Other Contract Services | | \$210 | \$0 | \$0 | φ∪ | \$0 | \$17,561 | \$17,495 | \$18,817 | -\$70 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | φU | \$54,014 |
| Moving | | \$7,571 | \$0 | \$0 | \$0 | \$0 | \$0 | \$616 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$8,187 |
| Building & Additions | | \$359,141 | \$2,441 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$776 | \$560 | \$1,717,465 | \$9,584,253 | \$2,330,248 | \$13,994,884 |
| Architect | | \$31,782 | | \$235,230 | \$0 | \$43,992 | \$0 | \$690,099 | | \$38,643 | \$48,442 | \$388,611 | \$973,427 | | \$567,231 | \$469,372 | \$31,852 | \$6,229,854 |
| Engineering | | \$1,838 | \$0 | \$0 | \$0 | \$0 | \$0 | \$6,205 | \$27,363 | \$3,171 | \$0 | \$0 | \$0 | \$55,680 | \$73,757 | \$5,360 | \$0 | \$173,373 |
| Inspection & Testing | | \$0 | \$0 | \$0 | \$0 | \$0 | \$25,670 | \$34,687 | \$0 | \$0 | \$0 | \$0 | \$2,478 | \$0 | \$69,480 | \$69,396 | \$0 | \$201,711 |
| Project Management | | \$4,650 | \$0 | \$2,470 | \$0 | \$1,100 | \$0 | \$124,148 | \$0 | \$0 | \$0 | \$6,675 | \$15,650 | \$11,616 | \$120,550 | \$3,275 | \$0 | \$290,134 |
| Cap Equipment | | \$59,063 | \$0 | \$0 | \$0 | \$0 | \$8,745 | \$8,056 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$75,864 |
| Total | | \$466,268 | \$3,207 | \$237,700 | \$0 | \$54,464 | \$110,445 | \$913,802 | \$254,701 | \$41,744 | \$48,442 | \$395,286 | \$992,330 | \$2,570,508 | \$2,548,483 | \$10,131,656 | \$2,362,100 | \$21,131,135 |
| Project Budget | \$130,224,164 | Received | | * Other Funding | Source: | | | | | | | | | | | | | |
| Less Other Funding* | \$109,093,029 | \$1,321,000 | | State of Californ | ia \$1,321,000 r | eceived | | | | | | | | | | | | |
| Net | \$21,131,135 | | | Measure S \$45, | 595,322, Measi | ure AA \$6,870,4 | 90, Measure V | \$33,624,909 | allocated | | | | | | | | | |
| Actual Measure U Expenditures | \$21,131,135 | | | Measure U, S & | AA Interests \$2 | 21,681,308 alloc | ated | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | | | |

Student Services Building

Project Discription:

Consolidates various student services departments and college administration in a single complex at the front of the campus

Facility Size: 110,000 sq/ft & 500 cars underground parking structure


Status:

In construction

Architect: Steinberg Architects, Morris Architects

Contractor:

Minaco, Bernards



| Projects | Budget | 02/03 Final | 03/04 Final | 04/05 Final | 05/06 Final | 06/07 Final | 07/08 Final | 08/09 Final | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|---|---------------|-------------|-------------|-------------------|------------------|------------------|--------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-----------------|
| • | | • | • | | | | | | | | | | • | | | • | | |
| U7100090 | | | | | | | | | | | | | | | | | | |
| Science Complex Additional (P) | | | | | | | | | | | | | | | | | | |
| Architect | | \$0 | \$0 | \$0 | \$0 | \$246,425 | \$61,911 | \$0 | \$0 | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$308,336 |
| Total | | \$0 | \$0 | \$0 | | \$246,425 | \$61,911 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$308,336 |
| Project Budget | \$124,958,336 | • | | Other Funding | Source: | | | | | | | | | | | | | |
| Less Other Funding | \$124,650,000 | | | State of Californ | nia \$40,088,000 | allocated | | | | | | | | | | | | |
| Net | \$308,336 | | | Measure AA \$2, | 244,008, Measi | ure V \$82,317,9 | 92 allocated | | | | | | | | | | | |
| Actual Measure U Expenditures | \$308,336 | | | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| U6780000, U7100022, U7100331, U7100550, | | | I | | | | | | | | | | | | | | | |
| U7100005, U7100030, U7100031, U7100029, | | | | | | | | | | | | | | | | | | |
| U7100003, U7100008, U7100332, U7100072. | | | | | | | | | | | | | | | | | | |
| U7100042, U7100056, U7100039 | | | | | | | | | | | | | | | | | | |
| Infrastructure & Safety (Q) | | | | | | | | | | | | | | | | | | |
| Supplies | | \$0 | \$0 | \$254 | \$0 | \$0 | \$0 | \$1,700 | \$1,393 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$3,347 |
| Consultants | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$16,734 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$16,734 |
| Maintenance Agreement | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$14,673 | \$12,979 | \$12,979 | \$0 | \$0 | \$0 | \$0 | \$0 | \$40,632 |
| Legal | | \$0 | \$0 | \$0 | \$0 | \$0 | \$3,527 | \$3,294 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$6,821 |
| Other Contract Services | | \$0 | \$0 | \$0 | \$0 | \$0 | \$7,825 | \$81,445 | \$203,383 | \$3,320 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$295,973 |
| Building & Additions | | \$681,900 | \$195,175 | \$20,600 | \$0 | \$200,620 | \$733 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$1,099,028 |
| Architect | | \$69,081 | \$42,108 | \$0 | \$155,321 | \$448,507 | \$91,127 | \$4,227 | \$0 | \$0 | \$0 | -\$1,365 | \$0 | \$0 | \$0 | \$0 | \$0 | \$809,005 |
| Engineering | | \$8,050 | \$0 | \$0 | \$6,750 | \$12,000 | \$18,429 | \$2,360 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$47,589 |
| Inspection & Testing | | \$2,241 | \$4,250 | \$0 | \$0 | \$0 | \$5,807 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$12,298 |
| Project Management | | \$0 | \$2,805 | \$0 | | \$3,520 | \$1,840 | \$38 | \$196 | \$0 | | | \$0 | | | \$0 | \$0 | \$8,399 |
| Cap Equipment | | \$0 | \$0 | \$343,861 | \$0 | \$0 | \$0 | \$895,171 | \$349,531 | \$40,002 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$1,628,565 |
| Non-Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$4,216 | \$0 | \$29,694 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$33,910 |
| Advertising | | \$0 | \$785 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | |
| Total | | \$761,272 | \$245,122 | \$364,715 | \$162,071 | \$664,647 | \$129,287 | \$1,004,968 | \$558,718 | \$57,995 | \$42,673 | \$11,614 | \$0 | \$0 | \$0 | \$0 | \$0 | \$4,003,084 |
| Project Budget | \$4,003,084 | | | | | | | | | | | | | | | • | | |
| Less Other Funding | \$0 | | | | | | | | | | | | | | | | | |
| Net | \$4,003,084 | | | | | | | | | | | | | | | | | |
| Actual Measure U Expenditures | \$4,003,084 | | | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | | | |

| Projects | Budget | 02/03 Einal | 03/04 Einal | 04/05 Einal | 05/06 Einal | 06/07 Einal | 07/08 Einal | 08/09 Einal | 00/10 Einal | 10/11 Final | 11/12 Einal | 12/13 Einal | 13/14 Final | 14/15 Einal | 15/16 Final | 16/17 Final | 17/19 Einal | Combined Totals |
|-------------------------------|-------------|---------------|----------------------|---------------------|--------------------|-------------------|--------------------|-------------------|---------------|---------------|---------------|---------------|---------------|--------------------|--------------------|---------------------|---------------------------|-----------------|
| Fiojects | Duuget | 02/03 i iliai | 03/04 i iiiai | 04/03 i iiiai | 03/00 1 11141 | 00/07 I IIIai | 07/00 i iliai | 00/03 i iliai | 03/10 1 11141 | 10/11 I IIIai | 11/12 I IIIai | 12/13 11101 | 13/14 1 11101 | 14/13 | 13/10 1 11101 | 10/17 1 11101 | 17/10 Tillal | Combined Totals |
| U7100007 | | | | | | | | | | | | | | | | | | |
| Restroom Improvement (R) | | | | | | | | | | | | | | | | | | |
| Supplies | + | \$0 | \$564 | \$0 | \$1,075 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$1,639 |
| Other Contract Services | | \$0 | | | \$3.803 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 \$0 | | \$0 | | \$3,803 |
| Building & Additions | | \$0 | | | \$7,803 | \$0 | \$0 \$0 | \$0 \$0 | \$0 | \$0 \$0 | \$0 \$0 | \$0 \$0 | | \$0 \$0 | | \$C | | \$9,196 |
| | | | | | | | | | | | | | | | | | | |
| Inspection & Testing | | \$0 | | | \$820 | \$0 | \$0 | \$0 \$0 | \$0 | \$0 | | \$0 | | \$0 | | | | \$2,863 |
| Total | | \$0 | \$3,912 | \$0 | \$13,589 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$17,501 |
| Project Budget | \$17,501 | | | | | | | | | | | | | | | | | |
| Less Other Funding | \$0 | | | | | | | | | | | | | | | | | |
| Net | \$17,501 | | | | | | | | | | | | | | | | | |
| Actual Measure U Expenditures | \$17,501 | | | | | | | | | | | | | | | | | |
| Running Balance | \$0 |) | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| U7100004, U7110020 | | | | | | | | | | | | | | | | | | |
| Master Planning (S) | | | | | | | | | | | | | | | | | | |
| Consultants | | \$9,000 | \$26,516 | \$158,449 | \$374,329 | \$125,404 | \$17,998 | \$363,342 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$1.075.038 |
| Architect | | \$0 | \$17,617 | \$126,433 | \$104,083 | \$126,701 | \$346,827 | \$276,985 | \$0 | \$0 | \$0 | \$0 | | \$0 | | \$0 | | \$998.647 |
| Rental / Lease | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | \$0 | \$0 | | \$0 | | \$6,450 |
| Postage | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | | \$0 | | | | \$30,000 |
| Reimbursement to SMC | | \$0 | | | \$180 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | | \$0 | | \$180 |
| Project Management | | \$0 | | | \$0 | \$0 | \$0 | \$113 | \$0 | \$0 | | \$0 | \$0 | \$0 | | \$0 | | \$113 |
| Total | | \$9.000 | \$44.133 | | \$478.593 | \$252.105 | \$364.825 | \$640,439 | \$0 | \$0 | | \$0 | | | | \$0 | | \$2,110,430 |
| Project Budget | \$2,110,430 | | ψ 11 ,100 | 4021,000 | ψ47 0,030 | Ψ 2 02,100 | \$004,020 | \$040,400 | 40 | ΨΟ | 40 | Ψ0 | | Ψ0 | Ψ | Ψ. | , 40 | Ψ2,110,400 |
| Less Other Funding | \$2,110,430 | 1 | | | | | | | | | | | | | | | | |
| Net | \$2,110,430 | 4 | | | | | | | | | | | | | | | | |
| Actual Measure U Expenditures | \$2,110,430 | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| Running Balance | \$0 | 1 | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| U7100024 | | | | | | | | | | | | | | | | | | |
| 14th and Pico Project (T) | | | | | | | | | | | | | | | | | | |
| Consultants | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | | \$0 | | \$888 |
| Architect | | \$258,601 | \$47,343 | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | | \$0 | | \$305,94 |
| Inspection & Testing | | \$12,070 | \$0 | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | | \$12,070 |
| Project Management | | \$0 | \$340 | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | | \$0 | | \$340 |
| Total | | \$270,671 | \$48,571 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$319,242 |
| Project Budget | \$319,242 | ! | | | | | | | • | | | | | | | | | |
| Less Other Funding | \$0 | | | | | | | | | | | | | | | | | |
| Net | \$319,242 | 1 | | | | | | | | | | | | | | | | |
| Actual Measure U Expenditures | \$319,242 | | | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | | | |
| g | , 40 | 1 | | | | | | | | | | | | | | | | |
| Grand Total | 1 | £44 000 400 | £40.422.055 | \$28.685.697 | \$E4.040.4401 | \$2E 270 774 | \$5,283,853 | 66 E0E E72 | \$912.880 | -\$723.860 | \$91.341 | -\$716.916 | \$1.041.732 | \$2.570.508 | \$2.548.483 | \$9.637.840 | \$2,362,100 | \$4E0 000 070 |
| Granu rotal | 1 | φ11,000,400 | ⇒10,43∠,055 | ⊉∠0,000,69 / | ₽34,940,416 | \$25,275,771 | ა ნ,∠ნა,ნნ3 | φυ,000,0/3 | φ91∠,000 | -\$1∠3,060 | \$91,541 | -\$/10,916 | \$1,041,732 | \$∠,570,508 | \$∠,546,483 | \$9,537,84 € | ı ३∠,36∠,100 | \$159,998,873 |

Note: Project N had no expenses

| Measure U Interest | | 17-18 |
|--|-------------|-------------|
| Student Services Building (O) | | |
| Building & Additions | | \$7,054,856 |
| Total | | \$7,054,856 |
| Project Budget | \$7,054,856 | |
| Actual Measure U Interest Expenditures | \$7,054,856 | |
| Running Balance | \$0 | |

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure S Project Schedule As of June 30, 2018

| | Project Name | Completion | 201 | 8 | 20 | 019 | 202 | 0 | 2 | 021 | 202 | 22 |
|----|--|---------------|------|--------|----|-----|------|-------|-------|-----|-----|----|
| 1 | Athletic Fields Phase I, Corsair Field | Completed | | | | | | | | | | |
| 1A | Athletic Fields Phase I, John Adams | Completed | | | | | | | | | | |
| 2 | Performing Arts Center | Completed | | | | | | | | | | |
| 3 | Career Opportunity Center | Completed | | | | | | | | | | |
| 4 | Replacement Health/PE/Fitness Building | Completed | | | | | | | | | | |
| 5 | Early Childhood Development/Childcare | June 2020 | | | | | | | | | | |
| 6 | Malibu Site Acquisition and Facility | December 2021 | | | | | | | | | | |
| 7 | Energy Efficiency Projects | Completed | | | | | | | | | | |
| 8 | Satellite Campus Parking Facilities and Roadway Improvements | Deferred | | | | | | | | | | |
| 9 | Parking Garage, Grounds and Equipment - Student Services | March 2019 | | | | | | | | | | |
| 10 | Pico Promenade Improvements | Completed | | | | | | | | | | |
| 11 | Master Planning | Completed | | | | | | | | | | |
| 12 | Other Bond Related Expenses | On-Going | | | | | | | | | | |
| 13 | Adv. Architecture Related Exp for AA | Completed | | | | | | | | | | |
| 14 | Real Property Acquisition | Completed | | | | | | | | | | |
| 15 | Signage Safety/Information | Completed | | | | | | | | | | |
| 16 | Cost of Issuance | Completed | | | | | | | | | | |
| 17 | Unissuable Bond | Completed | | | | | | | | | | |
| | | | In P | lannii | ng | | In C | onstr | uctio | n | | |


| Projects | Budget | 04/05 Final | 05/06 Final | 06/07 Final | 07/08 Final | 08/09 Final | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|---|-------------|-------------|-------------|----------------|-------------------|----------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-----------------|
| | | | | | | | | | | | | | | | | |
| S7100019 | | | | | | | | | | | | | | | | |
| Athletic Field Phase I, Corsair Field (1) | | | | | | | | | | | | | | | | |
| Legal | | \$0 | \$0 | \$0 | \$301 | \$175 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$476 |
| Building & Additions | | \$0 | \$0 | \$0 | \$300,380 | \$2,579,095 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$2,879,475 |
| Architect | | \$27,332 | \$43,815 | \$197,557 | \$252,736 | \$279,173 | \$26,563 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$827,176 |
| Inspection & Testing | | \$0 | \$0 | \$0 | \$23,411 | \$57,585 | \$640 | \$296 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$81,932 |
| Project Management | | \$0 | \$0 | \$0 | \$9,871 | \$42,374 | \$565 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$52,810 |
| Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$483,017 | \$35,271 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$518,288 |
| Non-Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$2,066 | \$10,312 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$12,378 |
| Total | | \$27,332 | \$43,815 | \$197,557 | \$586,699 | \$3,443,485 | \$73,350 | \$296 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$4,372,535 |
| Project Budget | \$4,440,065 | Received | | | | | | | | | | | | | | |
| Less Other Funding* | \$67,530 | \$67,530 | | * Other Fundin | g Source: | | | | | | | | | | | |
| Net | \$4,372,535 | | | Metropolitan W | ater District \$6 | 7,530 received | | | | | | | | | | |
| Actual Measure S Expenditures | \$4,372,535 | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | |

Athletic Field Phase I, Corsair Field Project Description: Renovation of the Corsair Field, stadium lighting and sound system Status: Completed, 2009

00...p.0.00, 20


Architect: CO Architects

Contractor: Byrom Davey, Inc.



| Projects | Budget | 04/05 Final | 05/06 Final | 06/07 Final | 07/08 Final | 08/09 Final | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|---|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-----------------|
| | | | | | | | | | | | | | | | | |
| S7100038 | | | | | | | | | | | | | | | | |
| Athletic Field Phase I, John Adams (1A) | | | | | | | | | | | | | | | | |
| Legal | | \$0 | \$0 | \$0 | \$75 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$75 |
| Building & Additions | | \$0 | \$0 | \$0 | \$16,556 | \$1,395,261 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$1,411,817 |
| Architect | | \$0 | \$5,807 | \$93,941 | \$12,150 | \$31,818 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$143,715 |
| Inspection & Testing | | \$0 | \$2,874 | \$3,207 | \$0 | \$49,984 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$56,066 |
| Project Management | | \$0 | \$0 | \$0 | \$10,921 | \$45,170 | \$38 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$56,128 |
| Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$1,290,672 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$1,290,672 |
| Non-Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$11,334 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$11,334 |
| Total | | \$0 | \$8,681 | \$97,148 | \$39,701 | \$2,824,239 | \$38 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$2,969,807 |
| Project Budget | \$2,969,807 | | | | | | | | | | | | | - | | |
| Less Other Funding | \$0 | | | | | | | | | | | | | | | |
| Net | \$2,969,807 | | | | | | | | | | | | | | | |
| Actual Measure S Expenditures | \$2,969,807 |] | | | | | | | | | | | | | | |
| Running Balance | \$0 | 1 | | | | | | | | | | | | | | |

Athletic Field Phase I, John Adams Project Description: Renovation of John Adams Field and lighting Status: Completed, 2008 Architect: Caldwell Architects Contractor: Byrom Davey, Inc.




| Projects | Budget | 04/05 Final | 05/06 Final | 06/07 Final | 07/08 Final | 08/09 Final | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|-------------------------------|--------------|-------------|--------------|-----------------|-----------------|----------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-----------------|
| | | | | | | | | | | | | | | | | |
| S7100012 | | | | | | | | | | | | | | | | |
| Performing Arts Center (2) | | | | | | | | | | | | | | | | |
| Consultants | | \$0 | \$0 | \$0 | \$121,790 | \$76,639 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$198,429 |
| Other Contract Services | | \$0 | \$0 | \$4,269 | \$0 | \$22,729 | \$22 | \$68 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$27,088 |
| Supplies | | \$0 | \$0 | \$0 | \$14,565 | \$5,810 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$20,375 |
| Legal | | \$0 | \$0 | \$34,329 | \$275,667 | \$492,731 | \$15,629 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$818,356 |
| Advertising | | \$0 | \$0 | \$0 | \$320 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$320 |
| Building & Additions | | \$7,784,151 | \$10,292,986 | \$8,930,813 | \$2,991,903 | \$1,629,990 | \$50,000 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$31,679,843 |
| Architect | | \$0 | \$811,312 | \$182,457 | \$412,309 | \$121,588 | \$108 | \$1,962 | \$0 | \$0 | \$87,054 | \$0 | \$0 | \$0 | \$0 | \$1,616,790 |
| Engineering | | \$0 | | \$5,250 | \$1,500 | \$9,650 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | \$20,000 |
| Inspection & Testing | | \$104,308 | \$722,685 | \$411,193 | \$210,381 | \$22,256 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$1,470,823 |
| Project Management | | \$31,984 | \$155,732 | \$248,876 | \$263,690 | \$47,915 | \$3,244 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$751,441 |
| Cap Equipment | | \$0 | \$0 | \$130,218 | \$292,565 | \$342,693 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | \$765,476 |
| Non-Cap Equipment | | \$0 | \$0 | \$15,124 | \$93,106 | \$220,455 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$328,685 |
| Total | | \$7,920,443 | \$11,986,315 | \$9,962,528 | \$4,677,797 | \$2,992,455 | \$69,003 | \$2,030 | \$0 | \$0 | \$87,054 | \$0 | \$0 | \$0 | \$0 | \$37,697,625 |
| Project Budget | \$40,690,201 | Received | | - | | | | | | | _ | - | | • | | |
| Less Other Funding* | \$2,992,576 | \$2,992,576 | | * Other Funding | | | | | | | | | | | | |
| Net | \$37,697,625 | | | Madison Project | t Foundation \$ | 2,992,576 rece | ived | | | | | | | | | |
| Actual Measure S Expenditures | \$37,697,625 | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | |

Performing Arts Center

Project Description:
Construction of a state-of-the-art 499 seat performing arts theater

Status:
Completed, 2008

Architect:
Renzo Zecchetto
Contractor:
FTR International



| Proiects | Budget | 04/05 Final | 05/06 Final | 06/07 Final | 07/08 Final | 08/09 Final | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|--|--------------|----------------|-------------|-----------------|----------------|-----------------|-------------|-------------|-------------|--------------|-------------|-------------|-------------|-------------|-------------|-----------------|
| ojecte | Dauget | 0 1100 1 11101 | | 00.01.1 | 01100111101 | 00.00111141 | | | | 12.10.1.1.0. | | | 10/10/11/01 | 1 | | |
| S7100033, S7100144, S7100060 | | | | | | | | | | | | | | | | |
| Replacement Health/PE/Fitness Building (4) | | | | | | | | | | | | | | | | |
| Supplies | | \$4,809 | \$288 | \$0 | \$0 | \$0 | \$163 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$5,260 |
| Legal | | \$0 | \$0 | \$0 | \$0 | \$1,413 | \$75 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$1,488 |
| Other Contract Services | | \$1,634 | \$25,934 | \$0 | \$0 | \$253 | \$165 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$27,985 |
| Repair Facility | | \$0 | \$4,861 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$4,861 |
| Building & Additions | | \$0 | \$0 | \$0 | \$0 | | \$526,552 | \$0 | | \$0 | \$0 | \$6,037,080 | \$4,775,714 | | \$0 | |
| Architect | | \$0 | \$0 | \$0 | \$0 | \$0 | \$41,044 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | |
| Inspection & Testing | | \$0 | \$0 | | \$0 | | \$14,363 | \$0 | | \$0 | \$0 | \$0 | \$0 | | \$0 | |
| Project Management | | \$0 | \$0 | \$0 | \$0 | | \$23,425 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | |
| Cap Equipment | | \$0 | \$0 | | \$0 | | \$0 | \$17,613 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | |
| Total | | \$6,443 | \$31,083 | \$0 | \$0 | \$129,663 | \$605,787 | \$17,613 | \$0 | \$0 | \$0 | \$6,037,080 | \$4,775,714 | \$0 | \$0 | \$11,603,383 |
| Project Budget | \$58,272,030 | | | | | | | | | | | | | | | |
| Less Other Funding* | \$46,668,647 | | | * Other Funding | | | | | | | | | | | | |
| Net | \$11,603,383 | | | Measure AA \$4 | | | | | | | | | | | | |
| Actual Measure S Expenditures | \$11,603,383 | | | SCE \$190,847. | 28, Gas Co. \$ | 18,000 received | t | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | |
| S7100045 | | | | | | | | | | | | | | | | |
| Early Childhood Development/Childcare (5) | | | | | | | | | | | | | | | | ı |
| Supplies | | \$0 | \$0 | \$0 | \$0 | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$294 | |
| Consultants | | \$0 | \$0 | \$0 | \$9,200 | | \$0 | \$0 | \$0 | \$4,800 | \$12,930 | \$14,078 | \$1,388 | | \$0 | |
| Legal | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$1,690 | | \$0 | |
| Building & Additions | | \$0 | \$0 | | \$0 | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$747,457 | \$747,699 |
| Architect | | \$0 | \$0 | \$0 | \$0 | | \$0 | \$0 | \$966 | \$51,792 | \$142,428 | \$142,968 | \$476,827 | | \$67,918 | |
| Inspection & Testing | | \$0 | \$0 | \$0 | \$0 | | | \$0 | \$0 | \$37,796 | \$7,475 | \$823 | \$2,323 | | \$4,085 | |
| Project Management | | \$0 | \$0 | | \$0 | | \$0 | \$1,246 | \$21,980 | \$58,247 | \$33,435 | \$8,803 | \$3,118 | | \$307,493 | \$434,320 |
| Total | | \$0 | \$0 | \$0 | \$9,200 | \$0 | \$0 | \$1,246 | \$22,946 | \$152,635 | \$196,268 | \$166,670 | \$485,344 | \$85,555 | \$1,127,247 | \$2,247,111 |
| Project Budget | \$30,925,693 | | | | | | | | | | | | | | | |
| Less Other Funding* | \$22,067,115 | \$0 | | * Other Funding | | | | | | | | | | | | |
| Net | \$8,858,578 | | | City of Santa M | | | | | | | | | | | | |
| Actual Measure S Expenditures | \$2,247,111 | | | Measure V \$15 | ,405,517 alloc | ated | | | | | | | | | | |
| Running Balance | \$6,611,468 | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | |
| S7100077, S7100015 | | | | | | | | | | | | | | | | |
| Malibu Site Acquisition and Facilities (6) | | | | | | | | | | | | | | | | |
| Consultants | | \$0 | \$0 | \$0 | \$0 | | \$0 | | \$72,157 | \$68,109 | \$30,342 | \$66,277 | \$60,262 | | \$17 | |
| Legal | | \$0 | \$27,722 | \$16,787 | \$6,159 | | \$0 | | \$0 | \$0 | \$1,360 | \$78,851 | \$40,114 | | \$6,324 | |
| Other Contract Services | | \$0 | \$0 | \$0 | \$0 | | \$0 | | | \$0 | \$0 | \$1,820 | \$0 | | \$0 | |
| Building & Additions | | \$0 | \$0 | | \$0 | | \$0 | \$0 | | \$0 | \$536 | \$0 | \$0 | | \$2,019,660 | \$2,020,197 |
| Architect | | \$0 | \$0 | \$0 | \$0 | | \$0 | \$0 | \$966 | \$257,584 | \$732,891 | \$173,610 | \$34,753 | | \$341,307 | \$1,692,884 |
| Engineering | | \$0 | \$0 | \$0 | \$0 | | \$0 | \$0 | \$0 | \$785 | \$562 | \$0 | \$0 | | \$0 | |
| Inspection & Testing | | \$4,388 | \$3,750 | \$141,462 | \$0 | | \$0 | \$0 | \$98,022 | \$15,575 | \$22,939 | \$10,960 | \$0 | | \$39,460 | \$336,555 |
| Project Management | | \$0 | \$0 | \$220 | \$0 | | | \$2,886 | \$55,064 | \$53,185 | \$47,778 | \$118,144 | \$97,856 | | \$431,268 | \$852,799 |
| Storm/Waste Water Treatment Center | | \$0 | \$2,500,000 | \$0 | \$0 | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | |
| Total | 005.000.000 | \$4,388 | \$2,531,472 | \$158,468 | \$6,159 | \$2,530,504 | \$0 | \$2,886 | \$228,301 | \$395,237 | \$836,407 | \$449,662 | \$232,985 | \$208,931 | \$2,838,036 | \$10,423,438 |
| Project Budget | \$25,000,000 | | | | | | | | | | | | | | | |
| Less Other Funding* | \$0 | | | | | | | | | | | | | | | |
| Net | \$25,000,000 | | | | | | | | | | | | | | | |
| Actual Measure S Expenditures | \$10,423,438 | | | | | | | | | | | | | | | |
| Running Balance | \$14,576,562 | | | | | | | | | | | | | | | |

| Projects | Budget | 04/05 Final | 05/06 Final | 06/07 Final | 07/08 Final | 08/09 Final | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|--------------------------------|-----------|-------------|-------------|----------------|-----------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-----------------|
| | | | | | | | | | | | | | | | | |
| S7100043, S7100066 | | | | | | | | | | | | | | | | |
| Energy Efficiency Projects (7) | | | | | | | | | | | | | | | | |
| Legal | | \$0 | \$0 | \$0 | \$0 | \$988 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$988 |
| Building & Additions | | \$0 | \$0 | \$0 | \$0 | \$106,921 | \$355,294 | -\$180,342 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$281,873 |
| Engineering | | \$0 | \$0 | \$0 | \$10,500 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$10,500 |
| Inspection & Testing | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| Project Management | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| Total | | \$0 | \$0 | \$0 | \$10,500 | \$107,910 | \$355,294 | -\$180,342 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$293,361 |
| Project Budget | \$510,683 | Received | | | | | | | | | | | | | | |
| Less Other Funding* | \$217,322 | \$217,322 | | * Other Fundin | g Source: | | | | | | | | | | | |
| Net | \$293,361 | | | SCE & The Ga | s Co. \$217,322 | 2 received | | | | | | | | | | |
| Actual Measure S Expenditures | \$293,361 | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | - |

| S7100091, S7100092, S7100147 | | | | | | | | | | | | | | | | |
|--|----------------|-----|-----|-----------------------------------|----------------|------------------|--------------|----------|---------|---------|----------|----------|----------|-----|-----|-------------|
| Satellite Campus Parking Facilities and Roadway Im | provements (8) | | | | | | | | | | | | | | | |
| Legal | | \$0 | \$0 | \$0 | \$300 | \$175 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$475 |
| Other Contract Services | | \$0 | \$0 | \$0 | \$300 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$300 |
| Advertising | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| Consultants | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| Supplies | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| Building & Additions | | \$0 | \$0 | \$0 | \$278,178 | \$1,860,152 | \$449,543 | \$37,777 | \$0 | \$0 | \$0 | \$64 | \$0 | \$0 | \$0 | \$2,625,714 |
| Architect | | \$0 | \$0 | \$324,919 | \$324,864 | \$136,911 | \$34,490 | \$1,397 | \$2,289 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$824,871 |
| Engineering | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$30,896 | \$5,470 | \$12,165 | \$0 | \$0 | \$48,531 |
| Inspection & Testing | | \$0 | \$0 | \$0 | \$31,100 | \$185,947 | \$28,218 | \$360 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$245,626 |
| Project Management | | \$0 | \$0 | \$0 | \$18,288 | \$64,880 | \$31,137 | \$8,659 | \$0 | \$2,569 | \$10,730 | \$6,046 | \$535 | | \$0 | \$142,844 |
| Non-Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$0 | \$3,387 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$3,387 |
| Total | | \$0 | \$0 | \$324,919 | \$653,031 | \$2,248,065 | \$546,775 | \$48,194 | \$2,289 | \$2,569 | \$41,626 | \$11,580 | \$12,700 | \$0 | \$0 | \$3,891,747 |
| Project Budget | \$7,022,417 | | | | | | - | | | | | | | | | |
| Less Other Funding | \$3,130,670 | | | Other Funding | | | | | | | | | | | | |
| Net | \$3,891,747 | | | Measure AA \$2 | 2,130,670, Mea | sure V \$1,000,0 | 00 allocated | | | | | | | | | |
| Actual Measure S Expenditures | \$3,891,747 | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | |

| Projects | Budget | 04/05 Final | 05/06 Final | 06/07 Final | 07/08 Final | 08/09 Final | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|---|---------------|-------------|-------------|------------------|-------------------|-----------------|---------------|----------------|-------------|-------------|-------------|-------------|-------------|--------------|--------------|-----------------|
| | | | | | | | | | | | | | | | | |
| S7100142 | | | | | | | | | | | | | | | | |
| Parking Garage and Grounds - Student Services (9) | | | | | | | | | | | | | | | | |
| Supplies | | \$0 | \$0 | \$0 | \$0 | \$1,745 | \$0 | \$0 | \$648 | \$0 | \$0 | \$813 | \$0 | | | \$3,206 |
| Consultants | | \$0 | \$0 | \$0 | \$0 | \$20,700 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$1,740 | | | \$22,440 |
| Legal | | \$0 | \$0 | \$0 | \$0 | \$2,154 | \$17,486 | \$4,800 | \$2,257 | \$17,221 | \$0 | \$3,570 | \$0 | | | \$47,488 |
| Other Contract Services | | \$0 | \$0 | \$0 | \$0 | \$1,508 | \$10,952 | \$1,986 | \$46 | \$0 | \$12,083 | \$5,034 | \$0 | \$0 | \$0 | \$31,608 |
| Site Improvement | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$1,086 | \$0 | \$1,308 | \$0 | \$0 | \$0 | \$2,394 |
| Building & Additions | | \$0 | \$0 | \$0 | \$0 | \$2,555,940 | \$5,925,152 | \$78,717 | \$77,320 | \$5,509 | \$715 | \$0 | \$3,721 | \$11,308,792 | \$16,249,515 | \$36,205,381 |
| Architect | | \$0 | \$0 | \$0 | \$2,266,766 | \$2,674,054 | \$0 | \$37,111 | \$75,163 | \$0 | \$0 | \$0 | \$0 | \$0 | \$287,176 | \$5,340,270 |
| Engineering | | \$0 | \$0 | \$0 | \$0 | \$4,813 | \$38,330 | \$42,968 | \$50,952 | \$9,735 | \$0 | \$0 | \$0 | \$0 | | \$195,968 |
| Inspection & Testing | | \$0 | \$0 | \$0 | \$0 | \$131,009 | \$161,847 | \$54,069 | \$32,306 | \$30,909 | | \$22,296 | \$38,186 | \$516,217 | \$851,397 | \$1,842,359 |
| Project Management | | \$0 | \$0 | \$0 | \$0 | \$158,766 | \$373,559 | \$184,088 | \$92,118 | \$224,994 | \$59,525 | \$29,714 | \$50,380 | \$285,057 | \$420,233 | \$1,878,433 |
| Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$0 | \$14,393 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$14,393 |
| Non-Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$11,381 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$11,381 |
| Total | | \$0 | \$0 | \$0 | \$2,266,766 | \$5,550,689 | \$6,541,719 | \$403,737 | \$342,192 | \$289,454 | \$76,445 | \$62,735 | \$94,027 | \$12,110,066 | \$17,857,492 | \$45,595,322 |
| Project Budget | \$130,224,164 | | | * Other Funding | g Source: | | | | | | | | | | | |
| Less Other Funding* | \$84,628,842 | | | State of Califor | nia \$1,321,000 | received | | | | | | | | | | |
| Net | \$45,595,322 | | | Mease U \$21,1 | 31,135, Measu | re AA \$6,870,4 | 90, Measure V | \$33,624,909 a | located | | | | | | | |
| Actual Measure S Expenditures | \$45,595,322 | | | Measure U, S & | & AA interests \$ | 21,681,308 all | ocated | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | |

Parking Garage and Grounds - Student Services

Project Description:
Consolidates various student services
departments and college administration in a
single complex at the front of the campus

Facility Size: 110,000 sq/ft & 500 cars underground parking structure


Status:

Phase 1 completed Phase 2 In construction

Steinberg Architects, Morris Architects

Contractor:

Minaco, Bernards



| Projects | Budget | 04/05 Final | 05/06 Final | 06/07 Final | 07/08 Final | 08/09 Final | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|--------------------------------------|-------------|-------------|-------------|-------------|-------------|-------------|--------------|----------------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-----------------------|
| S7100044 | | 1 | | | | | | | 1 | | - | | | | | |
| Pico Promenade Improvements (10) | | | | | | | | | | | | | | | | |
| Building & Additions | | \$0 | \$0 | \$0 | \$690 | \$883,401 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$884.091 |
| Architect | | \$0 | | | \$69,190 | \$28,540 | \$864 | \$0 | \$0 | | \$0 | \$0 | \$0 | | \$0 | \$98,595 |
| Inspection & Testing | | \$0 | | | \$09,190 | \$7,591 | \$0 | | \$0 | | \$0 | \$0 | \$0 | | \$0 | \$7.591 |
| Project Management | | \$0 | | | \$2,185 | \$25,548 | \$0 | | \$0 | | \$0 | \$0 | \$0 | | \$0 | \$27,733 |
| Total | | \$0 | | | \$72,066 | \$945,080 | \$864 | | \$0 | | \$0 | \$0 | \$0 | | \$0 | \$1,018,009 |
| Project Budget | \$1,018,009 | 1 | Ψυ | 40 | ψ12,000 | ψ343,000 | \$004 | 40 | ΨΟΙ | Ψ0 | ΨΟΙ | 401 | ΨΟ | 40 | 90 | ψ1,010,000 |
| Less Other Funding | \$1,010,000 | 1 | | | | | | | | | | | | | | |
| Net | \$1,018,009 | 2 | | | | | | | | | | | | | | |
| Actual Measure S Expenditures | \$1,018,009 | | | | | | | | | | | | | | | |
| Running Balance | \$1,010,000 | | | | | | | | | | | | | | | |
| Itulining balance | Ψ | 1 | | | | | | | | | | | | | | |
| S7100004 | | | | | | | | | | | | 1 | | | | |
| Master Planning (11) | | | | | | | | | | | | | | | | |
| Consultants | | \$0 | \$0 | \$0 | \$0 | \$0 | \$441,549 | \$13,320 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$454,869 |
| Printing | | \$0 | | | \$0 | \$0 | \$4.157 | \$13,320 | \$0 | | \$0 | \$0 | \$0 | | \$0 | \$4,157 |
| Advertising | | \$0 | | | \$0 | \$0 | \$3,000 | \$0 | \$0 | | \$0 | \$0 | \$0 | | \$0 | \$3,000 |
| Other Contract Services | | \$0 | | | \$0 | \$0 | \$442 | \$200 | \$0 | | \$0 | \$0 | \$0 | | \$0 | \$642 |
| Architect | | \$0 | | | \$0 | \$0 | \$192,358 | \$24,736 | \$0 | | \$0 | \$0 | \$0 | | \$0 | \$217.09 |
| Project Management | | \$0 | | | \$0 | \$0 | \$16,638 | \$9.341 | \$0 | | \$7,845 | \$0 | \$0 | | \$0 | \$33,824 |
| Filling Fees | | \$0 | | | \$0 | \$0 | \$10,030 | \$2.842 | \$0 | | \$0 | \$0 | \$0 | | \$0 | \$2.842 |
| Total | | \$0 | | | \$0 | | | | \$0 | | \$7.845 | \$0 | \$0 | | \$0 | \$716.428 |
| Project Budget | \$716.428 | | ΨΟ | 40 | ΨΟ | ΨΟ | ψ030, 143 | ψ30, 4 33 | 40 | ΨΟ | Ψ1,043 | 401 | ΨΟ | 40 | 90 | Ψ110, 4 20 |
| Less Other Funding | \$0 | | | | | | | | | | | | | | | |
| Net | \$716.428 | | | | | | | | | | | | | | | |
| Actual Measure S Expenditures | \$716,428 | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | |
| g = | | 1 | | | | | | | | | | | | | | |
| S7100048 | | | | | | | | | | | | | | | | |
| Other Bond Related Expenses (12) | | | | | | | | | | | | | | | | |
| Consultants | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$2,971 | \$2,524 | \$6,239 | \$1,354 | \$0 | \$0 | \$13,089 |
| Lease/Rental | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$11,142 | \$15,099 | \$15,285 | \$14,809 | \$13,418 | \$13,120 | \$16,611 | \$99,484 |
| Supplies | | \$0 | | | \$0 | \$0 | \$3.638 | \$0 | \$0 | | \$0 | \$0 | \$0 | \$0 | \$0 | \$3.638 |
| Legal | | \$0 | \$0 | \$0 | \$0 | \$0 | \$8,917 | \$15,649 | \$13,401 | \$450 | \$503 | \$38,130 | \$9.186 | \$0 | \$0 | \$86,236 |
| Software License | | \$0 | | | \$0 | \$0 | \$0 | \$1,997 | \$0 | \$3.565 | \$0 | \$4,200 | \$0 | \$0 | \$0 | \$9,762 |
| Advertising | | \$0 | | | \$0 | \$0 | \$2,278 | \$0 | \$0 | | \$0 | \$0 | \$0 | | \$0 | \$3,14 |
| Other Contract Services | | \$0 | | | \$0 | \$1.800 | \$17,206 | \$23,558 | \$19.208 | | \$13.627 | \$13,952 | \$12,963 | \$11.760 | \$18,900 | \$148,789 |
| Moving Services | | \$0 | | | \$0 | \$0 | \$400 | \$0 | \$0 | | \$0 | \$0 | \$0 | \$0 | \$0 | \$400 |
| Project Management | | \$0 | | \$0 | \$0 | \$0 | \$17,747 | \$13,179 | \$11,963 | | \$0 | \$0 | \$0 | \$0 | \$0 | \$42,888 |
| Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$10,086 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$10,086 |
| Non-Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$2,860 | \$0 | | \$0 | \$0 | \$0 | \$0 | \$0 | \$2,860 |
| Total | | \$0 | \$0 | \$0 | \$0 | \$1,800 | \$50,185 | | \$55,713 | | \$31,939 | \$77,330 | \$36,921 | \$25,744 | \$35,511 | \$420,373 |
| | \$609,282 | <u> </u> | | | | , , | | | , | | , | . , , | | | | , ,,,, |
| Project Budget | \$009,202 | | | | | | | | | | | | | | | |
| Project Budget Less Other Funding | \$0 | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | |
| Less Other Funding | \$0 | | | | | | | | | | | | | | | |

| Projects | Budget | 04/05 Final | 05/06 Final | 06/07 Final | 07/08 Final | 08/09 Final | 09/10 Final | 10/11 Final 11/ | 12 Final | 12/13 Final | 13/14 Final 14 | 4/15 Final | 15/16 Final | 16/17 Final | 17/18 Final C | Combined Totals |
|--|--|---|---|---|---|---|---|---|--|--|--|---|--|---|---|---|
| \$7100049 | | г г | | | | | | | | | | | | | г г | |
| Adv Architecture Related Exp for AA (13) | | | | | | | | | | | | | | | | |
| Legal | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| Other Contract Services | | \$0 | \$0 | | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 |
| Architect | | \$0 | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 |
| Engineering | | \$0 | \$0 | | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 |
| Inspection & Testing | | \$0 | \$0 | \$0 | \$0 | \$45,734 | -\$45,734 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| Project Management | | \$0 | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 |
| Total | | \$0 | \$0 | | | | -\$45,734 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 |
| Project Budget | \$0 | | ** | ** | ** | ¥ 10,101 | ¥, | 7- | 7.1 | ** | **1 | 7-1 | **! | ** | *** | |
| Less Other Funding | \$0 | | | | | | | | | | | | | | | |
| Net | \$0 | | | | | | | | | | | | | | | |
| Actual Measure S Expenditures | \$0 | 1 | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | |
| S7100057 | | | | | | | | | | | | | | | | |
| Real Property Acquisition (14) | | | | | | | | | | | | | | | | |
| Other Contract Services | | \$0 | \$0 | | | \$0 | \$18,721 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$18,721 |
| Architect | | \$0 | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 |
| Engineering | | \$0 | \$0 | | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 |
| Inspection & Testing | | \$0 | \$0 | | \$0 | \$0 | \$6,336 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$6,336 |
| Project Management | | \$0 | \$0 | | \$0 | \$0 | \$20,540 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$20,540 |
| Total | | \$0 | \$0 | \$0 | \$0 | \$0 | \$45,597 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$45,597 |
| Project Budget | \$45,597 | | | | | | | | | | | | | | | |
| Less Other Funding | \$0 | | | | | | | | | | | | | | | |
| Net | \$45,597 | | | | | | | | | | | | | | | |
| Actual Measure S Expenditures | \$45,597 | | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | | |
| S7100072 | 1 | | | | | | | | | 1 | | 1 | | | | |
| Campus Signage (15) | | | | | | | | | | | | | | | | |
| Supplies | | | | | \$0 | \$0 | \$0 | \$303 | \$0 | \$0 | \$0 | \$0 | 0.0 | | 1 | |
| | | | 0.2 | I ©∩ | | | | | ΨΟΙ | | | | | 90 | 102 | ¢303 |
| | | \$0 \$0 | \$0 \$0 | | \$0 | 90 | \$32.225 | | 0.2 | | | 0.0 | \$0 \$0 | \$0 \$0 | | \$303 \$55,950 |
| Consultants | | \$0 | \$0 | \$0 | \$0 | \$0 | \$32,225 | \$23,725 | \$0 \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$55,950 |
| Consultants Other Contract Services | | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$32,225 \$0 | \$23,725 \$187 | \$0 | \$0 \$836 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$0 \$1,051 | \$0 \$0 | \$55,950 \$2,074 |
| Consultants Other Contract Services Architect | | \$0 \$0 \$0 | \$0 \$0 \$0 | \$0 \$0 \$0 | \$0 \$0 \$0 | \$0 \$0 \$0 | \$32,225 \$0 \$0 | \$23,725 \$187 \$0 | \$0 \$0 | \$0 \$836 \$0 | \$0 \$0 \$0 | \$0 \$0 \$0 | \$0 \$0 \$0 | \$0 \$1,051 \$0 | \$0 \$0 \$0 | \$55,950 \$2,074 \$0 |
| Consultants Other Contract Services Architect Building & Additions | | \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 | \$23,725 \$187 \$0 \$638 | \$0 \$0 \$0 | \$0 \$836 \$0 \$0 | \$0 \$0 \$0 \$1,440 | \$0 \$0 \$0 \$1,325 | \$0 \$0 \$0 \$416,937 | \$0 \$1,051 \$0 \$0 | \$0 \$0 \$0 \$0 | \$55,950 \$2,074 \$0 \$420,339 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing | | \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 \$0 | \$23,725 \$187 \$0 \$638 \$0 | \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 | \$0 \$0 \$0 \$1,440 \$0 | \$0 \$0 \$0 \$1,325 \$0 | \$0 \$0 \$0 \$416,937 \$0 | \$0 \$1,051 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 | \$55,950 \$2,074 \$0 \$420,339 \$0 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management | | \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 | \$23,725 \$187 \$0 \$638 | \$0 \$0 \$0 | \$0 \$836 \$0 \$0 | \$0 \$0 \$0 \$1,440 | \$0 \$0 \$0 \$1,325 \$0 \$8,388 | \$0 \$0 \$0 \$416,937 | \$0 \$1,051 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing | | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 \$0 \$0 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 | \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$1,440 \$0 \$8,260 | \$0 \$0 \$0 \$1,325 \$0 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 | \$0 \$1,051 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$55,950 \$2,074 \$0 \$420,339 \$0 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management Cap Equipment | | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 \$0 \$0 \$0 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 \$156,258 | \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$1,440 \$0 \$8,260 \$0 | \$0 \$0 \$0 \$1,325 \$0 \$8,388 \$0 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 \$0 | \$0 \$1,051 \$0 \$0 \$0 \$165 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 \$156,258 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment | \$706,713 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 \$156,258 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$1,440 \$0 \$8,260 \$0 | \$0 \$0 \$0 \$1,325 \$0 \$8,388 \$0 \$0 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 \$0 \$0 | \$1,051 \$0 \$0 \$0 \$165 \$0 \$145 \$0 \$3,402 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total | \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 \$156,258 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$1,440 \$0 \$8,260 \$0 | \$0 \$0 \$0 \$1,325 \$0 \$8,388 \$0 \$0 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 \$0 \$0 | \$1,051 \$0 \$0 \$0 \$165 \$0 \$145 \$0 \$3,402 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget | | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 \$156,258 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$1,440 \$0 \$8,260 \$0 | \$0 \$0 \$0 \$1,325 \$0 \$8,388 \$0 \$0 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 \$0 \$0 | \$1,051 \$0 \$0 \$0 \$0 \$165 \$0 \$3,402 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures | \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 \$156,258 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$1,440 \$0 \$8,260 \$0 | \$0 \$0 \$0 \$1,325 \$0 \$8,388 \$0 \$0 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 \$0 \$0 | \$1,051 \$0 \$0 \$0 \$0 \$165 \$0 \$3,402 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net | \$0 \$706,713 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 \$156,258 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$1,440 \$0 \$8,260 \$0 | \$0 \$0 \$0 \$1,325 \$0 \$8,388 \$0 \$0 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 \$0 \$0 | \$1,051 \$0 \$0 \$0 \$0 \$165 \$0 \$3,402 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures | \$0 \$706,713 \$706,713 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 \$156,258 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$1,440 \$0 \$8,260 \$0 | \$0 \$0 \$0 \$1,325 \$0 \$8,388 \$0 \$0 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 \$0 \$0 | \$1,051 \$0 \$0 \$0 \$0 \$165 \$0 \$3,402 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance | \$0 \$706,713 \$706,713 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 \$156,258 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$1,440 \$0 \$8,260 \$0 | \$0 \$0 \$0 \$1,325 \$0 \$8,388 \$0 \$0 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 \$0 \$0 | \$1,051 \$0 \$0 \$0 \$0 \$165 \$0 \$3,402 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance S Cost of Issuance (16) | \$0 \$706,713 \$706,713 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$00 \$00 \$00 \$00 \$00 \$00 \$32,225 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 \$156,258 \$0 \$204,064 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 \$0 \$0 \$836 | \$0 \$0 \$0 \$1,440 \$0 \$8,260 \$0 \$9,700 | \$0 \$0 \$0 \$1,325 \$0 \$8,388 \$0 \$0 \$9,712 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 \$0 \$0 \$445,559 | \$0 \$1,051 \$0 \$0 \$0 \$165 \$0 \$3,402 \$4,618 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402 \$706,713 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance S Cost of Issuance (16) Cost of Issuance | \$0 \$706,713 \$706,713 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$2 \$2 \$32,225 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 \$156,258 \$0 \$204,064 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$30 \$30 \$30 \$30 \$3 | \$0 \$0 \$1,440 \$0 \$8,260 \$0 \$0 \$9,700 | \$0 \$0 \$1,325 \$0 \$8,388 \$0 \$0 \$9,712 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 \$0 \$0 \$445,559 | \$0 \$1,051 \$0 \$0 \$0 \$165 \$3,402 \$4,618 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402 \$706,713 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance S Cost of Issuance (16) Cost of Issuance Total | \$0 \$706,713 \$706,713 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$00 \$00 \$00 \$00 \$00 \$00 \$32,225 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 \$156,258 \$0 \$204,064 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 \$0 \$0 \$836 | \$0 \$0 \$0 \$1,440 \$0 \$8,260 \$0 \$9,700 | \$0 \$0 \$0 \$1,325 \$0 \$8,388 \$0 \$0 \$9,712 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 \$0 \$0 \$445,559 | \$0 \$1,051 \$0 \$0 \$0 \$165 \$0 \$3,402 \$4,618 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402 \$706,713 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance S Cost of Issuance (16) Cost of Issuance Total | \$706,713 \$706,713 \$706,713 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$2 \$2 \$32,225 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 \$156,258 \$0 \$204,064 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$30 \$30 \$30 \$30 \$3 | \$0 \$0 \$1,440 \$0 \$8,260 \$0 \$0 \$9,700 | \$0 \$0 \$1,325 \$0 \$8,388 \$0 \$0 \$9,712 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 \$0 \$0 \$445,559 | \$0 \$1,051 \$0 \$0 \$0 \$165 \$3,402 \$4,618 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402 \$706,713 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance S Cost of Issuance (16) Cost of Issuance Total Project Budget Less Other Funding | \$119,470 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$2 \$2 \$32,225 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 \$156,258 \$0 \$204,064 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$30 \$30 \$30 \$30 \$3 | \$0 \$0 \$1,440 \$0 \$8,260 \$0 \$0 \$9,700 | \$0 \$0 \$1,325 \$0 \$8,388 \$0 \$0 \$9,712 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 \$0 \$0 \$445,559 | \$0 \$1,051 \$0 \$0 \$0 \$165 \$3,402 \$4,618 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402 \$706,713 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance S Cost of Issuance (16) Cost of Issuance Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance | \$119,470 \$119,470 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$2 \$2 \$32,225 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 \$156,258 \$0 \$204,064 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$30 \$30 \$30 \$30 \$3 | \$0 \$0 \$1,440 \$0 \$8,260 \$0 \$0 \$9,700 | \$0 \$0 \$1,325 \$0 \$8,388 \$0 \$0 \$9,712 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 \$0 \$0 \$445,559 | \$0 \$1,051 \$0 \$0 \$0 \$165 \$3,402 \$4,618 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402 \$706,713 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance S Cost of Issuance (16) Cost of Issuance Total Project Budget Less Other Funding Net Actual Measure S Expenditures Cost of Issuance Total Project Budget Less Other Funding Net Actual Measure AA Expenditures | \$119,470 \$119,470 \$119,470 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$2 \$2 \$32,225 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 \$156,258 \$0 \$204,064 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$30 \$30 \$30 \$30 \$3 | \$0 \$0 \$1,440 \$0 \$8,260 \$0 \$0 \$9,700 | \$0 \$0 \$1,325 \$0 \$8,388 \$0 \$0 \$9,712 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 \$0 \$0 \$445,559 | \$0 \$1,051 \$0 \$0 \$0 \$165 \$3,402 \$4,618 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402 \$706,713 |
| Consultants Other Contract Services Architect Building & Additions Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance \$ Cost of Issuance (16) Cost of Issuance Total Project Budget Less Other Funding Net Actual Measure S Expenditures Running Balance | \$119,470 \$119,470 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$32,225 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$2 \$2 \$32,225 | \$23,725 \$187 \$0 \$638 \$0 \$22,953 \$156,258 \$0 \$204,064 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | \$0 \$836 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$30 \$30 \$30 \$30 \$3 | \$0 \$0 \$1,440 \$0 \$8,260 \$0 \$0 \$9,700 | \$0 \$0 \$1,325 \$0 \$8,388 \$0 \$0 \$9,712 | \$0 \$0 \$0 \$416,937 \$0 \$28,622 \$0 \$0 \$445,559 | \$0 \$1,051 \$0 \$0 \$0 \$165 \$3,402 \$4,618 | \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | \$55,950 \$2,074 \$0 \$420,339 \$0 \$68,388 \$156,258 \$3,402 \$706,713 |

Grand Total

\$7,958,606 \$14,601,366 \$10,740,621 \$8,321,918 \$20,819,624 \$8,933,245 \$617,492 \$651,441 \$878,632 \$1,287,285 \$6,814,769 \$6,083,251 \$12,554,384 \$21,858,285

\$122,120,920

| Projects | Budget | 04/05 Final | 05/06 Final | 06/07 Final | 07/08 Final | 08/09 Final | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Total |
|---|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|----------------|
| | | | | | | | | | | | | | | | | |
| Measure S Interest | | 17-18 | | | | | | | | | | | | | | |
| Parking Garage and Grounds - Student Services (9) | | | | | | | | | | | | | | | | |
| Site Imptovement | | \$568 | | | | | | | | | | | | | | |
| Building & Additions | | \$8,224,377 | | | | | | | | | | | | | | |
| Architect | | \$189,078 | | | | | | | | | | | | | | |
| Engineering | | \$11,000 | | | | | | | | | | | | | | |
| Inspection & Testing | | \$125,080 | | | | | | | | | | | | | | |
| Project Management | | \$171,448 | | | | | | | | | | | | | | |
| Total | | \$8,721,552 | | | | | | | | | | | | | | |
| Project Budget | \$9,433,526 | | | | | | | | | | | | | | | |
| Actual Measure S Interest Expenditures | \$8,721,552 | | | | | | | | | | | | | | | |
| Running Balance | \$711,974 | | | | | | | | | | | | | | | |

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure AA Project Schedule As of June 30, 2018

| | Project Name | Completion | : | 2017 | , | | 201 | 18 | 2 | 019 | | 2 | 020 | 2 | 2021 | 2 | 022 |
|-----|---|----------------|---|------|----|-----|------|----|----|-------|-------|-------|-----|---|------|---|-----|
| 101 | Environmental Performance - Central Plant Connections | Completed | | | | | | | | | | | | | | | |
| 102 | Infrastructure & Technology - Information Technology Relocation | Completed | | | | | | | | | | | | | | | |
| 103 | Media and Technology Complex - Academy Site | Completed | | | | | | | | | | | | | | | |
| 104 | Replacement Health/PE/Fitness/Dance Building with Central Plant | Completed | | | | | | | | | | | | | | | |
| 105 | Drescher - Academic Modernization, Bookstore, Pico Promenade | Deferred | | | | | | | | | | | | | | | |
| 106 | Replacement Math and Science Extension Building | September 2022 | | | | | | | | | | | | | | | |
| 107 | Madison East Wing Seismic Upgrade | Completed | | | | | | | | | | | | | | | |
| 108 | Renovation of Corsair Stadium | Completed | | | | | | | | | | | | | | | |
| 109 | Career Opportunity and Advancement Center (Bundy) | Completed | | | | | | | | | | | | | | | |
| 110 | Malibu Center | December 2021 | | | | | | | | | | | | | | | |
| 111 | Business & Facilities Infrastructure | Completed | | | | | | | | | | | | | | | |
| 112 | Master Planning, Program Management, Overhead | On-Going | | | | | | | | | | | | | | | |
| 113 | Energy Efficiency Projects | Completed | | | | | | | | | | | | | | | |
| 114 | Community Classroom & Facility Projects | Completed | | | | | | | | | | | | | | | |
| 115 | Real Property Acquisition | Completed | | | | | | | | | | | | | | | |
| 116 | Roadways, Walkways, Grounds, Parking Lots, and Garages | Completed | | | | | | | | | | | | | | | |
| 117 | Infrastructure & Technology - Technology | Completed | | | | | | | | | | | | | | | |
| 118 | Infrastructure & Technology - Utility | Completed | | | | | | | | | | | | | | | |
| 119 | Emergency Lighting, Fire Alarm, and Security System | On-Going | | | | | | | | | | | | | | | |
| 120 | Student Services | March 2019 | | | | | | | | | | | | | | | |
| 121 | Cost of Issuance | Completed | | | | | | | | | | | | | | | |
| 122 | Management Reserve | On-Going | | | | | | | | | | | | | | | |
| 123 | Unissuable Bond | Completed | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | |
| | | 57 | | | ın | ria | nnir | ıg | Ir | 1 Con | ıstrı | ICTIO | n | | | | |

| Projects | Budget | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|---|--------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-----------------|
| • | | | • | • | | · | | · | | | |
| AA 7100062 | | | | | | | | | | | |
| Environmental Performance - Central Plant Connections (101) | | | | | | | | | | | |
| Legal | | \$0 | \$0 | \$0 | \$125 | \$0 | \$0 | \$0 | \$0 | \$0 | \$125 |
| Other Contract Services | | \$0 | \$0 | \$49,837 | \$16,239 | \$0 | \$0 | \$0 | \$0 | \$9,920 | |
| Consultants | | \$0 | \$0 | \$0 | \$0 | \$28 | \$0 | \$0 | \$0 | \$0 | \$28 |
| Building & Additions | | \$0 | \$0 | \$0 | \$361 | \$729 | \$640 | \$1,328,592 | \$6,934,044 | \$446,861 | \$8,711,229 |
| Architect | | \$0 | \$385 | \$148,311 | \$176,897 | \$36,256 | \$0 | \$0 | \$0 | \$0 | \$361,849 |
| Engineering | | \$48,500 | \$0 | \$4,000 | \$0 | \$152,010 | \$39,638 | \$66,918 | \$138,887 | \$62,883 | \$512,836 |
| Inspection & Testing | | \$0 | \$0 | \$7,688 | \$0 | \$0 | \$0 | \$7,310 | \$137,150 | \$4,382 | |
| Project Management | | \$0 | \$17,263 | \$55,116 | \$48,685 | \$61,908 | \$19,313 | \$104,575 | \$526,072 | \$99,840 | \$932,771 |
| Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| Non-Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| Total | | \$48,500 | \$17,648 | \$264,951 | \$242,307 | \$250,931 | \$59,591 | \$1,507,396 | \$7,736,152 | \$623,886 | \$10,751,362 |
| Project Budget | \$11,206,164 | | | | | | | - | | | |
| Less Other Funding | \$0 | | | | | | | | | | |
| Net | \$11,206,164 | | | | | | | | | | |
| Actual Measure AA Expenditures | \$10,751,362 | | | | | | | | | | |
| Running Balance | \$454,802 | | | | | | | | | | |

| Projects | Budget | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|---|--------------|-------------|----------------------|-------------|-------------|--------------|-------------|-------------|-------------|-------------|-----------------|
| | | | | | | | | | | | |
| AA 7100063 | | | | | | | | | | | |
| Infrastructure & Technology - IT Relocation (102) | | | | | | | | | | | |
| Supplies | | \$0 | \$0 | \$965 | \$8,442 | \$3,137 | \$2,600 | \$0 | \$0 | \$0 | \$15,144 |
| Consultants | | \$0 | \$0 | \$0 | \$0 | \$408 | \$0 | \$7,800 | \$0 | \$0 | \$8,208 |
| Maintenance Contract | | \$0 | \$0 | \$0 | \$0 | \$107,390 | \$0 | \$77,074 | \$79 | \$0 | \$184,543 |
| Legal | | \$0 | \$0 | \$0 | \$1,363 | \$50 | \$0 | \$0 | \$0 | \$0 | \$1,413 |
| Printing | | \$0 | \$0 | \$0 | \$0 | \$1,624 | \$0 | \$0 | \$0 | \$0 | \$1,624 |
| Postage | | \$0 | \$0 | \$0 | \$0 | \$1,567 | \$0 | \$0 | \$0 | \$0 | \$1,567 |
| Other Contract Services | | \$0 | \$0 | \$2,163 | \$15,259 | \$23,356 | \$0 | \$19,050 | \$4,500 | \$0 | \$64,328 |
| Moving | | \$0 | \$0 | \$0 | \$577 | \$266 | \$27,655 | \$22,618 | \$0 | \$0 | \$51,116 |
| Site Improvement | | \$0 | \$0 | \$0 | \$24 | \$0 | \$0 | \$0 | \$0 | \$0 | \$24 |
| Building & Additions | | \$0 | \$0 | \$0 | \$1,767,083 | \$9,667,362 | \$4,288,987 | \$1,203,916 | \$165,229 | -\$19,798 | \$17,072,780 |
| Architect | | \$105,049 | \$482,261 | \$505,580 | \$183,181 | \$287,201 | \$236,860 | \$120,091 | \$0 | \$0 | \$1,920,223 |
| Engineering | | \$0 | \$0 | \$10,037 | \$11,065 | \$17,147 | \$19,512 | \$25,994 | \$1,956 | \$0 | \$85,712 |
| Inspection & Testing | | \$10,291 | \$8,793 | \$21,449 | \$137,523 | \$499,982 | \$200,262 | \$568 | \$0 | \$0 | \$878,868 |
| Project Management | | \$33,460 | \$76,290 | \$84,991 | \$331,754 | \$431,730 | \$297,951 | \$22,978 | \$1,500 | \$0 | \$1,280,653 |
| Cap Equipment | | \$0 | \$0 | \$0 | \$29,422 | \$645,830 | -\$29,090 | \$589,604 | \$9,811 | \$0 | \$1,245,576 |
| Non-Cap Equipment | | \$0 | \$0 | \$0 | \$18,344 | \$10,852 | \$277,219 | \$1,891 | \$20,689 | \$0 | \$328,994 |
| Total | | \$148,800 | \$567,344 | \$625,185 | \$2,504,035 | \$11,697,901 | \$5,321,956 | \$2,091,584 | \$203,764 | -\$19,798 | \$23,140,771 |
| Project Budget | \$23,160,569 | Received | • | | - | - | • | | | _ | |
| Less Other Funding | \$19,798 | \$19,798 | * Other Funding Sou | rce: | | | | | | | |
| Net | \$23,140,771 | | Edison \$19,798 rece | ived | | | | | | | |
| Actual Measure AA Expenditures | \$23,140,771 | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | |

Infrastructure & Technology -IT Relocation

Project Description:
Relocation of IT/Telecom Departments, and renovation of Media Center


Facility Size: 9,230 sq/ft

Status: Completed

Architect: Morris Architects

Contractor:

Minco, Bernards Brothers

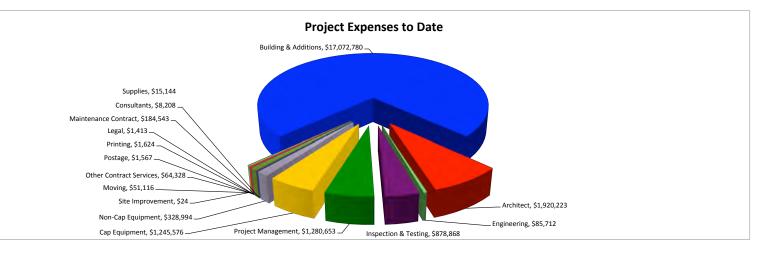

| Projects | Budget | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals | | | | |
|---|---------------|---|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-----------------|--|--|--|--|
| | | | | | | | | | | | | | | | |
| AA 7100061 | | | | | | | | | | | | | | | |
| Media and Technology Complex - Academy Site (103) | | | | | | | | | | | | | | | |
| Consultants | | \$0 | \$0 | \$20,675 | \$12,576 | \$9,488 | \$7,789 | \$2,102 | \$0 | \$12,922 | \$65,551 | | | | |
| Supplies | | \$0 | \$0 | \$0 | \$19,481 | \$1,048 | \$289 | \$0 | \$9,251 | \$40,519 | \$70,588 | | | | |
| Maintenance Contract | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$15,922 | \$23,561 | \$39,483 | | | | |
| Legal | | \$16,903 | \$0 | \$7,958 | \$43,363 | \$5,066 | \$26,186 | \$49,155 | \$15,435 | \$36,221 | \$200,285 | | | | |
| Software Support | | \$0 | \$0 | \$0 | \$1,982 | \$0 | \$0 | \$0 | \$6,548 | \$6,975 | \$15,505 | | | | |
| Service Fee | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$17,000 | \$0 | \$17,000 | | | | |
| Other Contract Services | | \$3,993 \$5,763 \$13,466 \$39,188 \$0 \$0 \$5,853 \$22,622 \$18,628 \$105 | | | | | | | | | | | | | |
| Moving Expenses | | \$0 \$0 \$0 \$38,756 \$0 \$0 \$0 \$0 \$97,543 \$136,7 | | | | | | | | | | | | | |
| Site Improvement | | \$0 \$0 \$0 \$100,505 \$664 \$606 \$476 \$622 \$526 \$103,3 | | | | | | | | | | | | | |
| Building & Additions | | \$0 \$538 \$1,498,660 \$3,543,657 \$11,820,615 \$17,734,534 \$23,465,347 \$16,267,550 \$25,548,089 \$99,878 | | | | | | | | | | | | | |
| Architect | | \$2,097,553 | \$2,508,588 | \$295,753 | \$265,481 | \$778,015 | \$517,794 | \$1,048,935 | \$991,386 | \$869,801 | \$9,373,305 | | | | |
| Engineering | | \$16,459 | \$29,293 | \$9,102 | \$29,223 | \$8,203 | \$72,993 | \$118,368 | \$72,786 | \$51,971 | \$408,398 | | | | |
| Inspection & Testing | | \$64,905 | \$27,527 | \$123,842 | \$235,287 | \$563,746 | \$1,381,801 | \$641,972 | \$525,264 | \$207,240 | \$3,771,584 | | | | |
| Project Management | | \$121,786 | \$233,826 | \$269,249 | \$506,917 | \$800,315 | \$930,115 | \$1,207,850 | \$1,121,670 | \$859,779 | \$6,051,506 | | | | |
| Cap Equipment | | \$0 | \$0 | \$0 | \$186,301 | \$0 | \$0 | \$0 | \$0 | \$1,458,273 | \$1,644,574 | | | | |
| Non-Cap Equipment | | \$0 | \$0 | \$0 | \$10,782 | \$0 | \$0 | \$0 | \$326,845 | \$490,727 | \$828,354 | | | | |
| Total | | \$2,321,599 \$2,805,534 \$2,238,694 \$5,033,499 \$13,987,159 \$20,672,105 \$26,540,059 \$19,392,902 \$29,722,772 \$122,714,32 | | | | | | | | | | | | | |
| Project Budget | \$130,549,713 | 9,713 Received | | | | | | | | | | | | | |
| Less Other Funding* | \$6,835,391 | | | | | | | | | | | | | | |
| Net | \$123,714,322 | | | | | | | | | | | | | | |
| Actual Measure AA Expenditures | \$122,714,322 | 14.322 Edison \$31,979.48 received | | | | | | | | | | | | | |
| Running Balance | \$1,000,000 | | | | | | | | | | | | | | |

Media and Technology Complex - Academy Site

Project Description:

Renovation and new extension to the existing building, new building for KCRW, and a new parking structure

Facility Size:

Building - 116,000 sq/ft Parking Structure - 450 spaces

Status:


In construction

Architect:

Clive Wilkinson Architects

Contractor:

H.B. Parkco Construction Fast Track Construction CW Driver



| Projects | Budget | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals | | | | |
|---|--------------|---|-------------------|-----------------|-------------|-------------|-------------|--------------|--------------|-------------|-----------------|--|--|--|--|
| | | | | | | | | | | | | | | | |
| AA 7100060 | | | | | | | | | | | | | | | |
| Repl. Health/PE/Fitness/Dance Building with Central Plant (104) | | | | | | | | | | | | | | | |
| Consultants | | \$0 | \$0 | \$0 | \$14 | \$62 | \$2,304 | \$184 | \$0 | \$0 | \$2,564 | | | | |
| Supplies | | \$0 | \$0 | \$0 | \$0 | \$7,089 | \$195 | \$484 | \$20,947 | \$0 | \$28,715 | | | | |
| Legal | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$663 | \$80 | \$0 | \$742 | | | | |
| Software Support | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$1,209 | \$0 | \$1,209 | | | | |
| Site Improvement | | \$0 | \$0 | \$0 | \$0 | \$0 | \$559 | \$440 | \$575 | \$0 | \$1,574 | | | | |
| Off Campus Printing | | \$0 | \$0 | \$0 | \$0 | \$0 | \$2,165 | \$0 | \$0 | \$0 | \$2,165 | | | | |
| Postage | | \$0 \$0 \$0 \$0 \$0 \$1.505 \$0 \$0 \$1.505 \$0 \$0 \$1.505 | | | | | | | | | | | | | |
| Other Contract Services | | \$120 \$38 \$112 \$32,634 \$0 \$1,019 \$581 \$0 \$2,644 \$37,1· | | | | | | | | | | | | | |
| Building & Additions | | \$0 \$0 \$0 \$817 \$4,188 \$1,623 \$13,783,023 \$14,880,829 \$5,315,393 \$33,985,4 | | | | | | | | | | | | | |
| Architect | | \$256,076 \$1,568,564 \$1,790,207 \$518,973 \$177,583 \$364,853 \$585,900 \$373,345 \$210,312 \$5,845,8 | | | | | | | | | | | | | |
| Engineering | | \$0 | \$8,507 | \$31,650 | \$7,871 | \$6,529 | \$9,276 | \$76,712 | \$51,025 | \$11,318 | \$202,888 | | | | |
| Inspection & Testing | | \$36,892 | \$490 | \$21,150 | \$1,285 | \$360 | \$133,756 | \$846,765 | \$358,724 | \$60,826 | \$1,460,249 | | | | |
| Project Management | | \$34,968 | \$113,379 | \$118,783 | \$94,768 | \$108,528 | \$463,418 | \$564,240 | \$487,065 | \$312,539 | \$2,297,686 | | | | |
| Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$164,793 | \$68,425 | \$233,218 | | | | |
| Non-Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$0 | \$9,015 | \$0 | \$206,229 | \$127,078 | \$342,322 | | | | |
| Total | | \$328,056 | \$1,690,978 | \$1,961,901 | \$656,362 | \$304,338 | \$989,689 | \$15,858,991 | \$16,544,820 | \$6,108,535 | \$44,443,670 | | | | |
| Project Budget | \$58,272,030 | | | | | | | | | | | | | | |
| Less Other Funding* | \$11,812,230 | | | | | | | | | | | | | | |
| Net | \$46,459,800 | | Measure S \$11,60 | 3,383 allocated | | | | | | | | | | | |
| Actual Measure AA Expenditures | \$44,443,670 | | | | | | | | | | | | | | |
| Running Balance | \$2,016,130 | | | | | | | | | | | | | | |



Project Description: Replacement of locker rooms, fitness center, dance studios, and new central

Facility Size:


62,000 sq/ft

Status: In construction

Architect:

Gensler Architects


Contractor: Bernards Brothers



| Projects | Budget | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals | | | | |
|--|---------------|---|-------------------|-----------------|-------------|-------------|-------------|-------------|-------------|-------------|-----------------|--|--|--|--|
| | | | | | | | | | | | | | | | |
| AA 7100065 | | | | | | | | | | | | | | | |
| Drescher - Academic Modernization, Bookstore, Pico Promenade (105) | | | | | | | | | | | | | | | |
| Legal | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | |
| Other Contract Services | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | |
| Site Acquisition | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | |
| Inspection & Testing | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | |
| Project Management | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$5,082 | | | | |
| Total | | \$0 | \$0 | \$5,082 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$5,082 | | | | |
| Project Budget | \$13,005,082 | | | | | | | | | | | | | | |
| Less Other Funding | \$13,000,000 | | * Other Funding S | | | | | | | | | | | | |
| Net | \$5,082 | | Measure V 13,00 | 0,000 allocated | | | | | | | | | | | |
| Actual Measure AA Expenditures | \$5,082 | | | | | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | |
| AA 7100090 | | | | | | | | | | | | | | | |
| Replacement Math and Science Extension Building (106) | | | | | | | | | | | | | | | |
| Legal | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | |
| Other Contract Services | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$1,525 | \$1,525 | | | | |
| Site Acquisition | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | |
| Building & Additions | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$4,796 | \$4,796 | | | | |
| Architect | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$1,787,824 | \$1,787,824 | | | | |
| Engineering | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | | |
| Inspection & Testing | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$0 | \$70,223 | \$70,223 | | | | |
| Project Management | | \$0 | | | \$0 | \$4,950 | \$0 | \$0 | \$800 | \$228,760 | \$234,510 | | | | |
| Total | | \$0 \$0 \$0 \$0 \$0 \$4,950 \$0 \$0 \$800 \$2,093,128 \$2,098,878 | | | | | | | | | | | | | |
| Project Budget | \$124,958,336 | 58,336 | | | | | | | | | | | | | |
| Less Other Funding | \$122,714,328 | | | | | | | | | | | | | | |
| Net | \$2,244,008 | | | | | | | | | | | | | | |
| Actual Measure AA Expenditures | \$2,098,878 | 098,878 State of California \$40,088,000 allocated | | | | | | | | | | | | | |
| Running Balance | \$145,130 | | | | | | | | | | | | | | |

| Projects | Budget | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|---|--------------|-------------|-------------|-------------|-------------|-------------|-------------|--------------|-------------|-------------|-----------------|
| · · · · · · · · · · · · · · · · · · · | | | | | | | | | | | |
| AA 7100047 | | | | | | | | | | | |
| Madison East Wing Seismic Upgrade (107) | | | | | | | | | | | |
| Supplies | | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | \$6,197 | \$0 | \$6,197 |
| Consultants | | \$0 | \$0 | \$0 | \$0 | \$135 | | \$0 | \$0 | \$0 | \$163 |
| Off Campus Printing | | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | \$0 | \$0 | \$285 |
| Maintenance Contract | | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | \$357 | \$0 | \$357 |
| Legal | | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | \$7,579 | \$11,822 | \$19,400 |
| Software Support | | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | \$806 | \$0 | \$806 |
| Other Contract Services | | \$0 | \$364 | \$997 | \$0 | \$0 | | \$711 | \$0 | \$0 | \$3,400 |
| Building & Additions | | \$0 | \$656 | \$312,643 | \$0 | \$4,248 | | \$8,829,626 | \$4,949,223 | \$3,967,591 | \$24,094,358 |
| Architect | | \$76,073 | \$398,050 | \$550,589 | \$65,444 | \$57,480 | | \$404,764 | \$122,764 | \$103,824 | \$1,978,088 |
| Engineering | | \$0 | \$0 | \$10,707 | \$778 | \$0 | | \$33,184 | \$37,491 | \$90 | \$96,042 |
| Inspection & Testing | | \$0 | \$19,848 | \$16,752 | \$3,036 | \$5,851 | | \$405,443 | \$112,876 | \$4,703 | \$1,244,832 |
| Project Management | | \$5,557 | \$128,878 | \$112,573 | \$67,447 | \$118,242 | | \$481,165 | \$322,379 | \$31,230 | \$1,762,343 |
| Cap Equipment | | \$0 | \$0 | \$30,603 | \$0 | \$0 | \$0 | \$0 | \$537,627 | \$0 | \$568,230 |
| Non-Cap Equipment | | \$0 | \$0 | \$71,827 | \$9,788 | \$0 | 7.7 | \$0 | \$285,236 | \$0 | \$366,851 |
| Total | | \$81,630 | \$547,796 | \$1,106,691 | \$146,492 | \$185,956 | \$7,416,101 | \$10,154,894 | \$6,382,534 | \$4,119,259 | \$30,141,353 |
| Project Budget | \$30,143,816 | | | | | | | | | | |
| Less Other Funding | \$0 | | | | | | | | | | |
| Net | \$30,143,816 | | | | | | | | | | |
| Actual Measure AA Expenditures | \$30,141,353 | | | | | | | | | | |
| Running Balance | \$2,463 | | | | | | | | | | |





| An incident of Cornair Stadium (108) 50 50 50 50 50 50 50 5 | Projects | Budget | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|---|-------------------------|-------------|---------------|---------------|---------------|---------------|---------------|----------------|---------------|---------------|---------------|-----------------------|
| Renovacion to Corrast Statulum (168) So So So So So So So S | 1 Tojects | Duaget | 03/10 1 11141 | 10/11 I IIIai | 11/12 I IIIQI | 12/13 1 11101 | 13/14 11101 | 1-7/13 1 11101 | 13/10 1 11141 | 10/17 1 11101 | 17/10 1 11101 | Combined Totals |
| Renovation to Cornair Statutum (168) | A A 7100068 | | | | | | | | | | | |
| Come Contract Services So So So So So So So S | | | | | | | | | | | | |
| Sulforn So So So So So So So S | | | 60 | ¢ 0 | 60 | * 0 | 60 | 60 | 6 0 | 60 | 60 | \$0 |
| Architect So \$30,789 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | | | | | | | | | | | | |
| Engineering | | | | | | | | | | | | |
| Inspection & Testing | | | | | | | | | | | | |
| Project Management | | | | | | | | | | | | |
| Total | | | | | | | | | | | | |
| Project Budget | | | | | | | | | | | | |
| Less Other Funding | | *** | \$0 | \$35,299 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$35,299 |
| Net | | | | | | | | | | | | |
| Actual Measure AA Expenditures | | | | | | | | | | | | |
| A 7100067, 7100152, 7100155, 7100157 | | | | | | | | | | | | |
| A 7100067, 7100152, 7100155, 7100157 Businosa & Facilities Infrastructure (111) Supplies \$0 \$0 \$0 \$0 \$1,403 \$4,840 \$50 \$0 \$0 \$0 \$0 \$50 \$50 \$50 \$50 \$50 \$5 | | | | | | | | | | | | |
| Business & Facilities Infrastructure (111) Supplies S0 S0 S1 S4840 S0 S0 S0 S0 S0 S0 S0 | Running Balance | \$0 | | | | | | | | | | |
| Business & Facilities Infrastructure (111) Supplies S0 | | | | | | | | | | | | |
| Supplies S0 S0 S1 493 54,840 S0 S0 S0 S0 S0 S0 S0 | | | | | | | | | | | | |
| Service Fee | | | | | | | | | | | | |
| Consultants | | | | | | | | | | | | |
| Maintenance Contract S0 S0 S0 S0 S1,366 S0 S0 S0 S0 S0 S0 S0 | Service Fee | | | | | | | | | | | |
| Legal Sol So | Consultants | | | | \$0 | | | \$8 | \$0 | | | |
| Software License | Maintenance Contract | | | | \$0 | | | \$0 | \$0 | \$0 | \$0 | \$1,366 |
| Other Contract Services \$0 \$5,289 \$6,988 \$750 \$0 \$2,209 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | Legal | | | | \$75 | | | | \$1,105 | | \$0 | |
| Moving Services \$0 | Software License | | \$0 | \$0 | \$0 | \$0 | \$375 | \$0 | \$0 | \$0 | \$0 | \$375 |
| Building & Additions \$0 \$34,672 \$198,667 \$200,586 \$284,668 \$0 \$0 \$0 \$0 \$0 \$0 \$7 Architect \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$ | Other Contract Services | | \$0 | \$6,289 | \$6,988 | | \$0 | \$2,209 | \$0 | | \$0 | \$16,236 |
| Architect 90 \$0 \$0 \$0 \$80,626 \$170,132 \$37,906 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | Moving Services | | \$0 | | | | | | \$0 | \$0 | \$0 | |
| Engineering | Building & Additions | | \$0 | \$34,672 | \$198,667 | \$200,585 | \$284,668 | \$0 | \$0 | \$0 | \$0 | \$718,592 |
| Inspection & Testing | Architect | | \$0 | \$0 | \$80,626 | \$170,132 | \$37,906 | \$0 | \$0 | \$0 | \$0 | \$288,664 |
| Inspection & Testing | Engineering | | \$0 | \$0 | \$0 | \$3,705 | \$9,735 | \$6,840 | \$0 | \$0 | \$0 | \$20,280 |
| Project Management \$0 \$3,073 \$154,904 \$87,291 \$139,821 \$3,571 \$0 \$0 \$0 \$3 \$3 \$3 \$3 \$4 \$3 \$3 \$3 | | | \$0 | \$0 | \$8,142 | \$10,938 | \$10,500 | \$0 | \$0 | | | \$29,580 |
| Cap Equipment S0 S0 S0 S35,892 S80,090 S0 S0 S0 S0 S1 Non-Cap Equipment S0 S89,204 S0 S44,590 S193,782 S0 S0 S0 S0 S0 Total S1,968,124 Less Other Funding S1,968,124 Actual Measure AA Expenditures S1,968,124 Running Balance S0 S0 S0 S0 S0 S0 S0 AA7100004 Master Planning, Program Management, Overhead (112) Supplies S0 S0 S0 S0 S0 S0 S0 S | Project Management | | \$0 | \$3.073 | | \$87,291 | \$139.821 | \$3.571 | \$0 | \$0 | \$0 | \$388,659 |
| Non-Cap Equipment \$0 \$89,204 \$0 \$84,590 \$193,782 \$0 \$0 \$0 \$30 | | | | | | | | | \$0 | | | |
| Total \$0 \$133,238 \$449,401 \$608,656 \$763,095 \$12,628 \$1,105 \$0 \$0 \$1,96 Project Budget | | | | | | | | | | | | |
| Project Budget \$1,968,124 Less Other Funding \$1,968,124 Actual Measure AA Expenditures \$1,968,124 Running Balance \$50 AA 7100004 | | | \$0 | \$133,238 | \$449,401 | \$608,656 | \$763.095 | \$12,628 | \$1,105 | | | \$1,968,124 |
| Less Other Funding \$1,968,124 Actual Measure AA Expenditures \$1,968,124 Running Balance \$0 AA7100004 Master Planning, Program Management, Overhead (112) Supplies \$0 Architect \$0 Froject Management \$0 S0 S0 S0 S0 S0 S0 S0 S0 S0 | | \$1,968,124 | ** | ***** | ¥ , | 7000,000 | ***** | T, | ¥ -, | ** | ** | + 1,111,11 |
| Net | | | | | | | | | | | | |
| Actual Measure AA Expenditures \$1,968,124 Running Balance \$0 AA 7100004 Master Planning, Program Management, Overhead (112) Supplies S0 | | \$1,968,124 | | | | | | | | | | |
| Running Balance \$0 | | | | | | | | | | | | |
| AA710004 Master Planning, Program Management, Overhead (112) Supplies Sup | | | | | | | | | | | | |
| Master Planning, Program Management, Overhead (112) Supplies \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 | | , 40 | | | | | | | | | | |
| Master Planning, Program Management, Overhead (112) \$0 | ΛΛ 7100004 | | | | - | | | | | | | |
| Supplies \$0 < | | | | | | | | | | | | |
| Architect \$0 \$0 \$0 \$0 \$139,302 \$187,927 \$245,329 \$57 Project Management \$0 \$0 \$0 \$76,015 \$150 \$0 \$49,170 \$135,533 \$26 Cap Equipment \$0 | | | *** | 60 | * 0 | 60 | 60 | ** | * 0 | 60 | 60 | 60 |
| Project Management \$0 \$0 \$0 \$76,015 \$150 \$0 \$49,170 \$135,533 \$26 Cap Equipment \$0 <t< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td>\$0 \$572,558</td></t<> | | | | | | | | | | | | \$0 \$572,558 |
| Cap Equipment \$0 \$0 \$0 \$0 \$0 \$0 \$0 | | | | | | | | | | | | |
| | | | | | | | | | | | | \$260,868 |
| | | | \$0 \$0 | \$0 \$0 | | | | | | \$0 \$0 | \$0 | |
| | | | | | | | | | | | | |
| | | 0000 :0= | \$0 | \$0 | \$0 | \$0 | \$/6,015 | \$150 | \$139,302 | \$237,097 | \$380,863 | \$833,427 |
| Project Budget \$833,427 | | | | | | | | | | | | |
| Less Other Funding \$0 | | | | | | | | | | | | |
| Net \$833,427 | | | | | | | | | | | | |
| Actual Measure AA Expenditures \$833,427 | | | | | | | | | | | | |
| Running Balance \$0 | Running Balance | J \$0 | | | | | | | | | | |

| Projects | Budget | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|---|--------------|---------------|----------------------|---------------------|---------------|---------------|-------------------|---------------|---------------|---------------|----------------------|
| Tiojects | Budget | 03/10 1 11141 | 10/11111111111 | 11/12 1 11101 | 12/13 1 11101 | 13/14 1 11101 | 1-7/10/111101 | 15/10 I IIIai | 10/17 1 11101 | 17710 I IIIai | Combined Totals |
| AA 7100154 | 1 1 | | | T | | | | | 1 | | |
| Energy Efficiency Projects (113) | | | | | | | | | | | |
| | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| Legal | | | \$0 | \$0 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$0 | \$0 \$0 | \$0 \$0 |
| Other Contract Services Building & Additions | | \$0 \$0 | \$0 \$0 | \$189 | \$2,108,853 | \$990,389 | -\$97.621 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$3.001.810 |
| | | | | | | | | | | | |
| Architect | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| Engineering | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| Inspection & Testing | | \$0 | \$0 | \$0 | \$4,020 | \$0 | \$10,118 | \$0 | \$0 | \$0 | \$14,138 |
| Project Management | | \$0 | \$0 | \$0 | \$0 | \$0 | \$825 | \$0 | \$0 | \$0 | \$825 |
| Non-Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| Total | | \$0 | \$0 | \$189 | \$2,112,873 | \$990,389 | -\$86,678 | \$0 | \$0 | \$0 | \$3,016,773 |
| Project Budget | \$3,508,088 | | | | | | | | | | |
| Less Other Funding | \$491,315 | | * Other Funding So | | | | | | | | |
| Net | \$3,016,773 | | DWP \$18,715.00 r | | | | | | | | |
| Actual Measure AA Expenditures | \$3,016,773 | | SCE \$446,519.77 | | | | | | | | |
| Running Balance | \$0 | | Gas Co. \$26,080 r | eceived | | | | | | | |
| | | | | | | | | | | | |
| AA 7100064 | | | | | | | | | | | |
| Community Classroom & Facility Projects (114) | | | | | | | | | | | |
| Supplies | | \$0 | \$0 | \$0 | \$124 | \$0 | \$0 | \$0 | \$0 | \$0 | \$124 |
| Legal | | \$0 | \$0 | \$1,867 | \$1,418 | \$0 \$0 | \$0 \$0 | \$0 | \$0 | \$0 | \$3,285 |
| Other Contract Services | | \$0 | \$3,720 | \$1,869 | \$1,410 | \$0 \$0 | \$0 \$0 | \$0 | \$0 | \$0 | \$5,588 |
| Building & Additions | | \$0 \$0 | \$434,578 | \$1,369,441 | \$408,696 | -\$1,003 | \$0 \$0 | \$0 | \$0 \$0 | \$0 \$0 | \$2,211,712 |
| | | \$0 \$0 | | | | | \$0 \$0 | | \$0 \$0 | | |
| Architect Engineering | | \$0 \$0 | \$263,833 \$3,220 | \$48,120 \$3,143 | \$1,318 | \$0 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$313,272 \$6,363 |
| | | | | | \$0 | \$0 | | | | | |
| Inspection & Testing | | \$0 | \$41,002 | \$80,885 | \$1,495 | \$0 | \$0 | \$0 | \$0 | \$0 | \$123,382 |
| Project Management | | \$135 | \$117,247 | \$143,780 | \$27,570 | \$0 | \$0 | \$0 | \$0 | \$0 | \$288,732 |
| Non-Cap Equipment | | \$0 | \$0 | \$209,726 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$209,726 |
| Total | | \$135 | \$863,599 | \$1,858,831 | \$440,621 | -\$1,003 | \$0 | \$0 | \$0 | \$0 | \$3,162,183 |
| Project Budget | \$3,162,183 | | | | | | | | | | |
| Less Other Funding | \$0 | | | | | | | | | | |
| Net | \$3,162,183 | | | | | | | | | | |
| Actual Measure AA Expenditures | \$3,162,183 | | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | |
| | | | | | | | | | | | |
| AA 7100057 | | | | | | | | | | | |
| Real Property Acquisition (115) | | | | | | | | | | | |
| Legal | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$659 | \$659 |
| Other Contract Services | + | \$0 | \$39 | \$7,000 | \$0 | \$15,800 | \$0 | \$0 | \$0 | \$0 | \$22,839 |
| Site Acquisition | | \$1,739,979 | \$4,001,204 | \$9,022,207 | \$0 | \$13,800 | \$0 \$0 | \$0 | \$5,013,226 | \$4,821,600 | \$24,598,214 |
| Inspection & Testing | | \$8,689 | \$4,001,204 | \$9,022,207 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$0 | \$5,013,226 | \$4,621,600 | \$24,596,214 |
| Project Management | | \$8,689 | \$7,986 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$10,074 |
| Total | | \$1,748,667 | \$4.009.228 | \$9.029.207 | \$0 \$0 | | \$0 \$0 | \$0 \$0 | \$5,013,226 | \$4,822,259 | \$24,638,386 |
| | 604.050.475 | \$1,748,667 | \$4,009,228 | \$9,029,207 | \$0 | \$15,800 | \$0 | \$0 | \$5,013,226 | \$4,822,259 | \$24,638,386 |
| Project Budget | \$24,859,475 | | | | | | | | | | |
| Less Other Funding | \$0 | | | | | | | | | | |
| Net | \$24,859,475 | | | | | | | | | | |
| Actual Measure AA Expenditures | \$24,638,386 | | | | | | | | | | |
| Running Balance | \$221,089 | | | | | | | | | | |

| Projects | Budget | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|--|-------------|-------------|-----------------|--------------------|--------------------|----------------------|-----------------|-------------|-------------|-------------|-----------------|
| | | | | | | | | | | | |
| AA 7100058, 7100151, 7100156, 7100059 | | | | | | | | | | | |
| Roadways, Walkways, Grounds, Parking Lots, and Garages (116) | | | | | | | | | | | |
| Supplies | | \$0 | \$0 | \$0 | \$0 | \$4,616 | \$0 | \$0 | | | \$4,616 |
| Legal | | \$0 | \$0 | \$0 | \$125 | \$0 | \$0 | \$0 | | | \$125 |
| Consultants | | \$0 | \$0 | \$0 | \$48,090 | \$5,018 | \$0 | \$0 | \$0 | \$0 | \$53,108 |
| Other Contract Services | | \$218 | \$770 | \$122 | \$25,249 | \$0 | \$0 | \$0 | \$0 | \$0 | \$26,358 |
| Building & Additions | | \$185,345 | \$6,731 | \$113,784 | \$321,603 | \$975,401 | \$0 | \$0 | \$0 | \$0 | \$1,602,864 |
| Architect | | \$0 | \$0 | \$0 | \$103,569 | \$19,225 | \$1,240 | \$0 | \$0 | \$0 | \$124,035 |
| Engineering | | \$0 | \$0 | \$0 | \$1,095 | \$1,445 | \$0 | \$0 | \$0 | \$0 | \$2,540 |
| Inspection & Testing | | \$13,380 | \$7,865 | \$13,553 | \$20,126 | \$42,865 | \$0 | \$0 | \$0 | \$0 | \$97,787 |
| Project Management | | \$24,404 | \$12,439 | \$21,945 | \$54,095 | \$104,943 | \$1,411 | \$0 | \$0 | \$0 | \$219,237 |
| Total | | \$223,347 | \$27,804 | \$149,403 | \$573,951 | \$1,153,512 | \$2,652 | \$0 | | | |
| Project Budget | \$7,022,417 | , .,. | , ,, | , ,, ,, | , , | , , , . | , , , | | | | , , , |
| Less Other Funding | \$4,891,747 | i , | Other Funding S | ource: | | | | | | | |
| Net | \$2,130,670 | | | ,747, Measure V \$ | 1,000,000 allocate | d | | | | | |
| Actual Measure AA Expenditures | \$2,130,670 | 1 | | , , | , , | - | | | | | |
| Running Balance | \$0 | 1 | | | | | | | | | |
| Turning Bulanco | | | | | | | | | | | |
| AA 7100069 | 1 | | | | 1 | | | | | | |
| Infrastructure & Technology - Technology (117) | | | | | | | | | | | |
| Software | | \$0 | \$0 | \$0 | \$0 | \$0 | \$218 | \$0 | \$0 | \$0 | \$218 |
| Supplies | | \$0 | \$0 | \$13.646 | \$7,587 | \$0 | \$16,966 | \$0 \$0 | | \$0 | |
| Maintenance Contract | | \$0 | \$9,472 | \$46,300 | \$210,581 | \$18,944 | \$42,415 | \$9,472 | | | \$337,186 |
| Other Contract Services | | \$0 | \$9,472 | \$0,300 | \$210,381 | \$10,944 | \$49,589 | \$9,472 | | | |
| Building & Additions | | \$0 | \$0 \$0 | \$0 | \$0 | \$0 \$0 | \$49,569 \$0 | \$0 | | | |
| Project Management | | \$0 | \$0 \$0 | \$0 | \$0 | \$0 \$0 | \$0 \$0 | \$0 | | | \$0 |
| Cap Equipment | | \$0 | \$207,423 | \$33,063 | \$576,294 | \$0 \$0 | \$1,145,668 | \$0 | | | \$1,962,449 |
| Non-Cap Equipment | | \$0 | \$07,423 | \$42,827 | \$570,294 | \$0 \$0 | \$3,447 | \$0 | | | |
| Total | | \$0 | \$216,896 | \$135,838 | \$794,963 | \$18,944 | \$1,258,304 | \$9,472 | | | |
| Project Budget | \$2,434,417 | ψU | \$210,090 | \$135,030 | \$194,963 | \$10,94 4 | \$1,250,304 | \$9,472 | ψŪ | ψU | \$2,434,417 |
| Less Other Funding | \$2,434,417 | - | | | | | | | | | |
| | | - | | | | | | | | | |
| Net | \$2,434,417 | - | | | | | | | | | |
| Actual Measure AA Expenditures | \$2,434,417 | - | | | | | | | | | |
| Running Balance | \$0 | | | | | | | | | | |
| AA 7400450 | | | | | | | | | | | |
| AA 7100150 | | | | | | | | | | | |
| Infrastructure & Technology - Utility (118) | | | 212.222 | | • | | | | | • | *** |
| Sofeware License | | \$0 | \$12,000 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | |
| Legal | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | \$0 |
| Building & Additions | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | \$0 | \$0 |
| Architect | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | |
| Inspection & Testing | | \$0 | \$4,979 | \$0 | \$0 | \$0 | \$0 | \$0 | | | \$4,979 |
| Project Management | | \$0 | \$3,240 | \$0 | \$0 | \$0 | \$0 | \$0 | | | \$3,240 |
| Cap Equipment | | \$0 | \$0 | \$7,534 | \$0 | \$0 | \$0 | \$0 | | \$0 | \$7,534 |
| Non-Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | | | |
| Total | | \$0 | \$20,219 | \$7,534 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$27,753 |
| Project Budget | \$27,753 | | | | | | | | | | |
| Less Other Funding | \$0 | | | | | | | | | | |
| Net | \$27,753 | | | | | | | | | | |
| Actual Measure AA Expenditures | \$27,753 |] | | | | | | | | | |
| Running Balance | \$0 | 1 | | | | | | | | | |

| Projects | Budget | 09/10 Final | 10/11 Final | 11/12 Final | 12/13 Final | 13/14 Final | 14/15 Final | 15/16 Final | 16/17 Final | 17/18 Final | Combined Totals |
|---|--------------|-------------|---------------------|---------------------|-------------------|---|---|--------------|------------------|--------------|-----------------|
| F | | | | | | | | | | | _ |
| AA 7100153 | | | | | | | | | | | |
| Emergency Lighting, Fire Alarm, and Security System (119) | | | | | | | | | | | |
| Supplies | | \$0 | | \$0 | \$0 | \$2,348 | \$0 | \$0 | \$2,671 | \$0 | |
| Consultants | | \$0 | \$0 | \$0 | \$0 | \$0 | \$16 | \$0 | \$0 | \$0 | |
| Telecom Fee | | \$0 | \$0 | \$0 | \$0 | \$0 | \$800 | \$0 | \$0 | \$0 | |
| Maintenance Contract | | \$0 | \$0 | \$648 | \$0 | \$39,700 | \$0 | \$2,700 | \$0 | \$0 | |
| Software Suppoert | | \$0 | \$0 | \$24,765 | \$0 | \$106,367 | \$0 | \$2,232 | \$0 | \$0 | |
| Other Contract Services | | \$0 | \$0 | \$0 | \$0 | \$47,695 | \$0 | \$4,643 | \$1,560 | \$0 | |
| Building & Additions | | \$0 | \$0 | \$0 | \$0 | \$110 | \$2,648,866 | \$4,129,145 | \$1,308,230 | \$763,170 | |
| Architect | | \$0 | \$0 | \$0 | \$0 | \$0 | \$18,925 | \$0 | \$0 | \$5,047 | \$23,972 |
| Enginnering | | \$0 | \$0 | \$0 | \$0 | \$211,030 | \$389,013 | \$156,247 | \$255,798 | \$358,560 | \$1,370,648 |
| Inspection & Testing | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$58,831 | \$4,800 | \$0 | \$63,631 |
| Project Management | | \$0 | \$0 | \$0 | \$0 | \$51,008 | \$52,044 | \$79,285 | \$16,500 | \$49,738 | \$248,574 |
| Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$89,415 | \$0 | \$5,871 | \$0 | \$0 | \$95,286 |
| Non-Cap Equipment | | \$0 | \$0 | \$6,087 | \$0 | \$392,586 | \$8,348 | \$0 | \$0 | \$0 | \$407,022 |
| Total | | \$0 | \$0 | \$31,500 | \$0 | \$940,259 | \$3,118,012 | \$4,438,953 | \$1,589,560 | \$1,176,515 | \$11,294,799 |
| Project Budget | \$11,520,794 | | | | | | | | | | |
| Less Other Funding | \$0 | | | | | | | | | | |
| Net | \$11,520,794 | | | | | | | | | | |
| Actual Measure AA Expenditures | \$11,294,799 | | | | | | | | | | |
| Running Balance | \$225,995 | | | | | | | | | | |
| | , ,,,,,,,, | | | | | | | | | | |
| AA 7100142 | | | 1 | | | | | | | | |
| Student Services (120) | | | | | | - | | | | | |
| Supplies | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 |
| Consultants | | \$0 \$0 | \$0 \$0 | \$0 \$0 | | \$0 | \$0 | \$0 \$0 | \$0 | \$0 | |
| Telecom Fee | | \$0 \$0 | | \$0 \$0 | \$0 | \$0 | \$0 | \$0 \$0 | \$0 | \$0 | |
| | | | \$0 | | \$0 \$0 | | | | \$0 \$0 | | |
| Maintenance Contract | | \$0 \$0 | \$0 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$0 \$0 | \$0 \$0 | |
| Software Suppoert | | | \$0 | | | | | | | | |
| Other Contract Services | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | |
| Building & Additions | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$3,165,626 | \$3,165,626 |
| Architect | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | |
| Enginnering | | \$0 | \$0 | \$0 | | \$0 | \$0 | \$0 | \$0 | \$0 | |
| Inspection & Testing | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | |
| Project Management | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | |
| Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | |
| Non-Cap Equipment | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | |
| Total | | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$0 | \$3,165,626 | \$3,165,626 |
| Project Budget | \$6,870,490 | | | | | | | | | | |
| Less Other Funding | \$0 | | * Other Funding So | | | | | | | | |
| Net | \$6,870,490 | | State of California | | | | | | | | |
| Actual Measure AA Expenditures | \$3,165,626 | | Mease U \$21,131, | 135, Measure S \$ | 45,595,322, Measu | ire V \$33,624,909 a | allocated | | | | |
| Running Balance | \$3,704,864 | | Measure U, S & AA | A interests \$21,68 | 1,308 allocated | | | | | | |
| <u> </u> | | | | | | | | | | | |
| Cost of Issuance (121) | | | | | | | | | | | |
| Cost of Issuance | | \$0 | \$0 | \$0 | \$0 | \$0 | \$285,000 | \$0 | \$213,026 | \$0 | \$498.026 |
| Total | | \$0 | | \$0 | | \$0 | \$285,000 | \$0 | | \$0 | |
| Project Budget | \$498,026 | 40 | + | ** | 40 | 40 | ,, ,,,, | +5 | 7-1-,0-0 | *** | ,,,,,, |
| Less Other Funding | \$0 | | | | | | | | | | |
| Net | \$498.026 | | | | | | | | | | |
| Actual Measure AA Expenditures | \$498,026 | | | | | | | | | | |
| Running Balance | \$498,026 | | | | | | | | | | |
| running balance | \$0 | | | | | | | | | | |
| | | A | 414 444 | A.= aa. : | A.A1 | *** *** * * * * * * * * * * * * * * * * | *** * * * * * * * * * * * * * * * * * * | *** = =1 | A - 1 - 1 | | |
| Grand Total | | \$4,900,734 | \$10,935,584 | \$17,864,407 | \$13,113,759 | \$30,388,248 | \$39,049,510 | \$60,741,756 | \$57,313,878 | \$52,193,046 | \$286,500,922 |

SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure V Project Schedule As of June 30, 2018

| | Project Name | Completion | 201 | 18 | 20 |)19 | 2 | 020 | | 20 | 21 | 2022 | 2 | 023 |
|-----|---|----------------|------|---------|----|-----|------|--------|----|----|----|------|---|-----|
| 101 | Replacement Math and Science Extension Building | September 2022 | | | | | | | | | | | | |
| 102 | Student Services | March 2019 | | | | | | | | | | | | |
| 103 | Malibu Center | December 2021 | | | | | | | | | | | | |
| 104 | Early Childhood Development/Childcare | June 2020 | | | | | | | | | | | | |
| 105 | Art Building Replacement | September 2022 | | | | | | | | | | | | |
| 106 | Business Building Renovation | December 2023 | | | | | | | T | | | | | |
| 107 | Air Conditioning | December 2019 | | | | | | | | | | | | |
| 108 | ADA | On-Going | | | | | | | | | | | | |
| 109 | Master Planning | December 2019 | | | | | | | | | | | | |
| 110 | Drescher Hall Modernization | On-Going | | | | | | | | | | | | |
| 111 | Outdoor Classroom | June 2022 | | | | • | | | | | | | | |
| 112 | SMMUSD | August 2021 | | | | | | | | | | | | |
| 113 | City of Santa Monica | On-Going | | | | | | | | | | | | |
| 114 | Classrooms Relocation | On-Going | | | | | | | | | | | | |
| 115 | TBD | On-Going | | | | | | | | | | | | |
| 120 | Other Bond Related Expenses | On-Going | | | | | | | | | | | | |
| 121 | Cost of Issuance | On-Going | | | | | | | | | | | | |
| 122 | Management Reserve | On-Going | | | | | | | | | | | | |
| 123 | Unissuable Bond | On-Going | | | | | | | | | | | | |
| | | | | | | | | | | | | | | |
| | | | In F | Plannii | ng | In | Cons | tructi | on | | | | | |

| Projects | Budget | 17/18 Final | Combined Totals |
|---|---------------|-------------|---|
| | | | |
| V 7100090 | | | |
| Replacement Math and Science Extension Building (101) | | | |
| Legal | | \$0 | |
| Other Contract Services | | \$0 | |
| Moving Services | | \$0 | \$0 |
| Building & Additions | | \$675 | |
| Architect | | \$2,047,911 | \$2,047,911 |
| Engineering | | \$0 | \$0 |
| Inspection & Testing | | \$30,804 | \$30,804 |
| Project Management | | \$130,874 | \$130,874 |
| Cap Equipment | | \$0 | |
| Non-Cap Equipment | | \$0 | \$0 |
| Total | | \$2,210,264 | \$2,210,264 |
| Project Budget | \$124,958,336 | | |
| Less Other Funding | \$42,640,344 | | * Other Funding Source: |
| Net | \$82,317,992 | | Measure U \$308,336, Measure AA \$2,244,008 allocated |
| Actual Measure V Expenditures | \$2,210,26 | 4 | State of California \$40,088,000 allocated |
| Running Balance | \$80,107,728 | | |
| F | | | |
| V 7100142 | | | |
| Student Services Building (102) | | | |
| Other Contract Services | | \$0 | |
| Building & Additions | | \$0 | |
| Architect | | \$0 | |
| Engineering | | \$0 | · |
| Inspection & Testing | | \$55,202 | \$55,202 |
| Project Management | | \$0 | 1.5 |
| Total | | \$55,202 | \$55,202 |
| Project Budget | \$130,224,164 | | * Other Funding Source: |
| Less Other Funding | \$96,599,255 | | State of California \$1,321,000 received |
| Net | \$33,624,909 | | Mease U \$21,131,135, Measure S 45,595,322, |
| Actual Measure V Expenditures | \$55,20 | 2 | Measure AA \$6,870,490 allocated |
| Running Balance | \$33,569,707 | | Measure U, S & AA interests \$21,681,308 allocated |

| Projects | Budget | 17/18 Final | Combined Totals | |
|-------------------------------|--------------|-------------|---|-----------|
| _ | | | | |
| V 7100240 | | | | |
| Art Complex (105) | | | | |
| Legal | | \$0 | | \$0 |
| Other Contract Services | | \$0 | | \$0 |
| Moving Services | | \$0 | | \$0 |
| Building & Additions | | \$184 | | \$184 |
| Architect | | \$0 | | \$0 |
| Engineering | | \$0 | | \$0 |
| Inspection & Testing | | \$0 | | \$0 |
| Project Management | | \$0 | | \$0 |
| Cap Equipment | | \$0 | | \$0 |
| Non-Cap Equipment | | \$0 | | \$0 |
| Total | | \$184 | | \$184 |
| Project Budget | \$32,914,000 | | | |
| Less Other Funding | \$8,914,000 | | * Other Funding Source: | |
| Net | \$24,000,000 | | State of California \$8,914,000 pending | |
| Actual Measure V Expenditures | \$18 | 4 | | |
| Running Balance | \$23,999,816 | | | |
| | | | | |
| V 7100188 | | | | |
| Air Conditioning (107) | | | | |
| Other Contract Services | | \$0 | | \$0 |
| Building & Additions | | \$0 | | \$0 |
| Architect | | \$0 | | \$0 |
| Engineering | | \$417,960 | | \$417,960 |
| Inspection & Testing | | \$0 | | \$0 |
| Project Management | | \$4,370 | | \$4,370 |
| Total | | \$422,330 | | \$422,330 |
| Project Budget | \$10,777,654 | | | |
| Less Other Funding | \$0 | | | |
| Net | \$10,777,654 | | | |
| Actual Measure V Expenditures | \$422,33 | b | | |
| Running Balance | \$10,355,324 | | | |

| Projects | Budget | 17/18 Final | Combined Totals |
|-----------------------------------|--------------|--------------|-----------------|
| 1 10,000 | Dauget | 177101111111 | Combined Totals |
| V 7100237 | | | |
| Outdoor Classroom (111) | | | |
| Other Contract Services | | \$0 | \$0 |
| Building & Additions | | \$0 | \$0 |
| Architect | | \$100,000 | \$100,000 |
| Engineering | | \$0 | \$0 |
| Inspection & Testing | | \$0 | \$0 |
| Project Management | | \$0 | \$0 |
| Total | | \$100,000 | \$100,000 |
| Project Budget | \$10,000,000 | | |
| Less Other Funding | \$0 | | |
| Net | \$10,000,000 | | |
| Actual Measure V Expenditures | \$100,00 | b | |
| Running Balance | \$9,900,000 | | |
| - | • | • | |
| S7100048 | | | |
| Other Bond Related Expenses (116) | | | |
| Consultants | | \$0 | \$0 |
| Lease/Rental | | \$0 | \$0 |
| Supplies | | \$0 | \$0 |
| Legal | | \$0 | \$0 |
| Software License | | \$0 | \$0 |
| Advertising | | \$0 | \$0 |
| Other Contract Services | | \$0 | \$0 |
| Moving Services | | \$0 | \$0 |
| Building & Additions | | \$184 | \$184 |
| Project Management | | \$0 | \$0 |
| Cap Equipment | | \$0 | \$0 |
| Non-Cap Equipment | | \$0 | \$0 |
| Total | | \$184 | \$184 |
| Project Budget | \$300,000 | | |
| Less Other Funding | \$0 | | |
| Net | \$300,000 |] | |
| Actual Measure V Expenditures | \$18 | þ | |
| Running Balance | \$299,816 | | |

| Projects | Budget | 17/18 Final | Combined Totals |
|-------------------------------|-----------|-------------|-----------------|
| | | | |
| Cost of Issuance (117) | | | |
| Cost of Issuance | | \$291,277 | \$291,277 |
| Total | | \$291,277 | \$291,277 |
| Project Budget | \$800,000 | | |
| Less Other Funding | \$0 | | |
| Net | \$800,000 | | |
| Actual Measure V Expenditures | \$291,27 | 4 | |
| Running Balance | \$508,723 | | |
| | • | | |
| Grand Total | | \$3,079,439 | \$3,079,439 |

SMC Bond Program Contractor List as of 6-30-2018

Student Services (Measure U #0, Measure S #9, Measure AA #120):

Architect – Steinberg Architects, Morris Architects

Contractor - Minco, Bernards Brothers

Engineering – IVA, Cogent Energy Engineering, XL Fire

Inspection & Testing – Geo Labs, BTC Labs - Vertical V, Peak Survey, LPI Rango Inc., Twining

nango me., r

Project Management – LPI

Replacement Health/PE/Fitness/Dance Building (Measure S #4, Measure AA #104):

Architect - Gensler Architects

Contractor – Bernards Brothers

Engineering – IVA, Glumac

Inspection & Testing – Geo Labs, Ellis Environmental, Twining, Rango Inc.

Project Management – LPI

Early Childhood Development (Measure S #5):

Architect - Carde Ten Architects

Consultant - Child Educational Center

Contractor - The Nazerian Group

Engineering – N/A

Inspection & Testing – Geo Labs, Rango Inc.

Project Management - LPI, Vanir

Malibu Site (Measure S #6, Measure AA #110):

Architect – Quatro Design Group

Contractor – Master Contracting

Consultant – m2 Strategic, Parker Environmental

Engineering – Ensitu Services

Inspection & Testing – Peak Surveys, Ellis Environmental, JL Inspection

Project Management – LPI, m6 Strategic, Vanir

Energy Efficiency Projects (Measure S #7, Measure AA #113):

Architect - N/A

Contractor – Compass Energy Solutions, Johnson Controls

Engineering – Compass Energy Solutions, Johnson Controls

Inspection & Testing – Ellis Environmental

Environmental Performance (Measure AA #101):

Architect - Kishimoto Architects

Contractor – SJ Amoroso Construction

Engineering – P2S Engineering

Inspection & Testing - Cannon, Peak Surveys

Project Management - LPI

Information Technology Relocation (Measure AA #102):

Architect - Morris Architects

Contractor - Minco, Bernards Brothers, Eidim AV Technology

Engineering – IVA, P2S Engineering

Inspection & Testing – Cannon, Peak Surveys, Geo Labs, Ellis Environmental, Twining, JL Inspection, Rango Inc.

Project Management – LPI, CCS Presentation

Media and Technology Complex (Measure AA #103):

Architect - Clive Wilkinson Architects, Morris Architects

Contractor – H.B. Parkco Construction, Fast Track Construction, CW Driver, Dimension Data, Key Code Media, Omega Construction

Consultant - EEG Services

Engineering – IVA, P2S Engineering

Inspection & Testing - Twining, Geo Labs, BTC Labs - Vertical V,

JL Inspection, EEG Services, Ellis Environmental, Rango

Inc., Cannon

Project Management - LPI

Madison East Wing Seismic Upgrade (Measure AA #107):

Architect - DLR Group - WWCOT, LPI

Contractor - Trimax, Bernards Brothers, Dimension Data

Engineering – IVA, Glumac

Inspection & Testing – Twining, Peak Surveys, LPI, All Group Engineering, EEG Services, Ellis Environmental

Project Management - LPI

Business & Facilities Infrastructure (Measure AA #111):

Architect - LPI, Gwynne Pugh Urban Studio

Contractor – REC+S, Inc., Omega Construction,

Concept Consultant, Inc.

Engineering – N/A

Inspection & Testing - Ellis Environmental, JL Inspection

Project Management - LPI

Community Classroom & Facility Project (Measure AA #114)

Architect – Morris Architects

Contractor – Waisman Construction, Spinitar, Trimax

Engineering – IVA

Inspection & Testing – LPI, Twining

Project Management - LPI

Satellite Campus Parking Facilities and Roadway Improvements (Measure S #8)

Architect - N/A

Contractor - N/A

Engineering - MK Engineering Group

Inspection & Testing - N/A

Project Management - LPI

Roadways, walkways, Grounds, Parking Lots, and Garages (Measure AA #116)

Architect - LPI, DLR Group - WWCOT

Contractor - Trimax, Pub Construction

Consultant – Walker Parking

Engineering – MK Engineering

Inspection & Testing - Ellis Environmental, Peak Surveys, LPI

Project Management - LPI

Emergency Lighting, Fire Alarm, and Security System (Measure AA #119)

Architect - N/A

Contractor – Red Hawk Fire and Security, Nexus

Consultant - IVA

Engineering – MDC Engineers

Inspection & Testing - Rango Inc.

Project Management - LPI

Signage Safety/Information (Measure S #15)

Architect - N/A

Contractor - Sign Excellence

Consultant - APCO

Engineering – N/A

Inspection & Testing - N/A

Project Management - LPI

Math and Science Addition (Measure AA #106)

Architect - Cannon Design

Contractor - N/A

Consultant - N/A

Engineering – Arup

Inspection & Testing – N/A

Project Management - Vanir
