
# SANTA MONICA Community college District



Annual Report 2016-2017 October 25, 2017



# Submitted to the Santa Monica Community College District BOARD OF TRUSTEES

- Dr. Andrew Walzer, Chair
- Barry Snell, Vice-Chair
- Dr. Susan Aminoff
- Dr. Nancy Greenstein
- Dr. Louise Jaffe, Chair
- Dr. Margaret Quiñones-Perez
- Rob Rader
- Chase Matthews, Student Trustee

# **CITIZENS' BOND OVERSIGHT COMMITTEE**

Sonya Sultan, Chair Katherine Reuter, Vice-Chair Jeffrey Graham Sion Roy Sharon Barovsky Michael Dubin Katherine Reuter Cassandra Santiago-Amzallag

## Staff Support

Greg Brown, Director of Facilities/Planning Emil Zordilla, Assistant Director, Facilities Planning Charlie Yen, Director of Contracts Ramin Nematollahi, Committee Coordinator



# Santa Monica Community College District CITIZENS' BOND OVERSIGHT COMMITTEE ANNUAL REPORT, 2016-2017

Statement of Compliance	
Measure U	3
Measure S	4
Measure AA	5
Citizens' Bond Oversight Committee Proceedings and Activities	6
Minutes of Meetings	
July 20, 2016	7
October 19, 2016	10
January 18, 2017	13
April 26, 2017	17
SMC Capital Outlay Program – Bond Project Descriptions and Project Status	20
SMC Capital Construction Budget Summary as of July 1, 2017	28
Bond Sales/Expenses Report	29
Bond Budgets	
Measure U	30
Measure S	32
Measure AA	34
Measure U Reports	
Project Schedule	
Expenditures	
Measure S Reports	
Project Schedule	46
Expenditures	47
Measure AA Reports	
Project Schedule	
Expenditures	56
SMC Bond Program Contractor List	66



# STATEMENT OF COMPLIANCE MEASURE U FUNDS

This Annual Report is submitted to the Board of Trustees by the Santa Monica Community College District Citizens' Bond Oversight Committee.

The Committee advises that, to the best of its knowledge, the Santa Monica Community College District is in compliance with the requirements in Article XIIIA, Section 1(b)(3) of the California Constitution. In particular, bond revenue has been expended only for the purposes so described in Measure U and no funds were used for any teacher or administrative salaries or other operating expenses as prohibited by Article XIIIA, Section 1(b)(3)(a) of the California Constitution.

> Respectfully Submitted:

\_\_\_\_\_Date:\_\_\_\_\_ Sonya Sultan, Chair Citizens' Bond Oversight Committee



# STATEMENT OF COMPLIANCE MEASURE S FUNDS

This Annual Report is submitted to the Board of Trustees by the Santa Monica Community College District Citizens' Bond Oversight Committee.

The Committee advises that, to the best of its knowledge, the Santa Monica Community College District is in compliance with the requirements in Article XIIIA, Section 1(b)(3) of the California Constitution. In particular, bond revenue has been expended only for the purposes so described in Measure S and no funds were used for any teacher or administrative salaries or other operating expenses as prohibited by Article XIIIA, Section 1(b)(3)(a) of the California Constitution.

Respectfully Submitted:

\_\_\_\_\_Date:\_\_\_\_\_ Sonya Sultan, Chair Citizens' Bond Oversight Committee



# STATEMENT OF COMPLIANCE MEASURE AA FUNDS

This Annual Report is submitted to the Board of Trustees by the Santa Monica Community College District Citizens' Bond Oversight Committee.

The Committee advises that, to the best of its knowledge, the Santa Monica Community College District is in compliance with the requirements in Article XIIIA, Section 1(b)(3) of the California Constitution. In particular, bond revenue has been expended only for the purposes so described in Measure AA and no funds were used for any teacher or administrative salaries or other operating expenses as prohibited by Article XIIIA, Section 1(b)(3)(a) of the California Constitution.

Respectfully Submitted: \_\_\_\_\_Date:\_\_\_\_\_ Sonya Sultan, Chair Citizens' Bond Oversight Committee



# CITIZENS' BOND OVERSIGHT COMMITTEE PROCEEDINGS AND ACTIVITIES

# Meetings of the Citizens' Bond Oversight Committee

The Committee conducts its meetings in accordance with provisions of the Ralph M. Brown Public Meetings Act, Government Code Sections 54950 *et seq*. Meeting notices and agendas are sent to members of the Committee within the required period of time and are also posted at eight Santa Monica College campus locations and satellite sites.

Meeting notices, agendas, minutes and all documents and reports received by the Committee members are a matter of public record and made available on the SMC website: <u>http://www.smc.edu/CBOC</u>

The SMC Bond Program website is located at: <u>www.smcbondprogram.com</u>

Minutes of the quarterly meetings are included on the following pages.



A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee was held on Wednesday, **July 20, 2016 at 8 a.m.** in Drescher 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

# I. <u>CALL TO ORDER</u>: 8:11 a.m.

# 2. <u>ROLL CALL</u>

- Jeffrey Graham, Chair Absent
- Sion Roy, Vice-Chair Present
- Sharon Barovsky Absent
- Michael Dubin Absent
- Katherine Reuter Present
- Sonya Sultan Present
- Zavanna Negron Absent

## Others Present:

- Chris Bonvenuto, Chief Director, Business Services
- Don Girard, Senior Director, Government Relations/Institutional Communications
- Ramin Nematollahi, Citizens' Bond Oversight Committee Coordinator
- Charlie Yen, Director, Contracts
- Emil Zordilla, Assistant Director, Facilities Planning

Due to lack of quorum, approval of the minutes and the selection of the chair and vice chair will be postponed to the October meeting.

## 3. <u>APPROVAL OF MINUTES</u>

Action was not taken due to lack of quorum.

## 4. ELECTION OF CHAIR AND VICE-CHAIR, 2016-2018

Action was not taken due to lack of quorum.

## 5. INTRODUCTION OF REAPPOINTED AND NEW MEMBERS

The SMCCD Board of Trustees reappointed Jeffery Graham and Katherine Reuter for 2 year term and appointed SMC Associated Students Zavanna Negron for a one-year-term.

## 6. <u>REPORTS and DISCUSSION</u>

## I. <u>SMC BOND RESOLUTION UPDATE:</u>

Don Girard, discussed the SMC Board's approval of a resolution to place a \$345M classroom repair and career training measure on the November Ballot. The measure would address the college's critical facility needs to serve the students of its communities at its current capacity. Most prominently, it will allow SMC to upgrade two classroom buildings on the main campus built in the 1950s; replace temporary trailers from 1984 and 1992 which serve as classrooms; replace or rebuild the Art complex; remodel the aging business building; and would qualify SMC for up to \$50 million in matching state funds to assist with the completion

of the Art complex and the addition of a new science wing to meet the needs of a growing STEM program. It will also allow SMC to repair classrooms, remove asbestos, and bring facilities up to current seismic, accessibility and safety standards. He further reported that the Santa Monica City Council unanimously endorsed SMC's proposed bond measure at its June 28, 2016 meeting.

- II. <u>SMC Bond Construction Projects Update</u>: Emil Zordilla, updated the committee on the bond constructions projects:
  - **Center for Media and Design**: The project is progressing as planned with construction for the building at 85% complete. The interior classrooms/instructor facilities are at 75% complete. Date of completion is schedule for end of 2016/first quarter of 2017.
  - **East Wing Performing Arts Center**: The Performing Arts Center East Wing was formerly the Madison Elementary School. The District has done several renovations to the campus and has recently added the Broad Stage and Edye 2<sup>nd</sup> Space as part of a Performing Arts Center. The project is on track to be completed by the end of 2016/first quarter of 2017.
  - **Health/P.E./Fitness/Central Plant**: Construction is focused on the mechanical/electrical and the interior of the building. The central plant loop is progressing as planned and construction is to be completed early 2017.
  - **Financial Aid Relocation**: The financial aid offices were successfully relocated and are currently occupied.
  - **Student Services Building**: The student services building contract was awarded to Bernard Bros., as the lowest bidder, and preliminary work is being completed so that the foundation can be poured. The project has a completion date of 2018.
  - **Malibu Campus**: The project has been approved by all the state agencies. The project will commence, after construction is completed by the City of Malibu for the Waste Water Maintenance system. Project is to be completed end of 2018.
  - **Early Childhood Education Center**: The plans have been submitted to the Division of State Architects (DSA) and construction is to commence May 2017. The project is to be completed end of 2018.

Measure U, S and AA and Bond Sales Expenses Reports (reports included with agenda)

• The SMC Bond Capital Construction Budget Summary as of June 30, 2016 reports the following:

Measure U Budget:	\$160,000,000
Measure S Budget:	\$143,500,000
Measure AA Budget	\$295,000,000
Other Funding Received:	\$ 26,019,534
Other Funding Pending:	\$ 52,594,548
Total Budget:	\$697,111,377
Estimate at Completion:	\$697,111,377
Bond Funds Remaining:	\$200,723,493

• Measure U: Total Measure U expenditures last period were \$675,208; total remaining funds are \$12,577,755; no budget variance.

- Measure S: Total expenditures last period were \$169,699 total remaining funds are \$55,834,360; no budget variance.
- Measure AA: Total expenditures last period were \$17,125,234; total remaining funds are \$132,311,378; no budget variance.
- The *Bond Sales/Expenses Report* indicates total bond amounts, bond issue dates/amounts, unsold bond amount and total available as of June 30, 2016.

Total Bond:	\$598,500,000
Total Available:	\$528,492,559
Total Expenses:	\$397,776,507
Total Available Remaining:	\$130,716,052
Total Unsold Bond:	\$ 70,007,441

- The SMC Bond Construction Program Contractor List as of June 30, 2016 was presented for information.
- Current information on all bond construction projects is available at: <u>http://smcbondprogram.com</u> and at <u>http://www.smc.edu/CBOC</u>

# 7. SCHEDULE OF MEETINGS FUTURE MEETINGS, 2016-2017

<u>Wednesdays at 8 a.m.</u> October 19, 2016 January 18, 2017 April 19, 2017

## 8. <u>ADJOURNMENT:</u> 9:03 AM

The next meeting of the Citizens' Bond Oversight Committee will be held on **Wednesday, October 19, 2016 at 8 a.m.** in Drescher 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.



A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee was held on Wednesday, **October 19, 2016 at 8 a.m.** in Drescher 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

# I. <u>CALL TO ORDER</u>: 8:05 a.m.

# 2. <u>ROLL CALL</u>

- Jeffrey Graham, Chair Present
- Sion Roy, Vice-Chair Present
- Sharon Barovsky Absent
- Michael Dubin Present
- Katherine Reuter Present
- Sonya Sultan Present
- Zavanna Negron Absent

# Others Present:

- Dr. Kathryn E. Jeffery, Superintendent/President
- Robert Isomoto, VP Business Administration
- Don Girard, Senior Director, Government Relations/Institutional Communications
- Greg Brown, Director Facilities
- Chris Bonvenuto, Chief Director, Business Services
- Ramin Nematollahi, Citizens' Bond Oversight Committee Coordinator
- Charlie Yen, Director, Contracts
- Emil Zordilla, Assistant Director, Facilities Planning

# 6. <u>APPROVAL OF MINUTES</u>

The minutes for the Citizens' Bond Oversight Committee Meeting of **April 20, 2016** and **July 20, 2016** were approved as is. *Motion was made by Katherine Reuter and seconded by Sonya Sultan and unanimously approved.* 

# 7. INTRODUCTION OF REAPPOINTED AND NEW MEMBERS

The SMCCD Board of Trustees (July 5, 2016) reappointed Jeffery Graham and Katherine Reuter for 2 year term and appointed SMC Associated Student Zavanna Negron for a one-year-term.

# 8. ELECTION OF CHAIR AND VICE-CHAIR, 2016-2018

Sonya Sultan was elected as the Chair and Katherine Reuter was elected as Vice-Chair and *unanimously approved by the committee.* 

# 9. <u>CITIZEN'S BOND OVERSIGHT COMMITTEE ANNUAL REPORT, 2015-2016</u>

The Annual Report 2015-2016 was approved as presented. *Motion was made by Michael Dubin and seconded Sonya Sultan and unanimously approved.* 

# 10. <u>REPORTS and DISCUSSION</u>

- **III.** <u>SMC Bond Construction Projects Update</u>: Greg Brown, Director of Facilities, gave a visual presentation of the bond constructions projects:
  - **Center for Media and Design**: The project is progressing as planned. Date of completion is schedule for first quarter of 2017.
  - **East Wing Performing Arts Center**: The Performing Arts Center East Wing, formerly the Madison Elementary School. The project is on track to be completed first quarter of 2017. Signage will be complete by end of 2016.
  - Core Performance Center: Formerly known as Center Health/P.E./Fitness/Central Plant, is projected to be completed by January of 2017. It will include 3 fitness studious, a 50-foot climbing wall, a large fitness center, weight-room and locker-rooms. A second phase of construction will renovate the existing classrooms in the Gymnasium the projected completion date is mid-2017. In the basement of the building is the Central Cooling plant which provided chilled water to aid the cooling systems to the campus the Library, Science Center, HSS and the Business center and will expand. It is projected that it will save the college \$150,000 annually.
  - **Student Services Building**: The foundation for the student services building has been poured and installing pillars. The project is progressing as planned and the project completion date is for the last quarter of 2018.
  - Malibu Campus: All approvals have been received. The City of Malibu Waste Water Maintenance system installation has commenced and projected completion is last quarter of 2018/first quarter of 2019.
  - **Early Childhood Education Center**: The plans have been submitted to the Division of State Architects (DSA) and coastal commission. The project is to be commence last quarter of 2017 with a completion date of last quarter of 2018.

## Measure U, S and AA and Bond Sales Expenses Reports (reports included with agenda)

• The SMC Bond Capital Construction Budget Summary as of September 30, 2016 reports the following:

Measure U Budget:	\$160,000,000
Measure S Budget:	\$143,500,000
Measure AA Budget	\$295,000,000
Other Funding Received:	\$ 26,019,534
Other Funding Pending:	\$ 52,594,548
Total Budget:	\$698,590,482
Estimate at Completion:	\$698,590,482
Bond Funds Remaining:	\$179,484,591

- **Measure U**: Total Measure U expenditures last period were \$38,051; total remaining funds are \$11,963,016; no budget variance.
- **Measure S**: Total expenditures last period were \$49,915 total remaining funds are \$55,741,834; no budget variance.
- **Measure AA**: Total expenditures last period were \$6,226,262; total remaining funds are \$111,779,741; no budget variance.

• The *Bond Sales/Expenses Report* indicates total bond amounts, bond issue dates/amounts, unsold bond amount and total available as of September 30, 2016.

\$598,500,000
\$528,492,559
\$419,015,409
\$109,477,150
\$ 70,007,441

- The *SMC Bond Construction Program Contractor List* as of September 30, 2016 was presented for information.
- Current information on all bond construction projects is available at: <u>http://smcbondprogram.com</u> and at <u>http://www.smc.edu/CBOC</u>

## 11. SCHEDULE OF MEETINGS FUTURE MEETINGS, 2016-2017

Wednesdays at 8 a.m. January 18, 2017 April 19, 2017

## **12.** <u>ADJOURNMENT:</u> 9:12 AM

The next meeting of the Citizens' Bond Oversight Committee will be held on **Wednesday, January 18, 2017 at 8 a.m.** in Drescher 300-E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.



A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee was held on Wednesday, **January 18, 2017 at 8 a.m.** in Drescher 300---E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

# 1. <u>CALL TO ORDER</u>: 8:05 a.m.

# 2. ROLL CALL --- Members

- Sonya Sultan, Chair --- Present
- Katherine Reuter, Vice---Chair --- Present
- Jeffrey Graham Present
- Sion Roy --- Present
- Sharon Barovsky --- Present
- Michael Dubin --- Present
- Zavanna

Negron – Absent

Others Present:

- Mr. Bill Rauch Partner, Varinek, Trine, Day & Company (VTD) CPA
- Dr. Kathryn E. Jeffery, Superintendent/President
- Don Girard, Senior Director, Government Relations/Institutional Communications
- Greg Brown, Director Facilities
- Chris Bonvenuto, Chief Director, Business Services
- Ramin Nematollahi, Citizens' Bond Oversight Committee Coordinator
- Charlie Yen, Director --- Contracts
- Emil Zordilla, Assistant Director, Facilities Planning

## 3. APPROVAL OF MINUTES

The minutes of the Citizens' Bond Oversight Committee meeting of October 19, 2016 were approved as is. *Motion was made by Katherine Reuter and seconded by Jeffrey Graham and unanimously approved by the committee.* 

## 4. <u>CONFLICT OF INTEREST FORM</u>

Members completed and endorsed forms. The forms are on file.

## 5. **REPORTS and DISCUSSION**

Chris Bonvenuto discussed Santa Monica College's previous audit firm (Vicenti, Lloyd & Stuzman, CPAs), which had served as SMC's auditor for 15 years and had given SMC "Unmodified Opinions". Varinek, Trine, Day & Company was selected after a formal bidding process and received a 3 year contract with an option of 2 years. Dr. Jeffery commented on the common and good practice of changing auditors.

A. Santa Monica Community College District

# Measure U, Measure S, Measure AA General Obligation Bonds Financial and Performance Audit, June 30, 2016

Mr. Bill Rauch, presented the 2015---2016 Financial and Performance Audit Reports and reviewed the findings with the committee. He reviewed the Opinion of the findings which state:

"In our opinion, the financial statements referred to above present fairly, in all material respects, the financial position of Measure U, Measure S, Measure AA General Obligation Bond Funds (Measure U, Measure S, and Measure AA) of the District as of June 30, 2016, and the respective changes in financial position for the year then ended in accordance with accounting principles generally accepted in the Unites State of America." (*Page 3, of the SMCCD, Measure U, Measure S & Measure AA General Obligation Bonds Financial And Performance Audits – June 30, 2016 – Varinek, Trine, Day & Co. LLP*)

He reiterated the "unmodified opinion", which is the highest mark that can be received for a financial and performance audit. He further reviewed, **The Statement of Revenues**, **Expenditures, and Changes in Fund Balance** on page 5. He also discussed the "None **Reported**" findings on Financial Statement Findings on page 17.

B. Santa Monica Community College District
 Measure U, Measure S, Measure AA General Obligation Bonds
 Performance Audit June 30, 2016

Mr. Rauch discussed the procedures performed for the performance audit. A sample of expenditures was selected starting July 1, 2015 and ending June 30, 2016, and supporting documentation was reviewed to ensure that funds were properly expended on specific project list. The sample included transactions totaling **\$49,446,725**, which represent **71** percent of the total expenditures of \$69,373,518.

Based on this testing, Varinek, Trine, Day & Co. LLP, verified that funds from Measures U, Measures S, and Measures AA general Obligation Bond Funds (Measure U, Measure S, Measure AA) were expended for the construction, renovation, funding and equipment of District facilities constituting authorized bond projects.

# Conclusion:

"The results of our test indicated that, in all significant respect, the Santa Monica Community College District has properly accounted for the expenditures held in the Measure, U, Measure S, and Measure AA general Obligation Bond Funds (Measure U, Measure S, Measure AA) and such expenditures were made for authorized bond projects. There were no salaries of administrative charged to the Measure U, Measure S, and Measure AA General Obligation Bond Funds for District general administration or operations." (*Page 4, of the SMCCD, Measure U, Measure S & Measure AA General Obligation Bonds Performance Audits – June 30, 2016 – Varinek, Trine, Day & Co. LLP*).

Mr. Rauch also discussed the "none reported" comment regarding the Schedule of Findings and Questioned Costs – Page 5, (June 30, 2016) and reiterated that "There were no audit findings reported in the prior year's Schedule of Findings and Questioned Costs."

Motion was made by Sharon Barovsky to accept the report as is and seconded by Katharine Reuter and unanimously approved by the committee.

**C.** SMC Bond Capital Construction Budget Summary as of December 31, 2016.

Emil Zordilla, Assistant Director, Facilities planning, gave a visual presentation of the bond construction project:

- **Center for Media and Design**: The project is progressing as planned. Date of Completion is first quarter of 2017 with a move in date of fall 2017.
- **East Wing Performing Arts Center**: The PAC is scheduled to open for spring 2017 semester.
- **Core Performance Center**: Formerly known as the Fitness Center is going to be completed in January and will be occupied spring 2017 semester.
- **Student Services Building**: Large structure beams will be placed in the coming weeks. The student services building is schedule to open last quarter of 2018 and occupied by early 2019.
- **Malibu Campus**: Currently awaiting the finalization of lease from Los Angeles County. Bidding for the project will take place in the summer of 2017 with construction to begin in fall of 2017. Completion date is last quarter of 2019.
- **Early Childhood Education Center:** Awaiting coastal commission approval. Bidding for the project is expected in the summer of 2017 with construction to commence fall 2017. The project is schedule to be completed fall of 2018.
- D. Measure U, S and AA and Bond Sales Expense Reports

The SMC Bond Capital Construction Budget Summary as of December 31, 2016 reports the following:

Measure U Budget:	\$160,000,000
Measure S Budget:	\$143,500,000
Measure AA Budget:	\$295,000,000
Other Funding Received:	\$ 26,195,758
Other Funding Pending:	\$ 52,594,548
Total Budget:	\$698,766,706
Estimate at Completion:	\$698,590,482
Bond Funds Remaining:	\$158,468,301

• Measure U: Total Measure U Expenditures last period were \$3,144,064; total remaining funds are

**\$8,848,412**; no budget variance.

- Measure S: Total Measure S Expenditures last period were \$180,983; total remaining funds are \$55,560,851; no budget variance.
- Measure AA: Total Measure AA Expenditures last period were \$17,720,703; total remaining funds are \$94,059,038; no budget variance.
- The Bond Sales/Expense Report indicates total bond amounts, bond issue dates/amounts unsold bond amount and total available as of December 31, 2016.

Total Bond:	\$598,500,000
Total Available:	\$528,492,559
Total Expenses:	\$440,031,699

 Total Available Remaining:
 \$ 88,460,860

 Total Unsold Bond:
 \$ 70,007,441

- The SMC Bond Construction Program Contractor List as of December 31, 2016 was included in the packet.
  - Current information on all bond construction projects is available at: <u>http://smcbondprogram.com</u> and at <u>http://www.smc.edu/CBOC</u>

# 7. SCHEDULE OF MEETINGS, 2016---2017

Wednesday, April 19, 2017 at 8 a.m.

# 8. <u>ADJOURNMENT:</u> 9:10 am

The next meeting of the Citizens' Bond Oversight Committee will be held on Wednesday, April 19, 2017 at 8 a.m. in Drescher Hall Room 300---E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.



A meeting of the Santa Monica Community College District Citizens' Bond Oversight Committee was held on Wednesday, **April 26, 2017 at 8 a.m.** in Drescher 300---E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

# 6. <u>CALL TO ORDER</u>: 8:02 a.m.

# 7. ROLL CALL --- Members

- Sonya Sultan, Chair --- Present
- Katherine Reuter, Vice-Chair --- Absent
- Jeffrey Graham Present
- Sion Roy --- Present
- Sharon Barovsky --- Present
- Michael Dubin Present
- Zavanna Negron Present

## **Others Present:**

- Chris Bonvenuto, Chief Director, Business Services
- Don Girard, Senior Director, Government Relations/Institutional Communications
- Ramin Nematollahi, Citizens' Bond Oversight Committee Coordinator
- Lee Paul, LPI Inc.
- Charlie Yen, Director --- Contracts
- Emil Zordilla, Assistant Director, Facilities Planning

## 8. <u>APPROVAL OF MINUTES</u>

The minutes of the Citizens' Bond Oversight Committee meeting of January 18, 2017 were approved as is. *Motion was made by Michael Dubin and seconded by Sharon Barovsky and unanimously approved by the committee.* 

## 9. **REPORTS and DISCUSSION**

E. SMC Bond Capital Construction Budget Summary as of March 31, 2017.

Charlie Yen and Emil Zordilla, discussed the SMC bond Capital Constructer Budget Summary as of March 31, 2017.

- **Center for Media and Design**: The project is progressing as planned. Date of Completion, first quarter of 2017 with a move in date of fall 2017.
- **East Wing Performing Arts Center**: The PAC is currently open and being occupied.
- **Core Performance Center**: First phase has been completed the second phase, has started with the older-locker-rooms and bathrooms being renovated.
- **Student Services Building**: Construction is proceeding as planned and completion date is set for 2019.
- Malibu Campus: Currently awaiting the finalization of lease from Los Angeles

County. Bidding for the project will take place in the summer of 2017 with construction to begin in fall of 2017. Completion date is last quarter of 2019.

- **Early Childhood Education Center:** Awaiting coastal commission approval. Bidding for the project is expected in the summer of 2017 with construction to commence fall 2017. The project is schedule to be completed fall of 2018.
- F. Measure U, S and AA and Bond Sales Expense Reports

The SMC Bond Capital Construction Budget Summary as of March 31, 2017 reports the following:

Measure U Budget:	\$160,000,000
Measure S Budget:	\$143,500,000
Measure AA Budget:	\$295,000,000
Interest	\$ 21,476,400
Other Funding Received:	\$ 26,210,381
Other Funding Pending:	\$ 52,594,548
Total Budget:	\$ 698,781,329
Estimate at Completion:	\$ 698,781,329
Bond Funds Remaining:	\$ <b>130,855,454</b>

- Measure U: Total Measure U Expenditures last period were \$6,803,747; total remaining funds are
  - **\$2,044,655**; no budget variance.
- Measure S: Total Measure S Expenditures last period were \$4,153,959; total remaining funds are \$51,406,892; no budget variance.
- Measure AA: Total Measure AA Expenditures last period were \$16,655,141; total remaining funds are \$77,403,897; no budget variance.

• The Bond Sales/Expense Report

Indicates total bond amounts, bond issue dates/amounts unsold bond amount and total available as of March 31, 2017.

Total Bond:	\$598,500,000		
Total Available:	\$528,492,559		
Total Expenses:	\$467,644,546		
Total Available Remaining:	\$ 60,848,013		
Total Unsold Bond:	\$ 70,007,441		

- Measure V funds will be issued in August 2018 and will be reflected in 2018-2019 tax rolls.
   Funds will be used for joint use auditorium project with JAMS (John Adams Middle School).
   Upgrade the 'Face of the College', Drescher Hall North side to compliment the Student Services Building.
- The SMC Bond Construction Program Contractor List as of March 31, 2017 was included in the packet.

# G. <u>INFORMATION – EXPIRING TERMS OF MEMBERS OF THE CITIZENS' BOND OVERSIGHT</u> <u>COMMITTEE</u>

The term of the following member(s) of the Citizens' Bond Oversight Committee is expiring effective **June 30, 2017** and is eligible for reappointment:

- Sharon Barovsky, Local Community/Malibu
- Michael Dubin, Business Community / Taxpayers' Organization
- Sonya Sultan, Local/Business Community
- Sion Roy, Business Community/Taxpayers' Organization
- The associate student representative will be selected in September.

The term of the following member(s) of the Citizens' Bond Oversight Committee is expiring effective **June 30, 2018** and is eligible for reappointment:

• Jeffrey Graham, Local Business

The term of the following member(s) of the Citizens' Bond Oversight Committee is expiring effective **June 30**, **2018** and is not eligible for reappointment, as they will have served 3 consecutive terms:

• Katharine Reuter, Senior Citizens' Organization

The Board of Trustees will follow a recruitment and application process to appoint/reappoint members to fill the vacancies.

# 9. SCHEDULE OF MEETINGS, 2016---2017

Wednesday, July 19, 2017 at 8 a.m.

## **10.** <u>ADJOURNMENT:</u> 8:37 am

The next meeting of the Citizens' Bond Oversight Committee will be held on **Wednesday**, July 19, 2017 at 8 a.m. in Drescher Hall Room 300----E (the Loft) at Santa Monica College, 1900 Pico Boulevard, Santa Monica, California.

Current information on all bond construction projects is available at: <u>http://smcbondprogram.com</u> and at <u>http://www.smc.edu/CBOC</u>



SANTA MONICA COMMUNITY COLLEGE DISTRICT

**Capital Outlay Program** 

**Bond Project Report** 

July 1, 2017

Prepared by SMC Facilities Planning

The District's capital outlay program consists of larger non-maintenance projects that are generally over \$100,000, typically financed by local taxpayer approved bonds. The capital projects include new buildings, replacement buildings, renovations, property acquisition, parking, site work, landscaping, infrastructure, security, and technology.

Over the last several decades, Santa Monica and Malibu voters have approved five safety and modernization bond measures in support of the college's career and academic programs:

Proposition T	1992	\$ 23,000,000
Measure U	2002	\$160,000,000
Measure S	2004	\$135,000,000
Measure AA	2008	\$295,000,000
Measure V	2016	\$345,000,000

By way of background, local bonds financed the original Main Campus, built in the 1950s and 1960s. However, in subsequent years until 1992, the District depended primarily on limited state funding, so only a few large projects were built. After the 1994 Northridge Earthquake and the extensive damage to the Main Campus, the District received federal FEMA support for rebuilding which started the current era of major construction on the campus.

In addition to the local bonds listed above, there has been significant financial support from federal, state and city sources along with the District's own capital funds.

The 1998 Facilities Master plan was a major effort in guiding the modernization and development of the Main Campus after the Northridge earthquake. Additional facility assessments were conducted in 2001, 2002, and 2003. In 2007, a master plan was added for the development of the Bundy Campus. In 2010, an update of the Facilities Master Plan was completed to address other safety and modernization improvements on the Main Campus and to incorporate the satellite campuses.

A new Facilities Master Plan Update is currently underway and will be completed in 2017 to guide the progress in completing Measure AA projects and new projects under Measure V.

Highlights of the completed projects include the purchase of the Bundy Campus and Emeritus College, and the construction of the Theatre Arts, Broad Stage, HSS Building, Campus Quad and Information Technology.

## Projects completed in 2017:

Core Performance Center Music Hall at the SMC Performing Arts Center Center for Media and Design

## Projects expected to start construction in 2018:

Malibu Campus Santa Monica Early Childhood Lab School

*Projects expected to be completed in 2019:* Student Services

Bond Program Overview

Project	Funding Source	Total Cost	Status 6/30/17
Purchase of Bundy Site	U	\$30,280,878	Completed 2002
Emeritus College	U, SMC Foundation	\$9,603,782	Completed 2003
Purchase of 1738 Pearl Street	U	\$749,208	Completed 2003
Library Renovation & Expansion	T, State, FEMA	\$23,600,000	Completed 2003
PE/Dance/Athletics Office Relocation	U	\$2,797,033	Completed 2004
Math Complex	U	\$1,458,690	Completed 2004
Bundy Campus West Building	U	\$23,291,387	Completed 2005
Malibu Storm Water Infrastructure P-I	S	\$2,500,000	Completed 2005
Renovation of Theatre Arts	U	\$19,544,314	Completed 2006
Music Complex - Performing Arts	U	\$4,623,547	Completed 2007
HSS North/South	U, State, FEMA, City	\$29,240,945	Complete 2006/7
Shuttle Parking Acquisition & Constr.	U	\$18,969,509	Completed 2007
Malibu Storm Water Infrastructure P-II	S	\$2,500,000	Completed 2008
Broad Stage - Performing Arts	S, SMC Foundation	\$40,690,201	Completed 2008
Athletic Fields - John Adams	S	\$2,969,807	Completed 2008
Main Campus Quad	U	\$11,388,463	Completed 2008
Bundy New Driveway & Signal	S	\$3,825,841	Completed 2009
Athletic Fields - Corsair Field	S	\$4,440,065	Completed 2009
Pico Phase I - Lot 6 & Structures	S	\$1,018,009	Completed 2009
Infrastructure & Safety Phase I	U	\$4,003,084	Completed 2010
Purchase of 1516 Pico Blvd.	AA	\$1,748,667	Completed 2010
Purchase of 1510 Pico Blvd.	AA	\$4,009,228	Completed 2011
Purchase of 919 Santa Monica Blvd.	AA	\$9,029,287	Completed 2011
Bundy/Airport Classroom Relocations	AA	\$3,162,183	Completed 2012
Library Village Relocation & Bike Park	AA	\$1,448,275	Completed 2013
Bundy/Airport Parking	AA	\$2,035,375	Completed 2013
Information Technology	AA	\$23,978,879	Completed 2015
Media & Technology – Academy Site	AA	\$103,219,665	Finish Fall 2017
East Wing - Performing Arts Center	AA	\$27,608,816	Completed 2017
Health, PE, Fitness, Dance, Cent. Plant	S, AA	\$58,272,030	Finish Fall 2017
Security and Fire Alarm Upgrade	AA	\$10,320,799	Finish Fall 2017
Central Plant Loop Connections	AA	\$11,206,164	Finish Fall 2017
Student Services	U, S, AA	\$130,224,164	Under Construction
Child Development Center	AA, City	\$13,176,578	DSA Approved
Malibu Campus	S, AA	\$35,000,000	DSA Approved
Math and Science	AA, V, State	\$87,944,336	Planning Fall 2017

## **Center for Media & Design (Academy Campus)**

**Project Description:** This project includes the construction of a new 440-space Parking Structure. Also includes major renovation of the existing 50,000 SF AET building, a new 30,000 SF addition to the existing AET building, a new 33,000 SF building for the KCRW radio station, a new central courtyard, and new landscaping.

**Current Progress:** Construction on the parking structure is almost complete. Progress interior walls and finishes, electrical, mechanical and plumbing are underway on the other buildings. Site work and landscaping are underway.

Project Schedule: Parking Structure and Academic Buildings early fall 2017; KCRW late fall 2017Estimated Project Cost: \$103,219,665Funding Sources: Measure AA, KCRW Foundation

#### Music Hall- Performing Arts Campus (East Wing Earthquake Renovation)

**Project Description:** Replacement of the seismically deficient East Wing of the Madison Building with a new facility for the Music Department including a Music Hall for rehearsals, performances and special events; a piano teaching lab; and a classroom for voice and choir instruction. Project includes new plaza and entry to the Edye Second Space.

Project Schedule: Completed Spring 2017 Estimated Project Cost: \$\$27,608,816 Funding Sources: Measure AA

#### Core Performance Center (Replacement Health, Fitness, Dance, and PE Building and Central Plant)

**Project Description:** The project consists of the demolition of the existing 1958 Locker Room building and replacing it with a new three-story 66,000 SF complex. The new building consists of athletic facilities, fitness center with climbing wall, fitness studios and dance studios.

Since this building is located in the center of campus, it is an ideal location for the central cooling plant which is an energy efficiency project designed to generate chilled water for efficiently for air cooling in buildings throughout the main campus.

Project Schedule: Phase 1 Completed; Phase 2 late fall 2017Estimated Project Cost: \$58,272,030Funding Sources: Measure S, AA, State and Utility Energy Incentives

#### **Security and Fire Alarm**

**Project Description:** To better protect student and staff during emergency situations the college is upgrading all its security systems, including access control, video surveillance, and intrusion alarms as well as its fire alarm and mass notification systems to newer digital technologies.

Project Schedule: Fire alarm complete, security in construction with spring 2018 completion.Estimated Project Cost: \$10,320,799Funding Sources: Measure AA

**Project Description:** To connect and retrofit individual buildings to the chilled water loop from the Central Plant. Buildings include Business, HSS, Library and Science.

Current Progress: HSS, Business, Science, and Library in final stages of construction.

Project Schedule: In construction, estimated completion fall 2017. Estimated Project Cost: \$11,206,164 Funding Sources: Measure

# **Student Services Building**

**Project Description:** The new Student Services building will facilitate the centralization of all Student Services operations that are presently dispersed throughout the campus and housed in temporary buildings. This project provides office and service space for approximately 25 Student Services functions. The new building will be sited near the Pico Boulevard main entrance to the SMC campus and thereby provide immediate access for students and members of the college community.

This proposed project also includes accommodation for vehicular access/egress, and underground parking, all in compliance with the Master Plan goal to provide more below grade vehicle parking at the main campus.

**Current Progress:** Parking garage in complete, above ground building underway.

Project Schedule: In construction, completion Winter 2019. Estimated Project Cost: \$\$130,224,164 Funding Sources: Measure S, U and AA

## **Projects in Pre-Construction Phase**

## Malibu Site Campus

**Project Description:** In the 1970s and early 1980s, Santa Monica College offered about 70 general education classes and several non-credit classes in Malibu throughout a semester. Today, the program is limited to a few classes offered in school district buildings.

The recommended site acquisition and facility will be a classroom facility to provide general education classes, science, art and Emeritus College classes. There is also an interpretive center to highlight natural environment and history of Malibu and a Sheriff's sub-station. The District has worked cooperatively with the City of Malibu and the County of Los Angeles in planning a site at the Malibu Civic Center.

**Current Progress:** Approvals received from DSA, City of Malibu, and the Coastal Commission. Additional approvals from the County of Los Angeles expected in Fall 2017.

Project Schedule: Construction start in Spring 2018 Estimated Project Cost: \$35,000,000 Funding Sources: Measure S, AA

#### Santa Monica Early Childhood Lab School

**Project Description:** SMC currently has no dedicated childcare facility and offers lab instruction though various local childcare providers. The District lacks a teaching laboratory facility in Early Childhood Education available at many other community colleges. This project provides for a childcare center for the community plus college instructional facilities. The City of Santa Monica is a partner in this project, providing the site at the Civic Center and a portion of the building funds.

Current Progress: DSA approval received, awaiting approval by Coastal Commission.

Project Schedule: Pending approval by the Coastal Commission, construction start in Spring 2018.

Estimated Project Cost: \$13,176,578 Funding Sources: Measure S with City of Santa Monica

Projects in Active Design Phases

None

## Future Projects (Measure V)

*The following projects were included in the 2016 Measure V Bond language and will be further developed during the Facilities Master Plan Update process:* 

**Science and Math Extension.** Santa Monica College is renowned for its science and allied health programs; however, the existing labs for Life, Physical and Earth Sciences are at capacity; also, the current facility for the Math Department consists of temporary trailers and lacks the infrastructure for smart classrooms or support for the use of modern technology for instructional use. Consolidating Math and Science programs into a new Science Extension building supports interdisciplinary interaction. The building extension would qualify for up to \$40 million in State funding, which requires a local match. The building will contain an upgraded planetarium and a community lab for all ages, including a nutrition and culinary lab in support of the College's nutrition program. Approval received for partial state funding. *Planning to start fall 2017.* 

**Replacement of Temporary Classrooms.** Bond proceeds would be used to replace the 1994 temporary trailer Math Village classroom complex with permanent First Year Experience classrooms, student support study space and instructional support labs. These trailers were rushed into service following the 1994 Northridge Earthquake and have exceeded their time of usable service. Additionally, proceeds would be used to replace the 1984 modular English as a Second Language classroom building. This modular building lacks fire sprinklers, is poorly ventilated and has also exceeded its time of usable service.

**Upgrading, Renovation or Replacement of Two 1950's Buildings.** The 1952 Liberal Arts building has the poorest Facility Condition Index rating on the College's main campus, lacks fire sprinklers and does not have an elevator. The 1952 Letters & Science building has the second poorest Facility Condition Index rating on the main campus, and also lacks both fire sprinklers and an elevator.

**Renovation of Business Building.** The 1981 Business Building is overdue for renovation. The building houses a large number of computer classrooms and labs.

**Replacement of Campus Police Station.** The current police facility is antiquated and undersized. Applying bond proceeds to the replacement, construction, renovation and relocation of the campus police

station and including a public space for community and neighborhood use will improve public and campus safety.

**Upgrading, Renovation or Replacement of Art Building.** An upgraded, renovated or newly constructed art structure will replace aging building systems and improve space distribution for the many disciplines within the Art Department. The College is eligible to receive up to \$10 million in State funding for this project, which requires a local match.

Landscaping/ Water Conservation Improvements and Completing Pico Boulevard Frontage Improvements. Applying bond proceeds for landscaping improvements, including landscaping improvements to complete the main campus Pico Boulevard frontage, will improve water conservation through water reclamation and installation of drought resistant landscaping.

**Completing Master Plan Improvements at the Santa Monica College Performing Arts Center Campus.** Construction at the Performing Arts Center campus has proceeded in phases, in coordination with available funding. The first phase added the Broad Stage and the Edye Second Space theaters. The second phase has added an East Wing rehearsal hall and music performance labs. The final phase, to be funded from bond proceeds, will include an underground three-level parking structure to replace most of the existing surface parking, along with an above-ground art gallery and green-space plaza. The theaters at the Performing Arts Center are among the most heavily used theaters in Los Angeles County.

**Designing and Installing an Outdoor Classroom.** The design, construction, installation and improvement of a venue for outdoor plays and class lectures.

**Converting Library Interiors.** Conversion of existing Library floor space used for book stacks to construct and install additional student study areas, tutoring and collaborative learning spaces that will support student success.

**Making Environmental Performance Improvements.** Bond funds will be used to upgrade District facilities to achieve energy or resource use efficiency and water conservation and achieve sustainability for District operations.

**Upgrading Technology Infrastructure.** Bond proceeds will be applied to renovate, replace, upgrade, acquire, install and integrate major site, building and utility systems, equipment and related infrastructure, including lighting, electrical, wiring and related infrastructure for modern technology, classroom instructional technology, communications and security technology (including security cameras and monitoring systems), data, voice, public address and audio-visual communication, energy efficiency, management monitoring systems, networks, fixtures, controls and equipment, cable infrastructure, network expansion, wireless access points and other communications and administrative systems.

#### COMMUNITY JOINT USE PROJECTS

**Providing for a Joint Use Project with the City of Santa Monica.** The College will provide up to \$20 million in bond funds for the expansion of the City of Santa Monica's Memorial Park to accommodate soccer and/or other field sports for use by College students and the general public.

**Providing for a Joint Use Project with the Santa Monica-Malibu Unified School District.** The Johns Adams Middle School Auditorium, adjacent to the College's main campus, has suffered earthquake damage and is no longer in service. The College will make available bond funds as needed to assist the School District in renovating or replacing the auditorium with a seating capacity of approximately 750, for joint use.

**Providing for City of Malibu Infrastructure and Community Educational Facilities.** The College will provide up to \$25 million in funding enhancements to its instructional presence in Malibu in partnership with the City of Malibu.

		nica College E Measure U	Measure S	Measure AA	Measure V	-		Other Funding		Estimate at		Bond Funds
Project Number	Project Name	Budget	Budget	Budget	Budget	Interest	Received *	Pending **	Total Budget	Completion	Status	Remaining
U-A	Purchase of BAE Airport Site	\$30,280,878							\$30,280,878	\$30,280,878	Completed	\$(
U-B	Emeritus College Facility	\$8,909,940					\$693,842		\$9,603,782	\$9,603,782	Completed	\$(
U-C	Purchase of 1738 Pearl Street	\$749,208							\$749,208	\$749,208	Completed	\$(
U-D	PE Temp. Bldg. Replacement	\$2,797,033							\$2,797,033	\$2,797,033	Completed	\$0
U-E	Remodel Library Village for Math	\$1,458,690							\$1,458,690	\$1,458,690	Completed	\$0
U-F	SM Airport Campus Site Improvements	\$4,170,264							\$4,170,264	\$4,170,264	Completed	\$0
U-G	SM Airport Campus West Building	\$19,709,741							\$19,709,741	\$19,709,741	Completed	\$0
U-H	Theater Arts Renovation	\$19,544,314							\$19,544,314	\$19,544,314	Completed	\$0
U-I	Earthquake Rpl. Liberal Arts North	\$6,011,584					\$6,496,141		\$12,507,725	\$12,507,725	Completed	\$0
U-K	Earthquake Rpl. Liberal Arts South	\$6,108,150					\$10,625,070		\$16,733,220	\$16,733,220	Completed	\$0
U-L	Shuttle Replacement Parking	\$18,969,509							\$18,969,509	\$18,969,509	Completed	\$0
U-M	North Quad Plaza	\$11,388,463							\$11,388,463	\$11,388,463	Completed	\$0
U-Q	Infrastructure & Safety	\$4,003,084							\$4,003,084	\$4,003,084	Completed	\$0
U-R	Restroom Improvements	\$17,501							\$17,501	\$17,501	Completed	\$0
S-1	Athletic Fields Phase I, Corsair Field	, ,	\$4,372,535				\$67,530		\$4,440,065	\$4,440,065	Completed	\$0
S-1A	Athletic Fields Phase I, John Adams		\$2,969,807				<i>¥0.,000</i>		\$2,969,807	\$2,969,807	Completed	\$0
S-10	Pico Promenade Improvements, Phase I		\$1,018,009						\$1,018,009	\$1,018,009	Completed	\$0
S-13	Adv. Architecture Related Exp for AA		\$0						\$0	\$0	Completed	\$0
AA-114	Community Classroom & Facility Projects			\$3,162,183					\$3,162,183	\$3,162,183	Completed	\$0
U-T	14th and Pico Project	\$319,242		\$3,102,103					\$319,242	\$319,242	Completed	\$0
U-N	Letters & Sci Demo/Restore	\$0							\$0	\$0	Completed	\$0
S-14, AA-115	Real Property Acquisition	ŲÇ	\$45,597	\$24,902,902					\$24,948,499	\$24,948,499	Completed	\$5,086,775
AA-108	Renovation of Corsair Stadium		Ş43,337	\$35,299					\$35,299	\$35,299	Completed	\$3,080,773
S-2	Performing Arts Complex		\$37,697,625	,2 <u>,</u> 2 <u>,</u>			\$2,992,576		\$40,690,201	\$40,690,201	Completed	\$0
U-J	Music Complex	\$2,011,371	\$37,097,023				\$2,618,113		\$4,629,484	\$4,629,484	Completed	\$0
S-3, AA-109	Career Opportunity Center	\$2,011,371		\$0			\$2,018,113		\$4,029,484	\$4,029,484	Completed	\$0
AA-118	Infrastructure & Technology - Utility			ېر \$27,753					\$27,753	\$0 \$27,753	Completed	\$0
AA-118 AA-111	Business & Facilities Infrastructure			\$1,968,124					\$1,968,124	\$1,968,124	Completed	\$0 \$0
				\$1,968,124					\$1,968,124			\$0
AA-117	Infrastructure & Technology - Technology		¢202.201				\$708,637			\$2,434,417	Completed	
	Energy Efficiency Projects		\$293,361	\$3,016,773			\$708,637		\$4,018,771	\$4,018,771	Completed	\$0
S-15	Signage Safety/Information		\$706,713	622 4 CO E CO					\$706,713	\$706,713	Completed	\$0
AA-102	Infrastructure & Technology - Information Technology Relocation			\$23,160,569			¢000.444	ć5 044 050	\$23,160,569	\$23,160,569	Completed	\$0
AA-103	Media and Technology Complex - Academy Site			\$103,219,665			\$990,441	\$5,844,950	\$110,055,056		In Construction	
	Madison East Wing Seismic Upgrade		¢14 CO2 202	\$27,608,816			ć200.047		\$27,608,816		Completed	\$1,586,722
	Replacement Health/PE/Fitness Central Plant Building		\$11,603,383				\$208,847		\$58,272,030		In Construction	
AA-119	Emergency Lighting, Fire Alarm, and Security System			\$11,520,794					\$11,520,794		In Construction	
AA-101	Environmental Performance - Central Plant Connections	624 422 262	A 17 15 C 0 10	\$11,206,164		444074645	<u> </u>		\$11,206,164		In Construction	
	Student Services Building	\$21,132,262	\$47,456,043	\$30,944,318	\$15,095,896				\$130,224,164		In Construction	
	Early Childhood Development/Childcare		\$7,000,000			\$1,858,578		\$6,661,598	\$15,520,176	\$15,520,176		\$5,880,136
	Malibu Site Acquisition and Facility	40.1.0.1.1	\$25,000,000	4					\$25,000,000	\$25,000,000	In Design	\$17,414,598
U-S, S-11, AA-112		\$2,110,430	\$716,428	\$750,000					\$3,576,858	\$3,576,858	-	\$297,436
	Satellite Campus Parking Facilities and Roadway		\$3,891,747	\$2,130,670					\$7,022,417	\$7,022,417	In Planning	\$1,000,000
	Replacement Math and Science Extension Building	\$308,336		\$1,244,008				\$40,088,000	\$90,401,286	\$90,401,286	In Planning	\$49,999,200
	Drescher - Academic Modernization, Bookstore, Pico Promenade II			\$5,082	\$13,000,000				\$13,005,082	\$13,005,082	In Planning	\$13,000,000
S-12	Other Bond Related Expenses		\$609,282						\$609,282	\$609,282	In Planning	\$224,420
	TBD				\$238,343,162				\$238,343,162	\$238,343,162	In Planning	\$238,343,162
S-16, AA-212	Cost of Issuance		\$119,470	\$498,026					\$1,417,496	\$1,417,496	In Planning	\$800,000
	Management Reserve				\$28,000,000				\$35,438,652	\$35,438,652		\$28,704,637
	Project Totals	\$160,000,000	\$143,500,000	\$295,000,000	\$345,000,000	\$22,867,238	\$26,722,197	\$52,594,548	\$1,045,683,983	\$1,045,683,983		\$451,292,717
	* City of SM: \$10,206,823; FEMA: \$1,962,572; State: \$5,779,000; Pro Emeritus College Foundation: \$693,842; Bond Interest and Cost of Is ** City of SM: 6,661,598; KCRW: \$5,844,950; State: \$40,088,000	-		; SCE: \$824,48	6; Gas Co.: \$106	5,262; Madison	Foundation: \$2,	992,576; KCRW:	\$958,462;			


#### SANTA MONICA COMMUNITY COLLEGE DISTRICT Bond Sales / Expenses Report As of June 30, 2017

Measure U Bond \$160,000,000		
Bond Issue Date		Amount
	2002	\$25,000,000
	2004	\$21,999,971
	2005	\$89,999,923
	2007	\$11,999,987
	2010	\$10,998,992
Total Available		\$159,998,873
Expenses as of 6-30-17		\$157,636,773
Total Available Remaining		\$2,362,100
Unsold Bond Amount		\$1,127
Total Available as of 7-1-17		\$2,363,227

Measure S Bond \$143,500,000 (1)		
Bond Issue Date		Amount
	2005	\$58,000,000
	2007	\$8,500,000
	2009	\$56,997,857
	2017	\$20,000,000
Total Available		\$143,497,857
Expenses as of 6-30-17		\$100,262,634
Total Available Remaining		\$43,235,223
Unsold Bond Amount		\$2,143
Total Available as of 7-1-17		\$43,237,366

Measure AA Bond \$295,000,000	
Bond Issue Date	Amount
2010	\$100,000,000
2014	\$144,995,829
2017	\$50,000,000
Total Available	\$294,995,829
Expenses as of 6-30-17	\$234,307,876
Total Available Remaining	\$60,687,953
Unsold Bond Amount	\$4,171
Total Available as of 7-1-17	\$60,692,124

Total Bond	\$598,500,000
Total Available	\$598,492,559
Total Expenses as of 6-30-17	\$492,207,283
Total Available Remaining	\$106,285,276
Total Unsold Bond	\$7,441

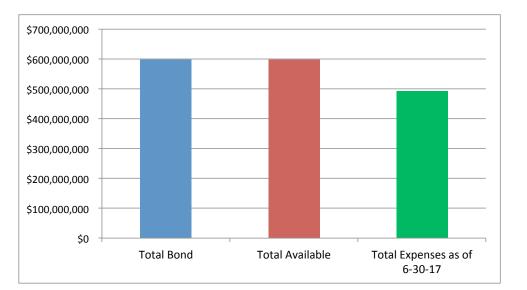


Interest	Measure U	Measure S	Measure AA
As of 6-30-17	\$6,993,502	\$10,705,497	\$5,532,013
Arbitrage Payment as of 6-30-17	\$0	\$420,037	\$0
Available Interest as of 6-30-17	\$6,993,502	\$10,285,460	\$5,532,013

Cost of Issuance Refund	Measure U	Measure S
As of 6-30-17	\$20,688	\$35,575

(1) Original Bond \$135,000,000.00, refunding on 2-15-07 received additional \$8,500,000.00

#### SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure U Bond Budget As of June 30, 2017

	Project Name	Completion	Project Budget	Measure U Allocation	Other Funding	Measure U Expenditures as of 6/30/17	Measure U Expenditures as of 3/31/17	Measure U Expenditures Last Period	Total Measure U Remaining
Α	Purchase of BAE Airport Site	Completed	\$30,280,878	\$30,280,878	\$0	\$30,280,878	\$30,280,878	\$0	\$0
В	Emeritus College Facility	Completed	\$9,603,782	\$8,909,940	\$693,842	\$8,909,940	\$8,909,940	\$0	\$0
С	Purchase of 1738 Pearl Street	Completed	\$749,208	\$749,208	\$0	\$749,208	\$749,208	\$0	\$0
D	PE Temp. Bldg. Replacement	Completed	\$2,797,033	\$2,797,033	\$0	\$2,797,033	\$2,797,033	\$0	\$0
Е	Remodel Library Village for Math	Completed	\$1,458,690	\$1,458,690	\$0	\$1,458,690	\$1,458,690	\$0	\$0
F	SM Airport Campus Site Improvements	Completed	\$4,170,264	\$4,170,264	\$0	\$4,170,264	\$4,170,264	\$0	\$0
G	SM Airport Campus West Building	Completed	\$19,709,741	\$19,709,741	\$0	\$19,709,741	\$19,709,741	\$0	\$0
Н	Theater Arts Renovation	Completed	\$19,544,314	\$19,544,314	\$0	\$19,544,314	\$19,544,314	\$0	
1	Earthquake Rpl. Liberal Arts North	Completed	\$12,507,725	\$6,011,584	\$6,496,141	\$6,011,584	\$6,505,400	-\$493,816	\$0
J	Music Complex	Completed	\$4,629,484	\$2,011,371	\$2,618,113	\$2,011,371	\$2,011,371	\$0	\$0
K	Earthquake Rpl. Liberal Arts South	Completed	\$16,733,220	\$6,108,150	\$10,625,070	\$6,108,150	\$6,108,150	\$0	\$0
L	Shuttle Replacement Parking	Completed	\$18,969,509	\$18,969,509	\$0	\$18,969,509	\$18,969,509	\$0	\$0
М	North Quad Plaza	Completed	\$11,388,463	\$11,388,463	\$0	\$11,388,463	\$11,388,463	\$0	\$0
N	Letters & Sci Demo/Restore	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0	Student Services Building	March 2019	\$130,224,164	\$21,132,262	\$109,091,902	\$18,769,035	\$18,593,781	\$175,254	\$2,363,227
Р	Science Complex Addition	Completed	\$90,401,286	\$308,336	\$90,092,950	\$308,336	\$308,336	\$0	\$0
Q	Infrastructure & Safety	Completed	\$4,003,084	\$4,003,084	\$0	\$4,003,084	\$4,003,084	\$0	\$0
R	Restroom Improvements	Completed	\$17,501	\$17,501	\$0	\$17,501	\$17,501	\$0	\$0
S	Master Planning	Completed	\$2,110,430	\$2,110,430	\$0	\$2,110,430	\$2,110,430	\$0	\$0
Т	14th and Pico Project	Completed	\$319,242	\$319,242	\$0	\$319,242	\$319,242	\$0	\$0
	Project Totals		\$379,618,018	\$160,000,000	\$219,618,018	\$157,636,773	\$157,955,335	-\$318,562	\$2,363,227

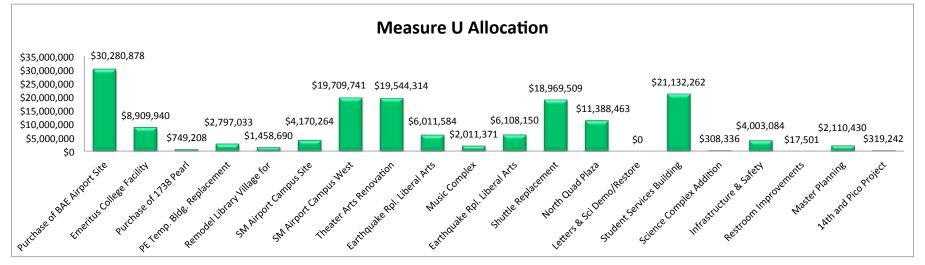

# SANTA MONICA COMMUNITY COLLEGE DISTRICT

# Measure U Bond Budget History

as of June 30, 2017


	Project Name	Completion	Preliminary Measure U Budget	Measure U Budget as of 3/31/17	Measure U Budget as of 6/30/17	Variance	Measure U Remaining as of 6/30/17
А	Purchase of BAE Airport Site	Completed	\$30,000,000	\$30,280,878	\$30,280,878	\$0	\$0
В	Emeritus College Facility	Completed	\$8,883,381	\$8,909,940	\$8,909,940	\$0	\$0
С	Purchase of 1738 Pearl Street	Completed	\$749,208	\$749,208	\$749,208	\$0	\$0
D	PE Temp. Bldg. Replacement	Completed	\$2,673,247	\$2,797,033	\$2,797,033	\$0	\$0
Е	Remodel Library Village for Math	Completed	\$1,425,565	\$1,458,690	\$1,458,690	\$0	\$0
F	SM Airport Campus Site Improvements	Completed	\$6,200,000	\$4,170,264	\$4,170,264	\$0	\$0
G	SM Airport Campus West Building	Completed	\$20,071,124	\$19,709,741	\$19,709,741	\$0	\$0
Н	Theater Arts Renovation	Completed	\$16,992,296	\$19,544,314	\$19,544,314	\$0	\$0
1	Earthquake Rpl. Liberal Arts North	Completed	\$5,352,752	\$6,505,400	\$6,011,584	-\$493,816	\$0
J	Music Complex	Completed	\$4,802,537	\$2,011,371	\$2,011,371	\$0	\$0
К	Earthquake Rpl. Liberal Arts South	Completed	\$2,863,566	\$6,108,150	\$6,108,150	\$0	\$0
L	Shuttle Replacement Parking	Completed	\$17,256,000	\$18,969,509	\$18,969,509	\$0	\$0
Μ	North Quad Plaza	Completed	\$3,939,759	\$11,388,463	\$11,388,463	\$0	\$0
Ν	Letters & Sci Demo/Restore	Completed	\$1,192,250	\$0	\$0	\$0	\$0
0	Student Services Building	March 2019	\$23,952,004	\$20,638,446	\$21,132,262	\$493,816	\$2,363,227
Р	Science Complex Addition	Completed	\$10,613,910	\$308,336	\$308,336	\$0	\$0
Q	Infrastructure & Safety	Completed	\$5,000,000	\$4,003,084	\$4,003,084	\$0	\$0
R	Restroom Improvements	Completed	\$400,000	\$17,501	\$17,501	\$0	\$0
S	Master Planning	Completed	\$500,000	\$2,110,430	\$2,110,430	\$0	\$0
Т	14th and Pico Project	Completed	\$14,662,000	\$319,242	\$319,242	\$0	\$0
	Project Totals		\$177,529,599	\$160,000,000	\$160,000,000	\$0	\$2,363,227

#### SANTA MONICA COMMUNITY COLLEGE DISTRICT

Measure S Bond Budget

As of June 30, 2017

	Project Name	Completion	Project Budget	Measure S Allocation	Other Funding	Measure S Expenditures as of 6/30/17	Measure S Expenditures as of 3/31/17	Measure S Expenditures Last Period	Total Measure S Remaining
1	Athletic Fields Phase I, Corsair Field	Completed	\$4,440,065	\$4,372,535	\$67,530	\$4,372,535	\$4,372,535	\$0	\$0
1A	Athletic Fields Phase I, John Adams	Completed	\$2,969,807	\$2,969,807	\$0	\$2,969,807	\$2,969,807	\$0	\$0
2	Performing Arts Complex	Completed	\$40,690,201	\$37,697,625	\$2,992,576	\$37,697,625	\$37,697,625	\$0	\$0
3	Career Opportunity Center	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	June 2017	\$58,272,030	\$11,603,383	\$46,668,647	\$11,603,383	\$11,603,383	\$0	\$0
5	Early Childhood Development/Childcare	September 2019	\$15,520,176	\$7,000,000	\$8,520,176	\$1,119,864	\$1,095,906	\$23,958	\$5,880,136
6	Malibu Site Acquisition and Facility	September 2019	\$25,000,000	\$25,000,000	\$0	\$7,585,402	\$7,561,052	\$24,350	\$17,414,598
7	Energy Efficiency Projects	Completed	\$510,683	\$293,361	\$217,322	\$293,361	\$293,361	\$0	\$0
8	Satellite Campus Parking Facilities and Roadway Improvements	Deferred	\$7,022,417	\$3,891,747	\$3,130,670	\$3,891,747	\$3,891,747	\$0	\$0
9	Parking Garage, Grounds and Equipment - Student Services	March 2019	\$130,224,164	\$47,456,043	\$82,768,121	\$27,737,831	\$19,741,170	\$7,996,661	\$19,718,212
10	Pico Promenade Improvements	Completed	\$1,018,009	\$1,018,009	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	Completed	\$716,428	\$716,428	\$0	\$716,428	\$716,428	\$0	\$0
12	Other Bond Related Expenses	On-Going	\$609,282	\$609,282	\$0	\$384,862	\$381,080	\$3,782	\$224,420
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	Completed	\$45,597	\$45,597	\$0	\$45,597	\$45,597	\$0	\$0
15	Signage Safety/Information	Completed	\$706,713	\$706,713	\$0	\$706,713	\$705,408	\$1,305	\$0
16	Cost of Issuance	On-Going	\$119,470	\$119,470	\$0	\$119,470	\$0	\$119,470	\$0
	Project Totals		\$287,865,042	\$143,500,000	\$144,365,042	\$100,262,634	\$92,093,108	\$8,169,526	\$43,237,366

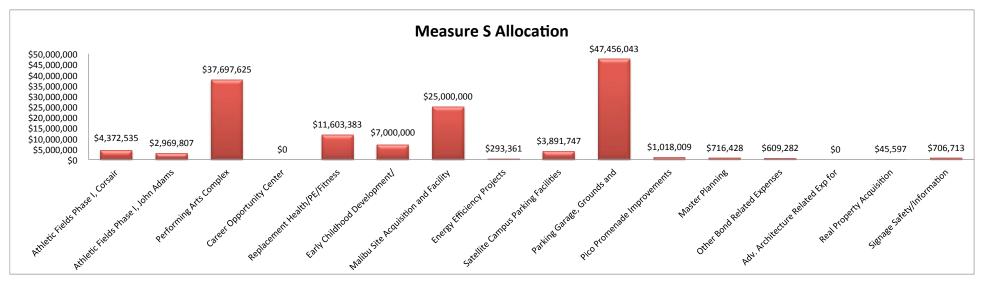


# SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure S Bond Budget History

as of June 30, 2017

	Project Name	Completion	Preliminary Measure S Budget	Measure S Budget as of 3/31/17	Measure S Budget as of 6/30/17	Variance	Measure S Remaining as of 6/30/17
1	Athletic Fields Phase I, Corsair Field	Completed	\$1,800,000	\$4,372,535	\$4,372,535	\$0	\$0
1A	Athletic Fields Phase I, John Adams	Completed	\$35,200,000	\$2,969,807	\$2,969,807	\$0	\$0
2	Performing Arts Complex	Completed	\$24,000,000	\$37,697,625	\$37,697,625	\$0	\$0
3	Career Opportunity Center	Completed	\$20,000,000	\$0	\$0	\$0	\$0
4	Replacement Health/PE/Fitness Building	June 2017	\$20,000,000	\$11,603,383	\$11,603,383	\$0	\$0
5	Early Childhood Development/Childcare	September 2019	\$7,000,000	\$7,000,000	\$7,000,000	\$0	\$5,880,136
6	Malibu Site Acquisition and Facility	September 2019	\$25,000,000	\$25,000,000	\$25,000,000	\$0	\$17,414,598
7	Energy Efficiency Projects	Completed	\$2,000,000	\$293,361	\$293,361	\$0	\$0
8	Satellite Campus Parking Facilities and Roadway Improvements	Deferred	\$0	\$3,891,747	\$3,891,747	\$0	\$0
9	Parking Garage, Grounds and Equipment - Student Services	March 2019	\$0	\$47,456,533	\$47,456,043	-\$490	\$19,718,212
10	Pico Promenade Improvements, Phase I	Completed	\$0	\$1,018,009	\$1,018,009	\$0	\$0
11	Master Planning	Completed	\$0	\$716,428	\$716,428	\$0	\$0
12	Other Bond Related Expenses	On-Going	\$0	\$609,282	\$609,282	\$0	\$224,420
13	Adv. Architecture Related Exp for AA	Completed	\$0	\$0	\$0	\$0	\$0
14	Real Property Acquisition	Completed	\$0	\$45,597	\$45,597	\$0	\$0
15	Signage Safety/Information	Completed	\$0	\$706,223	\$706,713	\$490	\$0
16	Cost of Issuance	On-Going	\$0	\$119,470	\$119,470	\$0	\$0
	Project Totals		\$135,000,000	\$143,500,000	\$143,500,000	\$0	\$43,237,366

#### SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget As of June 30, 2017

	Project Name	Completion	Project Budget	Measure AA Allocation	Other Funding	Measure AA Expenditures as of 6/30/17	Measure AA Expenditures as of 3/31/17	Measure AA Expenditures Last Period	Total Measure AA Remaining
101	Environmental Performance - Central Plant Connections	August 2017	\$11,206,164	\$11,206,164	\$0	\$10,127,475	\$8,893,242	\$1,234,233	\$1,078,689
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$23,160,569	\$23,160,569	\$0	\$23,160,569	\$23,145,587	\$14,982	\$0
103	Media and Technology Complex - Academy Site	December 2017	\$110,055,056	\$103,219,665	\$6,835,391	\$92,991,550	\$82,790,943	\$10,200,607	\$10,228,115
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	December 2017	\$58,272,030	\$46,459,800	\$11,812,230	\$38,335,136	\$35,361,758	\$2,973,378	\$8,124,664
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	Deferred	\$13,005,082	\$5,082	\$13,000,000	\$5,082	\$5,082	\$0	\$0
106	Replacement Math and Science Extension Building	In Planning	\$90,401,286	\$1,244,008	\$89,157,278	\$5,750	\$4,950	\$800	\$1,238,258
107	Madison East Wing Seismic Upgrade	Completed	\$27,608,816	\$27,608,816	\$0	\$26,022,094	\$24,718,409	\$1,303,685	\$1,586,722
108	Renovation of Corsair Stadium	Completed	\$35,299	\$35,299	\$0	\$35,299	\$35,299	\$0	\$0
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$0	\$0	\$0	\$0	\$0	\$0	\$0
110	Malibu Center	September 2019	\$25,000,000	\$0	\$25,000,000	\$0	\$0	\$0	\$0
111	Business & Facilities Infrastructure	Completed	\$1,968,124	\$1,968,124	\$0	\$1,968,124	\$1,968,124	\$0	\$0
112	Master Planning, Program Management, Overhead	On-Going	\$750,000	\$750,000	\$0	\$452,564	\$246,945	\$205,619	\$297,436
113	Energy Efficiency Projects	Completed	\$3,508,088	\$3,016,773	\$491,315	\$3,016,773	\$3,016,773	\$0	\$0
114	Community Classroom & Facility Projects	Completed	\$3,162,183	\$3,162,183	\$0	\$3,162,183	\$3,162,183	\$0	\$0
115	Real Property Acquisition	Completed	\$24,902,902	\$24,902,902	\$0	\$19,816,127	\$19,852,902	-\$36,775	\$5,086,775
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Deferred	\$7,022,417	\$2,130,670	\$4,891,747	\$2,130,670	\$2,130,670	\$0	\$0
117	Infrastructure & Technology - Technology	Completed	\$2,434,417	\$2,434,417	\$0	\$2,434,417	\$2,434,417	\$0	\$0
118	Infrastructure & Technology - Utility	Completed	\$27,753	\$27,753	\$0	\$27,753	\$27,753	\$0	\$0
119	Emergency Lighting, Fire Alarm, and Security System	On-Going	\$11,520,794	\$11,520,794	\$0	\$10,118,284	\$9,516,066	\$602,218	\$1,402,510
120	Student Services	March 2019	\$130,224,164	\$30,944,318	\$99,279,846	\$0	\$0	\$0	\$30,944,318
121	Cost of Issuance	On-Going	\$498,026	\$498,026	\$0	\$498,026	\$285,000	\$213,026	\$0
	Management Reserve	On-Going	\$208,847	\$704,637	\$0	\$0	\$0	\$0	\$704,637
	Project Totals		\$544,763,170	\$295,000,000	\$250,467,807	\$234,307,876	\$217,596,103	\$16,711,773	\$60,692,124



# SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Bond Budget History as of June 30, 2017

	Project Name	Completion	Preliminary Measure AA	Measure AA Budget as of	Measure AA Budget as of	Variance	Measure AA Remaining as
101	Fruite amontal Defermence Control Dight Connections	August 2017	Budget	<b>3/31/17</b>	6/30/17	ćo	of 6/30/17
101	Environmental Performance - Central Plant Connections	August 2017	\$12,034,042		\$11,206,164	\$0	1 /= =/===
102	Infrastructure & Technology - Information Technology Relocation	Completed	\$13,287,218		\$23,160,569	-\$1,239,058	
103	Media and Technology Complex - Academy Site	July 2017		\$103,219,665	\$103,219,665	\$0	. , ,
104	Replacement Health/PE/Fitness/ Dance Building with Central Plant	December 2017	\$29,232,317		\$46,459,800	-\$18,000	
105	Drescher - Academic Modernization, Bookstore, Pico Promenade II	Deferred	\$34,026,480	. ,	\$5,082	\$0	
106	Replacement Math and Science Extension Building	In Planning	\$68,259,000	\$4,950	\$1,244,008	\$1,239,058	\$1,238,258
107	Madison East Wing Seismic Upgrade	Completed	\$6,146,000	\$27,608,816	\$27,608,816	\$0	\$1,586,722
108	Renovation of Corsair Stadium	Completed	\$11,203,000	\$35,299	\$35,299	\$0	\$(
109	Career Opportunity and Advancement Center (Bundy)	Completed	\$32,384,000	\$0	\$0	\$0	\$(
110	Malibu Center	September 2019	\$6,069,031	\$0	\$0	\$0	\$(
111	Business & Facilities Infrastructure	Completed	\$17,506,952	\$1,968,124	\$1,968,124	\$0	\$(
112	Master Planning, Program Management, Overhead	On-Going	\$2,000,000	\$750,000	\$750,000	\$0	\$297,430
113	Energy Efficiency Projects	Completed	\$5,371,136	\$3,016,773	\$3,016,773	\$0	\$
114	Community Classroom & Facility Projects	Completed	\$0	\$3,162,183	\$3,162,183	\$0	\$(
115	Real Property Acquisition	Completed	\$0		\$24,902,902	\$0	\$5,086,77
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Deferred	\$0		\$2,130,670	\$0	\$
117	Infrastructure & Technology - Technology	Completed	\$0		\$2,434,417	\$0	\$(
118	Infrastructure & Technology - Utility	Completed	\$0		\$27,753	\$0	\$(
119	Emergency Lighting, Fire Alarm, and Security System	On-Going	\$0		\$11,520,794	\$0	
120	Student Services	March 2017	\$0	. , ,	\$30,944,318	-\$493,816	. , ,
121	Cost of Issuance	On-Going	\$0		\$498,026	-\$1,974	\$(
	Management Reserve	On-Going	\$0		\$704,637	\$513,790	
	Project Totals		\$295.000.000	\$295,000,000	\$295,000,000	\$0	

### SANTA MONICA COMMUNITY COLLEGE DISTRICT

# Measure U Project Schedule As of June 30, 2017

	Project Name	Completion	2014	2015	2016	2017	2018	2019
А	Purchase of BAE Airport Site	Completed						
В	Emeritus College Facility	Completed						
С	Purchase of 1738 Pearl Street	Completed						
D	PE Temp. Bldg. Replacement	Completed						
Е	Remodel Library Village for Math	Completed						
F	SM Airport Campus Site Improvements	Completed						
G	SM Airport Campus West Building	Completed						
н	Theater Arts Renovation	Completed						
- I	Earthquake Rpl. Liberal Arts North	Completed						
J	Music Complex	Completed						
К	Earthquake Rpl. Liberal Arts South	Completed						
L	Shuttle Replacement Parking	Completed						
М	North Quad Plaza	Completed						
Ν	Letters & Sci Demo/Restore	Completed						
0	Student Services Building	March 2019						
Р	Science Complex Addition	Completed						
Q	Infrastructure & Safety	Completed						
R	Restroom Improvements	Completed						
S	Master Planning	Completed						
Т	14th and Pico Project	Completed						
	* SM Airport Campus also known as Bundy	Site	In Co	nstruction				

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
110/000	Duugot	02.0011114	00.0111111	e nee i mai		00/07 1 11/01	• · · · · · · · · · · · · · · ·		00,101,114					1.0.101.0.00		10/11/11/04	oombinou rotalo
U7100010																	
Purchase of BAE Airport Site (A)																	
Site Acquisition		\$0	\$0	\$0	\$30,280,878	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$30,280,878
Total		\$0			\$30,280,878	\$0			\$0						\$0		
Project Budget	\$30,280,878				1.1.1.1.1.1.1.1												1
Less Other Funding	\$0																
Net	\$30,280,878																
Actual Measure U Expenditures	\$30,280,878																
Running Balance	\$0																
v																	
U7100028							1										
Emeritus College Facility (B)																	
Site Acquisition		\$8,658,675	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$8,658,675
Legal		\$14,649	\$3,009	\$20,421	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$38,078
Architect		\$93,735	\$27,831	\$161	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$121,727
Engineering		\$18,400	\$0	\$0		\$0			\$0			\$0			\$0	\$0	
Supply		\$0	\$4,461	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,461
Building & Additions		\$0	\$17,496	\$0	\$4,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$21,496
Cap Equipment		\$0	\$49,406	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$49,406
Non-Cap Equipment		\$0	-\$2,197	\$0	-\$108	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0	-\$2,305
Total		\$8,785,459	\$100,007	\$20,582	\$3,892	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$8,909,940
Project Budget	\$9,603,782	Received															
Less Other Funding*	\$693,842	\$693,842		* Other Fundin	g Source:												
Net	\$8,909,940			Emeritus Colle	ge Foundation	\$693,842 recei	ved										
Actual Measure U Expenditures	\$8,909,940				•												
Running Balance	\$0																
	•																
U7100006																	
1738 Pearl Street (C)																	
Site Acquisition		\$0	\$704,534	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$704,534
Site Improvement		\$0		\$0		\$0		\$0	\$0				\$0		\$0	\$0	
Building & Additions		\$0		\$0		\$0									\$0		
Total		\$0		\$0		\$0											
Project Budget	\$749,208																
Less Other Funding	\$0	1															
Net	\$749,208	1															
Actual Measure U Expenditures	\$749,208	1															
Running Balance	\$0	1															

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
U7100026																	
PE Temporary Building Replacement (D)																	
Architect		\$148,055	\$42,372	\$6,220		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0				
Building & Additions		\$43,866	\$1,922,493	\$415,932		\$0	\$0										
Inspection & Testing		\$6,455	\$136,510	\$716	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0				
Project Management		\$4,800	\$56,247	\$5,225	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0				
Advertising and Moving Expenses		\$763	\$0	\$6,893		\$0	\$0										
Total		\$203,939	\$2,157,622	\$434,987	\$485	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,797,033
Project Budget	\$2,797,033																
Less Other Funding	\$0																
Net	\$2,797,033																
Actual Measure U Expenditures	\$2,797,033																
Running Balance	\$0																
U7100310																	
Remodel Library Village for Math (E)																	
Moving Exp.		\$0	\$38,625	\$0	\$0	\$0	\$0		\$0			\$0					
Building & Additions		\$0	\$1,036,490	\$115,653		\$0	\$0		\$0	\$0		\$0		\$0	\$0	\$0	
Architect		\$104,992	\$27,141	\$1,340		\$0	\$0			\$0		\$0					
Engineering		\$0	\$2,658	\$0	\$0	\$0	\$0				\$0		\$0				
Inspection & Testing		\$0	\$27,083	\$25,175		\$0	\$0					\$0					
Project Management		\$0	\$51,679	\$4,400		\$0	\$0					\$0					
Advertising and Moving Expenses		\$207	\$10,137	\$12,623		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0				
Total		\$105,199	\$1,193,813	\$159,191	\$486	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,458,690
Project Budget	\$1,458,690																
Less Other Funding	\$0																
Net	\$1,458,690																
Actual Measure U Expenditures	\$1,458,690																
Running Balance	\$0																


Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
	-																
U7100027																	
SM Airport Campus Site Improvements (F)																	
Supplies		\$0		\$975		\$0	\$0			\$0		\$0	\$0			\$0	
Misc Fees		\$0		\$0	\$0	\$34,274	\$0		\$0	\$0	ψŪ	\$0	\$0			\$0	
Other Contract Services		\$3,860	\$11,508	\$8,434	\$1,501	\$0	\$0		\$0	\$0		\$0	\$0			\$0	
Site Improvement		\$0			\$5,790	\$7,237	\$0			\$0			\$0			\$0	
Building & Additions		\$0			\$4,824	\$0	\$0			\$0			\$0			\$0	
Architect		\$104,934		\$0	\$43,570	\$0			\$0	\$0							
Engineering		\$35,000	\$148,304	\$950	\$10,040	\$0			\$0	\$0			\$0				
Inspection & Testing		\$5,032	\$118,662	\$191,271			\$0			\$0			\$0				
Project Management		\$750	\$155,798	\$38,425		\$220	\$(			\$0			\$0				
City Fees, Advertising and Security System		\$16,587	\$1,802		\$150	\$4,375	\$0			\$0		\$0	\$0			\$0	
Total		\$166,163	\$1,958,530	\$1,926,352	\$73,113	\$46,106	\$(	50 \$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,170,264
Project Budget	\$4,170,264																
Less Other Funding	\$0																
Net	\$4,170,264																
Actual Measure U Expenditures	\$4,170,264																
Running Balance	\$4,170,204																
Running Balance																	
Running Balance U7110027 SM Airport Campus West Building (G)																	
Running Balance U7110027 SM Airport Campus West Building (G) Supply		\$0			\$28,017	\$0	\$(		\$0	\$0		\$0	\$0			\$0	
Running Balance U7110027 SM Airport Campus West Building (G) Supply Other Contract Services		\$0	\$0	\$0	\$3,576	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,576
Running Balance U7110027 SM Airport Campus West Building (G) Supply Other Contract Services Moving Expenses		\$0 \$0	\$0 \$0	\$0 \$180	\$3,576 \$15,824	\$0 \$0	\$0 \$0	0 \$0 0 \$0	\$0 \$0	\$3,576 \$16,004							
Running Balance U7110027 SM Airport Campus West Building (G) Supply Other Contract Services		\$0 \$0 \$0	\$0 \$0 \$0	\$0 \$180 \$15,037,532	\$3,576 \$15,824 \$1,256,065	\$0 \$0 \$46,946	\$0 \$0 \$0	0 \$0 0 \$0 0 \$0	\$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$0	\$3,576 \$16,004 \$16,340,543
Running Balance U7110027 SM Airport Campus West Building (G) Supply Other Contract Services Moving Expenses		\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$971,954	\$0 \$180 \$15,037,532 \$1,043,950	\$3,576 \$15,824 \$1,256,065 \$49,779	\$0 \$0 \$46,946 \$1,147	\$0 \$0 \$0 \$0 \$0	0 \$0 0 \$0 0 \$0 0 \$0 0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$3,576 \$16,004 \$16,340,543 \$2,066,830
Running Balance U7110027 SM Airport Campus West Building (G) Supply Other Contract Services Moving Expenses Building & Additions		\$0 \$0 \$0	\$0 \$0 \$971,954 \$2,920	\$0 \$180 \$15,037,532 \$1,043,950 \$9,800	\$3,576 \$15,824 \$1,256,065 \$49,779 \$5,010	\$0 \$0 \$46,946	\$0 \$0 \$0	\$0         \$0           \$0         \$0           \$0         \$0           \$0         \$0           \$0         \$0           \$0         \$0           \$0         \$0           \$0         \$0           \$0         \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$3,576 \$16,004 \$16,340,543 \$2,066,830 \$18,693
Running Balance U7110027 SM Airport Campus West Building (G) Supply Other Contract Services Moving Expenses Building & Additions Architect		\$0 \$0 \$0 \$0 \$0	\$0 \$0 \$971,954 \$2,920	\$0 \$180 \$15,037,532 \$1,043,950 \$9,800 \$126,510	\$3,576 \$15,824 \$1,256,065 \$49,779 \$5,010 \$9,856	\$0 \$0 \$46,946 \$1,147	\$0 \$0 \$0 \$0 \$0	\$0         \$0           \$0         \$0           \$0         \$0           \$0         \$0           \$0         \$0           \$0         \$0           \$0         \$0           \$0         \$0           \$0         \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0	\$3,576 \$16,004 \$16,340,543 \$2,066,830 \$18,693 \$157,539
Running Balance U7110027 SM Airport Campus West Building (G) Supply Other Contract Services Moving Expenses Building & Additions Architect Engineering Inspection & Testing Project Management		\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$971,954 \$2,920 \$21,173 \$14,450	\$0 \$180 \$15,037,532 \$1,043,950 \$9,800 \$126,510 \$313,715	\$3,576 \$15,824 \$1,256,065 \$49,779 \$5,010 \$9,856 \$13,956	\$0 \$0 \$46,946 \$1,147 \$963 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	b \$0 b \$0 b \$0 b \$0 b \$0 c \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$3,576 \$16,004 \$16,340,543 \$2,066,830 \$18,693 \$157,539 \$342,121
Running Balance U7110027 SM Airport Campus West Building (G) Supply Other Contract Services Moving Expenses Building & Additions Architect Engineering Inspection & Testing		\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$971,954 \$2,920 \$21,173 \$14,450	\$0 \$180 \$15,037,532 \$1,043,950 \$9,800 \$126,510 \$313,715 \$326,382	\$3,576 \$15,824 \$1,256,065 \$49,779 \$5,010 \$9,856 \$13,956 \$4,792	\$0 \$0 \$46,946 \$1,147 \$963 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$3,576 \$16,004 \$16,340,543 \$2,066,830 \$18,693 \$157,539 \$342,121 \$380,969
Running Balance U7110027 SM Airport Campus West Building (G) Supply Other Contract Services Moving Expenses Building & Additions Architect Engineering Inspection & Testing Project Management		\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$971,954 \$2,920 \$21,173 \$14,450 \$49,795	\$0 \$180 \$15,037,532 \$1,043,950 \$9,800 \$126,510 \$313,715	\$3,576 \$15,824 \$1,256,065 \$49,779 \$5,010 \$9,856 \$13,956	\$0 \$0 \$46,946 \$1,147 \$963 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$3,576 \$16,004 \$16,340,543 \$2,066,830 \$18,693 \$157,539 \$342,121 \$380,969 \$337,798
Running Balance U7110027 SM Airport Campus West Building (G) Supply Other Contract Services Moving Expenses Building & Additions Architect Engineering Inspection & Testing Project Management Cap Equipment		\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$971,954 \$2,920 \$21,173 \$14,450 \$49,795 \$0	\$0 \$180 \$15,037,532 \$1,043,950 \$9,800 \$126,510 \$313,715 \$326,382	\$3,576 \$15,824 \$1,256,065 \$49,779 \$5,010 \$9,856 \$13,956 \$4,792 \$57,240	\$0 \$0 \$46,946 \$1,147 \$963 \$0 \$0 \$0 \$0	\$ \$( \$( \$( \$( \$( \$( \$( \$( \$( \$( \$() \$()	0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$3,576 \$16,004 \$16,340,543 \$2,066,830 \$18,693 \$157,539 \$342,121 \$380,969 \$337,798
Running Balance U7110027 SM Airport Campus West Building (G) Supply Other Contract Services Moving Expenses Building & Additions Architect Engineering Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Non-Cap Equipment		\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$971,954 \$2,920 \$21,173 \$14,450 \$49,795 \$0	\$0 \$180 \$15,037,532 \$1,043,950 \$9,800 \$126,510 \$313,715 \$326,382 \$280,558	\$3,576 \$15,824 \$1,256,065 \$49,779 \$5,010 \$9,856 \$13,956 \$4,792 \$57,240	\$0 \$0 \$46,946 \$1,147 \$963 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$3,576 \$16,004 \$16,340,543 \$2,066,830 \$18,693 \$157,539 \$342,121 \$380,969 \$337,798							
Running Balance U7110027 SM Airport Campus West Building (G) Supply Other Contract Services Moving Expenses Building & Additions Architect Engineering Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total	\$0 	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$971,954 \$2,920 \$21,173 \$14,450 \$49,795 \$0	\$0 \$180 \$15,037,532 \$1,043,950 \$9,800 \$126,510 \$313,715 \$326,382 \$280,558	\$3,576 \$15,824 \$1,256,065 \$49,779 \$5,010 \$9,856 \$13,956 \$4,792 \$57,240	\$0 \$0 \$46,946 \$1,147 \$963 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$3,576 \$16,004 \$16,340,543 \$2,066,830 \$18,693 \$157,539 \$342,121 \$380,969 \$337,798							
Running Balance U7110027 SM Airport Campus West Building (G) Supply Other Contract Services Moving Expenses Building & Additions Architect Engineering Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Total Project Budget	\$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$971,954 \$2,920 \$21,173 \$14,450 \$49,795 \$0	\$0 \$180 \$15,037,532 \$1,043,950 \$9,800 \$126,510 \$313,715 \$326,382 \$280,558	\$3,576 \$15,824 \$1,256,065 \$49,779 \$5,010 \$9,856 \$13,956 \$4,792 \$57,240	\$0 \$0 \$46,946 \$1,147 \$963 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$3,576 \$16,004 \$16,340,543 \$2,066,830 \$18,693 \$157,539 \$342,121 \$380,969 \$337,798							
Running Balance U7110027 SM Airport Campus West Building (G) Supply Other Contract Services Moving Expenses Building & Additions Architect Engineering Inspection & Testing Project Management Cap Equipment Non-Cap Equipment Non-Cap Equipment Total Project Budget Less Other Funding	\$19,709,741	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$971,954 \$2,920 \$21,173 \$14,450 \$49,795 \$0	\$0 \$180 \$15,037,532 \$1,043,950 \$9,800 \$126,510 \$313,715 \$326,382 \$280,558	\$3,576 \$15,824 \$1,256,065 \$49,779 \$5,010 \$9,856 \$13,956 \$4,792 \$57,240	\$0 \$0 \$46,946 \$1,147 \$963 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0           0         \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$3,576 \$16,004 \$16,340,543 \$2,066,830 \$18,693 \$157,539 \$342,121 \$380,969 \$337,798							

Projects	Budget	02/03 Final	03/04 Einal	04/05 Einal	05/06 Final	06/07 Final	07/08 Einal	08/09 Einal	00/10 Einal	10/11 Einal	11/12 Einal	12/13 Einal	13/14 Einal	14/15 Einal	15/16 Einal	16/17 Final	Combined Totals
110/000	Budget	02/00111101	00/04111101	04/00111101	00/00111101	oo,or mia	enree i mai j	oo,oo i mar	oo/rorman	10/11/11/11	10/12 1 11/0	12/10/11/14	10/14111101	14/10111101	10/10 milai	10/17 1 1101	oombilied lotais
U7100025																	
Theatre Arts Renovation (H)																	
Supplies		\$0	\$8,904	-\$14	\$12,858	\$16,619	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$38,367
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Moving Services		\$0	\$0	\$0	\$0	\$14,061	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$14,061
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$5,245	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$5,245
Rental / Lease		\$0	\$1,446	\$2,200	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,646
Building & Additions		\$528	\$1,326,630	\$4,540,487	\$10,897,603	\$56,122	\$25,220	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$16,846,590
Architect		\$289,913	\$369,213	\$423,416	\$82,639	\$0	\$0	\$0		\$0	\$0	\$0	\$47,365	\$0		\$0	
Engineering		\$6,174	\$2,981	\$16,606	\$2,375	\$1,250	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Inspection & Testing		\$150	\$14,785	\$353,890	\$297,675	\$1,116	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$667,616
Project Management		\$150	\$45,698	\$184,219	\$193,898	\$14,818	\$230	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$439,013
Cleaning, Storage and Installation		\$0	\$812	\$0	\$2,548	\$2,267	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$5,627
Cap Equipment		\$0	\$31,638	\$0	\$6,458	\$59,689	\$0	\$0		\$0		\$0	\$0	\$0	\$0	\$0	
Non-Cap Equipment		\$0	\$2,388	\$0		\$145,294	\$0	\$0		\$0		\$0	\$0			\$0	
Total		\$296,915	\$1,804,496	\$5,520,804	\$11,532,803	\$311,236	\$25,450	\$5,245	\$0	\$0	\$0	\$0	\$47,365	\$0	\$0	\$0	\$19,544,314
Project Budget	\$19,544,314																
Less Other Funding	\$0																
Net	\$19,544,314																
, , , , , , , , , , , , , , , , , , ,	\$19,544,314 \$19,544,314																
Net																	
Net Actual Measure U Expenditures Running Balance	\$19,544,314																
Net Actual Measure U Expenditures Running Balance U7100110	\$19,544,314																
Net Actual Measure U Expenditures Running Balance	\$19,544,314																
Net Actual Measure U Expenditures Running Balance U7100110	\$19,544,314	\$0	\$0	\$0		\$1,408	\$0	\$75		\$0		\$0	\$0		\$0	\$0	
Net - Actual Measure U Expenditures Running Balance U7100110 Earthquake Rpl. Liberal Arts North (I) Supplies Legal	\$19,544,314	\$0	\$0	\$0	\$0	\$887	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$887
Net Actual Measure U Expenditures Running Balance U7100110 Earthquake Rpl. Liberal Arts North (I) Supplies Legal Other Contract Services	\$19,544,314	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$887 \$75	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$887 \$75
Net - Actual Measure U Expenditures Running Balance U7100110 Earthquake Rpl. Liberal Arts North (I) Supplies Legal	\$19,544,314	\$0	\$0 \$0 \$0	\$0 \$0 \$1,043,660	\$0	\$887 \$75 -\$973,001	\$0 \$0 \$321,345	\$0 \$0 \$14,898	\$0 \$0 \$0	\$0	\$0 \$0 \$0	\$0	\$0 \$0 \$0	\$0 \$0 \$0	\$0 \$0 \$0	\$0	\$887 \$75 \$3,867,060
Net Actual Measure U Expenditures Running Balance U7100110 Earthquake Rpl. Liberal Arts North (I) Supplies Legal Other Contract Services	\$19,544,314	\$0 \$0 \$265 \$0	\$0 \$0 \$0 \$0 \$611,732	\$0 \$0	\$0 \$0 \$5,916,281 \$209,490	\$887 \$75	\$0 \$0 \$321,345 \$21,215	\$0 \$0 \$14,898 \$3,465	\$0 \$0 \$0 \$0	\$0 \$0 -\$834,764 \$0	\$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$1,127,809 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 -\$493,816 \$0	\$887 \$75 \$3,867,060 \$1,165,289
Net S Actual Measure U Expenditures Running Balance U7100110 Earthquake Rpl. Liberal Arts North (I) Supplies Legal Other Contract Services Building & Additions	\$19,544,314	\$0 \$0 \$265	\$0 \$0 \$0	\$0 \$0 \$1,043,660	\$0 \$0 \$5,916,281	\$887 \$75 -\$973,001	\$0 \$0 \$321,345	\$0 \$0 \$14,898	\$0 \$0 \$0	\$0 \$0 -\$834,764	\$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$1,127,809	\$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0	\$0 \$0 -\$493,816	\$887 \$75 \$3,867,060 \$1,165,289
Net Actual Measure U Expenditures Running Balance U7100110 Earthquake Rpl. Liberal Arts North (I) Supplies Legal Other Contract Services Building & Additions Architect Engineering Inspection & Testing	\$19,544,314	\$0 \$0 \$265 \$0 \$3,248 \$0	\$0 \$0 \$611,732 \$4,295 \$0	\$0 \$0 \$1,043,660 \$102,824 \$0 \$28,312	\$0 \$0 \$5,916,281 \$209,490	\$887 \$75 -\$973,001 \$216,563 \$0 \$77,942	\$0 \$0 \$321,345 \$21,215 \$250 \$0	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 -\$834,764 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$1,127,809 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$493,816 \$0 \$0 \$0 \$0	\$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458
Net Actual Measure U Expenditures Running Balance U7100110 Earthquake Rpl. Liberal Arts North (I) Supplies Legal Other Contract Services Building & Additions Architect Engineering	\$19,544,314	\$0 \$0 \$265 \$0 \$3,248	\$0 \$0 \$611,732 \$4,295	\$0 \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549	\$0 \$0 \$5,916,281 \$209,490 \$250	\$887 \$75 -\$973,001 \$216,563 \$0	\$0 \$0 \$321,345 \$21,215 \$250 \$0 \$255	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$0 \$1,155	\$0 \$0 \$0 \$0 \$0 \$0 \$286	\$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$493,816 \$0 \$0 \$0 \$0 \$0 \$0	\$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 \$314,475
Net Actual Measure U Expenditures Running Balance U7100110 Earthquake Rpl. Liberal Arts North (I) Supplies Legal Other Contract Services Building & Additions Architect Engineering Inspection & Testing	\$19,544,314	\$0 \$265 \$0 \$3,248 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$611,732 \$4,295 \$0 \$26,072 -\$4	\$0 \$0 \$1,043,660 \$102,824 \$0 \$28,312	\$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0	\$887 \$75 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 \$0	\$0 \$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$286 \$0	\$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$493,816 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,456 \$314,475 \$7,330
Net     -       Actual Measure U Expenditures       Running Balance       U7100110       Earthquake Rpl. Liberal Arts North (i)       Supplies       Legal       Other Contract Services       Building & Additions       Architect       Engineering       Inspection & Testing       Project Management       Advertising and Fees       Cap-Equipment	\$19,544,314	\$0 \$0 \$265 \$3,248 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$611,732 \$4,295 \$0 \$0 \$26,072 -\$4 \$0	\$0 \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 \$0	\$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$0 \$0	\$887 \$75 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 \$0 \$25,356	\$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0 \$12,579	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$286 \$0 \$286 \$0 \$0	\$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$493,816 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 \$314,475 \$7,330 \$37,935
Net Summer U Expenditures Actual Measure U Expenditures Running Balance U7100110 Earthquake Rpl. Liberal Arts North (I) Legal Other Contract Services Building & Additions Architect Engineering Inspection & Testing Project Management Advertising and Fees	\$19,544,314	\$0 \$265 \$0 \$3,248 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$611,732 \$4,295 \$0 \$26,072 -\$4 \$0 \$0 \$0 \$0	\$0 \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 \$7,334 \$0 \$0 \$0	\$0 \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$0 \$2,033	\$887 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 \$0 \$25,356 \$170,425	\$0 \$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0 \$12,579 \$4,093	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$286 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$493,816 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 \$314,475 \$7,330 \$37,935 \$176,550
Net     -       Actual Measure U Expenditures       Running Balance       U7100110       Earthquake Rpl. Liberal Arts North (I)       Supplies       Legal       Other Contract Services       Building & Additions       Architect       Engineering       Inspection & Testing       Project Management       Advertising and Fees       Cap-Equipment	\$19,544,314 \$0	\$0 \$0 \$265 \$3,248 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$611,732 \$4,295 \$0 \$0 \$26,072 -\$4 \$0	\$0 \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 \$7,334 \$0 \$0 \$0	\$0 \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$0 \$2,033	\$887 \$75 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 \$0 \$25,356	\$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0 \$12,579	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$286 \$0 \$286 \$0 \$0	\$0 \$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$493,816 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 \$314,475 \$7,330 \$37,935 \$176,550
Net     Actual Measure U Expenditures       Running Balance       U7100110       Earthquake Rpl. Liberal Arts North (I)       Supplies       Legal       Other Contract Services       Building & Additions       Architect       Engineering       Inspection & Testing       Project Management       Advertising and Fees       Cap-Equipment       Non-Cap Equipment       Total       Project Budget	\$19,544,314 \$0 \$0 \$12,507,725	\$0 \$265 \$0 \$3,248 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$611,732 \$4,295 \$0 \$26,072 -\$4 \$0 \$0 \$0 \$0	\$0 \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 \$7,334 \$0 \$0 \$0	\$0 \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$0 \$2,033	\$887 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 \$0 \$25,356 \$170,425	\$0 \$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0 \$12,579 \$4,093	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$286 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$493,816 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 \$314,475 \$7,330 \$37,935 \$176,550
Net Carlow Construction of the set of the se	\$19,544,314 \$0	\$0 \$265 \$0 \$3,248 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$13,513	\$0 \$0 \$611,732 \$4,295 \$0 \$26,072 -\$4 \$0 \$0 \$642,095	\$0 \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 \$7,334 \$0 \$0 \$0	\$0 \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$0 \$2,033 <b>\$6,583,194</b>	\$887 -\$973,001 \$216,563 \$0 \$77,942 \$124,222 \$0 \$25,356 \$170,425	\$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0 \$12,579 \$4,093	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$286 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$493,816 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 \$314,475 \$7,330 \$37,935 \$176,550
Net     Actual Measure U Expenditures       Running Balance       U7100110       Earthquake Rpl. Liberal Arts North (I)       Supplies       Legal       Other Contract Services       Building & Additions       Architect       Engineering       Inspection & Testing       Project Management       Advertising and Fees       Cap-Equipment       Non-Cap Equipment       Total       Project Budget	\$19,544,314 \$0 \$0 \$12,507,725	\$0 \$265 \$0 \$3,248 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$611.732 \$4.295 \$26.072 -\$4 \$0 \$0 \$642,095	\$0 \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$7,334 \$7,334 \$0 \$0 <b>\$1,215,679</b> * Other Fundin	\$0 \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$0 \$2,033 <b>\$6,583,194</b>	\$887 \$75 \$75,001 \$216,563 \$0 \$77,942 \$124,222 \$0 \$25,356 \$170,425 <b>-\$356,123</b>	\$0 \$321,345 \$21,215 \$250 \$0 \$255 \$0 \$12,579 \$4,093	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$286 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$493,816 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 \$314,475 \$7,330 \$37,935 \$176,550
Net     Actual Measure U Expenditures       Actual Measure U Expenditures       Running Balance       U7100110       Earthquake Rpl. Liberal Arts North (I)       Supplies       Legal       Other Contract Services       Building & Additions       Archited       Engineering       Inspection & Testing       Project Management       Advertising and Fees       Cap-Equipment       Non-Cap Equipment       Total       Less Other Funding*	\$19,544,314 \$0 \$0 \$12,507,725 \$5,496,141	\$0 \$265 \$0 \$3,248 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$611,732 \$4,295 \$26,072 -\$4 \$0 \$26,072 -\$4 \$0 \$26,072 \$2	\$0 \$0 \$1,043,660 \$102,824 \$0 \$28,312 \$33,549 \$7,334 \$0 \$1,215,679 * Other Fundin City of Santa M	\$0 \$0 \$5,916,281 \$209,490 \$250 \$326,203 \$128,937 \$0 \$0 \$2,033 \$6,583,194 g Source: tonica \$4,039,7	\$887 \$75 \$75,001 \$216,563 \$0 \$77,942 \$124,222 \$0 \$25,356 \$170,425 <b>-\$356,123</b>	\$0 \$0 \$321,345 \$21,215 \$250 \$0 \$12,579 \$4,093 \$359,737	\$0 \$0 \$14,898 \$3,465 \$0 \$0 \$1,155 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$286 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 -\$834,764 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$1,127,809 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$	\$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$0 \$0 -\$493,816 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0 \$0	\$887 \$75 \$3,867,060 \$1,165,289 \$8,043 \$432,458 \$314,475 \$7,330 \$37,935 \$176,550

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
											I						
U7100013, U7100047																	
Music Complex (J)																	
Advertising		\$0	\$0				\$0	\$0	\$0	\$0		\$0		\$0			
Supplies		\$0	\$0	\$0	\$0	\$194	\$19,094	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$19,288
Consultants		\$0	\$0	\$0	\$0	\$0	\$36,000	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$36,000
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$180	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$180
Moving Services		\$0	\$0	\$0	\$0	\$0	\$6,330	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,330
Building & Additions		\$0	\$0	\$356,464	\$1,293,726	-\$737,213	\$273,531	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,186,509
Architect		\$0	\$187,922	\$22,500	\$37,227	\$38,448	\$4,052	\$14,356	\$0	\$681		\$3,992	\$2,038	\$0			
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$21,370	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$21,370
Inspection & Testing		\$0	\$0	\$29,740	\$19,265	\$26,238	\$35,880	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$111,122
Project Management		\$0	\$170	\$36,739	\$36,351	\$56,914	\$16,200	\$1,288	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$147,662
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$62,600	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$62,600
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$29,852	\$78,582	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$108,434
Total		\$0	\$188,092	\$445,879	\$1,386,568	-\$585,566	\$532,447	\$37,014	\$0	\$681	\$225	\$3,992	\$2,038	\$0	\$0	\$0	\$2,011,371
Project Budget	\$4,629,484	Received															
Less Other Funding*	\$2,618,113	\$2,618,113		* Other Fundin	g Source:												
Net	\$2,011,371			Prop T Refinar	nce \$2,618,113	received											
Actual Measure U Expenditures	\$2,011,371																
Running Balance	\$0																
U7100111																	
Earthquake Rpl. Liberal Arts South (K)																	
Supply		\$0	\$0	\$855	\$2,497	\$379	\$23,811	\$75	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$27,618
Legal		\$0	\$0	\$0	\$0	\$0	\$2,203	\$50	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,253
Moving Services		\$0	\$0	\$0	\$0	\$0	\$4,063	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,063
Consultants		\$0	\$0	\$0	\$17,265	\$41,435	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$58,700
Other Contract Services		\$0	\$0	\$6,154	\$202	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6.356
Building & Additions		\$0	\$0	\$26,302	\$3.091.306	\$5,706,802	-\$4,642,459	\$0	\$91,516	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,273,467
Architect		\$0	\$0	\$836,555	-\$503,297	\$163,506	\$183,877	\$39,984	\$2,549	\$0		\$0		\$0			
Engineering		\$0	\$0	\$3,125	\$150	\$5,344	\$500	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$9,119
Inspection & Testing		\$0	\$0			\$296,015	\$68,273	\$0	\$0	\$0		\$0	\$0	\$0			
Project Management		\$0	\$0			\$262,598	\$52,690	\$1,722	\$1,278	\$0		\$0		\$0			
Cap-Equipment		\$0	\$0	\$0			\$0	\$0	\$0	\$0	\$0	\$0		\$0			
Non-Cap Equipment		\$0	\$0				\$45,388	-\$7,074	\$0	\$0		\$0		\$0			
Total		\$0	\$0		\$2,831,909			\$34,757	\$95,342	\$0		\$0					
Project Budget	\$16,733,220	Received															
Less Other Funding*	\$10.625.070	\$10,625,070		* Other Fundin	a Source:												
Net	\$6,108,150	,.==,			Aonica \$6,167.0	70 received											
Actual Measure U Expenditures	\$6,108,150	1			rnia \$4,458,000												
Running Balance	\$0	1			,,	· · · · · -											

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
U7100221																	
Shuttle Replacement Parking (L)																	
Supplies		\$0	\$0	\$0		\$0	\$1,347	\$0		\$0	\$0	\$0		\$0	\$0		\$1,347
Legal		\$0	\$0	\$0	\$8,462	\$35,103	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$43,565
Site Acquisition		\$0	\$0	\$0	\$0	\$16,903,087	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$16,903,087
Site Improvement		\$0	\$0	\$0	\$0	\$3,027	\$0			\$0	\$0	\$0		\$0	\$0	\$0	\$3,027
Building & Additions		\$0	\$0	\$0	\$0	\$484,000	\$1,252,224	\$2,353	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,738,577
Architect		\$0	\$0	\$0	\$0	\$51,569	\$7,208	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$58,777
Inspection & Testing		\$0	\$0	\$0	\$0	\$139,822	\$41,250	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$181,072
Project Management		\$0	\$0	\$0	\$0	\$7,631	\$32,425	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$40,056
Total		\$0	\$0	\$0	\$8,462	\$17,624,240	\$1,334,455	\$2,353	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$18,969,509
Project Budget	\$18,969,509																
Less Other Funding	\$0																
Net	\$18,969,509																
Actual Measure U Expenditures	\$18,969,509																
Running Balance	\$0																
U7100321																	
North Quad Plaza (M)																	
Legal		\$0	\$0	\$0	\$0	\$0	\$3,825	\$5,604	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$9,429
Building & Additions		\$0	\$0	\$0	\$0	-\$443	\$6,130,081	\$3,634,487	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$9,764,125
Architect		\$0	\$231,055	\$8,444	\$140,048	\$435,618	\$171,225	\$68,633	\$2,901	\$10,483	\$0	\$0	\$0	\$0	\$0	\$0	\$1,068,407
Engineering		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$186,220	\$107,477	\$328	\$0	\$0			\$0	\$0	\$0	\$294,025
Project Management		\$0	\$0	\$760	\$210	\$2,200	\$135,601	\$55,782	\$606	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$195,158
Printing		\$0	\$1,900	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$1,900
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$55,420	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$55,420
Total		\$0	\$232,955	\$9,204	\$140,258	\$437,375	\$6,626,952	\$3,927,402	\$3,834	\$10,483	\$0	\$0	\$0	\$0	\$0	\$0	\$11,388,463
Project Budget	\$11,388,463																
Less Other Funding	\$0																
Net	\$11,388,463																
Actual Measure U Expenditures	\$11,388,463																
Running Balance	\$0																

Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
U7100500, U7126450, U7100334, U7100142																	
Student Services Building (O)																	
Supplies		\$2,014	\$0	\$0	\$0	\$0	\$0	\$718	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$2,732
PC Upgrades		\$0	\$765	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$765
Consultants		\$0	\$0	\$0	\$0					\$0	\$0	\$0				\$0	
Legal		\$0	\$0	\$0	\$0	\$38	\$2,775	\$31,776	\$0		\$0	\$0				\$0	\$34,588
Other Contract Services		\$210	\$0	\$0	\$0	\$0	\$17,561	\$17,495	\$18,817	-\$70	\$0	\$0	\$0	\$0	\$0	\$0	\$54,014
Moving		\$7,571	\$0	\$0	\$0	\$0	\$0	\$616	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$8,187
Building & Additions		\$359,141	\$2,441	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$776	\$560	\$1,717,465	\$9,584,253	\$11,664,636
Architect		\$31,782	\$0	\$235,230	\$0	\$43,992	\$0	\$690,099	\$208,521	\$38,643	\$48,442	\$388,611	\$973,427	\$2,502,652	\$567,231	\$469,372	\$6,198,002
Engineering		\$1,838	\$0	\$0	\$0	\$0	\$0	\$6,205	\$27,363	\$3,171	\$0	\$0	\$0	\$55,680	\$73,757	\$5,360	\$173,373
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$25,670	\$34,687	\$0	\$0	\$0	\$0		\$0	\$69,480	\$69,396	
Project Management		\$4,650	\$0	\$2,470	\$0	\$1,100	\$0	\$124,148	\$0	\$0	\$0	\$6,675	\$15,650	\$11,616	\$120,550	\$3,275	\$290,134
Cap Equipment		\$59,063	\$0	\$0	\$0	\$0	\$8,745	\$8,056	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$75,864
Total		\$466,268	\$3,207	\$237,700	\$0	\$54,464	\$110,445	\$913,802	\$254,701	\$41,744	\$48,442	\$395,286	\$992,330	\$2,570,508	\$2,548,483	\$10,131,656	\$18,769,035
Project Budget	\$130,224,164	Received		* Other Fundin	g Source:												
Less Other Funding*	\$109,091,902	\$1,321,000		State of Califor	nia \$1,321,000	received											
Net	\$21,132,262			Measure S \$47	,456,043, Meas	ure AA \$30,944	4,318, Measure	V \$15,095,89	6 allocated								
Actual Measure U Expenditures	\$18,769,035			Measure U, S &	& AA Interests \$	18,070,541 allo	cated										
Running Balance	\$2,363,227																



Projects	Budget	02/03 Final	03/04 Final	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
U7100090																	
Science Complex Additional (P)																	
Architect		\$0	\$0	\$0	\$0	\$246,425	\$61,911	\$0				\$0					
Total		\$0	\$0		\$0	\$246,425	\$61,911	\$0	\$0	\$0	\$0	\$0	\$0	\$0	) \$0	\$0	\$308,336
Project Budget	\$90,401,286			* Other Funding													
Less Other Funding	\$90,092,950			State of Californ	nia \$40,088,000	) pending											
Net	\$308,336			Measure AA \$4	,950, Measure	V \$50,000,000 a	llocated										
Actual Measure U Expenditures	\$308,336																
Running Balance	\$0																
U6780000, U7100022, U7100331, U7100550,																	
U7100005, U7100030, U7100031, U7100029,																	
U7100003, U7100008, U7100332, U7100072,																	
U7100042, U7100056, U7100039																	
Infrastructure & Safety (Q)																	
Supplies		\$0	\$0	\$254	\$0	\$0	\$0	\$1,700	\$1,393	\$0	\$0	\$0	\$0	\$0	) \$0	\$0	\$3,347
Consultants		\$0	\$0	\$0	\$0	\$0	\$0		\$0			\$0	\$0				\$16,734
Maintenance Agreement		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$14.673	\$12.979	\$12.979	\$0	\$0	) \$0	\$0	\$40,632
Legal		\$0	\$0	\$0	\$0	\$0	\$3,527	\$3,294	\$0		\$0	\$0	\$0	\$0			\$6,821
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$7,825	\$81,445	\$203,383	\$3,320	\$0	\$0	\$0	\$0	) \$0	\$0	\$295,973
Building & Additions		\$681,900	\$195,175	\$20,600	\$0	\$200,620	\$733	\$0	\$0	\$0	\$0	\$0	\$0	\$0	) \$0	\$0	\$1,099,028
Architect		\$69,081	\$42,108	\$0	\$155,321	\$448,507	\$91,127	\$4,227	\$0	\$0	\$0	-\$1,365	\$0	\$0	) \$0		\$809,005
Engineering		\$8,050	\$0	\$0	\$6,750	\$12,000	\$18,429	\$2,360	\$0	\$0	\$0	\$0	\$0	\$0	) \$0	\$0	\$47,589
Inspection & Testing		\$2,241	\$4,250	\$0	\$0	\$0	\$5,807	\$0	\$0	\$0	\$0	\$0	\$0	\$0	) \$0	\$0	\$12,298
Project Management		\$0	\$2,805	\$0	\$0	\$3,520	\$1,840	\$38	\$196	\$0	\$0	\$0	\$0	\$0	) \$0	\$0	\$8,399
Cap Equipment		\$0	\$0	\$343,861	\$0	\$0	\$0	\$895,171	\$349,531	\$40,002	\$0	\$0	\$0	\$0	) \$0	\$0	\$1,628,565
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$4,216	\$0	\$29,694	\$0	\$0	\$0	\$0	\$0	\$33,910
Advertising		\$0	\$785	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	) \$0	\$0	\$785
Total		\$761,272	\$245,122	\$364,715	\$162,071	\$664,647	\$129,287	\$1,004,968	\$558,718	\$57,995	\$42,673	\$11,614	\$0	\$0	) \$0	\$0	\$4,003,084
Project Budget	\$4,003,084																
Less Other Funding	\$0																
Net	\$4,003,084																
Actual Measure U Expenditures	\$4,003,084																
Running Balance	\$0																

Projects	Budget	02/03 Einal	03/04 Einal	04/05 Einal	05/06 Einal	06/07 Final	07/08 Einal	08/09 Einal	09/10 Einal	10/11 Einal	11/12 Einal	12/13 Einal	13/14 Einal	14/15 Einal	15/16 Einal	16/17 Einal	Combined Totals
Filipetta	Duugei	02/05111181	05/04111181	04/03 i iiiai	05/00111181	00/07 1 11141	07/00111181	00/03 1 11181	03/10111141	TU/TTTTIIIai	11/12 1 mai	12/15 T IIIdi	15/14111181	14/13 T IIIai	15/101111	TO/T/TIMA	
U7100007																	T
Restroom Improvement (R)																	
Supplies		\$0	\$564	\$0	\$1,075	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,639
Other Contract Services		\$0	\$0	\$0	\$3,803	\$0	\$0		\$0	\$0		\$0		\$0			
Building & Additions		\$0	\$1,305	\$0	\$7,891	\$0	\$0		\$0	\$0		\$0		\$0			
Inspection & Testing		\$0	\$2.043	\$0	\$820	\$0	\$0		\$0	\$0		\$0		\$0			
Total		\$0	\$3,912	\$0	\$13,589	\$0	\$0		\$0			\$0		\$0			
Project Budget	\$17,501	<b>+</b> -	++,+		<i></i> ,	+-		+-	4-		<b>*</b> *		+-	+-	, , , , , , , , , , , , , , , , , , ,		
Less Other Funding	\$0																
Net	\$17,501																
Actual Measure U Expenditures	\$17,501																
Running Balance	\$0																
Ranning Balanoo	ψũ																
U7100004. U7110020													1			1	
Master Planning (S)																	
Consultants		\$9,000	\$26,516	\$158,449	\$374,329	\$125,404	\$17.998	\$363,342	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1.075.03
Architect		\$3,000	\$17,617	\$126,433	\$104,083	\$126,701	\$346,827	\$276,985	\$0			\$0		\$0			
Rental / Lease		\$0	\$17,017	\$6,453	\$104,003	\$120,701	\$040,027		\$0 \$0	\$0		\$0		\$0			
Postage		\$0	\$0	\$30,000	\$0	\$0	\$0		\$0	\$0		\$0		\$0			
Reimbursement to SMC		\$0	\$0	\$30,000	\$180	\$0	\$0 \$0		\$0 \$0	\$0		\$0		\$0	\$0	\$0	) \$30,000 \$180
Project Management		\$0	\$0	\$0	\$ 100 ¢0	\$0	\$0 \$0		\$0	\$0		\$0		\$0			
Total		\$9.000	\$44,133	\$321,335	\$478,593	\$252,105	\$364,825		\$0 \$0	\$0 \$0		\$0 \$0		\$0			
Project Budget	\$2,110,430	\$9,000	\$44,133	\$321,335	\$470,593	\$252,105	<b>\$364,625</b>	\$640,439	\$U	\$U	\$U	\$U	<b>\$</b> 0	<b>\$</b> U	ຸ່ຈຸບ	ર ગ	\$2,110,430
Less Other Funding	\$2,110,430																
Net Actual Measure U Expenditures	\$2,110,430 \$2,110,430																
Running Balance	\$2,110,430																
Running Balance	<u>۵</u> 0																
12100001															1	1	T
U7100024																	
14th and Pico Project (T)																	
Consultants		\$0	\$888	\$0	\$0	\$0	\$0		\$0	\$0		\$0		\$0			
Architect		\$258,601	\$47,343	\$0	\$0	\$0	\$0		\$0	\$0	\$0	\$0		\$0			
Inspection & Testing		\$12,070	\$0	\$0	\$0	\$0	\$0		\$0	\$0		\$0		\$0			
Project Management		\$0	\$340	\$0	\$0	\$0	\$0		\$0	\$0		\$0		\$0			
Total		\$270,671	\$48,571	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$319,242
Project Budget	\$319,242																
Less Other Funding	\$0																
Net	\$319,242																
Actual Measure U Expenditures	\$319,242																
Running Balance	\$0																
Grand Total		\$11,068,400	\$10,432,055	\$28,685,697	\$54,940,416	\$25,278,771	\$5,283,853	\$6,585,573	\$912,880	-\$723,860	\$91,341	-\$716,916	\$1,041,732	\$2,570,508	\$2,548,483	\$9,637,840	\$157,636,774


Note: Project N had no expenses

### SANTA MONICA COMMUNITY COLLEGE DISTRICT


# Measure S Project Schedule As of June 30, 2017

	Project Name	Completion	2015	2016	2017	2018	2019
1	Athletic Fields Phase I, Corsair Field	Completed					
1A	Athletic Fields Phase I, John Adams	Completed					
2	Performing Arts Center	Completed					
3	Career Opportunity Center	Completed					
4	Replacement Health/PE/Fitness Building	June 2017					
5	Early Childhood Development/Childcare	September 2019					
6	Malibu Site Acquisition and Facility	September 2019					
7	Energy Efficiency Projects	Completed					
8	Satellite Campus Parking Facilities and Roadway Improvements	Deferred					
9	Parking Garage, Grounds and Equipment - Student Services	March 2019					
10	Pico Promenade Improvements	Completed					
11	Master Planning	Completed					
12	Other Bond Related Expenses	On-Going					
13	Adv. Architecture Related Exp for AA	Completed					
14	Real Property Acquisition	Completed					
15	Signage Safety/Information	Completed					
16	Cost of Issuance	On-Going					
			In Plann	hing	In Constr	ruction	

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
S7100019															
Athletic Field Phase I, Corsair Field (1)															
Legal		\$0	\$0	\$0	\$301	\$175	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$476
Building & Additions		\$0	\$0	\$0	\$300,380	\$2,579,095	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,879,475
Architect		\$27,332	\$43,815	\$197,557	\$252,736	\$279,173	\$26,563	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$827,176
Inspection & Testing		\$0	\$0	\$0	\$23,411	\$57,585	\$640	\$296	\$0	\$0	\$0	\$0	\$0	\$0	\$81,932
Project Management		\$0	\$0	\$0	\$9,871	\$42,374	\$565	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$52,810
Cap Equipment		\$0	\$0	\$0	\$0	\$483,017	\$35,271	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$518,288
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$2,066	\$10,312	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$12,378
Total		\$27,332	\$43,815	\$197,557	\$586,699	\$3,443,485	\$73,350	\$296	\$0	\$0	\$0	\$0	\$0	\$0	\$4,372,535
Project Budget	\$4,440,065	Received													
Less Other Funding*	\$67,530	\$67,530		* Other Fundin	g Source:										
Net	\$4,372,535		-	Metropolitan W	ater District \$6	7,530 received									
Actual Measure S Expenditures	\$4,372,535														
Running Balance	\$0														



Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
S7100038															
Athletic Field Phase I, John Adams (1A)															
Legal		\$0	\$0	\$0	\$75	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$75
Building & Additions		\$0	\$0	\$0	\$16,556	\$1,395,261	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,411,817
Architect		\$0	\$5,807	\$93,941	\$12,150	\$31,818	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$143,715
Inspection & Testing		\$0	\$2,874	\$3,207	\$0	\$49,984	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$56,066
Project Management		\$0	\$0	\$0	\$10,921	\$45,170	\$38	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$56,128
Cap Equipment		\$0	\$0	\$0	\$0	\$1,290,672	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,290,672
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$11,334	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$11,334
Total		\$0	\$8,681	\$97,148	\$39,701	\$2,824,239	\$38	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$2,969,807
Project Budget	\$2,969,807														
Less Other Funding	\$0	]													
Net	\$2,969,807	1													
Actual Measure S Expenditures	\$2,969,807														
Running Balance	\$0														



Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
07/000/0											1				
S7100012															
Performing Arts Center (2)					<b>0404 700</b>		<b>*</b> 0			**				<b>*</b> 0	<b>\$100.100</b>
Consultants		\$0	\$0		\$121,790	\$76,639		\$0	\$0	\$0	\$0		\$0	\$0	\$198,429
Other Contract Services		\$0 \$0				\$22,729		\$68 \$0	\$0	\$0				\$0 \$0	\$27,088 \$20,375
Supplies						\$5,810			\$0						
Legal		\$0				\$492,731		\$0	\$0				\$0	\$0	\$818,350
Advertising		\$0				\$0		\$0	\$0					\$0	\$32
Building & Additions		\$7,784,151	\$10,292,986		\$2,991,903	\$1,629,990		\$0	\$0				\$0	\$0	\$31,679,843
Architect		\$0	\$811,312	\$182,457	\$412,309	\$121,588		\$1,962	\$0			\$0		\$0	\$1,616,79
Engineering		\$0		\$5,250		\$9,650		\$0	\$0						\$20,00
Inspection & Testing		\$104,308	\$722,685		\$210,381	\$22,256		\$0	\$0						\$1,470,82
Project Management		\$31,984	\$155,732		\$263,690	\$47,915		\$0							\$751,44
Cap Equipment		\$0				\$342,693		\$0	\$0						\$765,47
Non-Cap Equipment		\$0	\$0			\$220,455		\$0	\$0					\$0	\$328,68
Total		\$7,920,443	\$11,986,315	\$9,962,528	\$4,677,797	\$2,992,455	\$69,003	\$2,030	\$0	\$0	\$87,054	\$0	\$0	\$0	\$37,697,62
Project Budget	\$40,690,201	Received													
Less Other Funding*	\$2,992,576	\$2,992,576		* Other Fundin											
Net	\$37,697,625			Madison Proje	ct Foundation \$	2,992,576 rece	eived								
Actual Measure S Expenditures	\$37,697,625														
Running Balance	\$0														
Performing Arts Center						Proje	ct Expens	es to Dat	e						
Project Description: Construction of a state-of-the-art 499 seat performing arts theater												Building & Addit	ions, \$31,679,84	3	
Status: Completed, 2008						125									
Architect: Renzo Zecchetto			Adverti	sing, \$320							/	Archit Additional Archite	ect, \$1,527,774 ect fee paid for b	y Madison	
Contractor: FTR International			Legal,	\$818,356								F	oundation		

Consultants, \$198,429 \_\_\_\_

Cap Equip., \$765,476

Non-Cap Equip., \$328,685

Supplies, \$20,375\_

Other Contract Services, \$27,088 \_

\_Engineering, \$20,000

Project Management, \$751,441

\_\_\_ Inspection & Testing, \$1,470,823

Strolling 1         I <th< th=""><th>Projects</th><th>Budget</th><th>04/05 Final</th><th>05/06 Final</th><th>06/07 Final</th><th>07/08 Final</th><th>08/09 Final</th><th>09/10 Final</th><th>10/11 Final</th><th>11/12 Final</th><th>12/13 Final</th><th>13/14 Final</th><th>14/15 Final</th><th>15/16 Final</th><th>16/17 Final</th><th>Combined Totals</th></th<>	Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
Replacement Health/PE/Finses Building (4)         4         0																
Singles         Note         514.000         518.00         50																
Instal         Sol         Sol<																<b>*</b> = 000
Offer Contract Services         S0         50																
Begar Facility         S0         540         50																
Building Additions         90         50         50         50         50         50         50         50         50         51																
Archited:         S0         S0         S10         S0         S10         S0																
Inspector A Testing         50 <td></td>																
Project Management         Sol																
Case Expending         Stol																
Total         S6,443         \$58,472.030 (480.00F runding' 484.0668.477.03)         \$50         \$50         \$50         \$50         \$50,77.14         \$50         \$11,603.383           Project Budging (480.00F runding' (480.006 micros)         \$11,003.383         *Other Funding Source: Memure A.84.458,800 allocated SCE \$150,947.28, 0se Co. \$16,000 received         \$50         \$50         \$50         \$50         \$50         \$50,77.14         \$50         \$11,603.383           Forming Balance         \$11,003.383         SCE \$150,947.28, 0se Co. \$16,000 received         \$50<																
Project Elonget         558,272.00 (action of the funding)*         * Other Funding Source: Met action for the funding Source: Standa Massite S Expenditures         * Other Funding Source: Met action for the funding Source: Standa Massite S Expenditures         * Other Funding Source: Met action for the funding Source: Standa Massite S Expenditures         * Other Funding Source: Met action for the funding Source: Standa Massite S Expenditures         * Other Funding Source: Met action for the funding Source: Standa Massite S Expenditures         * Other Funding Source: City of Standa Monita S Cot S Standa S S Standa S S Standa				¢24.092												
Lies Other Funding*         546 (68 647) (Messure A Starbard As 645.800 allocated SCE \$190,847 28, Gas Ca \$18,000 received SCE \$190,847 28,010 \$10,800 \$0,90 \$0,		¢50 070 020	30,443	\$31,003	<b>\$</b> U	φU	\$129,003	\$005,767	\$17,013	ο <b>3</b> 0	φU	φU	\$0,037,000	ə4,775,714	<b>3</b> 0	\$11,003,303
Net         Still dots 383 Running Balance         Measure AA \$46,458,000 accided SCE \$19.00.472,635 C.6 \$18.000 received           Running Balance         50					Othor Fundin	a Couroo:										
Actual Measure S Expenditures Ronning Balance         STI (00:3) SCE \$190,047.28, GaS Co. \$18,000 received           STI 00045         S	<u> </u>						otod									
Running Balance         S0           S7100045 <td< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td>4</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></td<>								4								
2         1         1           Consultants         5710045         50         50         50         50         512.030         514.078         51.388         50         542.305           Logal         50					50L φ 190,047	.20, 0as 00. 31	0,000 received									
Early Childhood Development/Childcare (6) </td <td>Running Balance</td> <td>φU</td> <td></td>	Running Balance	φU														
Consultants         S0         S0         S0         S0         S0         S1,000         S1,2930         S1,078         S1,388         S0         S4,2395           Building & Additions         S0	S7100045															
Legal         S0	Early Childhood Development/Childcare (5)															
Building & Additions         Sol	Consultants		\$0	\$0	\$0	\$9,200	\$0	\$0	\$0	\$0	\$4,800	\$12,930	\$14,078	\$1,388	\$0	
Architect         S0         S3         S2         S2         S2         S0         S42         S0         S3         S2         S3	Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0			\$1,690	\$6,905	\$8,595
Inspection & Testing       \$0       \$1246       \$22,946       \$152,858       \$196,268       \$485,670       \$485,541       \$33,345       \$8,803       \$3,1118       \$0       \$126,828       \$196,268	Building & Additions				\$0											
Project Management         \$0         \$0         \$0         \$0         \$1,246         \$21,980         \$58,247         \$33,435         \$8,803         \$3,116         \$0         \$126,828           Project Budget         \$15,520,176         Received         \$0         \$0         \$0         \$1,246         \$22,946         \$152,635         \$196,268         \$166,670         \$485,344         \$85,555         \$1,119,864           Less Other Funding*         \$8,820,176         \$00         \$0         \$1,246         \$22,946         \$152,635         \$196,268         \$166,670         \$485,344         \$85,555         \$1,119,864           Actual Measure S Expenditures         \$1,119,864         * Other Funding Source: City of Santa Monica \$6,661,598 commited Measure S interest \$1,858,078 allocated         \$166,670         \$485,344         \$85,555         \$1,119,864           Synton         \$50,000         \$0         \$0         \$0         \$0         \$0         \$1,246         \$22,946         \$152,635         \$166,670         \$485,344         \$85,555         \$1,119,864           Running Balance         \$57,000,000         \$60         \$00         \$00         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0 <t< td=""><td>Architect</td><td></td><td>\$0</td><td></td><td>\$0</td><td>\$0</td><td>\$0</td><td></td><td></td><td></td><td></td><td>\$142,428</td><td>\$142,968</td><td>\$476,827</td><td>\$78,408</td><td>\$893,388</td></t<>	Architect		\$0		\$0	\$0	\$0					\$142,428	\$142,968	\$476,827	\$78,408	\$893,388
Total         S0         S0         S0         S0         S0         S0         S1246         S1246         S1246         S126,253         S196,268         S166,670         S485,344         S85,555         S11,119,864           Less Other Funding*         S6,520,176         S0         S0         S1,246         S22,946         S152,635         S196,268         S166,670         S485,344         S85,555         S11,119,864           Less Other Funding*         S7,000,000         VI of Santa Monica S6,661,598 commited Measure S Interest S1,858,578 allocated         S11,119,864         S22,946         S152,635         S196,268         S166,670         S485,344         S85,555         S11,119,864           Running Balance         S7,000,000         S0         S20         S20         S0         S0         S20         S0         S20																
Project Budget         \$15,520,176         Received           Less Other Funding*         \$86,820,176         \$0           Net         \$7,000,076         \$0           Actual Measure S Expenditures         \$1,119,864         Measure S interest \$1,858,578 allocated           Running Balance         \$5,860,136         City of Santa Monica \$6,661,588 commited Measure S interest \$1,858,578 allocated           S7100077, S7100015         \$0         \$0         \$0         \$0,00         \$0         \$0,00	Project Management		\$0		\$0											\$126,828
Less Other Funding*         \$8,850,176         \$CO           Net         \$7,000,000         \$11,119,864         Statal Monias Se 68,1588 commited Measure S interest \$1,858,578 allocated           Running Balance         \$5,880,136         Statal Monias Se 66,1588 commited Measure S interest \$1,858,578 allocated           S7100077, S7100015         Stata Monias Se 66,1589 commited Measure S interest \$1,858,578 allocated         Stata Monias Se 66,1598 commited Measure S interest \$1,858,578 allocated           Mailbu Site Acquisition and Facilities (6)         Stata Monias Se 500         Stata Monias Se 500         Stata Monias Se 500           Legal         Stata Monias Se 500         Stata Monias Se 500         Stata Monias Stata Monias Se 500         Stata Monias Stata Monias Se 500         Stata Monias Manias Man	Total		÷ -	\$0	\$0	\$9,200	\$0	\$0	\$1,246	\$22,946	\$152,635	\$196,268	\$166,670	\$485,344	\$85,555	\$1,119,864
Net         \$7,000,000         City of Santa Monica \$6,661,508 commited Measure S Expenditures         \$1,119,864 (Measure S Interest \$1,858,578 allocated           Running Balance         \$5,880,136         City of Santa Monica \$6,661,508 commited Measure S Interest \$1,858,578 allocated           S7100077, S7100015              Malibu Site Acquisition and Facilities (6)              Consultants         \$0																
Actual Measure S Expenditures         \$1,119,864         Measure S interest \$1,858,578 allocated           S7100077, S7100015         Measure S interest \$1,858,578 allocated         State         State <td>Less Other Funding*</td> <td></td> <td>\$0</td> <td></td>	Less Other Funding*		\$0													
Running Balance         \$5,880,136           S7100077, S7100015         S7100077, S7100015         S72,157         \$68,109         \$30,342         \$66,277         \$60,262         \$3,3406         \$330,553         Legal         S710077,S710015         S0         \$5																
S7100077, S7100015         S700077, S7100015         S7000015         S70000015         S70000015         S7000015         S7000015         S70000016         S70000016         S70000016         S700000016         S7000000016         S7000000000         S7000000000000000000					Measure S inte	erest \$1,858,578	3 allocated									
Malibu Site Acquisition and Facilities (6)  <	Running Balance	\$5,880,136														
Malibu Site Acquisition and Facilities (6)  <	07400077 07400045												1		1	
Consultants         \$0         \$0         \$0         \$0         \$0         \$0         \$72,157         \$68,109         \$30,342         \$66,277         \$60,262         \$3,406         \$330,553           Legal         \$0         \$27,722         \$16,787         \$61,59         \$504         \$0         \$0         \$0         \$1,360         \$78,851         \$40,114         \$7,353         \$178,849           Other Contract Services         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$1,360         \$78,851         \$40,114         \$7,353         \$178,849           Building & Additions         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$1,320         \$10         \$10         \$3,912           Building & Additions         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$13,610         \$34,753         \$17,72         \$1,351,575           Engineering         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0 <td< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></td<>																
Legal         \$0         \$27,722         \$16,787         \$6,159         \$504         \$0         \$0         \$0         \$1,360         \$78,851         \$40,114         \$7,353         \$178,849           Other Contract Services         \$0			¢0	¢0	¢0	¢0	¢20.000	¢o	¢0	670 457	¢c0.400	¢20.242	¢cc 077	¢c0.0c0	¢0.400	¢220 EE2
Other Contract Services         \$0																
Building & Additions         \$0 <td></td> <td>   </td> <td></td>																
Architect         \$0																
Engineering         \$0																
Inspection & Testing         \$4,388         \$3,750         \$141,462         \$0         \$0         \$0         \$98,022         \$15,575         \$22,939         \$10,960         \$0         \$20         \$20         \$0         \$0         \$0         \$20         \$0         \$0         \$0         \$0         \$2297,096         \$0         \$22,939         \$10,960         \$0         \$22,939         \$118,144         \$97,856         \$44,00         \$421,532           Storm/Waste Water Treatment Center         \$0         \$2,500,000         \$0 <td></td>																
Project Management         \$0         \$0         \$220         \$0         \$0         \$2,886         \$55,064         \$53,185         \$47,778         \$118,144         \$97,856         \$46,400         \$421,532           Storm/Waste Water Treatment Center         \$0         \$2,500,000         \$0 <td></td>																
Storm/Waste Water Treatment Center         \$0         \$2,500,000         \$0<																
Total         \$4,388         \$2,531,472         \$158,468         \$6,159         \$2,630,504         \$0         \$2,886         \$228,301         \$395,237         \$836,407         \$449,662         \$232,985         \$208,931         \$7,585,402           Project Budget         \$25,000,000         \$0         \$2,886         \$228,301         \$395,237         \$836,407         \$449,662         \$232,985         \$208,931         \$7,585,402           Less Other Funding*         \$0         \$0         \$2,886         \$228,301         \$395,237         \$836,407         \$449,662         \$208,931         \$7,585,402           Net         \$25,000,000         \$25,000,000         \$25,000,000         \$7,585,402         \$7,585,402         \$449,662         \$232,985         \$208,931         \$7,585,402           Actual Measure S Expenditures         \$7,585,402         \$																
Project Budget         \$25,000,000           Less Other Funding*         \$0           Net         \$25,000,000           Actual Measure S Expenditures         \$7,585,402																
Less Other Funding*         \$0           Net         \$25,000,000           Actual Measure S Expenditures         \$7,585,402		\$25,000,000	<b>\$4,388</b>	\$2,331,472	ə 100,468	<b>Φ</b> 0, 159	<i>φ</i> ∠,550,504	\$0	₹2,886	₹220,301	<b>\$390,23</b> 7	<b>φουσ,40</b> 7	<u>⊅443,662</u>	<b>⊅∠</b> 3∠,985	j ⊅200,931	ə <i>1</i> ,303,402
Net         \$25,000,000           Actual Measure S Expenditures         \$7,585,402																
Actual Measure S Expenditures \$7,585,402																
אסטקודיד,ווי (יוע אינט אינע אינע אינע אינע אינע אינע אינע אינע																
		φ17,414,090														

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
S7100043, S7100066															
Energy Efficiency Projects (7)															
Legal		\$0		\$0	\$0	\$988	\$0	\$0			\$0			\$0	\$988
Building & Additions		\$0		\$0	\$0	\$106,921	\$355,294	-\$180,342			\$0				\$281,873
Engineering		\$0		\$0	\$10,500	\$0	\$0	\$0			\$0				\$10,500
Inspection & Testing		\$0		\$0	\$0	\$0	\$0	\$0			\$0				\$0
Project Management		\$0		\$0	\$0	\$0	\$0	\$0			\$0			\$0	\$0
Total		\$0	\$0	\$0	\$10,500	\$107,910	\$355,294	-\$180,342	\$0	\$0	\$0	\$0	\$0	\$0	\$293,361
Project Budget	\$510,683	Received													
Less Other Funding*	\$217,322	\$217,322		* Other Funding	g Source:										
Net	\$293,361			SCE & The Ga	s Co. \$217,322	received									
Actual Measure S Expenditures	\$293,361														
Running Balance	\$0														
S7100091, S7100092, S7100147															
Satellite Campus Parking Facilities and Roadway In	nprovements (	8)													
Legal		\$0	\$0	\$0	\$300	\$175	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$475
Other Contract Services		\$0	\$0	\$0	\$300	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$300
Advertising		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0 \$0
Consultants		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$278,178	\$1,860,152	\$449,543	\$37,777	\$0	\$0	\$0	\$64	\$0	\$0	\$2,625,714
Architect		\$0	\$0	\$324,919	\$324,864	\$136,911	\$34,490	\$1,397	\$2,289	\$0	\$0	\$0	\$0	\$0	\$824,871
Engineering		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$30,896	\$5,470	\$12,165	\$0	\$48,531
Inspection & Testing		\$0	\$0	\$0	\$31,100	\$185,947	\$28,218	\$360	\$0		\$0			\$0	\$245,626
Project Management		\$0	\$0	\$0	\$18,288	\$64,880	\$31,137	\$8,659	\$0	\$2,569	\$10,730	\$6,046	\$535	\$0	\$142,844
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$3,387	\$0	\$0	\$0	\$0			\$0	\$3,387
Total		\$0	\$0	\$324,919	\$653,031	\$2,248,065	\$546,775	\$48,194	\$2,289	\$2,569	\$41,626	\$11,580	\$12,700	\$0	\$3,891,747
Project Budget	\$7,022,417														
Less Other Funding	\$3,130,670			* Other Funding	g Source:										
Net	\$3,891,747			Measure AA \$2	,130,670, Meas	ure V \$1,000,0	00 allocated								
Actual Measure S Expenditures	\$3,891,747														
Running Balance	\$0														

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
S7100142															
Parking Garage and Grounds - Student Services (9)															
Supplies		\$0	\$0	\$0	\$0	\$1,745	\$0	\$0	\$648	\$0	\$0	\$813	\$0	\$0	\$3,206
Consultants		\$0	\$0	\$0		\$20,700	\$0	\$0	\$0	\$0 \$0	\$0	\$0	\$1,740	\$0	\$22,440
Legal		\$0	\$0	\$0		\$2,154	\$17.486	\$4.800	\$2.257	\$17,221	\$0	\$3.570	\$0	\$0	\$47,488
Other Contract Services		\$0	\$0	\$0	\$0	\$1,508	\$10,952	\$1,986	\$46	\$0	\$12,083	\$5,034	\$0	\$0	\$31,608
Site Improvement		\$0	\$0	\$0		\$0	\$0	\$0	\$0	\$1,086	\$0	\$1,308	\$0	\$0	\$2,394
Building & Additions		\$0	\$0	\$0		\$2,555,940	\$5,925,152	\$78,717	\$77,320	\$5,509	\$715	\$0	\$3,721	\$11,308,792	\$19,955,865
Architect		\$0	\$0	\$0		\$2,674,054	\$0	\$37,111	\$75,163	\$0	\$0	\$0	\$0	\$0	\$5,053,094
Engineering		\$0	\$0	\$0		\$4,813	\$38,330	\$42,968	\$50,952	\$9,735	\$0	\$0	\$0	\$0	\$146,797
Inspection & Testing		\$0	\$0	\$0		\$131,009		\$54,069	\$32,306	\$30,909	\$4,123	\$22,296	\$38,186	\$516,217	\$990,962
Project Management		\$0	\$0	\$0		\$158,766	\$373,559	\$184,088	\$92,118	\$224,994	\$59,525	\$29,714	\$50,380	\$285,057	\$1,458,200
Cap Equipment		\$0	\$0	\$0		\$0	\$14,393	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$14,393
Non-Cap Equipment		\$0	\$0	\$0		\$0	\$0	\$0	\$11,381	\$0	\$0	\$0	\$0	\$0	\$11,381
Total		\$0	\$0		\$2,266,766	\$5,550,689	\$6,541,719	\$403,737	\$342,192	\$289,454	\$76,445	\$62,735	\$94,027	\$12,110,066	\$27,737,831
	\$130,224,164			* Other Fundin											
Less Other Funding*	\$82,768,121 \$47,456,043				nia \$1,321,000		,318, Measure \	1 \$45 005 000							
Net Actual Measure S Expenditures	\$47,456,043							\$15,095,896	allocated						
Running Balance	\$27,737,831 \$19,718,213			Measure 0, 5	& AA interests \$	18,070,541 all	ocated								
Ruilling Balance	φ19,7 10,213														
Services Project Description: Consolidates various student services departments and college administration in a single complex at the front of the campus Facility Size: 110,000 sq/ft & 500 cars underground parking structure				Buildin <sub>i</sub>	g & Additions, \$1		are S Shar					Architect,	\$5 052 004		
Status: Phase 1 completed Phase 2 In construction Architect: Steinberg Architects, Morris Architects Contractor: Minaco, Bernards			Other Contra	nprovement, \$2, act Services, \$31 Legal, \$47, nsultants, \$22,4 Supplies, \$3,2	,608 488 40 06	Cap Equipment,	\$14,393 Proje	ect Management	, \$1,458,200	-	ing, \$146,797 esting, \$990,962				

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
S7100044		,										· · · · · ·		,	I
Pico Promenade Improvements (10)	· · · · · · · · · · · · · · · · · · ·	+									·				
Building & Additions	· · · · · · · · · · · · · · · · · · ·	\$0	\$0	\$0	\$690	\$883.401	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$884.091
Architect	<del>ر ا</del>	\$0	\$0	\$0		\$28,540	\$864	\$0						\$0	
Inspection & Testing		\$0	\$0	\$0		\$7,591	\$0	\$0							
Project Management	· · · · · · · · · · · · · · · · · · ·	\$0	\$0	\$0		\$25,548	\$0	\$0					\$0		
Total	·	\$0				\$945,080	\$864	\$0							
Project Budget	\$1,018,009		ψŪ	<del>,</del>	ψ1 <u>2</u> ,000	<i><b>\</b></i> <b>\\\\\\\\\\\\\</b>	\$004		ψŪ	ψŪ	<del>\</del>				\$1,010,000
Less Other Funding	\$0														
Net	\$1,018,009														
Actual Measure S Expenditures	\$1,018,009														
Running Balance	\$0														
	ψŪ	<u> </u>													I
S7100004	[!	[!													
Master Planning (11)															
Consultants	(	\$0	\$0	\$0			\$441,549	\$13,320	\$0				\$0		\$454,869
Printing	(	\$0	\$0	\$0			\$4,157	\$0					\$0		
Advertising	(	\$0	\$0	\$0		\$0	\$3,000	\$0	\$0				\$0		
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$442	\$200	\$0	\$0	\$0	\$0	\$0	\$0	\$642
Architect		\$0	\$0	\$0	\$0	\$0	\$192,358	\$24,736	\$0		\$0	\$0	\$0	\$0	\$217,094
Project Management		\$0	\$0	\$0	\$0	\$0	\$16,638	\$9,341	\$0		\$7,845	\$0			\$33,824
Filling Fees		\$0	\$0	\$0	\$0	\$0	\$0	\$2,842	\$0	\$0	\$0	\$0	\$0	\$0	
Total		\$0	\$0	\$0	\$0	\$0	\$658,143	\$50,439	\$0	\$0	\$7,845	\$0	\$0	\$0	\$716,428
Project Budget	\$716,428	· · · · · ·													
Less Other Funding	\$0														
Net	\$716,428														
Actual Measure S Expenditures	\$716,428	1													
Running Balance	\$0	1													
07/000/0												·			
S7100048	]	L]									<u>ا</u>	L		l	
Other Bond Related Expenses (12)	L]										<u> </u>				
Consultants	L]	\$0	\$0	\$0		\$0	\$0	\$0	\$0		\$2,524		\$1,354		
Lease/Rental	L]	\$0	\$0	\$0		\$0	\$0	\$0			\$15,285		\$13,418		
Supplies	L]	\$0	\$0	\$0		\$0	\$3,638	\$0	\$0		\$0		\$0		
Legal	L]	\$0	\$0	\$0		\$0	\$8,917	\$15,649					\$9,186		
Software License	L	\$0	\$0	\$0		\$0	\$0	\$1,997	\$0				\$0		
Advertising	L	\$0	\$0	\$0		\$0	\$2,278	\$0	\$0		\$0		\$0		
Other Contract Services	L	\$0	\$0	\$0			\$17,206	\$23,558	\$19,208				\$12,963		
Moving Services	L]	\$0	\$0	\$0			\$400	\$0	\$0				\$0		
Project Management		\$0	\$0	\$0		\$0	\$17,747	\$13,179	\$11,963	\$0			\$0		
Cap Equipment		\$0	\$0	\$0		\$0	\$0	\$10,086	\$0				\$0		
Non-Cap Equipment		\$0	\$0	\$0		\$0	\$0	\$2,860	\$0				\$0		
Total		\$0	\$0	\$0	\$0	\$1,800	\$50,185	\$67,328	\$55,713	\$37,901	\$31,939	\$77,330	\$36,921	\$25,744	\$384,862
Project Budget	\$609,282	1													
Less Other Funding	\$0														
Net	\$609,282	1													
Actual Measure S Expenditures Running Balance	\$384,862 \$224,420	1													

Projects	Budget	04/05 Final	05/06 Final	06/07 Final	07/08 Final	08/09 Final	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
	Duugot	•			••					12/10/11/14					Companya Potalo
S7100049															
Adv Architecture Related Exp for AA (13)															
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0		\$0		\$0		\$0			\$0				
Architect		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Engineering		\$0	\$0	\$0		\$0	\$0	\$0			\$0		\$0		\$0 \$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$45,734	-\$45,734	\$0	\$0	\$0	\$0	\$0	\$0	\$0	
Project Management		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$0	\$0			\$45,734	-\$45,734	\$0	\$0		\$0	\$0			\$0
Project Budget	\$0									· · · · ·					· · · · ·
Less Other Funding	\$0 \$0 \$0														
Net	\$0														
Actual Measure S Expenditures	\$0														
Running Balance	\$0														
S7100057															
Real Property Acquisition (14)															
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$18,721	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$18,721
Architect		\$0	\$0	\$0		\$0		\$0			\$0				
Engineering		\$0	\$0	\$0		\$0		\$0			\$0				
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$6,336	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,336
Project Management		\$0	\$0	\$0		\$0	\$20,540	\$0			\$0	\$0	\$0		
Total		\$0	\$0	\$0	\$0	\$0	\$45,597	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$45,597
Project Budget	\$45,597					· · · ·				•					
Less Other Funding	\$0														
Net	\$45,597														
Actual Measure S Expenditures	\$45,597														
Running Balance	\$0														
S7100072															
Campus Signage (15)															
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$303	\$0	\$0	\$0	\$0	\$0	\$0	\$303
Consultants		\$0	\$0	\$0	\$0	\$0	\$32,225	\$23,725	\$0	\$0	\$0			\$0	\$55,950
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$187	\$0	\$836	\$0	\$0	\$0	\$1,051	\$2,074
Architect		\$0		\$0		\$0		\$0			\$0				
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$638	\$0	\$0	\$1,440	\$1,325	\$416,937	'\$0	\$420,339
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0		\$0	\$0	\$0		\$22,953			\$8,260	\$8,388	\$28,622	\$165	\$68,388
Cap Equipment		\$0		\$0		\$0		\$156,258			\$0				
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$3,402	\$3,402
Total		\$0	\$0	\$0	\$0	\$0	\$32,225	\$204,064	\$0	\$836	\$9,700	\$9,712	\$445,559	\$4,618	\$706,713
Project Budget	\$706,713														
Less Other Funding	\$0														
Net	\$706,713														
Actual Measure S Expenditures	\$706,713														
Running Balance	\$0														
S															
Cost of Issuance (16)										1					
Cost of Issuance		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$119,470	\$119,470
Total		\$0				\$0		\$0							
Project Budget	\$119,470		,-				<i>7</i> -	÷-	, , , , , , ,						,
Less Other Funding	\$0														
Net	\$119,470														
Actual Measure AA Expenditures	\$119,470														
Running Balance	\$0														
¥ · · ·															

Grand Total


\$7,958,606 \$14,601,366 \$10,740,621 \$8,321,918 \$20,819,624 \$8,933,245 \$617,492 \$651,441 \$878,632 \$1,287,285 \$6,814,769 \$6,083,251 \$12,554,384 \$100,262,635

# SANTA MONICA COMMUNITY COLLEGE DISTRICT Measure AA Project Schedule As of June 30, 2017


	Project Name	Completion	201	5	20	016	20	17		20	18	2019	20	20
101	Environmental Performance - Central Plant Connections	August 2017												
102	Infrastructure & Technology - Information Technology Relocation	Completed												
103	Media and Technology Complex - Academy Site	December 2017												
104	Replacement Health/PE/Fitness/Dance Building with Central Plant	December 2017												
105	Drescher - Academic Modernization, Bookstore, Pico Promenade	Deferred												
106	Replacement Math and Science Extension Building	In Planning												
107	Madison East Wing Seismic Upgrade	Completed												
108	Renovation of Corsair Stadium	Completed												
109	Career Opportunity and Advancement Center (Bundy)	Completed												
110	Malibu Center	September 2019												
111	Business & Facilities Infrastructure	Completed												
112	Master Planning, Program Management, Overhead	On-Going												
113	Energy Efficiency Projects	Completed												
114	Community Classroom & Facility Projects	Completed												
115	Real Property Acquisition	Completed												
116	Roadways, Walkways, Grounds, Parking Lots, and Garages	Deferred												
117	Infrastructure & Technology - Technology	Completed												
118	Infrastructure & Technology - Utility	Completed												
119	Emergency Lighting, Fire Alarm, and Security System	On-Going												
120	Student Services	March 2019						•						
121	Cost of Issuance	On-Going												
				In I	Plann	ing	In	Con	struc	tion				

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
AA 7100062										
Environmental Performance - Central Plant Connections (101)										
Legal		\$0	\$0	\$0	\$125	\$0	\$0	\$0	\$0	\$125
Other Contract Services		\$0	\$0	\$49,837	\$16,239	\$0	\$0	\$0	\$0	\$66,076
Consultants		\$0	\$0	\$0	\$0	\$28	\$0	\$0	\$0	\$28
Building & Additions		\$0	\$0	\$0	\$361	\$729	\$640	\$1,328,592	\$6,934,044	\$8,264,368
Architect		\$0	\$385	\$148,311	\$176,897	\$36,256	\$0	\$0	\$0	\$361,849
Engineering		\$48,500	\$0	\$4,000	\$0	\$152,010	\$39,638	\$66,918	\$138,887	\$449,953
Inspection & Testing		\$0	\$0	\$7,688	\$0	\$0	\$0	\$7,310	\$137,150	\$152,147
Project Management		\$0	\$17,263	\$55,116	\$48,685	\$61,908	\$19,313	\$104,575	\$526,072	\$832,931
Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Total		\$48,500	\$17,648	\$264,951	\$242,307	\$250,931	\$59,591	\$1,507,396	\$7,736,152	\$10,127,475
Project Budget	\$11,206,164									
Less Other Funding	\$0									
Net	\$11,206,164									
Actual Measure AA Expenditures	\$10,127,475									
Running Balance	\$1,078,689									


Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
AA 7100063										
Infrastructure & Technology - IT Relocation (102)										
Supplies		\$0	\$0	\$965	\$8,442	\$3,137	\$2,600	\$0	\$0	\$15,144
Consultants		\$0	\$0	\$0	\$0	\$408	\$0	\$7,800	\$0	\$8,208
Maintenance Contract		\$0	\$0	\$0	\$0	\$107,390	\$0	\$77,074	\$79	\$184,543
Legal		\$0	\$0	\$0	\$1,363	\$50	\$0	\$0	\$0	\$1,413
Printing		\$0	\$0	\$0	\$0	\$1,624	\$0	\$0	\$0	\$1,624
Postage		\$0	\$0	\$0	\$0	\$1,567	\$0	\$0	\$0	\$1,567
Other Contract Services		\$0	\$0	\$2,163	\$15,259	\$23,356	\$0	\$19,050	\$4,500	\$64,328
Moving		\$0	\$0	\$0	\$577	\$266	\$27,655	\$22,618	\$0	\$51,116
Site Improvement		\$0	\$0	\$0	\$24	\$0	\$0	\$0	\$0	\$24
Building & Additions		\$0	\$0	\$0	\$1,767,083	\$9,667,362	\$4,288,987	\$1,203,916	\$165,229	\$17,092,578
Architect		\$105,049	\$482,261	\$505,580	\$183,181	\$287,201	\$236,860	\$120,091	\$0	\$1,920,223
Engineering		\$0	\$0	\$10,037	\$11,065	\$17,147	\$19,512	\$25,994	\$1,956	\$85,712
Inspection & Testing		\$10,291	\$8,793	\$21,449	\$137,523	\$499,982	\$200,262	\$568	\$0	\$878,868
Project Management		\$33,460	\$76,290	\$84,991	\$331,754	\$431,730	\$297,951	\$22,978	\$1,500	\$1,280,653
Cap Equipment		\$0	\$0	\$0	\$29,422	\$645,830	-\$29,090	\$589,604	\$9,811	\$1,245,576
Non-Cap Equipment		\$0	\$0	\$0	\$18,344	\$10,852	\$277,219	\$1,891	\$20,689	\$328,994
Total		\$148,800	\$567,344	\$625,185	\$2,504,035	\$11,697,901	\$5,321,956	\$2,091,584	\$203,764	\$23,160,569
Project Budget	\$23,160,569									
Less Other Funding	\$0									
Net	\$23,160,569									
Actual Measure AA Expenditures	\$23,160,569									
Running Balance	\$0									

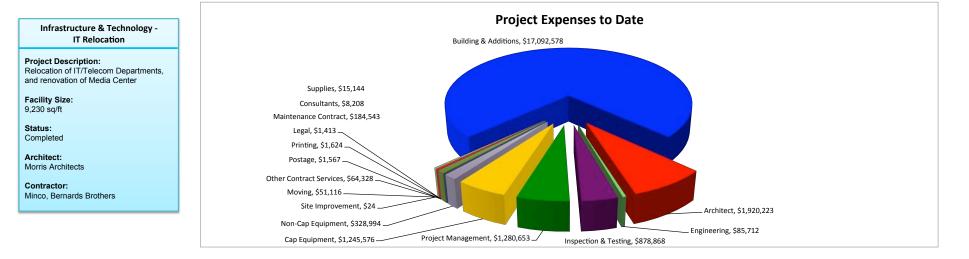

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
AA 7100061										
Media and Technology Complex - Academy Site (103)										
Consultants		\$0	\$0	\$20,675	\$12,576	\$9,488	\$7,789	\$2,102	\$0	\$52,629
Supplies		\$0	\$0	\$0	\$19,481	\$1,048	\$289	\$0	\$9,251	\$30,069
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$15,922	\$15,922
Legal		\$16,903		\$7,958	\$43,363	\$5,066	\$26,186	\$49,155	\$15,435	\$164,065
Software Support		\$0	\$0	\$0	\$1,982	\$0	\$0	\$0	\$6,548	\$8,530
Service Fee		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$17,000	\$17,000
Other Contract Services		\$3,993	\$5,763	\$13,456	\$39,188	\$0	\$0	\$5,853	\$22,622	\$90,875
Moving Expenses		\$0	\$0	\$0	\$38,756	\$0	\$0	\$0	\$0	\$38,756
Site Improvement		\$0		\$0	\$100,505	\$664	\$606	\$476	\$622	\$102,873
Building & Additions		\$0	\$538	\$1,498,660	\$3,543,657	\$11,820,615	\$17,734,534	\$23,465,347	\$16,267,550	\$74,330,900
Architect		\$2,097,553	\$2,508,588	\$295,753	\$265,481	\$778,015	\$517,794	\$1,048,935	\$991,386	\$8,503,504
Engineering		\$16,459	\$29,293	\$9,102	\$29,223	\$8,203	\$72,993	\$118,368	\$72,786	\$356,427
Inspection & Testing		\$64,905	\$27,527	\$123,842	\$235,287	\$563,746	\$1,381,801	\$641,972	\$525,264	\$3,564,343
Project Management		\$121,786	\$233,826	\$269,249	\$506,917	\$800,315	\$930,115	\$1,207,850	\$1,121,670	\$5,191,727
Cap Equipment		\$0	\$0	\$0	\$186,301	\$0	\$0	\$0	\$0	\$186,301
Non-Cap Equipment		\$0	\$0	\$0	\$10,782	\$0	\$0	\$0	\$326,845	\$337,627
Total		\$2,321,599	\$2,805,534	\$2,238,694	\$5,033,499	\$13,987,159	\$20,672,105	\$26,540,059	\$19,392,902	\$92,991,550
Project Budget	\$110,055,056	Received								
Less Other Funding*	\$6,835,391	\$990,441	* Other Funding S	ource:						
Net	\$103,219,665			n \$6,803,412 comn	nited, \$958,462 re	ceived				
Actual Measure AA Expenditures	\$92,991,550		Edison \$31,979.48	3 received						
Running Balance	\$10,228,115									




Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
·										
AA 7100060										
Repl. Health/PE/Fitness/Dance Building with Central Plant (104)										
Consultants		\$0	\$0	\$0	\$14	\$62	\$2,304	\$184	\$0	
Supplies		\$0	\$0	\$0	\$0	\$7,089	\$195	\$484	\$20,947	\$28,715
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$663	\$80	\$742
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$1,209	
Site Improvement		\$0	\$0	\$0	\$0	\$0	\$559	\$440	\$575	\$1,574
Off Campus Printing		\$0	\$0	\$0	\$0	\$0	\$2,165	\$0	\$0	\$2,165
Postage		\$0	\$0	\$0	\$0	\$0	\$1,505	\$0	\$0	\$1,505
Other Contract Services		\$120	\$38	\$112	\$32,634	\$0	\$1,019	\$581	\$0	
Building & Additions		\$0	\$0	\$0	\$817	\$4,188	\$1,623	\$13,783,023	\$14,880,829	\$28,670,479
Architect		\$256,076	\$1,568,564	\$1,790,207	\$518,973	\$177,583	\$364,853	\$585,900	\$373,345	\$5,635,501
Engineering		\$0	\$8,507	\$31,650	\$7,871	\$6,529	\$9,276	\$76,712	\$51,025	\$191,571
Inspection & Testing		\$36,892	\$490	\$21,150	\$1,285	\$360	\$133,756	\$846,765	\$358,724	
Project Management		\$34,968	\$113,379	\$118,783	\$94,768	\$108,528	\$463,418	\$564,240	\$487,065	\$1,985,148
Cap Equipmwnt		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$164,793	\$164,793
Non-Cap Equipment		\$0	\$0	\$0	\$0	\$0	\$9,015	\$0	\$206,229	\$215,244
Total		\$328,056	\$1,690,978	\$1,961,901	\$656,362	\$304,338	\$989,689	\$15,858,991	\$16,544,820	\$38,335,136
Project Budget	\$58,272,030									
Less Other Funding*	\$11,812,230		* Other Funding S	ource:						
Net	\$46,459,800		Measure S \$11,60	3,383 allocated						
Actual Measure AA Expenditures	\$38,335,136		SCE \$190,847.28	Gas Co. \$18,000	received					
Running Balance	\$8,124,664									

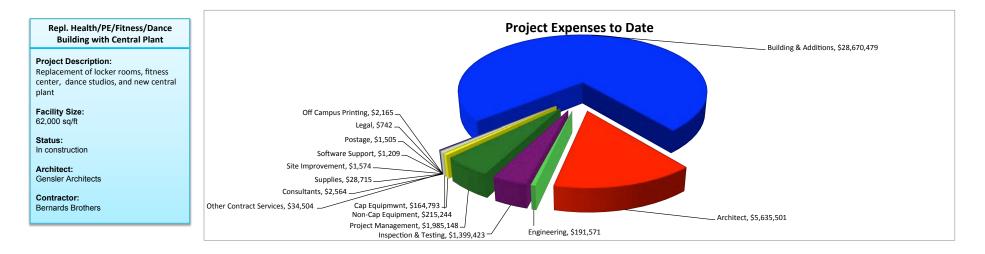

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals		
AA 7100065												
Drescher - Academic Modernization, Bookstore, Pico Promenade (105)												
Legal		\$0	\$0		\$0		\$0	\$0	\$0			
Other Contract Services		\$0	\$0		\$0		\$0	\$0	\$0			
Site Acquisition		\$0	\$0	\$0	\$0		\$0	\$0	\$0			
Inspection & Testing		\$0	\$0	\$0	\$0		\$0	\$0	\$0			
Project Management		\$0	\$0		\$0		\$0	\$0	\$0			
Total		\$0	\$0	\$5,082	\$0	\$0	\$0	\$0	\$0	\$5,082		
Project Budget	\$13,005,082											
Less Other Funding	\$13,000,000	* Other Funding Source:										
Net	\$5,082		Measure V 13,00	0,000 allocated								
Actual Measure AA Expenditures	\$5,082											
Running Balance	\$0											
AA 7100090												
Replacement Math and Science Extension Building (106)												
Legal		\$0	\$0		\$0		\$0	\$0	\$0			
Other Contract Services		\$0	\$0		\$0		\$0	\$0	\$0			
Site Acquisition		\$0	\$0		\$0		\$0	\$0	\$0			
Inspection & Testing		\$0	\$0		\$0		\$0	\$0	\$0			
Project Management		\$0	\$0		\$0		\$0	\$0	\$800	\$5,750		
Total		\$0	\$0	\$0	\$0	\$4,950	\$0	\$0	\$800	\$5,750		
Project Budget	\$90,401,286											
Less Other Funding	\$89,157,278	* Other Funding Source:										
Net	\$1,244,008			336, Measure V \$5		ed						
Actual Measure AA Expenditures	\$5,750	:	State of California	\$40,088,000 pend	ling							
Running Balance	\$1,238,258											

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
AA 7100047										
Madison East Wing Seismic Upgrade (107)										
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$6,197	\$6,197
Consultants		\$0	\$0	\$0	\$0	\$135	\$28	\$0	\$0	\$163
Off Campus Printing		\$0	\$0	\$0	\$0	\$0	\$285	\$0	\$0	\$285
Maintenance Contract		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$357	\$357
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$7,579	\$7,579
Software Support		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$806	\$806
Other Contract Services		\$0	\$364	\$997	\$0	\$0	\$1,328	\$711	\$0	\$3,400
Building & Additions		\$0	\$656	\$312,643	\$0	\$4,248	\$6,030,371	\$8,829,626	\$4,949,223	\$20,126,767
Architect		\$76,073	\$398,050	\$550,589	\$65,444	\$57,480	\$199,100	\$404,764	\$122,764	\$1,874,264
Engineering		\$0	\$0	\$10,707	\$778	\$0	\$13,792	\$33,184	\$37,491	\$95,952
Inspection & Testing		\$0	\$19,848	\$16,752	\$3,036	\$5,851	\$676,323	\$405,443	\$112,876	\$1,240,129
Project Management		\$5,557	\$128,878	\$112,573	\$67,447	\$118,242	\$494,874	\$481,165	\$322,379	\$1,731,114
Cap Equipment		\$0	\$0	\$30,603	\$0	\$0	\$0	\$0	\$537,627	\$568,230
Non-Cap Equipment		\$0	\$0	\$71,827	\$9,788	\$0	\$0	\$0	\$285,236	\$366,851
Total		\$81,630	\$547,796	\$1,106,691	\$146,492	\$185,956	\$7,416,101	\$10,154,894	\$6,382,534	\$26,022,094
Project Budget	\$27,608,816									
Less Other Funding	\$0									
Net	\$27,608,816									
Actual Measure AA Expenditures	\$26,022,094									
Running Balance	\$1,586,722									



Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
	Duuget	oo, ro r mar	10/11/1mai	10/12/11/04	12/10/1114	10/141110	14/10/11/14	10,101111	10/11/1 mai	Combined Totals
AA 7100068								1		
Renovation to Corsair Stadium (108)										
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Building & Additions		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$30,759	\$0	\$0	\$0 \$0	\$0	\$0	\$0	\$30,759
Engineering		\$0	\$0	\$0	\$0 \$0	\$0 \$0	\$0	\$0	\$0	\$0
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Project Management		\$0	\$4,540	\$0	\$0	\$0	\$0	\$0	\$0	\$4,540
Total		\$0	\$35,299	\$0	\$0		\$0	\$0	\$0	\$35,299
Project Budget	\$35,299	++	+,	֥	÷+	÷-	++	÷+*		+,
Less Other Funding	\$0									
Net	\$35,299									
Actual Measure AA Expenditures	\$35,299									
Running Balance	\$0									
· · · · · · · · · · · · · · · · · · ·	÷÷									
AA 7100067, 7100152, 7100155, 7100157		I	1	1	1	1	1			
Business & Facilities Infrastructure (111)										
Supplies		\$0	\$0	\$0	\$1,493	\$4,840	\$0	\$0	\$0	\$6,333
Service Fee		\$0	\$0	\$0	\$12,885	\$0	\$0	\$0	\$0	\$12,885
Consultants		\$0	\$0	\$0	\$0	\$14	\$8	\$0	\$0	\$22
Maintenance Contract		\$0	\$0 \$0	\$0 \$0	\$0	\$1,366	\$0	\$0	\$0	\$1,366
Legal		\$0	\$0 \$0	\$75	\$0	\$0	\$0	\$1,105	\$0	\$1,180
Software License		\$0	\$0 \$0	\$0	\$0	\$375	\$0	\$0	\$0	\$375
Other Contract Services		\$0	\$6,289	\$6,988	\$750	\$0	\$2,209	\$0	\$0	\$16,236
Moving Services		\$0	\$0	\$0	\$395	\$0	\$0	\$0	\$0	\$395
Building & Additions		\$0	\$34,672	\$198,667	\$200,585	\$284,668	\$0	\$0	\$0	\$718,592
Architect		\$0	\$0	\$80,626	\$170,132	\$37,906	\$0	\$0	\$0	\$288,664
Engineering		\$0	\$0	\$0	\$3,705	\$9,735	\$6,840	\$0	\$0	\$20,280
Inspection & Testing		\$0	\$0	\$8,142	\$10,938	\$10,500	\$0	\$0	\$0	\$29,580
Project Management		\$0	\$3,073	\$154,904	\$87,291	\$139,821	\$3,571	\$0	\$0	\$388,659
Cap Equipment		\$0	\$0	\$0	\$35,892	\$80,090	\$0	\$0	\$0	\$115,982
Non-Cap Equipment		\$0	\$89,204	\$0	\$84,590	\$193,782	\$0	\$0	\$0	\$367,576
Total		\$0	\$133,238	\$449,401	\$608,656	\$763,095	\$12,628	\$1,105	\$0	\$1,968,124
Project Budget	\$1,968,124		\$100,200	<b></b>	\$000,000	\$100,000	¥12,020	\$1,100		\$1,000,124
Less Other Funding	\$0									
Net	\$1,968,124									
Actual Measure AA Expenditures	\$1,968,124									
Running Balance	\$0									
r taning Balanco	ψũ									
AA 7100004		I								
Master Planning, Program Management, Overhead (112)										
Supplies		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Architect		\$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0	\$0 \$0	\$139,302	\$187,927	\$0
Project Management		\$0	\$0 \$0	\$0 \$0	\$0 \$0	\$76,015	\$0 \$150	\$139,302	\$49,170	\$125,335
Cap Equipment		\$0	\$0 \$0	\$0 \$0	\$0 \$0	\$70,015	\$150	\$0 \$0		\$125,555
Non-Cap Equipment		\$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0	\$0	\$0 \$0	\$0 \$0
Total		\$0 \$0	\$0 \$0	\$0 \$0	\$0 \$0		\$150	\$139,302	\$237,097	\$452,564
Project Budget	\$750,000	\$U	\$U	\$U	\$U	\$70,015	\$15U	\$13 <del>3</del> ,302	əzər,097	<b>⊉</b> 402,004
Less Other Funding	\$750,000									
Net	\$0									
Actual Measure AA Expenditures	\$452,564									
Running Balance	\$297,436									
	φ <b>∠</b> 97,430									

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
	Lager									
AA 7100154										
Energy Efficiency Projects (113)										
Legal		\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
Other Contract Services		\$0	\$0	\$0	\$0	\$0	\$0			
Building & Additions		\$0	\$0	\$189	\$2,108,853	\$990,389	-\$97,621	\$0		
Architect		\$0	\$0	\$109	\$0	\$990,309	\$0			
Engineering		\$0	\$0	\$0 \$0	\$0		\$0			
Inspection & Testing		\$0	\$0		\$4,020	\$0	\$10,118			
Project Management		\$0	\$0	\$0 \$0	\$0 \$0	\$0	\$825	\$0		
Non-Cap Equipment		\$0	\$0		\$0	\$0	\$0			
Total		\$0 \$0	\$0 \$0		\$2,112,873					
Project Budget	\$3,508,088	φU	φU	\$105	φ <b>2</b> ,112,073	\$330,303	-400,070	φŪ	φU	\$3,010,773
Less Other Funding	\$491,315		* Other Funding S	ource:						
Net	\$3,016,773		DWP \$18.715.00							
Actual Measure AA Expenditures	\$3,016,773		SCE \$446.519.77							
Running Balance	\$3,010,773		Gas Co. \$26,080							
	50		Gas CU. 920,000	IECEIVEU						
AA 7100064	1	I								
Community Classroom & Facility Projects (114)										
		<b>60</b>	<b>*</b> 0	<b>\$</b> 0	¢404	<b>\$</b> 0	<b>*</b> 0	<b>*</b> 0	¢0	£404
Supplies		\$0 \$0	\$0	\$0 \$1,867	\$124	\$0	\$0 \$0			
Legal			\$0		\$1,418 \$0	\$0		\$0		
Other Contract Services Building & Additions		\$0 \$0	\$3,720 \$434,578	\$1,869 \$1,369,441	\$0 \$408,696	\$0 -\$1,003	\$0			
Architect		\$0	\$263,833	\$48,120	\$1,318	\$0	\$0			
Engineering		\$0	\$3,220	\$3,143	\$0	\$0	\$0			
Inspection & Testing		\$0	\$41,002	\$80,885	\$1,495		\$0			
Project Management		\$135	\$117,247	\$143,780	\$27,570	\$0	\$0			
Non-Cap Equipment		\$0	\$0		\$0	\$0	\$0			
Total		\$135	\$863,599	\$1,858,831	\$440,621	-\$1,003	\$0	\$0	\$0	\$3,162,183
Project Budget	\$3,162,183									
Less Other Funding	\$0									
Net	\$3,162,183									
Actual Measure AA Expenditures	\$3,162,183									
Running Balance	\$0									
	-									
AA 7100057										
Real Property Acquisition (115)										
Legal		\$0	\$0	\$0	\$0	\$0	\$0			
Other Contract Services		\$0	\$39	\$7,000	\$0	\$15,800	\$0			
Site Acquisition		\$1,739,979	\$4,001,204	\$9,022,207	\$0	\$0	\$0			
Inspection & Testing		\$8,689	\$7,986	\$0	\$0		\$0			
Project Management		\$0	\$0	\$0	\$0		\$0			
Total	004 000 000	\$1,748,667	\$4,009,228	\$9,029,207	\$0	\$15,800	\$0	\$0	\$5,013,226	\$19,816,127
Project Budget	\$24,902,902									
Less Other Funding	\$0									
Net	\$24,902,902									
Actual Measure AA Expenditures	\$19,816,127									
Running Balance	\$5,086,775									

Infrastructure & Technology (117)         Image of the solution of the solutis of the solutis of the solution of the solution of the solutis o	Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
Radways, Oreunds, Parking Lots, and Garges (116)         Image of the state o											
Supplies         Society of the second s											
Logid         S0         S0         S12         S0         S0         S12         S0         S0         S12         S0         S0         S12         S10         S0         S12         S10         S0         S12         S10         S10         S12         S10         S10         S12			<u> </u>	<u><u></u></u>	<b>*</b> 0	<u>*</u> 0	£4.040	<b>*</b> 0	¢0	<b>*</b> 0	¢4.040
Consultants         S0								\$0			
Offer Contral Services         Si22         Si22         Si22         Si22         Si2         Si2 </td <td></td>											
Building Acciditions         \$183,84         \$6,731         \$133,784         \$327,603         \$975,601         \$60         \$60         \$16,826           Engineering         80         50         \$10,856         \$10,856         \$14,408         80         \$60         \$80											
Architecit         Still											
Engineering Imaged no 1         Stol         St											
Insection A Testing         S13.880         S7.865         S13.581         S20.126         S42.865         S0         S0         S0         S0         S0         S0         S07.781           Total         513.581         S24.404         S12.533         S21.445         S42.605         S10.4381         S11.10         S13.0871           Total         S22.2347         S27.281         S27.821         S22.843         S11.551         S22.852         S0         S0         S21.93671           Total         S22.3347         S27.813         S7.851         S11.55.31         S22.852         S0         S0         S21.8571           Net         S22.3347         S27.813         S41.41         S2.2652         S0         S2.858         S0         S2.8581											
Project Management         S24.404         S12,439         S21,945         S54,095         S10,431         S1,411         S0         S0         S21,937           Project Management         S2,702,417         S23,437         S27,849         S14,9403         S27,395         S1,15512         S2,621         S0         S21,937           Project Management         S23,0377         Measure AL Exponditures         S23,0377         Measure AL Exponditures         S23,0377         Measure AL Exponditures         S23,0377         Measure AL Exponditures         S23,0377         S33,037,077,000,000 allocated           Antro00069         Technology - Technology (1177)         S0         S0<											
Total         Forder Langer         \$223.347         \$273.951         \$1,153.512         \$2,652         \$0         \$0         \$2,130,677           Cess Other Funding         \$4,891.747         \$4,917.47         *Other Funding Status         *Status											
Project Budget         57/022.417 (x1es Other Funding Source: Measure & S3.3817,47, Measure & \$1.000,000 allocated Xctual Measure & AExpenditures         * Other Funding Source: Measure & \$3.3817,47, Measure & \$1.000,000 allocated Xctual Measure & S3.3817,47, Measure & \$1.000,000 allocated Xctual Measure & \$1.000,000 allocated Xctual Measure & \$1.000,000 allocated Xctual Measure & Xctual Measure & \$1.000,000 allocated Xctual Measure & \$100,000,000 allocated Xctual Measure & \$100,000,000 allocated Xctual Measure & \$100,000,000,000,000,000,000,000,000,000											
Less Other Funding         54,891,747           Net         52,130,070           Actual Measure AA Expenditures         52,130,070           Manning Balance         0        <			\$223,347	\$27,804	\$149,403	\$573,951	\$1,153,512	\$2,652	\$0	\$0	\$2,130,670
Net         Stand         Stand         Measure S 33 891,747, Measure V \$1,000,000 allocated           Atzill Measure AA Expenditures         Standing         Standing         Standing           At7100509         Standing         Standing         Standing         Standing           Maintenance Contract         Standing         Standing         Standing         Standing           Standing         Standing         Standing         Standing         Standing         Standing           Standing         Standing         Standing         Standing         Standing         Standing         Standing           Standing	Project Budget		-	+ OII E II O							
Actual Measure AA Expenditures         S2 130 670           Art 700069         0           Art 700069         50           Software         50           Software         50           Software         50           Software         50           Software         50           Software         50           Supples         50           Supples         50           Software         50 <td></td>											
Running Balance         S0           AA 7100069			-	ivieasure S \$3,891	,747, Measure V \$	an,000,000 allocate	ea				
A 700069         Infrastructure & Technology - Technology (117)         Sol         S											
Infrastructure & Technology (117)         Image of the solution of the solutis of the solutis of the solution of the solution of the solutis o	Running Balance	\$0									
Software         Sol         So	AA 7100069										1
Software         Sol         So	Infrastructure & Technology - Technology (117)										
Supplies         Stop         \$13,646         \$7,587         \$0         \$16,966         \$0         \$0         \$33,7186           Other Contract         \$0         \$0,9472         \$46,300         \$0	Software		\$0	\$0	\$0	\$0	\$0	\$218	\$0	\$0	\$218
Maintenance Contract         S0         \$39,472         \$46,300         \$210,581         \$18,944         \$42,415         \$9,472         \$0         \$337,182           Diulfing & Additions         S0         \$0         \$0         \$0         \$49,685         \$00         \$1,45,668         \$0         \$0         \$1,46,668         \$0         \$0         \$1,46,668         \$0         \$0         \$5,46,77         \$500         \$0         \$1,45,668         \$0         \$0         \$5,46,77         \$500         \$1,45,668         \$0         \$0         \$5,46,477         \$50         \$50         \$50         \$50         \$50         \$50         \$50         \$50         \$50         \$50         \$50         \$50         \$50         \$50	Supplies				\$13.646						
Other Contract Services         S0         S0 <ths0< th="">         S0         S0         S0&lt;</ths0<>											
Building & Additions         S0         S1         S0         S2         S33.063         S762.294         S0         S1.456.688         S0         S0         S3.447         S0         S3.447         S0         S3.447         S0         S2.434.417           Case During         \$2.434.417         \$0         \$2.434.417         \$0         \$2.434.417         \$0         \$2.434.417         \$0         \$2.434.417         \$0         \$2.434.417         \$0         \$2.434.417         \$0         \$2.434.417         \$0         \$2.434.417         \$0         \$2.434.417         \$0         \$2.434.417         \$0         \$2.434.417         \$0         \$2.434.417         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0											
Project Management         S0											
Cap Equipment         S0         \$207,423         \$33,063         \$576,294         \$0         \$1145,668         \$0         \$0         \$1,982,447           Non-Cap Equipment         \$0         \$0         \$242,827         \$500         \$0         \$3,447         \$0         \$0         \$42,827         \$500         \$53,638         \$794,963         \$18,944         \$1,256,304         \$9,472         \$0         \$2,434,417           Vel         \$2,434,417         \$0         \$0         \$12,68,966         \$135,838         \$794,963         \$18,944         \$1,256,304         \$9,472         \$0         \$2,434,417           Rula Masere AA Expenditures         \$2,434,417         \$0         \$0         \$12,000         \$0         \$0         \$0         \$12,000         \$0         \$0         \$0         \$12,000         \$0         \$0         \$0         \$12,000         \$0         \$0         \$0         \$12,000         \$0         \$0         \$0         \$0         \$12,000         \$0											
Non-Cap Equipment         S0         S0         S42,827         S500         S0         S3,447         S0         S0         S46,775           Project Budget         \$2,434,417         \$0         \$2,434,417         \$0         \$2,434,417         \$0         \$2,434,417         \$0         \$2,434,417         \$0         \$2,434,417         \$0         \$2,434,417         \$0         \$0         \$2,434,417         \$0         \$0         \$2,434,417         \$0											
Total         \$0         \$216,896         \$135,838         \$794,963         \$18,944         \$1,258,304         \$9,472         \$0         \$2,434,417           Less Other Funding         \$0         \$2,434,417         \$0         \$135,838         \$794,963         \$18,944         \$1,258,304         \$9,472         \$0         \$2,434,417           Actual Measure AA Expenditures         \$2,434,417         \$0											
Project Budget         \$2,434,417           Less Other Funding         \$2,434,417           Actual Measure AA Expenditures         \$2,434,417           Running Balance         \$2,434,417           Actual Measure AA Expenditures         \$2,434,417           Running Balance         \$0           AA7100150	Total										
Less Other Funding         \$0           Net         \$2,434,417           Actual Measure AA Expenditures         \$2,434,417           Runnip Balance         \$0           AA 7100150         \$0           Infrastructure & Technology - Utility (118)         \$0           Sofeware License         \$0           Legal         \$0           Suiding & Additions         \$0           Strigg         \$0           Architet         \$0           Sofeware License         \$0           Legal         \$0           Suiding & Additions         \$0           Sofo \$0         \$0           Sofo \$10         \$0           Sofo \$20         \$0           Sofo \$3,240         \$0	Project Budget	\$2,434,417		,	,	,	1 1/1	. , ,	,		.,.,
Net         \$2.434.417           Actual Measure AA Expenditures         \$2.434.417           Actual Measure AA Expenditures         \$2.434.417           Steman Expenditures         \$2.434.417           Steman Expenditures         \$2.434.417           AA 7100150            Infrastructure & Technology - Utility (118)            Sofeware License         \$0											
Actual Measure AA Expenditures         \$2,434,417           Running Balance         \$0           AA7100150         Infrastructure & Technology - Utility (118)         Infrastructure & Technology - Stating - Sta	Net										
Running Balance         S0           AA 7100150         Infrastructure & Technology - Utility (118)         S0         \$0											
AA 7100150         AA 71000000000         AA 7100000000000000000000000000											
Infrastructure & Technology - Utility (118)		7-									
Sofeware License         \$0         \$12,000         \$0 </td <td>AA 7100150</td> <td></td>	AA 7100150										
Legal       \$0											
Building & Additions         \$0 <td></td>											
Architect       \$0											
Inspection & Testing         \$0         \$4,979         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$4,979         \$0         <											
Project Management         \$0         \$3,240         \$0         \$0         \$0         \$0         \$0         \$0         \$3,240           Cap Equipment         \$0											
Cap Equipment         \$0         \$0         \$7,534         \$0         \$0         \$0         \$0         \$7,534           Non-Cap Equipment         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$0         \$7,534         \$0         \$0         \$0         \$0         \$7,534         \$0											
Non-Cap Equipment         \$0											
Total         \$0         \$20,219         \$7,534         \$0         \$0         \$0         \$0         \$27,753           Project Budget         \$27,753         \$0         \$0         \$0         \$0         \$0         \$27,753           Less Other Funding         \$0											
Project Budget \$27,753 Less Other Funding \$0 Net \$27,753 Actual Measure AA Expenditures \$27,753											
Less Other Funding \$0 Net \$27,753 Actual Measure AA Expenditures \$27,753			\$0	\$20,219	\$7,534	\$0	\$0	\$0	\$0	\$0	\$27,753
Net \$27,753 Actual Measure AA Expenditures \$27,753	Project Budget										
Actual Measure AA Expenditures \$27,753											
	Net										
Running Balance \$0	Actual Measure AA Expenditures										
	Running Balance	\$0									

Projects	Budget	09/10 Final	10/11 Final	11/12 Final	12/13 Final	13/14 Final	14/15 Final	15/16 Final	16/17 Final	Combined Totals
AA 7100153										
Emergency Lighting, Fire Alarm, and Security System (119)										
Supplies		\$0	\$0	\$0	\$0	\$2,348	\$0	\$0	\$2,671	\$5,020
Consultants		\$0	\$0	\$0	\$0	\$0	\$16	\$0	\$0	\$16
Telecom Fee		\$0	\$0	\$0	\$0	\$0	\$800	\$0	\$0	\$800
Maintenance Contract		\$0	\$0	\$648	\$0	\$39,700	\$0	\$2,700	\$0	\$43,048
Software Suppoert		\$0	\$0	\$24,765	\$0	\$106,367	\$0	\$2,232	\$0	\$133,365
Other Contract Services		\$0	\$0	\$0	\$0	\$47,695	\$0	\$4,643	\$1,560	\$53,897
Building & Additions		\$0	\$0	\$0	\$0	\$110	\$2,648,866	\$4,129,145	\$1,308,230	\$8,086,351
Architect		\$0	\$0	\$0	\$0	\$0	\$18,925	\$0	\$0	\$18,925
Enginnering		\$0	\$0	\$0	\$0	\$211,030	\$389,013	\$156,247	\$255,798	\$1,012,088
Inspection & Testing		\$0	\$0	\$0	\$0	\$0	\$0	\$58,831	\$4,800	\$63,631
Project Management		\$0	\$0	\$0	\$0	\$51,008	\$52,044	\$79,285	\$16,500	\$198,836
Cap Equipment		\$0	\$0	\$0	\$0	\$89,415	\$0	\$5,871	\$0	\$95,286
Non-Cap Equipment		\$0	\$0	\$6,087	\$0	\$392,586	\$8,348	\$0	\$0	\$407,022
Total		\$0	\$0	\$31,500	\$0	\$940,259	\$3,118,012	\$4,438,953	\$1,589,560	\$10,118,284
Project Budget	\$11,520,794									
Less Other Funding	\$0									
Net	\$11,520,794									
Actual Measure AA Expenditures	\$10,118,284									
Running Balance	\$1,402,510									
· · · · · · · · · · · · · · · · · · ·										
AA										
Cost of Issuance (121)										
Cost of Issuance		\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$213,026	\$498,026
Total		\$0	\$0	\$0	\$0	\$0	\$285,000	\$0	\$213,026	\$498,026
Project Budget	\$498,026									
Less Other Funding	\$0									
Net	\$498,026									
Actual Measure AA Expenditures	\$498,026									
Running Balance	\$0									
, v										
Grand Total		\$4,900,734	\$10,935,584	\$17,864,407	\$13,113,759	\$30,388,248	\$39,049,510	\$60,741,756	\$57,313,878	\$234,307,876

## SMC Bond Program Contractor List as of 6-30-2017

Student Services (Measure U #0, Measure S #9, Measure AA #120): Architect – Steinberg Architects, Morris Architects Contractor – Minco, Bernards Brothers Engineering – IVA, Cogent Energy Engineering, XL Fire Inspection & Testing – Geo Labs, BTC Labs - Vertical V, Peak Survey, LPI Rango Inc., Twining Project Management – LPI
Replacement Health/PE/Fitness/Dance Building (Measure S #4, Measure AA #104):

Architect – Gensler Architects Contractor – Bernards Brothers Engineering – IVA, Glumac Inspection & Testing – Geo Labs, Ellis Environmental, Twining, Rango Inc. Project Management – LPI

Early Childhood Development (Measure S #5): Architect – Carde Ten Architects Consultant – Child Educational Center Contractor – N/A Engineering – N/A Inspection & Testing – Geo Labs Project Management – LPI

Malibu Site (Measure S #6, Measure AA #110): Architect – Quatro Design Group Contractor – N/A Consultant – m2 Strategic, Parker Environmental Engineering – Ensitu Services Inspection & Testing – Peak Surveys, Ellis Environmental, JL Inspection Project Management – LPI, m6 Strategic

Energy Efficiency Projects (Measure S #7, Measure AA #113): Architect – N/A Contractor – Compass Energy Solutions, Johnson Controls Engineering – Compass Energy Solutions, Johnson Controls Inspection & Testing – Ellis Environmental

Environmental Performance (Measure AA #101): Architect – Kishimoto Architects Contractor – SJ Amoroso Construction Engineering – P2S Engineering Inspection & Testing – Cannon, Peak Surveys Project Management – LPI Information Technology Relocation (Measure AA #102): Architect – Morris Architects Contractor – Minco, Bernards Brothers, Eidim AV Technology Engineering – IVA, P2S Engineering Inspection & Testing - Cannon, Peak Surveys, Geo Labs, Ellis Environmental, Twining, JL Inspection, Rango Inc. Project Management – LPI, CCS Presentation Media and Technology Complex (Measure AA #103): Architect - Clive Wilkinson Architects, Morris Architects Contractor – H.B. Parkco Construction, Fast Track Construction. CW Driver, Dimension Data, Key Code Media Consultant – EEG Services Engineering – IVA, P2S Engineering Inspection & Testing – Twining, Geo Labs, BTC Labs – Vertical V, **JL Inspection, EEG Services, Ellis Environmental, Rango** Inc., Cannon Project Management - LPI Madison East Wing Seismic Upgrade (Measure AA #107): Architect – DLR Group – WWCOT, LPI Contractor – Trimax, Bernards Brothers, Dimension Data Engineering – IVA, Glumac Inspection & Testing – Twining, Peak Surveys, LPI, All Group Engineering, EEG Services, Ellis Environmental Project Management - LPI Business & Facilities Infrastructure (Measure AA #111): Architect – LPI, Gwynne Pugh Urban Studio Contractor - REC+S, Inc., Omega Construction, Concept Consultant, Inc. Engineering – N/A Inspection & Testing – Ellis Environmental, IL Inspection Project Management – LPI Community Classroom & Facility Project (Measure AA #114) Architect – Morris Architects Contractor – Waisman Construction, Spinitar, Trimax Engineering – IVA Inspection & Testing – LPI, Twining Project Management – LPI

Satellite Campus Parking Facilities and Roadway Improvements (Measure S #8) Architect – N/A Contractor – N/A Engineering – MK Engineering Group Inspection & Testing – N/A Project Management – LPI

Roadways, walkways, Grounds, Parking Lots, and Garages (Measure AA #116) Architect – LPI, DLR Group - WWCOT Contractor – Trimax, Pub Construction Consultant – Walker Parking Engineering – MK Engineering Inspection & Testing – Ellis Environmental, Peak Surveys, LPI Project Management – LPI

Emergency Lighting, Fire Alarm, and Security System (Measure AA #119) Architect – N/A Contractor – Red Hawk Fire and Security, Nexus Consultant – IVA Engineering – MDC Engineers Inspection & Testing – Rango Inc. Project Management – LPI

Signage Safety/Information (Measure S #15) Architect – N/A Contractor – Sign Excellence Consultant – APCO Engineering – N/A Inspection & Testing – N/A Project Management – LPI
